



सत्यमेव जयते




OCMS

Ministry of Statistics & Programme Implementation

Government of India
Ministry of Statistics and Programme Implementation

472nd ————— *Flash Report on* **Central Sector Infrastructure** **Projects** —————

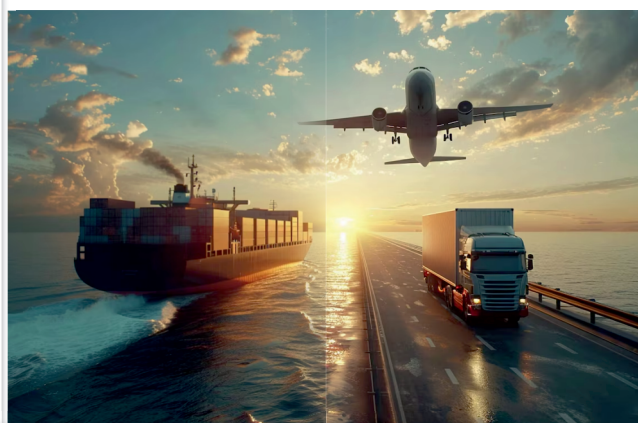

(Rs. 150 crore & above)

February 2025


CONTENTS

Synopsis	1-2
List of Tables	3-242
Table:-1. Overview of Ongoing Projects: Sector-wise Distribution.....	3-4
Table:-2. Overview of Ongoing Projects: State-wise Distribution.....	5-7
Table:-3. Project List: Completed during February 2025.....	8-12
Table:-4. Project List: Added during February 2025.....	13-13
Table:-5. Project List: Frozen/Deleted during February 2025.....	14-14
Table:-6. Project List: Ongoing Projects of North-East Region.....	15-37
Table:-7. Project List: Ongoing Projects as of 28th February 2025.....	38-242


SYNOPSIS

Flash Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above


Total Ongoing Projects
(1682, ₹25,82,886.62 crore)

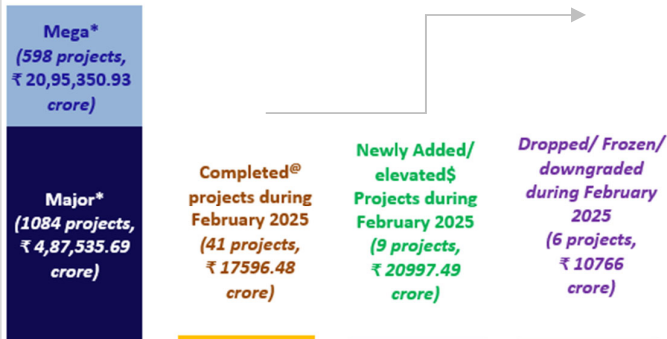


Note: @ Indicated legend is in format (Project Count, Cumulative Expenditure)
 other Indicated legends are in format (Project count, Original Cost)
 * Mega Project if having original cost >= 1000 crore
 * Major Project if original cost < 1000 crore
 \$ reported Anticipated cost more than 150 crore
 # reported Anticipated cost less than 150 crore

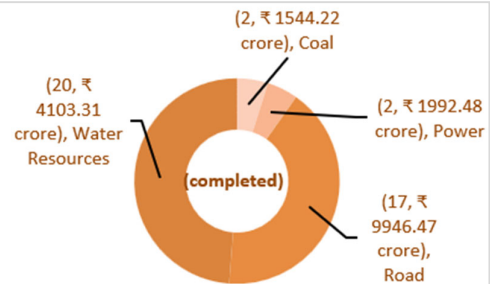




Note: all indicated legends are in format (Project count, Cumulative expenditure)

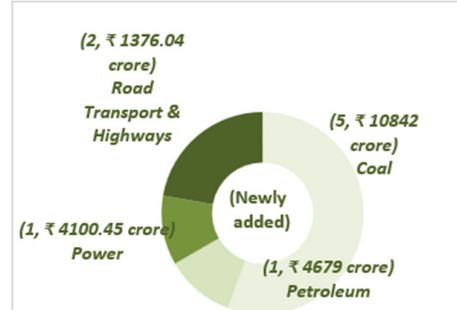

Note: all indicated legends are in format (Project count, Original Cost)

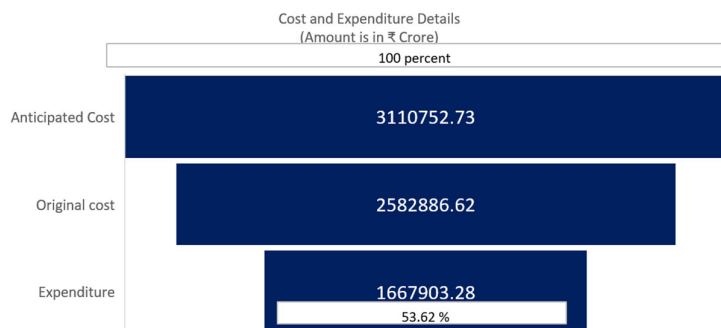


Total North East Region Ongoing Projects
(210, ₹17,6023.98 crore)

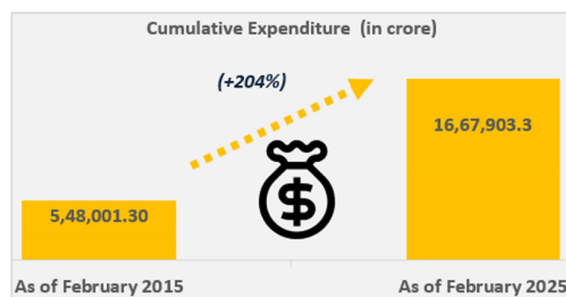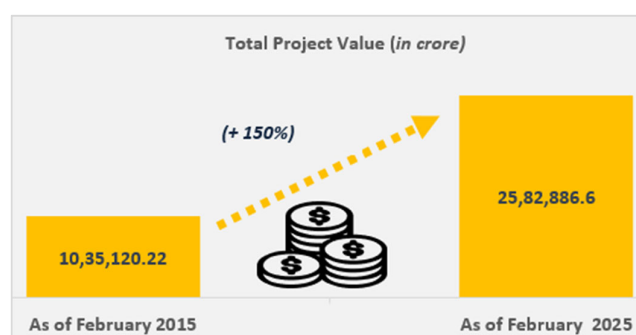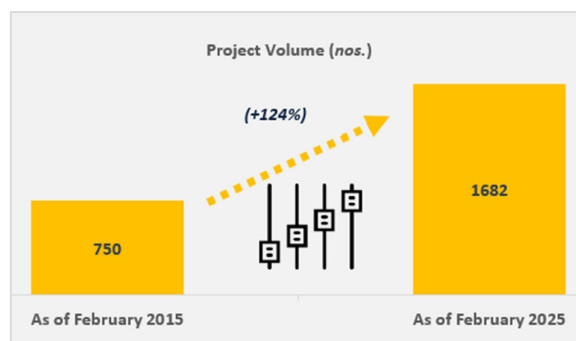

State Comparison : Major States (as per count)


[Outer Ring:Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

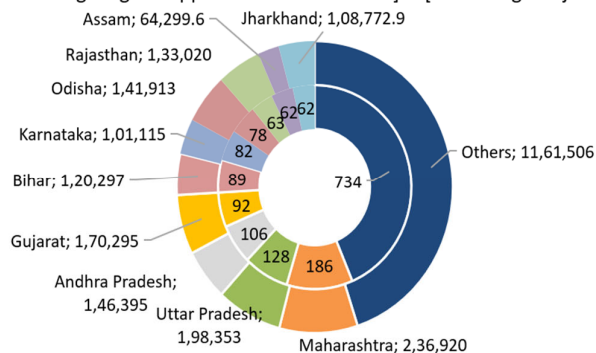


*Others include Tamilnadu, Madhya Pradesh, Delhi, Chhattisgarh, Haryana, Jammu & Kashmir, West Bengal, Kerala, Arunachal Pradesh, Punjab, Telangana, Uttarakhand, Himachal Pradesh, Manipur, Sikkim, Nagaland, Mizoram, Meghalaya, Tripura, Goa, A&N Iland, Ladakh and Multistate

Sectoral Comparison : Major Sectors (as per count)

[Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

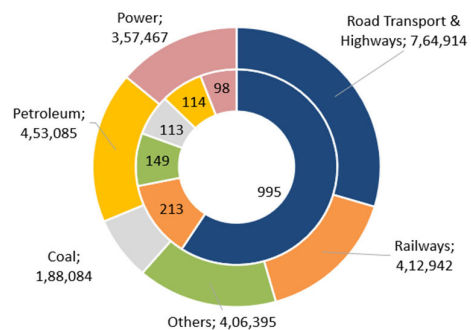

*Others include Water Resources, Civil Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Atomic energy, Home Affairs, Finance, DPIIT, DONER, Renewable Energy, Shipping & Ports, and Social Justice

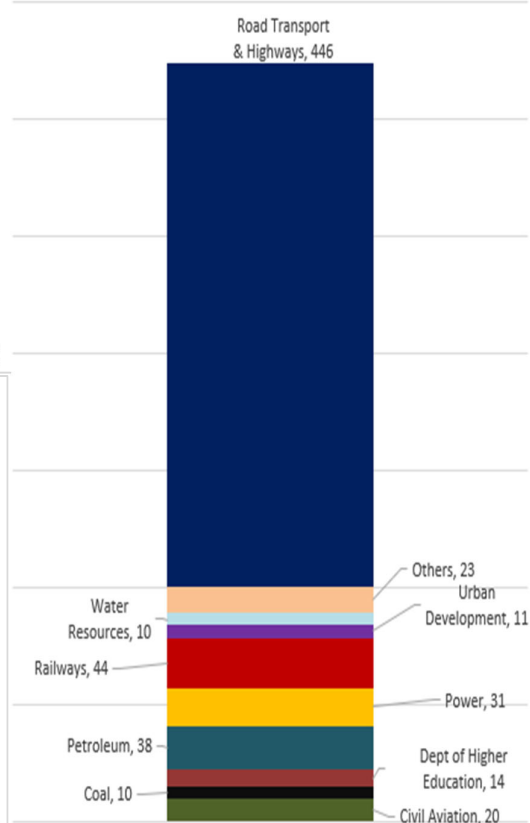Sectoral Distribution of total 647 projects with reported Physical Progress between 80-100%

Note: This report is as of February 2025, based on the (non-exhaustive) list of projects and information as reported by Line Ministries/implementing agencies on the OCMS (www.cspm.gov.in) portal latest by 8th March 2025.

A decorative scroll graphic with a light gray background and a dark gray border. The scroll is unrolled, with the top and bottom edges showing a dark gray shadow. The text "LIST OF TABLES" is centered within the scroll.

LIST OF TABLES

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	CIVIL AVIATION	41	28,200.17 (29,334.64) {32,092.62}	17,826.90
2	COAL	113	188,083.71 (192,627.75) {197,457.00}	65,192.11
3	DEPARTMENT OF HIGHER EDUCATION	20	9,680.92 (10,076.78) {10,127.07}	7,563.79
4	DPIIT	2	24,857.00 (31,457.00) {32,085.00}	16,146.72
5	FINANCE	2	577.27 (577.27) {569.04}	399.67
6	HEALTH AND FAMILY WELFARE	8	7,301.27 (7,358.40) {7,356.19}	4,862.03
7	HOME AFFAIRS	5	2,025.73 (2,949.25) {2,949.25}	2,449.20
8	MINES	8	7,559.78 (9,356.73) {9,833.57}	5,666.41
9	PETROLEUM	114	453,084.74 (510,893.64) {521,508.50}	2,64,675.47
10	POWER	98	357,467.03 (375,782.34) {439,920.36}	2,16,251.18
11	RAILWAYS	213	412,942.26 (532,643.20) {651,647.20}	4,35,962.61
12	ROAD TRANSPORT AND HIGHWAYS	995	764,913.52 (796,210.15) {808,253.14}	3,98,363.07
13	SHIPPING AND PORTS	1	5,369.18 (5,061.15) {5,061.15}	3,314.48
14	SOCIAL JUSTICE	1	170.99 (170.99) {170.99}	73.80
15	STEEL	13	12,381.62 (16,313.15) {16,313.15}	6,851.75
16	TELECOMMUNICATIONS	6	26,961.69 (26,949.89) {26,949.89}	8,150.32

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
17	URBAN DEVELOPMENT	27	265,881.46 (272,720.33) {286,578.30}	1,88,875.92
18	WATER RESOURCES	15	15,428.28 (15,429.03) {61,880.31}	25,277.85
	Total	1682	2,582,886.62 (2,835,911.69) {3,110,752.73}	16,67,903.28

*Either Revised or Original Cost

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ANDAMAN AND NICOBAR ISLANDS	10	2,956.02 (3,029.18) {3,010.04}	1,801.47
2	ANDHRA PRADESH	106	146,394.74 (156,575.07) {209,836.78}	1,25,850.46
3	ARUNACHAL PRADESH	19	46,132.10 (46,195.63) {66,045.78}	32,047.81
4	ASSAM	62	64,299.61 (64,604.42) {74,018.39}	46,070.61
5	BIHAR	89	120,297.42 (137,982.31) {148,672.29}	95,087.36
6	CHHATTISGARH	52	74,442.42 (78,499.19) {80,285.62}	33,849.84
7	DELHI	21	90,318.50 (95,772.35) {94,589.54}	74,756.92
8	GOA	4	1,526.58 (1,526.58) {1,613.08}	775.59
9	GUJARAT	92	170,294.74 (177,161.83) {179,701.93}	84,199.17
10	HARYANA	28	66,918.90 (76,247.06) {76,298.65}	37,725.08
11	HIMACHAL PRADESH	29	27,974.61 (29,004.29) {45,826.06}	30,890.78
12	JAMMU AND KASHMIR	54	75,963.99 (111,538.56) {123,986.08}	77,554.91
13	JHARKHAND	62	108,772.87 (115,318.41) {116,738.71}	63,470.38
14	KARNATAKA	82	101,114.55 (103,540.88) {105,197.86}	48,585.23
15	KERALA	32	64,106.75 (69,637.72) {70,321.90}	33,873.52

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
16	LADAKH	6	2,474.97 (2,474.97) {2,634.64}	1,203.63
17	MADHYA PRADESH	59	103,950.88 (110,148.68) {119,869.01}	38,613.16
18	MAHARASHTRA	186	236,920.28 (241,413.45) {272,676.85}	1,32,868.44
19	MANIPUR	30	15,093.08 (22,949.14) {30,156.61}	19,084.59
20	MEGHALAYA	14	5,877.44 (5,868.46) {5,822.82}	3,404.06
21	MIZORAM	20	11,677.77 (14,305.75) {20,243.12}	16,567.22
22	MULTI STATE	52	282,424.29 (334,194.65) {352,853.23}	2,39,085.05
23	NAGALAND	31	11,425.91 (17,111.27) {16,810.24}	8,608.76
24	ODISHA	78	141,913.44 (145,062.21) {153,639.47}	62,458.06
25	PUNJAB	39	37,885.48 (38,173.84) {38,262.08}	14,986.03
26	RAJASTHAN	63	133,019.86 (161,199.81) {162,240.73}	85,147.94
27	SIKKIM	21	14,334.80 (25,364.44) {26,224.73}	17,731.23
28	TAMIL NADU	62	87,827.48 (96,966.55) {102,583.97}	27,130.21
29	TELANGANA	52	28,645.95 (29,039.83) {30,970.34}	15,013.63
30	TRIPURA	13	7,183.27 (7,220.16) {7,305.64}	1,101.27

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
31	UTTAR PRADESH	128	198,352.66 (205,351.32) {220,046.81}	1,08,487.91
32	UTTARAKHAND	32	36,763.91 (42,031.16) {64,127.39}	44,733.66
33	WEST BENGAL	54	65,601.35 (70,402.52) {88,142.34}	45,139.30
	Total	1682	2,582,886.62 (2,835,911.69) {3,110,752.73}	16,67,903.28

***Either Revised or Original Cost**

Table:-3. Project List: Completed during February 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
COAL					
	1	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) (NCL) (N06000162) (MADHYA PRADESH)	1,255.17	03/2022	1,254.21
	2	MADHUBAND NLW WASHERY (BCCL) (N06000126) (JHARKHAND)	289.45	05/2014	300.01
POWER					
	3	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN (PGCIL) (N18000264) (MULTI STATE)	1,931.39	02/2020	1,972.44
	4	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PHASE-IV PART-I (BIKANER COMPLEX) PAR (PGCIL) (N18000372) (RAJASTHAN)	202.39	01/2025	20.04
ROAD TRANSPORT AND HIGHWAYS					
	5	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST (NHAI) (N24000655) (MAHARASHTRA)	247.02	03/2020	93.29
	6	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO (MoRTH) (N24001241) (RAJASTHAN)	255.23	10/2022	256.00
	7	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001377) (MAHARASHTRA)	731.89	01/2022	692.21
	8	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001378) (MAHARASHTRA)	362.46	01/2022	352.01

Table:-3. Project List: Completed during February 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	9	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001379) (MAHARASHTRA)	594.75	01/2022	585.20
	10	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432) (ASSAM)	300.00	08/2024	439.65
	11	PATAS-VASUNDE PHATA - BARAMATI BYPASS (NHAI) (N24001501) (MAHARASHTRA)	531.86	09/2023	520.71
	12	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-8) (NHAI) (N24001561) (RAJASTHAN)	839.63	10/2023	839.63
	13	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH. 319.400 TO CH. 331.030) [HARDEOGANJ VILL (NHAI) (N24001566) (RAJASTHAN)	1,640.10	05/2023	1,248.59
	14	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON (NHAI) (N24001569) (RAJASTHAN)	1,425.02	03/2023	1,420.03
	15	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S (NHAI) (N24001571) (RAJASTHAN)	1,341.36	12/2023	1,089.73
	16	REMAINING WORK OF 2L+PS OF TRICHY - KARAUKUDI SECTION OF NH-210, INCLUDING TRICHY BYPASS (NHAI) (N24001604) (TAMIL NADU)	166.90	03/2021	121.94

Table:-3. Project List: Completed during February 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	17	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D (NHAI) (N24001756) (MADHYA PRADESH)	1,352.56	10/2024	843.65
	18	4L OF SUHAGADI TO BARDIYA AMRA FROM KM. 89.200 TO KM. 135.351 OF NH-752D (PKG-III) (NHAI) (N24001758) (MADHYA PRADESH)	823.05	10/2024	402.85
	19	4L OF HARDA - BETUL (PKG-II) FROM KM. 30.00 TO KM.81.00 [TEMAGAON TO CHICHOLI] (NHAI) (N24001761) (MADHYA PRADESH)	520.28	02/2025	392.86
	20	DEVELOPMENT OF 4L UER II [PACKAGE - V] (SPUR TO BAHADURGARH BYPASS) (NH-10) FROM KM. 0.00 TO KM.7.30 (NHAI) (N24001778) (DELHI)	801.46	10/2023	473.76
	21	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND) (MoRTH) (N24000885) (WEST BENGAL)	160.27	09/2023	174.36
WATER RESOURCES					
	22	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH (UK JalNigam) (N30000004) (UTTARAKHAND)	158.00	11/2019	107.86
	23	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA (UP JalNigam) (N30000006) (UTTAR PRADESH)	767.59	09/2021	276.97
	24	FARRUKHABAD I AND D AND STP WORKS HAM (UP JalNigam) (N30000008) (UTTAR PRADESH)	213.62	03/2022	177.62

Table:-3. Project List: Completed during February 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	25	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS (UP JalNigam) (N30000010) (UTTAR PRADESH)	967.23	09/2021	254.98
	26	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH (UP JalNigam) (N30000013) (UTTAR PRADESH)	271.39	08/2021	182.26
	27	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 (DJB) (N30000015) (DELHI)	211.79	12/2021	208.71
	28	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S (DJB) (N30000016) (DELHI)	239.11	02/2022	268.13
	29	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI (DJB) (N30000017) (DELHI)	515.07	01/2021	388.08
	30	MATHURA SEWERAGE SCHEME (UP JalNigam) (N30000019) (UTTAR PRADESH)	460.45	12/2020	315.30
	31	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH (UP JalNigam) (N30000022) (UTTAR PRADESH)	206.05	10/2021	140.22
	32	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH (UP JalNigam) (N30000025) (UTTAR PRADESH)	298.12	07/2021	103.24
	33	I AND D AND STP AT CHAPPRA (BUIDCO) (N30000028) (BIHAR)	236.15	12/2020	150.75

Table:-3. Project List: Completed during February 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	34	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR (BUIDCO) (N30000037) (BIHAR)	225.77	03/2020	363.79
	35	SEWERAGE SCHEME AT PAHARI ZONE V PATNA (BUIDCO) (N30000040) (BIHAR)	356.37	04/2021	312.30
	36	SEWERAGE TREATMENT PLANT AT PAHARI PATNA (BUIDCO) (N30000043) (BIHAR)	191.62	11/2020	124.40
	37	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH (KMDA) (N30000045) (WEST BENGAL)	185.22	12/2021	49.99
	38	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR (KMDA) (N30000046) (WEST BENGAL)	274.76	12/2019	278.33
	39	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE (KMDA) (N30000047) (WEST BENGAL)	272.32	04/2020	307.73
	40	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI (KMDA) (N30000048) (WEST BENGAL)	172.10	12/2021	47.20
	41	INTERCEPTION AND DIVERSION WITH STP AT BALLY (KMDA) (N30000049) (WEST BENGAL)	164.93	12/2021	45.45
		Total	22,159.90		17,596.48

Table:-4. Project List: Added during February 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
<u>COAL</u>	1	BLOCK-E OCP (15 MTY) (BCCL) (N06000287) (JHARKHAND)	3-2024	5,850.83 (N.A.) {5,850.83}	3/2029 (N.A.) {3/2029}
	2	BALABHADRA OCP (MCL) (N06000288) (ODISHA)	4-2023	978.44 (N.A.) {978.44}	3/2030 (N.A.) {3/2030}
	3	INTEGRATED KULDA GARJANBAHAL OCP (MCL) (N06000289) (ODISHA)	4-2023	3,563.50 (N.A.) {3,563.50}	3/2030 (N.A.) {3/2030}
	4	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290) (ASSAM)	7-2022	159.77 (N.A.) {159.77}	11/2030 (N.A.) {11/2030}
	5	TIRAP OCP (CIL) (N06000291) (ASSAM)	11-2022	289.46 (N.A.) {289.46}	11/2027 (N.A.) {11/2027}
<u>PETROLEUM</u>	6	LUBE MODERNIZATION AND BOTTOM UPGRADATION PROJECT (HPCL) (N16000540) (MAHARASHTRA)	12-2024	4,679.00 (N.A.) {4,679.00}	3/2028 (N.A.) {3/2028}
<u>POWER</u>	7	600 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000406) (GUJARAT)	4-2022	4,100.45 (N.A.) {4,100.45}	3/2026 (N.A.) {3/2026}
<u>ROAD TRANSPORT AND HIGHWAYS</u>	8	CONSTRUCTION OF AMETHI BYPASS (PART-II) AT KM.30.050 OF NH-931 UNDER EPC MODE IN THE STATE OF UTTAR (MoRTH) (N24002214) (UTTAR PRADESH)	12-2022	283.86 (N.A.) {283.86}	2/2027 (N.A.) {2/2027}
	9	DEVELOPMENT OF SIX LANE ACCESS CONTROLLED GREEN FIELD HIGHWAY FROM KAVULAKUNTALA (KM.196+000) TO NARA (NHAI) (N24002215) (ANDHRA PRADESH)	2-2023	1,092.18 (N.A.) {1,092.18}	2/2027 (N.A.) {2/2027}
<u>Grand Total</u>				20,997.49 (-) {20,997.49}	

Table:-5. Project List: Frozen/Deleted during February 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore	Progress (%)
COAL						
	1	GARJANBAHAL OCP (MCL) (N06000117) (ODISHA)	1,375.38	03/2021	849.48	0
	2	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY (SECL) (N06000008) (CHHATTISGARH)	7,612.33	03/2023	4,647.14	0
	3	MUNGOLI NIRGUDA EXTENSION (DEEP) OC (WCL) (N06000231) (MAHARASHTRA)	826.80	03/2026	518.85	0
	4	KULDA EXPANSION OCP- 15 MTY (MCL) (N06000248) (ODISHA)	348.16	03/2018	207.75	0
ROAD TRANSPORT AND HIGHWAYS						
	5	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276) (MANIPUR)	228.97	04/2022	-	0
	6	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS (NHA) (N24000176) (TAMIL NADU)	374.00	05/2013	374.00	88.05
		Total	10,765.64		6,597.22	

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ARUNACHAL PRADESH	CIVIL AVIATION	1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (N.A.) {3/2025}	645.63 (N.A.) {712.15}	684.18	99.29
	POWER	2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	23,437.47	94.86
		3	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,026.06	14.23
	ROAD TRANSPORT AND HIGHWAYS	4	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (N.A.) {3/2025}	180.57 (244.10) {180.57}	160.46	96.62
		5	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2-2017	4/2022 (N.A.) {11/2023}	167.28 (N.A.) {167.28}	145.20	100
		6	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (N.A.) {6/2025}	1,718.59 (1,718.59) {1,718.59}	708.22	71
		7	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9-2016	12/2019 (N.A.) {9/2024}	568.92 (568.92) {568.92}	508.65	100
		8	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (N.A.) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		9	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (N.A.) {2/2025}	301.06 (N.A.) {301.06}	177.73	74.95
		10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3-2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100
		11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3-2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	588.85	100
		12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3-2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	480.44	100
		13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	389.68	95.26
		14	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2-2021	3/2024 (N.A.) {12/2024}	588.09 (N.A.) {588.09}	497.36	100
		15	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6-2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	366.59	100
		16	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	165.78	39

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		17	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (N.A.) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		18	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8-2020	4/2022 (N.A.) {9/2024}	294.04 (N.A.) {294.04}	147.13	100
		19	JORAM ? KOLORIANG ROAD FROM EXISTING KM 122.600 TO KM 138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (N.A.) {3/2025}	184.88 (N.A.) {184.88}	99.32	97.42
ASSAM	CIVIL AVIATION	20	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (N.A.) {5/2025}	1,142.00 (N.A.) {2,333.00}	1,647.43	80.61
	COAL	21	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	0.00	0
		22	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	0.00	0
	HEALTH AND FAMILY WELFARE	23	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (N.A.) {11/2024}	875.00 (873.92) {860.00}	782.74	99.3
	PETROLEUM	24	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.50	11.1
		25	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	56.33	88
		26	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	231.17	45.2
		27	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	166.40	42

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		28	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (N.A.) {6/2025}	543.91 (726.93) {726.93}	491.56	93.89
		29	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	14,677.15	70.6
		30	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,024.34	82.9
		31	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (N.A.) {5/2026}	412.00 (509.84) {509.84}	373.67	81.1
		32	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (N.A.) {9/2026}	277.00 (N.A.) {277.00}	166.84	61.6
		33	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (N.A.) {4/2025}	860.00 (N.A.) {860.00}	470.22	93.5
		34	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (N.A.) {6/2025}	430.76 (N.A.) {430.76}	279.38	80.06
		35	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	80.15	27
		36	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (N.A.) {7/2027}	156.36 (156.36) {156.36}	33.16	23

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		37	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (N.A.) {7/2027}	384.04 (N.A.) {384.04}	66.71	21.2
	RAILWAYS	38	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,570.03	92.3
	ROAD TRANSPORT AND HIGHWAYS	39	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (N.A.) {925.47}	192.50	30.65
		40	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	313.22	64.13
		41	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {3/2025}	625.64 (N.A.) {625.64}	522.74	97.22
		42	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3-2022	7/2024 (N.A.) {10/2024}	215.27 (N.A.) {215.27}	151.29	100
		43	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {5/2025}	204.10 (N.A.) {204.10}	136.11	92.12
		44	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	475.46	93.54
		45	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (N.A.) {6/2024}	175.00 (N.A.) {175.00}	200.80	100
		46	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION-HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	480.84	66.46

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		47	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {3/2025}	457.72 (N.A.) {457.72}	355.87	99.02
		48	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	18.59	12.24
		49	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	173.66	52.35
		50	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	9.62	15
		51	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,275.48	58.18
		52	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.73	100
		53	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	125.60	61.53
		54	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (N.A.) {5/2025}	261.13 (N.A.) {261.13}	64.96	57.26
		55	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (N.A.) {4/2025}	217.50 (N.A.) {217.50}	84.36	68.03
		56	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	216.83	97.76
		57	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (N.A.) {5/2025}	216.49 (241.52) {216.49}	104.36	81.26

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		58	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {3/2025}	437.39 (N.A.) {437.39}	468.40	78.2
		59	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	455.98	30.1
		60	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1-1991	6/2019 (N.A.) {6/2025}	520.01 (N.A.) {520.01}	305.01	95.85
		61	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (N.A.) {6/2025}	289.99 (N.A.) {289.99}	232.95	87.62
		62	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {3/2025}	294.17 (N.A.) {294.17}	359.24	85.59
		63	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {3/2025}	252.00 (N.A.) {330.30}	193.59	60.28
		64	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	369.39	55.23
		65	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	337.68	54.35

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		66	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	397.28	51.5
		67	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	286.30	87.68
		68	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	248.91	86.74
		69	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	463.59	34.62
		70	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	267.46	19.46
		71	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	374.62	19.25
		72	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	222.22	67.75
		73	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	125.03	12.2
		74	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3-2023	12/2025 (N.A.) {12/2026}	643.42 (N.A.) {643.42}	69.46	8.89

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		75	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	209.87	28.02
		76	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	95.94	17.15
		77	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.06	100
		78	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	445.96	24.05
		79	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	893.96	50.09
		80	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	244.30	39.56
		81	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	328.61	45.12
MANIPUR	CIVIL AVIATION	82	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (N.A.) {3/2026}	499.00 (N.A.) {499.00}	134.58	38.16
	RAILWAYS	83	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	3/2011 (N.A.) {12/2028}	4,454.17 (12,274.06) {19,517.70}	15,096.58	81.5
	ROAD TRANSPORT AND HIGHWAYS	84	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (N.A.) {3/2026}	578.98 (N.A.) {578.98}	106.92	56.7

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		85	MARREM KHULLEN TO JESSAMI SECTION IMPHAL- UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	0.00	4
		86	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	0.00	9.88
		87	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (N.A.) {3/2025}	310.76 (N.A.) {310.76}	129.15	90.86
		88	IMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (N.A.) {12/2025}	760.16 (N.A.) {760.16}	102.90	46.3
		89	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (N.A.) {9/2025}	315.56 (N.A.) {315.56}	110.91	74.92
		90	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (N.A.) {5/2025}	292.24 (N.A.) {292.24}	127.86	88.64
		91	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (N.A.) {5/2025}	365.53 (N.A.) {365.53}	156.31	77.36
		92	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (N.A.) {5/2025}	167.95 (204.12) {167.95}	88.05	69.89
		93	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (N.A.) {5/2025}	177.76 (N.A.) {177.76}	89.67	80.53
		94	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (N.A.) {6/2025}	379.39 (N.A.) {379.39}	198.61	57.91

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		95	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (N.A.) {5/2025}	226.32 (N.A.) {226.32}	96.41	73.82
		96	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (N.A.) {3/2025}	188.36 (N.A.) {188.36}	126.71	99.02
		97	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3-2021	12/2022 (N.A.) {3/2026}	195.14 (N.A.) {195.14}	61.81	50.79
		98	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (N.A.) {5/2025}	234.08 (N.A.) {234.08}	139.45	90.69
		99	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (N.A.) {10/2025}	410.68 (N.A.) {410.68}	124.31	61.42
		100	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (N.A.) {9/2025}	504.76 (N.A.) {504.76}	148.02	67.3
		101	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (N.A.) {3/2025}	152.11 (N.A.) {152.11}	66.00	95.98
		102	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (N.A.) {7/2025}	579.63 (N.A.) {579.63}	157.89	63.65
		103	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (N.A.) {6/2025}	477.86 (N.A.) {477.86}	239.80	83.92
		104	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (N.A.) {4/2025}	311.18 (N.A.) {311.18}	175.90	78.27
		105	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (N.A.) {2/2025}	467.41 (N.A.) {467.41}	264.24	100
		106	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (N.A.) {5/2025}	211.70 (N.A.) {211.70}	68.35	60.24
		107	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (N.A.) {7/2025}	467.00 (N.A.) {467.00}	188.84	76.37
		108	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (N.A.) {1/2025}	185.80 (N.A.) {185.80}	114.69	100
		109	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (N.A.) {5/2025}	483.87 (N.A.) {483.87}	278.89	92.43

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA		110	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (N.A.) {3/2025}	198.77 (N.A.) {198.77}	115.53	97.54
		111	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (N.A.) {5/2025}	673.27 (N.A.) {673.27}	376.21	77.71
	DEPARTMENT OF HIGHER EDUCATION	112	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (N.A.) {7/2025}	484.32 (429.70) {429.70}	292.55	81
	ROAD TRANSPORT AND HIGHWAYS	113	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (N.A.) {3/2025}	302.88 (N.A.) {302.88}	224.39	95.2
		114	RANIKOR- MAHESKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11-2021	6/2024 (N.A.) {3/2025}	283.50 (N.A.) {283.50}	225.92	87.52
		115	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM () (NHIDCL) (N24001313)	11-2020	12/2023 (N.A.) {10/2025}	351.12 (N.A.) {351.12}	264.92	45.57
		116	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	406.62	22.29
		117	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	200.09	17.1
		118	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	73.87	12.15

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		119	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3-2021	12/2022 (N.A.) {2/2025}	260.21 (N.A.) {260.21}	232.62	99.63
		120	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (N.A.) {3/2025}	553.51 (610.09) {553.51}	383.57	78.99
		121	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (N.A.) {2/2025}	157.86 (146.92) {157.86}	149.62	100
		122	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (N.A.) {12/2025}	359.86 (N.A.) {359.86}	224.90	82.99
		123	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	185.32	16.55
		124	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	255.10	16
		125	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	284.57	16.59
MIZORAM	RAILWAYS	126	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,774.22	94.52
	ROAD TRANSPORT AND HIGHWAYS	127	ZORINPUI- HMAWNGBU-LONGMASU (NH-502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	33.56	0.3
		128	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	210.02	58.76

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		129	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWL RANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	303.25	60.68
		130	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {3/2025}	519.09 (N.A.) {785.65}	658.71	95.75
		131	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {5/2024}	640.07 (N.A.) {1,286.35}	1,192.26	98.9
		132	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4-2017	6/2023 (N.A.) {3/2024}	642.96 (N.A.) {988.23}	720.30	99.34
		133	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {3/2025}	473.18 (N.A.) {688.25}	525.62	92.01
		134	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {3/2025}	537.82 (N.A.) {789.05}	753.11	95.16
		135	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {3/2025}	518.53 (N.A.) {906.76}	826.22	95.15
		136	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {3/2025}	404.29 (N.A.) {750.32}	613.21	93.57

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		137	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {3/2025}	428.11 (N.A.) {746.39}	578.81	91.25
		138	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL - TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9-2020	10/2022 (N.A.) {4/2025}	275.02 (N.A.) {247.25}	231.64	81.3
		139	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	262.50	99.37
		140	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {6/2025}	292.24 (N.A.) {331.17}	287.30	93.15
		141	DULTE- KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355)	3-2021	12/2022 (N.A.) {3/2024}	374.39 (N.A.) {318.92}	286.49	100
		142	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (N.A.) {12/2025}	233.25 (N.A.) {233.25}	172.09	64.55
		143	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	449.15	52.84
		144	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	343.91	50.6
		145	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (N.A.) {5/2024}	492.94 (N.A.) {492.94}	344.85	86.8
<u>NAGALAND</u>	<u>PETROLEUM</u>	146	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	2.90	15.5
	<u>RAILWAYS</u>	147	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	4,250.21	66

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	148	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	56.25	48.48
		149	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (N.A.) {9/2025}	258.52 (N.A.) {258.52}	80.21	71.8
		150	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (N.A.) {6/2026}	252.19 (N.A.) {252.19}	11.80	10.38
		151	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (N.A.) {3/2025}	297.24 (N.A.) {297.24}	121.54	73.15
		152	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (N.A.) {3/2025}	226.44 (N.A.) {226.44}	136.74	98.71
		153	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (N.A.) {6/2025}	192.93 (N.A.) {192.93}	94.72	83.42
		154	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {6/2025}	177.77 (199.02) {199.02}	38.12	51.33
		155	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3-2020	6/2022 (N.A.) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.4
		156	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (N.A.) {2/2025}	373.07 (534.41) {534.41}	382.50	99.81

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		157	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (N.A.) {9/2025}	429.52 (794.74) {794.74}	311.07	88.39
		158	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (N.A.) {3/2025}	387.00 (688.12) {688.12}	388.86	99.64
		159	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (N.A.) {3/2025}	500.09 (698.81) {698.81}	373.62	98.05
		160	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3-2018	9/2022 (N.A.) {7/2024}	285.68 (N.A.) {285.68}	193.90	99.9
		161	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (N.A.) {8/2025}	215.79 (N.A.) {215.79}	123.39	58.37
		162	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (N.A.) {9/2025}	323.98 (N.A.) {323.98}	106.68	44.38
		163	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	62.5
		164	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (N.A.) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		165	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (N.A.) {11/2025}	330.80 (N.A.) {330.80}	141.88	84.76

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		166	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (N.A.) {11/2026}	232.29 (350.88) {232.29}	65.36	11.52
		167	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (N.A.) {6/2026}	277.44 (N.A.) {277.44}	166.31	65.92
		168	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (N.A.) {6/2025}	159.85 (342.29) {159.85}	89.88	23.3
		169	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (N.A.) {2/2025}	202.36 (N.A.) {202.36}	73.20	27.78
		170	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9-2020	4/2022 (N.A.) {12/2025}	315.63 (N.A.) {315.63}	95.84	74.23
		171	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3-2017	11/2020 (N.A.) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
		172	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3-2019	12/2022 (N.A.) {1/2023}	237.51 (N.A.) {237.51}	215.47	100
		173	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	62.60	40.26

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
SIKKIM		174	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	25.94	18.29
		175	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	121.55	49.22
		176	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3-2022	12/2024 (N.A.) {1/2025}	605.36 (N.A.) {605.36}	269.26	100
	CIVIL AVIATION	177	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	17.83	9.25
	DEPARTMENT OF HIGHER EDUCATION	178	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8-2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	157.24	54
	POWER	179	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,126.44	65.28
		180	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,394.69	84.55
	RAILWAYS	181	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	12/2015 (N.A.) {12/2027}	1,339.48 (11,972.96) {11,972.96}	8,068.38	72.5
	ROAD TRANSPORT AND HIGHWAYS	182	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {4/2025}	311.00 (N.A.) {273.78}	256.55	94.63

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		183	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (N.A.) {4/2025}	345.38 (395.59) {395.59}	362.13	90.23
		184	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {3/2025}	402.94 (N.A.) {402.94}	243.64	76.54
		185	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (N.A.) {3/2025}	295.97 (N.A.) {295.97}	245.22	94.64
		186	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	0
		187	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (N.A.) {12/2023}	375.80 (N.A.) {375.80}	287.54	96.55
		188	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11-2017	10/2020 (N.A.) {4/2024}	290.05 (N.A.) {290.05}	218.36	100
		189	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (N.A.) {12/2025}	292.80 (N.A.) {292.80}	195.37	55.85
		190	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1-2021	9/2023 (N.A.) {12/2025}	332.20 (N.A.) {348.92}	149.38	41.04

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		191	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (N.A.) {6/2025}	410.60 (379.30) {379.30}	221.02	69.79
		192	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (N.A.) {6/2025}	230.45 (244.91) {244.91}	204.72	80.32
		193	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (N.A.) {7/2025}	493.42 (478.79) {478.79}	284.66	46.12
		194	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (N.A.) {12/2025}	816.79 (786.60) {786.60}	308.77	49.32
		195	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (N.A.) {12/2025}	183.31 (439.56) {439.56}	351.80	49.88
		196	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (N.A.) {12/2025}	262.84 (414.20) {414.20}	220.26	46.47
		197	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (N.A.) {1/2026}	385.15 (N.A.) {385.15}	170.32	80
TRIPURA	PETROLEUM	198	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (N.A.) {9/2025}	656.00 (N.A.) {656.00}	379.44	76.2

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	199	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {9/2025}	195.95 (N.A.) {195.95}	21.95	27.34
		200	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (N.A.) {5/2025}	456.88 (N.A.) {456.88}	106.10	45.8
		201	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {3/2025}	201.99 (N.A.) {287.47}	144.07	98.12
		202	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (N.A.) {11/2024}	159.13 (171.50) {171.50}	84.33	100
		203	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (N.A.) {12/2025}	354.79 (N.A.) {354.79}	34.08	59.09
		204	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (N.A.) {12/2024}	277.50 (302.02) {302.02}	256.89	99.94
		205	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	28.16	8.8
		206	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	8.33	5.53
		207	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	3.60	8.51
		208	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	26.01	21.84

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		209	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	8.31	0
		210	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	0
			Total			176,023.98 (49,583.42) {246,627.33}	1,44,615.55	

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDAMAN AND NICOBAR ISLANDS	CIVIL AVIATION	1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR (AAI) (N04000073)	10-2013	9/2018 (N.A.) {6/2023}	417.23 (707.73) {707.73}	698.80	100.00
	RAILWAYS	2	LUDHIANA KILA RAIPUR (19 KMS) WITH FREIGHT LINE AT GILL STATION ON LDH-JHL SECTION (NR) (N22000584)	3-2019	3/2025 (N.A.) {10/2025}	235.72 (N.A.) {235.72}	48.62	52.00
	ROAD TRANSPORT AND HIGHWAYS	3	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N (NHIDCL) (N24000745)	3-2017	12/2019 (N.A.) {9/2024}	409.85 (N.A.) {409.85}	214.23	94.59
		4	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O (NHIDCL) (N24000749)	3-2018	9/2020 (N.A.) {12/2024}	234.27 (N.A.) {234.27}	126.50	80.26
		5	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 (MoRTH) (N24000820)	11-2017	11/2019 (N.A.) {11/2019}	237.80 (N.A.) {238.00}	222.13	98.23
		6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000821)	11-2017	11/2019 (N.A.) {11/2019}	257.34 (N.A.) {238.00}	214.90	100.00
		7	AJANTHA TO BULDHANA (MoRTH) (N24001008)	2-2017	7/2019 (N.A.) {12/2023}	401.00 (401.00) {401.00}	260.08	97.00
		8	MAJOR BRIDGE OVER MIDDLE STRAIT CREEK (NHIDCL) (N24002207)	12-2024	2/2026 (N.A.) {2/2026}	371.80 (207.99) {207.99}	0.00	1.30
		9	PACKAGE-3A (NHIDCL) (N24002208)	2-2018	9/2025 (N.A.) {9/2025}	207.54 (154.01) {154.01}	16.21	23.98

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		10	PACKAGE-3B (NHIDCL) (N24002209)	2-2018	11/2025 (N.A.) {11/2025}	183.47 (N.A.) {183.47}	0.00	-
ANDHRA PRADESH	CIVIL AVIATION	11	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT (AAI) (N04000089)	8-2017	2/2020 (N.A.) {1/2024}	177.10 (N.A.) {177.10}	143.08	100.00
		12	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT (AAI) (N04000091)	4-2020	3/2023 (N.A.) {6/2025}	611.80 (N.A.) {611.80}	405.37	68.00
		13	RAJAHMUNDY AIRPORT: CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUD (AAI) (N04000103)	12-2022	8/2025 (N.A.) {8/2025}	347.15 (347.15) {347.15}	65.69	39.00
		14	KADAPPA AIRPORT- CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUDING MA (AAI) (N04000106)	3-2023	1/2026 (N.A.) {1/2026}	265.91 (N.A.) {265.91}	35.13	23.00
	DEPARTMENT OF HIGHER EDUCATION	15	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE (CPWD EDUCATION) (N42000005)	2-2019	6/2020 (N.A.) {6/2020}	655.34 (N.A.) {655.34}	366.21	95.00
		16	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC (CPWD EDUCATION) (N42000007)	9-2019	9/2022 (N.A.) {6/2024}	588.72 (656.39) {656.39}	666.18	100.00
	PETROLEUM	17	VISAKH REFINERY MODERNISATION PROJECT (HPCL) (N16000235)	7-2016	7/2020 (N.A.) {12/2024}	20,928.00 (30,609.00) {30,609.00}	28,002.00	98.80

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		18	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT (ONGC) (N16000247)	3-2016	6/2020 (N.A.) {3/2025}	34,012.00 (N.A.) {34,012.00}	32,565.18	96.00
		19	REVAMPING OF FACILITIES AT VIZAG TERMINAL (IOCL) (N16000343)	4-2018	4/2022 (N.A.) {3/2025}	355.00 (N.A.) {355.00}	247.73	80.20
		20	SWRO II WITH LLPH FACILITIES (HPCL) (N16000378)	9-2019	7/2020 (N.A.) {3/2025}	196.26 (196.26) {196.26}	171.66	87.60
		21	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY (HPCL) (N16000432)	9-2021	6/2024 (N.A.) {3/2026}	160.00 (220.00) {220.00}	21.12	53.00
		22	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS (IOCL) (N16000485)	3-2022	3/2030 (N.A.) {3/2030}	1,420.00 (N.A.) {1,420.00}	136.36	5.10
		23	MULTI-PRODUCT PIPELINE FROM KRISHNAPATNAM COASTAL INSTALLATION TO THE PROPOSED INSTALLATION AT HYDER (BPCL) (N16000499)	9-2019	3/2025 (N.A.) {10/2025}	1,932.00 (N.A.) {1,932.00}	1,491.62	78.00
		24	HP TRIJET UNIT IN VR (HPCL) (N16000535)	7-2024	7/2027 (N.A.) {7/2027}	193.00 (N.A.) {193.00}	0.23	15.00
		25	CONSTRUCTION OF AVIATION FUEL FARM FACILITIES AT BHOGAPURAM AIRPORT (HPCL) (N16000538)	8-2024	3/2026 (N.A.) {3/2026}	240.00 (N.A.) {240.00}	3.24	14.70
		26	VISAKHA RAIPUR PIPELINE PROJECT (HPCL) (N16000539)	9-2024	9/2027 (N.A.) {9/2027}	2,212.00 (N.A.) {2,212.00}	0.53	1.52
		27	TRANSMISSION SCHEME FOR SOLAR ENERGY ZONE IN ANANTHPURAM (2500MW) AND KURNOOL (1000MW) (PGCIL) (N18000380)	9-2023	3/2025 (N.A.) {9/2025}	1,249.00 (N.A.) {1,249.00}	270.81	50.00
	POWER							

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		28	AUGMENTATION OF 1500MVA 3RD 765/400KV TRANSFORMATION CAPACITY AT KURNOOL NEW SUBSTATION (PGCIL) (N18000395)	5-2023	9/2025 (N.A.) {9/2025}	164.00 (N.A.) {164.00}	66.00	12.00
	RAILWAYS	29	KOTLPALLI-NARASAPUR (NL) (SCR) (SCR) (220100265)	12-2001	3/2009 (N.A.) {3/2027}	1,045.20 (N.A.) {2,500.98}	1,150.84	-
		30	NADIKUDE-SRI KALAHASTI (SCR) (N22000286)	4-2011	3/2021 (N.A.) {5/2027}	2,288.70 (N.A.) {3,122.35}	1,890.80	-
		31	GUNTUR-GUNTAKAL (SCR) (N22000368)	4-2016	3/2022 (N.A.) {12/2025}	3,631.00 (N.A.) {3,887.48}	3,359.22	-
		32	VIJAYAWADA-GUDUR (RVNL) (N22000369)	4-2015	12/2023 (N.A.) {12/2024}	3,246.26 (N.A.) {6,238.67}	5,883.89	-
		33	KOTTAVALSA - KORAPUT DOUBLING (ECOR) (N22000377)	4-2015	3/2022 (N.A.) {3/2022}	2,499.71 (N.A.) {2,499.71}	1,871.98	69.50
		34	PENUKONDA-DHARMAVARAM, EXCL. DHARMAVARAM (41.5 KM) (SWR) (N22000555)	4-2019	3/2026 (N.A.) {12/2025}	294.67 (307.66) {307.66}	175.57	41.00
		35	MALUGUR-PALASAMUDRAM (17.98 KM) (PB#29/NR/2022-23) (SWR) (N22000556)	9-2022	12/2025 (N.A.) {12/2026}	323.14 (342.41) {342.41}	39.46	12.00
		36	DOUBLING BETWEEN GOOTY- PENDAKALLU (29.225) (SCR) (N22000585)	3-2023	3/2027 (N.A.) {3/2027}	351.83 (N.A.) {351.83}	0.00	-
		37	VIJAYAWADA KAZIPET BYEPASS LINE (SCR) (N22000586)	4-2016	12/2025 (N.A.) {12/2025}	226.72 (N.A.) {226.72}	204.23	-
		38	RENIGUNTA WADI GOOTY - BYPASS (SCR) (N22000587)	4-2016	12/2025 (N.A.) {12/2025}	302.00 (N.A.) {302.00}	194.28	50.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	39	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES (MoRTH) (N24000301)	3-2015	10/2015 (N.A.) {5/2021}	271.45 (N.A.) {271.45}	238.23	100.00
		40	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 (NHAI) (N24000811)	3-2018	12/2020 (N.A.) {12/2024}	314.43 (N.A.) {348.72}	85.61	66.48
		41	REHABILITATION AND UPGRADATION OF EXISTING NH- 167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 (MoRTH) (N24000931)	11-2016	5/2017 (N.A.) {11/2024}	290.15 (N.A.) {236.16}	205.02	90.00
		42	REHABILITATION AND UPGRADATION OF NEW NH- 544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG (MoRTH) (N24000937)	3-2018	8/2018 (N.A.) {11/2024}	289.67 (290.00) {285.29}	254.19	98.50
		43	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH- 214(NH216)(KAKINAD (MoRTH) (N24000964)	8-2016	1/2017 (N.A.) {5/2025}	350.61 (N.A.) {411.18}	457.55	98.20
		44	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 (MoRTH) (N24000969)	1-2017	9/2017 (N.A.) {3/2025}	263.45 (N.A.) {263.45}	257.85	90.00
		45	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) (NHAI) (N24001301)	11-2019	1/2024 (N.A.) {7/2024}	1,601.10 (N.A.) {1,601.10}	1,314.52	83.86

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		46	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU- GONDIGUDA SECT (MoRTH) (N24001386)	8-2020	3/2021 (N.A.) {10/2024}	222.61 (N.A.) {222.61}	160.53	95.00
		47	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI (NHAI) (N24001476)	9-2021	9/2022 (N.A.) {6/2025}	517.05 (N.A.) {655.06}	475.23	81.55
		48	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM- DEVARAP (NHAI) (N24001477)	9-2021	9/2022 (N.A.) {6/2025}	622.00 (N.A.) {817.91}	493.21	65.78
		49	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 (NHAI) (N24001817)	2-2019	3/2023 (N.A.) {10/2024}	757.45 (N.A.) {757.45}	604.86	97.51
		50	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG- IV) (NHAI) (N24001818)	2-2021	1/2025 (N.A.) {1/2025}	818.73 (N.A.) {1,105.00}	529.33	22.71
		51	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) (NHAI) (N24001819)	3-2021	1/2025 (N.A.) {1/2025}	1,102.63 (N.A.) {1,303.00}	1,060.74	90.28
		52	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) (NHAI) (N24001820)	2-2021	12/2024 (N.A.) {12/2024}	1,484.83 (N.A.) {1,768.00}	1,402.98	82.60

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		53	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP (NHAI) (N24001821)	11-2020	10/2024 (N.A.) {10/2024}	1,137.74 (N.A.) {1,289.00}	1,256.44	92.12
		54	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE (NHAI) (N24001822)	12-2020	10/2024 (N.A.) {10/2024}	1,075.27 (N.A.) {1,307.00}	1,029.13	77.31
		55	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A (NHAI) (N24001823)	1-2022	1/2025 (N.A.) {1/2025}	1,852.12 (N.A.) {1,787.00}	689.03	80.00
		56	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP (NHAI) (N24001824)	3-2020	1/2024 (N.A.) {12/2024}	1,863.09 (N.A.) {2,238.00}	1,227.61	98.26
		57	6L KANTAKAPALLE ? SABBAVARAM SECTION OF NH- 130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4) (NHAI) (N24001836)	2-2021	10/2024 (N.A.) {12/2025}	824.29 (N.A.) {924.00}	393.08	68.75
		58	6L JAKKUVA ? KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) (NHAI) (N24001837)	2-2021	3/2024 (N.A.) {3/2025}	663.60 (N.A.) {768.00}	343.41	97.74
		59	6L ALURU - JAKKUVA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) (NHAI) (N24001838)	2-2021	3/2024 (N.A.) {6/2025}	922.50 (N.A.) {1,128.68}	422.18	78.15

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		60	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA (NHAI) (N24001841)	12-2022	9/2025 (N.A.) {2/2026}	912.94 (N.A.) {912.94}	208.63	46.04
		61	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 (NHAI) (N24001842)	12-2022	11/2025 (N.A.) {11/2025}	750.81 (N.A.) {750.81}	122.50	31.24
		62	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH (NHAI) (N24001843)	12-2022	11/2025 (N.A.) {11/2025}	992.89 (N.A.) {992.89}	162.87	26.12
		63	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. (NHAI) (N24001844)	12-2022	10/2025 (N.A.) {10/2025}	1,058.90 (N.A.) {1,058.90}	211.29	31.30
		64	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 (NHAI) (N24001845)	2-2023	10/2025 (N.A.) {10/2025}	1,253.24 (N.A.) {1,253.24}	114.29	11.78
		65	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. (NHAI) (N24001846)	2-2023	10/2025 (N.A.) {10/2025}	1,200.42 (N.A.) {1,200.42}	57.89	3.20

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		66	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA (NHAI) (N24001847)	1-2023	11/2025 (N.A.) {11/2025}	956.14 (N.A.) {956.14}	175.16	33.07
		67	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTLA 196.000 KM. PACK (NHAI) (N24001848)	2-2023	10/2025 (N.A.) {10/2025}	909.02 (N.A.) {909.02}	95.23	10.15
		68	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 (NHAI) (N24001849)	5-2022	7/2025 (N.A.) {9/2025}	1,063.72 (N.A.) {1,063.72}	423.03	61.78
		69	CONSTRUCTION OF 4-LANE HIGHWAY FROM SAMARLAKOTA TO ACHAMPETA JUNCTION (FROM KM. 0.000 TO KM. 12.250 (NHAI) (N24001856)	5-2023	8/2025 (N.A.) {8/2025}	648.75 (N.A.) {648.75}	164.04	38.33
		70	4 LANING OF BATHALAPALLI TO MUDIGUBBA SECTION (DESIGN CHAINAGE KM. 96.300 TO 129.300) INCLUDING BATH (MoRTH) (N24001931)	3-2022	2/2025 (N.A.) {2/2025}	536.00 (N.A.) {536.00}	393.81	97.92
		71	2L+PS FROM KM. 0+000 TO KM. 32+000 (MUDIGUBBA TO PUTTAPARTHI) OF NH-342 (MoRTH) (N24001932)	3-2022	9/2024 (N.A.) {3/2025}	401.72 (N.A.) {401.72}	186.15	76.79
		72	NH440 RAYACHOTY TOVEMPALLI 2LPS (MoRTH) (N24001934)	12-2021	5/2024 (N.A.) {7/2025}	439.82 (N.A.) {439.82}	193.63	51.78
		73	4 LANE WITH PAVED SHOULDER FROM KM 0.000 TO KM 51.119 OF TADIPATRI TO MUDDANUR OF NH67 (MoRTH) (N24001935)	3-2022	8/2025 (N.A.) {8/2025}	724.17 (N.A.) {724.17}	456.16	97.38

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		74	NH165 FROM KM 0.000 TO KM 64.020 PAMARRU TO AKIVEEDU SECTION TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001939)	3-2020	9/2023 (N.A.) {12/2025}	529.24 (N.A.) {529.24}	312.17	51.78
		75	2LPS FROM KM36.400 TO KM. 107.224 OF NH167BG FROM DUTTALUR TO KAVALI SECTION (MoRTH) (N24001942)	3-2021	7/2024 (N.A.) {3/2025}	423.67 (N.A.) {423.67}	228.15	60.53
		76	NH167B FROM KM 99.103 CS PURAM TO KM 143.320 MALAKONDA TO 2LPS (MoRTH) (N24001949)	12-2021	3/2024 (N.A.) {1/2025}	277.30 (N.A.) {277.30}	195.88	98.00
		77	NH167B FROM KM.143.320 MALAKONDA TO 189.050 SINGARAYAKONDA ON NH 16 TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001950)	3-2021	2/2025 (N.A.) {2/2025}	369.81 (N.A.) {369.81}	295.47	98.20
		78	NH167AD FROM MACHERLA TO DACHEPALLI FROM KM.0.000 TO 43.659 TO 2LPS (MoRTH) (N24001951)	1-2022	1/2025 (N.A.) {1/2025}	403.22 (N.A.) {403.22}	283.58	97.00
		79	NH 167 B KADAPA NELLORE BORDER TO CSPURAM I.E. FROM KM 58.635 TO KM 99.409 (MoRTH) (N24001952)	3-2022	8/2025 (N.A.) {8/2025}	285.50 (N.A.) {285.50}	187.43	93.29
		80	NH-30-BHADRACHALAM TO KONTA SECTION 2LPS (MoRTH) (N24001953)	12-2021	9/2024 (N.A.) {3/2025}	388.71 (N.A.) {388.71}	207.87	78.88
		81	WIDENING TO 2LPS OF RAMPACHODAVARAM - KOYYURU SECTION OF NH516E FROM KM.43.700 TO KM 113.820 (MoRTH) (N24001954)	3-2022	1/2025 (N.A.) {1/2025}	568.12 (N.A.) {568.12}	341.83	91.05

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		82	GUDIWADA TOWN 2 LANE ROB AND ROAD IMPROVEMENT OF NH165 IN REPLACEMENT OF LC NO 3ESPL3 AT KM 231.700 (MoRTH) (N24001955)	3-2022	5/2025 (N.A.) {5/2025}	317.22 (N.A.) {317.22}	181.63	52.00
		83	2LPS FROM GONDIGUDA TO ARAKU BHALLAGUDA KM 27.480 TO KM 51.772 SECTION OF NH 516E (MoRTH) (N24001956)	8-2020	9/2023 (N.A.) {12/2024}	296.66 (N.A.) {296.66}	217.41	87.49
		84	2LPS OF KOYYURU TO CHAPRATHIPALEM SECTION OF NH 516E (MoRTH) (N24001957)	8-2020	7/2024 (N.A.) {3/2025}	349.29 (N.A.) {349.29}	179.64	72.83
		85	2LPS OF CHAPRATHIPALEM TO LAMBASINGI SECTION OF NH 516E (MoRTH) (N24001958)	8-2020	10/2024 (N.A.) {3/2025}	311.22 (N.A.) {311.22}	129.54	61.00
		86	4 LANE FROM KM 56.400 TO KM 120.300 FROM B.KOTHAPALLI JUNCTION TO GORANTLA OF NH 716G (MoRTH) (N24001959)	3-2022	9/2025 (N.A.) {9/2025}	839.98 (N.A.) {839.98}	351.02	62.00
		87	4L GREENFIELD ROAD CONNECTING NORTH AND SOUTH INDUSTRIAL CLUSTER OF KHANDALERU CREEK NEAR KRISHNAPAT (NHAI) (N24001979)	8-2022	9/2025 (N.A.) {9/2025}	609.43 (N.A.) {609.43}	25.24	41.07
		88	4 LANING OF NH 544D FROM EXISTING KM 346.300 OF NH 44 (DESIGN CHAINAGE KM 0.000) TO KM 39.380 (DESIG (NHAI) (N24001980)	10-2022	7/2025 (N.A.) {7/2025}	907.76 (N.A.) {907.76}	341.93	73.90
		89	CONSTRUCTION OF SIX LANING OF NAIDUPETA JUNCTION - TURPUKANUPUR SECTION FROM KM.57+046 TO KM.91+927 (NHAI) (N24001981)	7-2022	10/2025 (N.A.) {10/2025}	1,398.84 (N.A.) {1,398.84}	58.68	10.54

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		90	4L PS FROM KURNOOL (EXISTING KM. 5.400 OF NH- 40/DESIGN KM.0.000) TO MANDLEM (EXISTING KM.38.000/DESI (NHAI) (N24001982)	3-2023	10/2025 (N.A.) {10/2025}	827.39 (N.A.) {827.39}	331.66	98.50
		91	4 LANING FROM EXISTING KM 39.380 (DESIGN CH. 37.000) TO KM 74.450 (DESIGN CH. 69.000) OF MUCHUKOTA ? (NHAI) (N24001983)	10-2022	8/2025 (N.A.) {8/2025}	972.63 (N.A.) {1,055.23}	271.30	45.05
		92	4L PS FROM MANDLEM (EXISTING KM. 38.000/DESIGN KM.30.600) TO ATMAKUR (EXISTING KM.73.000/DESIGN KM 6 (NHAI) (N24001984)	3-2023	10/2025 (N.A.) {10/2025}	887.28 (N.A.) {887.28}	204.24	53.50
		93	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-II) FROM KM.96.000 TO KM 127.000 (BAIREDDYPALLE TO BANGAR (NHAI) (N24001985)	3-2021	6/2025 (N.A.) {6/2025}	1,942.94 (2,171.00) {2,171.00}	1,513.36	53.21
		94	4L OF PILERU TO KALUR SECTION FROM KM 55.900 TO KM 92.800 AND KM 94.500 TO KM 95.717 (NHAI) (N24001986)	10-2023	4/2025 (N.A.) {4/2025}	1,047.32 (N.A.) {1,047.32}	281.09	76.10
		95	CONSTRUCTION OF 1 NOS ROB, 2 NOS VUPS, SERVICE ROADS, PROVISION OF LIGHTING AND CONSTRUCTION OF OTHE (NHAI) (N24001987)	6-2023	12/2024 (N.A.) {12/2024}	152.05 (N.A.) {152.05}	131.33	76.40
		96	6L OF CHITTOOR TO THATCHUR FROM KUMARAJAPET TO VEERA KAVERI RAJA PURAM FROM KM 43.800 TO KM 61.380 O (NHAI) (N24001988)	2-2021	10/2025 (N.A.) {10/2025}	591.99 (703.00) {703.00}	453.03	53.22

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		97	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED HIGHWAY FROM CHILLAKURU CROSS ROAD TO TURPUKANUPUR KM 0+000 (NHAI) (N24002033)	7-2022	12/2025 (N.A.) {12/2025}	909.47 (N.A.) {909.47}	97.03	22.16
		98	COMPLETION OF BALANCE WORKS PENDING IN BIT AND PIECES (INCOMPLETE STRETCH AT 7 LOCATIONS) AND LISTED (NHAI) (N24002103)	9-2022	1/2025 (N.A.) {1/2025}	166.52 (N.A.) {166.52}	44.07	75.16
		99	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NARAYANMPET (CH. 203+500) TO CHANDRASEKHARPURAM (CH. 22 (NHAI) (N24002122)	2-2024	2/2026 (N.A.) {2/2026}	813.66 (N.A.) {813.66}	63.32	12.02
		100	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM CHANDRASEKHARAPURAM (CH. 228+000) TO POLAVARAM (CH. 260 (NHAI) (N24002123)	2-2024	2/2026 (N.A.) {2/2026}	1,292.65 (N.A.) {1,292.65}	89.89	7.10
		101	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM POLAVARAM (CH. 260+000) TO MARRIPUDI (CH. 285+500) OF [(NHAI) (N24002124)	2-2024	2/2026 (N.A.) {2/2026}	747.29 (N.A.) {747.29}	92.56	14.84
		102	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MARRIPUDI (CH. 285+500) TO SOMAVARAPPADU (CH. 314+600) (NHAI) (N24002125)	2-2024	2/2026 (N.A.) {2/2026}	976.40 (N.A.) {976.40}	161.92	30.80

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		103	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM SOMAVARAPPADU (CH.314.600) TO MUPPAVARAM (CH.343+240) O (NHAI) (N24002126)	2-2024	2/2026 (N.A.) {2/2026}	1,103.89 (N.A.) {1,103.89}	54.54	5.45
		104	4-LANE WITH PAVED SHOULDERS FROM KM 32/0 TO KM 79/650 (DESIGN CHAINAGE KM 32+000 TO KM 78+760) PUTTA (MoRTH) (N24002139)	3-2023	12/2025 (N.A.) {11/2025}	1,318.57 (N.A.) {1,318.57}	360.88	51.15
		105	SOMAYAJULAPALLI ? DHONE SECTION OF NH ? 340B FROM KM.0/0 TO 56/200 [DESIGN CH. KM 0/00 TO KM 53/33] (MoRTH) (N24002140)	4-2023	12/2025 (N.A.) {12/2025}	629.73 (N.A.) {629.73}	257.90	57.35
		106	2 LANE WITH PAVED SHOULDER CONFIGURATION FROM SEETHARAMAPURAM TO DUTTALURU SECTION OF NH-167 BG FROM (MoRTH) (N24002141)	6-2023	7/2025 (N.A.) {7/2025}	364.07 (N.A.) {364.07}	193.87	98.00
		107	2-LANE WITH PAVED SHOULDER CONFIGURATION OF LAMBASINGI TO PADERU SECTION (KM 205+000 TO KM 253+974) (MoRTH) (N24002142)	8-2023	11/2025 (N.A.) {11/2025}	361.24 (N.A.) {361.24}	34.23	15.00
		108	BYPASS ROAD TO ADONI TOWN CONNECTING NH-167 (HAGARI - JADCHARLA ROAD) FROM KM.62/700 TO 71/400 IN KU (MoRTH) (N24002143)	8-2023	2/2026 (N.A.) {2/2026}	361.24 (N.A.) {361.24}	91.88	49.45

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		109	VODAREVU-CHILAKALURIPET SECTION (DESIGN CHAINAGE 0+00 TO 47+000) OF NH-167A (PACKAGE-I) (MoRTH) (N24002144)	8-2023	2/2026 (N.A.) {2/2026}	1,064.24 (N.A.) {1,064.24}	382.03	54.00
		110	TADIPATRI BYPASS (KM 0+000 TO KM 6+285) OF 4-LANE ON NH- 67 IN ANANTAPURAMU (MoRTH) (N24002145)	11-2023	3/2026 (N.A.) {3/2026}	159.66 (N.A.) {159.66}	60.76	63.50
		111	KURNOOL/KADAPA BORDER- JAMMALAMADUGU SECTION OF NH-167K I.E. DESIGN CH. KM 248+010 TO KM 269+900 (MoRTH) (N24002146)	11-2023	11/2025 (N.A.) {11/2025}	292.63 (N.A.) {292.63}	31.16	13.18
		112	DORNALA TO KUNTA JUNCTION FROM DESIGN CHAINAGE KM 244+000 TO 267+990 SECTION OF NH-765 (PACKAGE-2) (MoRTH) (N24002147)	12-2022	1/2024 (N.A.) {3/2026}	244.83 (N.A.) {244.83}	82.23	65.70
		113	PADERU BYPASS (KM 0+000 TO KM 13+000) OF 2- LANE WITH PAVED SHOULDER ON NH-516E (MoRTH) (N24002148)	3-2023	3/2024 (N.A.) {2/2026}	244.43 (N.A.) {244.43}	22.77	-
		114	DAVUALAPALLY TO MALLAPALEM SECTION {DESIGN CH. KM 133+922 TO KM 154+216 (EXISTING CH. KM 133+922 TO (MoRTH) (N24002149)	1-2024	2/2024 (N.A.) {2/2026}	393.61 (N.A.) {393.61}	41.66	-
		115	DEVELOPMENT OF SIX LANE ACCESS CONTROLLED GREEN FIELD HIGHWAY FROM KAVULAKUNTALA (KM.196+000) TO NARA (NHAI) (N24002215)	2-2023	2/2027 (N.A.) {2/2027}	1,092.18 (N.A.) {1,092.18}	0.14	-
		116	POLAVARAM IRRIGATION PROJECT (PPA) (N30000002)	2-2009	3/2020 (N.A.) {3/2026}	10,151.04 (N.A.) {55,548.87}	21,670.32	72.86
	WATER RESOURCES							

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ARUNACHAL PRADESH	CIVIL AVIATION	117	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (N.A.) {3/2025}	645.63 (N.A.) {712.15}	684.18	99.29
	POWER	118	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	23,437.47	94.86
		119	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,026.06	14.23
	ROAD TRANSPORT AND HIGHWAYS	120	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (N.A.) {3/2025}	180.57 (244.10) {180.57}	160.46	96.62
		121	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2-2017	4/2022 (N.A.) {11/2023}	167.28 (N.A.) {167.28}	145.20	100.00
		122	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (N.A.) {6/2025}	1,718.59 (1,718.59) {1,718.59}	708.22	71.00
		123	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9-2016	12/2019 (N.A.) {9/2024}	568.92 (568.92) {568.92}	508.65	100.00
		124	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (N.A.) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		125	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (N.A.) {2/2025}	301.06 (N.A.) {301.06}	177.73	74.95
		126	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3-2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100.00
		127	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3-2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	588.85	100.00
		128	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3-2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	480.44	100.00
		129	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	389.68	95.26
		130	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2-2021	3/2024 (N.A.) {12/2024}	588.09 (N.A.) {588.09}	497.36	100.00
		131	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH- 415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6-2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	366.59	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		132	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH- 415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	165.78	39.00
		133	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (N.A.) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		134	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8-2020	4/2022 (N.A.) {9/2024}	294.04 (N.A.) {294.04}	147.13	100.00
		135	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (N.A.) {3/2025}	184.88 (N.A.) {184.88}	99.32	97.42
ASSAM	CIVIL AVIATION	136	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (N.A.) {5/2025}	1,142.00 (N.A.) {2,333.00}	1,647.43	80.61
	COAL	137	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	0.00	-
		138	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	0.00	-
	HEALTH AND FAMILY WELFARE	139	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (N.A.) {11/2024}	875.00 (873.92) {860.00}	782.74	99.30
	PETROLEUM	140	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (N.A.) {6/2025}	543.91 (726.93) {726.93}	491.56	93.89

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		141	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINERY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	14,677.15	70.60
		142	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,024.34	82.90
		143	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (N.A.) {5/2026}	412.00 (509.84) {509.84}	373.67	81.10
		144	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (N.A.) {9/2026}	277.00 (N.A.) {277.00}	166.84	61.60
		145	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (N.A.) {4/2025}	860.00 (N.A.) {860.00}	470.22	93.50
		146	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (N.A.) {6/2025}	430.76 (N.A.) {430.76}	279.38	80.06
		147	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	80.15	27.00
		148	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (N.A.) {7/2027}	156.36 (156.36) {156.36}	33.16	23.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		149	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (N.A.) {7/2027}	384.04 (N.A.) {384.04}	66.71	21.20
		150	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	56.33	88.00
		151	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	231.17	45.20
		152	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	166.40	42.00
		153	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.50	11.10
	<u>RAILWAYS</u>	154	BONGAIGAON-GOALPARA- GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,570.03	92.30
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	155	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {3/2025}	437.39 (N.A.) {437.39}	468.40	78.20
		156	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	455.98	30.10
		157	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1-1991	6/2019 (N.A.) {6/2025}	520.01 (N.A.) {520.01}	305.01	95.85

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		158	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (N.A.) {6/2025}	289.99 (N.A.) {289.99}	232.95	87.62
		159	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {3/2025}	294.17 (N.A.) {294.17}	359.24	85.59
		160	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {3/2025}	252.00 (N.A.) {330.30}	193.59	60.28
		161	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	216.83	97.76
		162	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (N.A.) {5/2025}	216.49 (241.52) {216.49}	104.36	81.26
		163	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,275.48	58.18
		164	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (N.A.) {5/2025}	261.13 (N.A.) {261.13}	64.96	57.26
		165	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (N.A.) {4/2025}	217.50 (N.A.) {217.50}	84.36	68.03
		166	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.73	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		167	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	125.60	61.53
		168	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (N.A.) {925.47}	192.50	30.65
		169	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	313.22	64.13
		170	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {3/2025}	625.64 (N.A.) {625.64}	522.74	97.22
		171	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3-2022	7/2024 (N.A.) {10/2024}	215.27 (N.A.) {215.27}	151.29	100.00
		172	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {5/2025}	204.10 (N.A.) {204.10}	136.11	92.12
		173	FOUR LANING OF SRIRAMPUR- DHUBRI PKG-2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	475.46	93.54
		174	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (N.A.) {6/2024}	175.00 (N.A.) {175.00}	200.80	100.00
		175	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	480.84	66.46

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		176	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {3/2025}	457.72 (N.A.) {457.72}	355.87	99.02
		177	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	18.59	12.24
		178	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	173.66	52.35
		179	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	9.62	15.00
		180	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	369.39	55.23
		181	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	337.68	54.35
		182	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	397.28	51.50

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		183	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	286.30	87.68
		184	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	248.91	86.74
		185	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	463.59	34.62
		186	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	267.46	19.46
		187	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	374.62	19.25
		188	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	222.22	67.75
		189	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	125.03	12.20
		190	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3-2023	12/2025 (N.A.) {12/2026}	643.42 (N.A.) {643.42}	69.46	8.89

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		191	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.06	100.00
		192	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	445.96	24.05
		193	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	893.96	50.09
		194	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	244.30	39.56
		195	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	328.61	45.12
		196	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	209.87	28.02
		197	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY) (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	95.94	17.15
BIHAR	CIVIL AVIATION	198	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II (AAI) (N04000082)	5-2018	10/2022 (N.A.) {6/2025}	1,216.90 (N.A.) {1,216.90}	921.43	84.59

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		199	DARBHANGA:DEVELOPMENT OF NEW CIVIL ENCLAVE AT DARBHANGA, BIHAR. SH- CONSTRUCTION OF NEW TERMINAL BUI (AAI) (N04000112)	7-2024	7/2026 (N.A.) {7/2026}	911.66 (N.A.) {911.66}	45.24	10.00
	DEPARTMENT OF HIGHER EDUCATION	200	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA (CPWD EDUCATION) (N28000100)	2-2016	6/2017 (N.A.) {1/2024}	496.18 (496.00) {460.00}	436.15	100.00
		201	PERMANENT CAMPUS FOR IIM BODH GAYA (CPWD EDUCATION) (N42000009)	9-2018	9/2020 (N.A.) {3/2025}	375.00 (N.A.) {375.00}	333.45	100.00
	PETROLEUM	202	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA (IOCL) (N16000386)	1-2020	4/2023 (N.A.) {8/2026}	14,810.00 (N.A.) {14,810.00}	10,409.36	83.80
		203	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA (IOCL) (N16000423)	6-2019	12/2029 (N.A.) {3/2030}	163.00 (N.A.) {163.00}	94.84	29.70
		204	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI (IOCL) (N16000453)	1-2022	4/2025 (N.A.) {8/2026}	389.00 (N.A.) {389.00}	30.92	26.10
		205	CITY GAS DISTRIBUTION PROJECTS AT GOPALGANJ SIWAN WEST CHAMPARAN EAST CHAMPARAN AND DEORIA DISTRICTS (BPCL) (N16000523)	12-2022	6/2030 (N.A.) {6/2030}	3,919.00 (N.A.) {3,919.00}	269.79	12.80
		206	CITY GAS DISTRIBUTION PROJECTS AT DARBHANGA, MADHUBANI, SUPAUL, SITAMARHI AND SHEOHAR DISTRICTS (BPCL) (N16000524)	12-2022	3/2030 (N.A.) {3/2030}	3,638.00 (N.A.) {3,638.00}	316.93	17.20

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	207	BARH STPP(3X660MW) NTPC (NTPC) (180100242)	2-2005	10/2011 (N.A.) {3/2025}	8,692.97 (21,312.11) {21,312.11}	22,183.97	94.00
		208	BUXAR THERMAL POWER PLANT (1320 MW) (SJVN) (N18000194)	3-2019	1/2024 (N.A.) {9/2025}	10,439.09 (N.A.) {12,999.36}	11,068.57	86.75
	RAILWAYS	209	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) (ECR) (220100257)	4-1997	(N.A.) {12/2026}	162.87 (614.45) {614.45}	463.54	50.00
		210	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR (ECR) (220100303)	4-2003	(N.A.) {12/2024}	528.65 (2,087.36) {2,087.36}	2,172.09	48.00
		211	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR (NFR) (N22000087)	9-2006	3/2019 (N.A.) {9/2025}	532.87 (2,132.03) {4,412.25}	3,421.86	85.00
		212	SAKRI-HASANPUR ROAD (NL) (ECR) (N22000171)	4-1999	(N.A.) {3/2027}	325.00 (735.20) {735.20}	594.78	78.00
		213	ARARIA-SUPAUL (NL) (ECR) (N22000177)	4-2008	(N.A.) {1/2025}	1,605.17 (1,605.17) {1,605.17}	1,534.31	31.00
		214	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC (ECR) (N22000181)	4-2009	3/2020 (N.A.) {3/2026}	548.00 (548.00) {783.83}	544.31	78.00
		215	SAMASTIPUR-DARBANGHA (ECR) (N22000329)	5-2015	(N.A.) {3/2025}	380.00 (519.33) {519.33}	615.14	64.00
		216	KIUL - GAYA DOUBLING PROJECT (ECR) (N22000349)	12-2015	3/2020 (N.A.) {11/2024}	1,200.20 (1,200.20) {1,771.07}	1,790.93	96.00
		217	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE (ECR) (N22000350)	12-2015	3/2020 (N.A.) {5/2025}	1,491.47 (1,491.47) {1,600.00}	1,680.42	77.00
		218	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM (ECR) (N22000472)	4-2016	3/2021 (N.A.) {12/2024}	744.04 (1,215.54) {1,215.54}	1,506.05	85.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		219	MUZAFFARPUR SAGALI DOUBLING 100.60 KM (<i>ECR</i>) (N22000473)	4-2016	3/2021 (N.A.) {12/2024}	731.64 (1,185.73) {1,300.00}	1,451.91	80.00
		220	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, (<i>ECR</i>) (N22000476)	4-1991	(N.A.) {12/2024}	329.39 (803.09) {2,722.16}	2,738.61	90.00
		221	DARBHANGA - BYPASS LINE CONNECTING SHISHO HALT AND KAKARGHATI EXCL DARBHANGA YARD (7.64 KM) (<i>ECR</i>) (N22000523)	6-2019	6/2025 (N.A.) {9/2024}	983.62 (253.23) {415.00}	414.90	80.00
		222	BARAUNI- BACHWARA 3RD AND 4TH LINE (<i>ECR</i>) (N22000524)	7-2022	7/2027 (N.A.) {6/2025}	486.00 (N.A.) {486.00}	117.15	30.00
		223	JHAJHA - BATIA (UMBRELLA WORK PB#23/2018-19/NR) (<i>ECR</i>) (N22000526)	2-2019	6/2028 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	2.53	-
		224	SONENAGAR BYE PASS LINE FROM CHIRALAPOTHU TO BAGHA BISHUNPUR (<i>ECR</i>) (N22000528)	10-2022	10/2027 (N.A.) {6/2025}	234.00 (223.69) {223.69}	22.57	-
		225	KATIHAR-KUMEDPUR & KATIHAR- MUKURIA (64.5 KM) (UMBRELLA WORK PB#57/2019-20/NR) (<i>NFR</i>) (N22000570)	8-2022	8/2027 (N.A.) {8/2027}	745.00 (N.A.) {745.00}	0.00	-
	ROAD TRANSPORT AND HIGHWAYS	226	PATNA-MUZAFFARPUR (<i>NHAI</i>) (N24000165)	8-2010	2/2013 (N.A.) {12/2024}	671.30 (N.A.) {671.30}	1,830.13	97.78
		227	4-LANNING OF CHAPRA-HAJIPUR (<i>NHAI</i>) (N24000187)	1-2011	7/2013 (N.A.) {6/2025}	575.00 (N.A.) {575.00}	567.62	88.95

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		228	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR (MoRTH) (N24000382)	1-2014	10/2019 (N.A.) {4/2025}	675.00 (N.A.) {780.77}	702.20	94.12
		229	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 (NHAI) (N24000480)	12-2015	4/2019 (N.A.) {3/2025}	1,041.10 (567.00) {639.58}	553.73	97.56
		230	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 (NHAI) (N24000507)	12-2015	12/2019 (N.A.) {12/2024}	1,167.45 (N.A.) {1,182.94}	735.99	96.00
		231	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 (MoRTH) (N24000531)	2-2016	11/2018 (N.A.) {3/2025}	319.68 (N.A.) {503.28}	440.98	98.80
		232	CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-I-KM 40.00 TO KM 65.400 AND K (MoRTH) (N24000576)	2-2016	5/2016 (N.A.) {3/2025}	178.85 (N.A.) {278.54}	232.61	98.35
		233	PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-III-KM 156.5 (MoRTH) (N24000578)	2-2016	5/2016 (N.A.) {3/2025}	553.30 (N.A.) {706.39}	712.38	98.00
		234	FOUR LANING OF GAYA-HISUA- RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR (MoRTH) (N24000579)	1-2014	10/2016 (N.A.) {6/2025}	1,408.85 (N.A.) {2,138.16}	1,715.99	96.65

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		235	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT- SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN (NHAI) (N24000665)	3-2017	3/2020 (N.A.) {6/2025}	672.89 (736.01) {830.31}	678.03	81.85
		236	SIX LANNING OF AUNTA- SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 (NHAI) (N24000696)	8-2017	2/2022 (N.A.) {3/2025}	950.64 (1,161.00) {1,168.33}	1,069.28	92.10
		237	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 (NHAI) (N24000714)	12-2017	10/2024 (N.A.) {12/2026}	2,598.00 (N.A.) {1,978.01}	1,299.17	72.80
		238	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I (NHAI) (N24000723)	1-2018	12/2021 (N.A.) {6/2025}	573.70 (644.50) {726.99}	476.99	81.22
		239	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER (NHAI) (N24000813)	3-2018	11/2021 (N.A.) {12/2024}	496.20 (470.18) {537.17}	399.41	97.40
		240	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND (MoRTH) (N24000943)	9-2018	6/2024 (N.A.) {5/2026}	1,478.40 (N.A.) {1,478.40}	876.56	63.55
		241	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 (MoRTH) (N24001201)	2-2019	9/2024 (N.A.) {9/2026}	2,926.42 (N.A.) {2,926.42}	1,208.79	51.89

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		242	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT (NHAI) (N24001303)	10-2013	12/2020 (N.A.) {12/2024}	649.90 (N.A.) {750.00}	711.53	98.30
		243	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE (NHAI) (N24001304)	10-2013	11/2020 (N.A.) {12/2024}	446.97 (598.48) {740.50}	638.80	96.30
		244	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA (NHAI) (N24001305)	10-2013	11/2020 (N.A.) {12/2024}	464.09 (605.53) {765.12}	698.25	97.30
		245	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N (NHAI) (N24001371)	10-2019	8/2023 (N.A.) {12/2024}	1,101.99 (N.A.) {1,101.99}	830.90	72.82
		246	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III) (NHAI) (N24001697)	2-2023	2/2025 (N.A.) {12/2025}	1,358.00 (N.A.) {1,358.00}	183.47	13.51
		247	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH (NHAI) (N24001698)	8-2022	8/2024 (N.A.) {8/2024}	1,198.02 (N.A.) {1,198.02}	2.27	-
		248	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT- GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3 (NHAI) (N24001699)	3-2022	12/2024 (N.A.) {7/2025}	312.58 (N.A.) {312.58}	174.80	71.82

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		249	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO (NHAI) (N24001700)	12-2021	3/2024 (N.A.) {12/2024}	552.55 (553.00) {553.00}	414.79	74.39
		250	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU (NHAI) (N24001701)	4-2022	4/2024 (N.A.) {9/2025}	1,769.50 (N.A.) {1,769.50}	3.12	-
		251	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT-GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: (NHAI) (N24001702)	12-2021	9/2024 (N.A.) {9/2024}	184.90 (185.00) {185.00}	163.01	95.60
		252	6 L OF AURANGABAD TO BIHAR-JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N (NHAI) (N24001703)	2-2022	5/2025 (N.A.) {5/2025}	786.81 (787.00) {787.00}	0.00	-
		253	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI (NHAI) (N24001704)	3-2021	3/2024 (N.A.) {12/2024}	1,020.84 (N.A.) {1,020.84}	89.52	-
		254	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C (NHAI) (N24001705)	3-2022	3/2024 (N.A.) {6/2025}	1,485.66 (N.A.) {1,485.66}	0.00	-
		255	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 (NHAI) (N24001708)	9-2020	6/2024 (N.A.) {12/2024}	2,156.22 (N.A.) {2,156.22}	2,134.67	98.23

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		256	BAKHTIYARPUR RAJAULI PKG-II FROM KM 54.405 TO KM 101.630 NH20 (NHAI) (N24001709)	9-2020	4/2023 (N.A.) {12/2024}	897.45 (N.A.) {1,090.00}	1,037.63	97.85
		257	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G (NHAI) (N24001711)	9-2020	3/2023 (N.A.) {12/2024}	939.43 (N.A.) {939.43}	370.62	100.00
		258	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO (NHAI) (N24001712)	8-2020	7/2023 (N.A.) {12/2024}	690.00 (N.A.) {690.00}	770.73	98.80
		259	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI?MOTIHARI- RAXAUL SECTION OF NH-28A FRO (NHAI) (N24001715)	12-2018	10/2020 (N.A.) {1/2024}	333.60 (466.59) {461.41}	460.38	100.00
		260	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH 122B FROM KM 29.730 TO KM 72.348 IN STATE OF BIH (MoRTH) (N24001870)	2-2022	11/2024 (N.A.) {11/2025}	624.43 (N.A.) {624.43}	247.68	79.00
		261	WIDENING AND STRENGTHENING FROM KM 70.15 TO KM 121.025 OF NH-80 (MoRTH) (N24001875)	3-2021	1/2025 (N.A.) {4/2025}	477.54 (N.A.) {477.54}	285.66	80.50
		262	WIDENING and STRENGTHENING FROM KM132.895 TO KM 190.15 NH-80 (MoRTH) (N24001876)	3-2021	3/2024 (N.A.) {9/2025}	566.15 (N.A.) {566.15}	222.62	53.40

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		263	CONSTRUCTION OF NEW 4-LANE BRIDGE (PARALLEL TO EXISTING VIKRAMASHILA SETU)FROM KM 8+920 TO KM 13+375 (MoRTH) (N24001877)	7-2020	5/2027 (N.A.) {5/2027}	1,110.23 (N.A.) {1,110.23}	288.28	32.80
		264	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH-319A FROM KM 0 TO KM 45 IN STATE OF BIHAR UNDER (MoRTH) (N24001878)	2-2022	12/2024 (N.A.) {4/2025}	427.29 (N.A.) {427.29}	166.93	68.40
		265	CONSTRUCTION OF PROPOSED 4_LANE REVELGUNJ BYPASS NH-19 IN THE STATE OF BIHAR ON EPC MODE CONNECTING (MoRTH) (N24001879)	3-2022	7/2025 (N.A.) {7/2025}	295.24 (N.A.) {295.24}	62.40	42.15
		266	CONSTRUCTION OF 6- LANE BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD (NH- (NHAI) (N24002062)	3-2023	9/2027 (N.A.) {9/2027}	3,012.27 (N.A.) {3,012.27}	99.17	5.78
		267	BALANCE WORK - WB-10 (GANDAK BRIDGE) KM 402.00 TO KM 440.00 (DEVANPUR - KOTWA) (NHAI) (N24002063)	12-2021	1/2024 (N.A.) {6/2025}	210.05 (N.A.) {210.05}	100.28	68.58
		268	PERMANENT RECTIFICATION OF 3 NOS. OF BLACK SPOTS IN PROJECT HIGHWAY NH-27 OF U.P BORDER - DEWAPUR - (NHAI) (N24002064)	12-2022	12/2025 (N.A.) {12/2025}	381.80 (N.A.) {381.80}	77.78	28.66
		269	4L GREENFIELD ALIGNMENT OF AMAS TO SHIVRAMPUR FROM 0.000 KM. TO 55.002 KM. OF NH 119 D (PKG-I) (NHAI) (N24002065)	2-2022	3/2025 (N.A.) {3/2025}	1,390.92 (N.A.) {1,390.92}	150.71	15.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		270	4L GREENFIELD ALIGNMENT OF SHIVRAMPUR TO RAMNAGAR FROM KM. 55.002 TO KM. 109.300 OF NH 119 D (PKG-I) (NHAI) (N24002066)	2-2022	7/2025 (N.A.) {7/2025}	1,494.31 (N.A.) {1,494.31}	38.28	4.59
		271	IMPROVEMENT OF 2 LANE WITH PAVED SHOULDER OF STRETCH FROM BIKRAMGANJ DAWATH MELAYABAGH NAWANAGR -DUM (MoRTH) (N24002133)	3-2021	3/2025 (N.A.) {6/2025}	178.63 (N.A.) {178.63}	98.83	83.86
		272	CONSTRUCTION OF 4 LANE ROB AND ITS APPROACHES AT THE LEVEL OF CROSSING (L C NO. 29-B) OF KM 29 (EKAN (MoRTH) (N24002193)	3-2023	7/2026 (N.A.) {7/2026}	201.08 (N.A.) {201.08}	10.34	15.00
		273	CONSTRUCTION OF 6-LANE ELEVATED / EXTRA DOSE CABLE BRIDGE ON RIVER GANGA PARALLEL TO AND WESTERN SID (MoRTH) (N24002194)	1-2024	11/2027 (N.A.) {11/2027}	3,064.45 (N.A.) {3,064.45}	58.84	0.76
		274	ESTIMATE FOR IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM RAMNAGAR TO ROSEDA FROM (KM 3.500 TO 4 (MoRTH) (N24002195)	1-2022	4/2026 (N.A.) {4/2026}	495.16 (N.A.) {495.16}	96.41	7.00
		275	CONSTRUCTION OF BHABHUA BYPASS FROM CH. 10+800(DESIGN CH. 10+800) TO CH. 19+860 (DESIGN CH. 18+150) (MoRTH) (N24002196)	2-2022	3/2026 (N.A.) {3/2026}	179.86 (N.A.) {179.86}	23.03	0.03

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		276	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM JUNCTION OF NH-22 NEAR HAJIPUR TO JUNCTION OF NH-12 (MoRTH) (N24002197)	2-2024	2/2026 (N.A.) {2/2026}	226.15 (N.A.) {226.15}	6.52	9.00
		277	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF BH/WBBORDER-AMDABAD- MANIHARI SECTION FROM DESIGN KM (MoRTH) (N24002198)	1-2022	3/2026 (N.A.) {3/2026}	353.27 (N.A.) {353.27}	24.44	-
	URBAN DEVELOPMENT	278	PATNA METRO RAIL CORPORATION LIMITED (PATNA METRO RAI) (N28000148)	2-2019	6/2024 (N.A.) {9/2024}	13,365.77 (N.A.) {13,925.50}	3,156.37	42.64
	WATER RESOURCES	279	SEWER NETWORK SPS AND STP BEGUSARAI (BUIDCO) (N30000026)	3-2018	7/2021 (N.A.) {12/2024}	230.06 (N.A.) {230.06}	253.75	96.00
		280	I AND D AND STP WORKS FOR BHAGALPUR (BUIDCO) (N30000027)	10-2017	9/2020 (N.A.) {4/2025}	254.13 (413.29) {413.29}	120.95	88.00
		281	SEWER NETWORKS SPS AND STP HAJIPUR (BUIDCO) (N30000035)	3-2018	8/2021 (N.A.) {6/2025}	305.19 (N.A.) {305.19}	330.68	93.00
		282	SEWER NETWORKS, SPS AND STP, MUNGER (BUIDCO) (N30000036)	3-2018	10/2021 (N.A.) {6/2024}	294.02 (350.79) {522.85}	418.80	100.00
		283	SAIDPUR SEWER NETWORK PATNA (BUIDCO) (N30000039)	4-2015	1/2021 (N.A.) {6/2022}	268.63 (N.A.) {493.85}	490.63	100.00
		284	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK (BUIDCO) (N30000044)	3-2017	5/2021 (N.A.) {2/2023}	277.42 (253.98) {277.42}	355.31	100.00
		285	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA (BUIDCO) (N30000050)	8-2017	6/2022 (N.A.) {12/2025}	578.89 (453.83) {578.89}	159.26	51.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		286	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA (BUIDCO) (N30000051)	8-2017	6/2022 (N.A.) {12/2025}	824.00 (734.09) {824.00}	377.31	52.00
CHHATTISGARH	COAL	287	GEVRA EXPANSION OCP (SECL) (35-70) MTY (SECL) (060100093)	6-2010	3/2023 (N.A.) {3/2025}	11,816.40 (N.A.) {11,816.40}	6,486.12	77.00
		288	PELMA OCP(15.00MTY) (SECL) (N06000045)	10-2022	3/2023 (N.A.) {3/2033}	1,624.59 (N.A.) {1,725.04}	14.92	17.00
		289	CHHAL OC SEAM -III (6.00 MTY) (SECL) (N06000104)	12-2013	3/2022 (N.A.) {3/2025}	610.63 (N.A.) {610.63}	572.68	85.00
		290	AMERA OC RCE (SECL) (N06000123)	2-2015	3/2018 (N.A.) {3/2026}	335.97 (N.A.) {335.97}	86.89	42.00
		291	AMGAON OPENCASST PROJECT RCE (SECL) (N06000135)	7-2015	3/2020 (N.A.) {3/2026}	316.10 (N.A.) {316.10}	188.33	65.00
		292	MAHAMAYA OPENCASST PROJECT (SECL) (N06000164)	5-2018	3/2026 (N.A.) {3/2026}	410.26 (N.A.) {410.26}	179.94	38.00
		293	JHIRIA WEST OPENCASST PROJECT (SECL) (N06000166)	1-2024	3/2029 (N.A.) {3/2029}	366.94 (N.A.) {366.94}	32.61	36.00
		294	BAROUD OC EXPANSION (3-10 MTY) (SECL) (N06000197)	8-2020	3/2029 (N.A.) {3/2029}	2,309.80 (N.A.) {2,309.80}	897.03	39.00
		295	JAMPALI OCP RCE (SECL) (N06000198)	5-2020	3/2024 (N.A.) {3/2025}	278.64 (N.A.) {278.64}	208.04	73.00
		296	PORDA CHIMTAPANI OCP (10 MTY) (SECL) (N06000199)	12-2020	3/2029 (N.A.) {3/2029}	2,310.12 (N.A.) {2,310.12}	45.96	10.00
		297	DIPKA OC EXPANSION 40 MTY (SECL) (N06000200)	12-2020	3/2029 (N.A.) {3/2029}	5,241.40 (N.A.) {5,241.40}	2,743.51	37.00
		298	JAGANNATHPUR OC RCE (3.0 MTY) (SECL) (N06000232)	7-2016	3/2020 (N.A.) {3/2025}	459.49 (N.A.) {459.49}	262.55	92.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		299	KATKONA RO UG PROJECT (1.74 MTY) (SECL) (N06000274)	1-2023	3/2029 (N.A.) {3/2029}	329.22 (N.A.) {329.22}	60.34	2.00
	DEPARTMENT OF HIGHER EDUCATION	300	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. (CPWD EDUCATION) (N28000141)	3-2020	7/2022 (N.A.) {3/2024}	808.62 (879.22) {808.62}	879.22	100.00
	PETROLEUM	301	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT (HPCL) (N16000413)	3-2021	3/2024 (N.A.) {3/2025}	456.00 (N.A.) {456.00}	373.90	96.90
	POWER	302	WESTERN REGION EXPANSION SCHEME XXV (PGCIL) (N18000350)	2-2023	11/2023 (N.A.) {3/2025}	385.84 (N.A.) {385.84}	251.71	85.00
		303	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII (PGCIL) (N18000354)	3-2023	9/2024 (N.A.) {4/2025}	271.69 (N.A.) {271.69}	179.03	97.00
		304	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME- XXVIII AND XXIX (PGCIL) (N18000355)	3-2023	3/2025 (N.A.) {3/2025}	260.30 (N.A.) {260.30}	180.79	98.00
		305	LARA SUPER THERMAL POWER PROJECT, STAGE-II (2X800 MW) (NTPC) (N18000381)	8-2023	6/2028 (N.A.) {6/2028}	15,530.00 (N.A.) {15,530.00}	1,179.38	5.50
	RAILWAYS	306	KIRANDUL - JAGDALPUR DOUBLING (ECOR) (N22000318)	12-2012	3/2020 (N.A.) {3/2024}	1,160.00 (N.A.) {1,440.00}	1,487.03	93.00
		307	JHARSUGUDA-BILASPUR 4TH LINE (SECR) (N22000484)	4-2015	3/2021 (N.A.) {12/2025}	1,973.00 (2,135.34) {2,135.34}	2,196.33	88.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		308	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR- PHASE I (IRCON) (N22000489)	4-2013	9/2018 (N.A.) {12/2025}	3,055.00 (N.A.) {3,438.39}	3,076.77	92.60
		309	Gauge conversion of Raipur(Kendri)- Dhamtari and Abhanpur-Rajim branch (67.20 km) (SECR) (N22000572)	7-2011	10/2024 (N.A.) {6/2025}	1,171.30 (N.A.) {1,171.30}	560.45	80.00
		310	NIPANIA-BHATAPRA (14.4 KM) 4TH LINE (PB#72/NR/2022-23) (SECR) (N22000573)	9-2022	12/2026 (N.A.) {12/2026}	170.49 (N.A.) {170.49}	0.12	-
		311	4TH LINE - BHATAPARA- HATHBAND (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000574)	12-2022	12/2026 (N.A.) {12/2026}	177.03 (N.A.) {177.03}	0.21	-
		312	4TH LINE - BHILAI-BHILAI NAGAR (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000575)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {177.34}	1.17	-
		313	4TH LINE - DADHAPARA-BELHA (9.2 KM) (PB#72/NR/2022-23) (SECR) (N22000576)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {169.06}	2.05	5.00
		314	4TH LINE - RAJNANDGAON- DONGARHGARH (31.2 KM) (PB#72/NR/2022-23) (SECR) (N22000577)	9-2022	9/2026 (N.A.) {9/2026}	328.34 (N.A.) {328.34}	9.17	5.00
		315	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (N22000579)	9-2022	9/2026 (N.A.) {9/2026}	167.64 (N.A.) {167.64}	0.00	-
		316	DOUBLING OF BORIDAND - AMBIKAPUR (SURAJPUR) (SECR) (N22000580)	6-2022	6/2030 (N.A.) {3/2027}	1,376.20 (1,242.94) {1,242.94}	134.06	10.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		317	DALLIRAJHARA - ROWGHAT (95 KM) {PART OF DALLIRAJHARA-JAGDALPUR (235 KM)} (RVNL) (N22000602)	3-2008	6/2025 (N.A.) {6/2025}	631.78 (N.A.) {1,627.56}	1,349.09	-
		318	CHIRIMIRI-NAGPUR HALT (SECR) (N22000616)	10-2018	6/2030 (N.A.) {6/2030}	241.00 (N.A.) {241.00}	0.00	-
	ROAD TRANSPORT AND HIGHWAYS	319	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 (MoRTH) (N24001217)	1-2016	8/2016 (N.A.) {3/2025}	497.14 (572.66) {572.66}	379.80	60.41
		320	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION (MoRTH) (N24001221)	1-2016	10/2016 (N.A.) {3/2025}	624.98 (N.A.) {731.50}	620.52	99.00
		321	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI (MoRTH) (N24001222)	3-2016	7/2016 (N.A.) {3/2025}	452.94 (N.A.) {435.61}	312.00	67.80
		322	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. (MoRTH) (N24001227)	3-2018	1/2019 (N.A.) {3/2025}	349.03 (N.A.) {349.03}	316.52	97.90
		323	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A (MoRTH) (N24001228)	11-2017	5/2019 (N.A.) {3/2025}	188.80 (N.A.) {188.80}	136.81	97.00
		324	DEVELOPMENT OF SIX LANE SARGI-BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA (NHAI) (N24001588)	12-2021	1/2025 (N.A.) {9/2025}	1,470.73 (N.A.) {1,470.73}	582.37	70.40

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		325	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA (NHAI) (N24001593)	11-2021	9/2024 (N.A.) {6/2025}	1,368.19 (N.A.) {1,368.19}	813.86	93.13
		326	4 LANE OF BILASPUR TO URGAL PROJECT (KM 0.00 TO KM 70.2) OF NH-130A (NHAI) (N24001611)	4-2020	3/2024 (N.A.) {9/2025}	1,855.59 (2,523.86) {2,523.86}	592.92	84.95
		327	UP GRADATION OF NH 930 SHERPAR TO KOHKA FROM KM 67.880 TO KM 114.860 TO TWO LANE WITH PAVED SHOULDER (MoRTH) (N24001917)	3-2020	5/2024 (N.A.) {3/2025}	278.97 (N.A.) {278.97}	200.22	83.10
		328	UP GRADATION OF NH 130C ABHANPUR TO PAUND FROM NK KM 0.000 TO KM. 40.380 TO TWO LANE WITH PAVED SHOU (MoRTH) (N24001919)	12-2020	9/2023 (N.A.) {3/2025}	193.16 (N.A.) {193.16}	97.57	79.70
		329	UPGRADATION OF NH 130A MUNGELI TO PONDIL FROM NH KM. 51.600 TO KM. 77.870 KM. 80.970 TO 96.970 TO 2 (MoRTH) (N24001920)	3-2021	9/2024 (N.A.) {3/2025}	218.57 (N.A.) {218.57}	122.29	81.42
		330	DEVELOPMENT OF SIX LANE BASANWAHI-MARANGPURI OF NH 130 CD FROM KM.99+500 TO 124+661 UNDER RAIPUR VIS (NHAI) (N24002017)	3-2022	10/2025 (N.A.) {9/2026}	1,307.16 (N.A.) {1,307.16}	199.32	23.44
		331	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 1 SECTION OF NH 53 FROM CH 0.000 TO CH 44.50 (NHAI) (N24002045)	6-2022	7/2025 (N.A.) {7/2025}	1,828.00 (N.A.) {1,828.00}	432.60	28.55

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		332	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 2 SECTION OF NH 53 FROM CH 44+500 TO CH.92+230 I (NHAI) (N24002046)	6-2022	5/2025 (N.A.) {5/2025}	1,958.94 (1,959.00) {1,958.94}	633.37	30.17
	<u>STEEL</u>	333	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 (NMDC) (N12000124)	11-2015	6/2023 (N.A.) {12/2025}	2,907.00 (5,427.06) {5,427.06}	2,544.37	71.20
		334	SCREENING PLANT-III AT KIRANDUL (NMDC) (N12000127)	3-2021	8/2024 (N.A.) {1/2026}	2,092.97 (2,718.84) {2,718.84}	1,404.67	68.92
		335	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (NMDC) (N12000130)	7-2021	11/2024 (N.A.) {12/2025}	282.44 (349.75) {349.75}	188.79	68.50
		336	REPLACEMENT OF CONVERTER VESSELS, TRUNNION RINGS, SUPPORT SYSTEM AND INSTALLATION OF SECONDARY EMISS (SAIL) (N12000131)	10-2023	6/2026 (N.A.) {6/2026}	471.83 (N.A.) {471.83}	44.24	8.18
		337	REBUILDING OF COKE OVEN BATTERY NO.7 AND 8 OF BHILAI STEEL PLANT (SAIL) (N12000134)	11-2023	10/2025 (N.A.) {10/2025}	884.10 (N.A.) {884.10}	322.20	61.25
	<u>URBAN DEVELOPMENT</u>	338	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV- 112 TYPE V-68 TYPE VI-5 SHOPS COMMUNI (CPWD) (N28000149)	5-2019	9/2020 (N.A.) {10/2024}	299.97 (299.97) {299.97}	266.00	87.66
<u>DELHI</u>	<u>CIVIL AVIATION</u>	339	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR (AAI) (N04000076)	11-2016	4/2020 (N.A.) {4/2024}	303.80 (374.98) {351.21}	340.71	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DPIIT</u>	340	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE (IICC FOR DPIIT) (N40000002)	11-2017	12/2019 (N.A.) {4/2025}	4,773.00 (N.A.) {5,401.00}	4,929.51	99.60
	<u>FINANCE</u>	341	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA (NPCC) (N07000001)	7-2018	4/2022 (N.A.) {4/2022}	228.50 (N.A.) {220.27}	176.28	85.00
	<u>HOME AFFAIRS</u>	342	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI (CPWD FOR MHA) (N28000071)	10-2013	10/2019 (N.A.) {9/2024}	1,219.21 (2,091.53) {2,091.53}	1,946.47	100.00
		343	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI (CPWD FOR MHA) (N45000002)	6-2019	7/2022 (N.A.) {9/2025}	277.35 (N.A.) {277.35}	97.44	60.00
	<u>RAILWAYS</u>	344	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE (NR) (N22000281)	4-2012	(N.A.) {6/2026}	295.68 (N.A.) {419.00}	163.51	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	345	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR (NHAI) (N24001771)	6-2020	12/2024 (N.A.) {12/2024}	1,479.22 (N.A.) {1,479.22}	1,491.26	99.00
		346	6L ACCESS CONTROLLED HIGHWAY FROM DND MAHARANI BAGH JN. WITH JAIPUR PUSHTA ROAD OF NH 148NA FROM (NHAI) (N24001773)	5-2020	7/2024 (N.A.) {9/2025}	1,467.44 (N.A.) {1,942.89}	1,113.43	84.93

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		347	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 (NHAI) (N24001777)	7-2020	10/2023 (N.A.) {6/2025}	2,171.80 (N.A.) {2,171.80}	958.13	99.99
		348	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) (NHAI) (N24001779)	3-2018	9/2022 (N.A.) {6/2025}	2,507.00 (N.A.) {3,030.73}	1,155.70	92.00
		349	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O (NHAI) (N24001781)	1-2018	10/2021 (N.A.) {3/2025}	2,067.67 (N.A.) {2,160.00}	1,496.49	99.15
		350	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM (NHAI) (N24001825)	7-2020	10/2023 (N.A.) {6/2025}	1,894.96 (N.A.) {1,894.96}	741.88	90.91
	TELECOMMUNICATIONS	351	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT (CPWD FOR TELECO) (N28000115)	10-2014	3/2018 (N.A.) {3/2025}	248.20 (N.A.) {248.20}	232.04	98.00
	URBAN DEVELOPMENT	352	DELHI MRTS PHASE-III (DMRC) (N28000056)	9-2011	3/2016 (N.A.) {8/2021}	38,585.00 (43,095.35) {40,180.91}	40,588.85	99.99
		353	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR (NBCC) (N28000105)	7-2016	(N.A.) {10/2024}	2,694.00 (N.A.) {2,694.00}	2,402.68	98.00
		354	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I (CPWD) (N28000128)	10-2016	7/2021 (N.A.) {6/2024}	1,180.00 (N.A.) {1,100.80}	36.69	2.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		355	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I (CPWD) (N28000129)	10-2016	3/2022 (N.A.) {6/2024}	1,128.00 (N.A.) {1,128.00}	634.97	58.00
		356	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS (DMRC) (N28000135)	7-2019	3/2025 (N.A.) {3/2026}	24,948.65 (N.A.) {24,948.65}	14,569.33	62.01
		357	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI (CPWD) (N28000153)	1-2022	11/2024 (N.A.) {5/2025}	646.52 (N.A.) {646.52}	430.86	85.00
		358	REDEVELOPMENT OF GPRA AT NETAJI NAGAR NEW DELHI PACKAGE 2 (NBCC) (N28000156)	10-2016	3/2024 (N.A.) {3/2025}	1,536.72 (N.A.) {1,536.72}	468.18	87.50
	<u>WATER RESOURCES</u>	359	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD ? 10MG/L (DJB) (N30000014)	3-2017	12/2022 (N.A.) {12/2024}	665.78 (N.A.) {665.78}	782.51	96.00
<u>GOA</u>	<u>CIVIL AVIATION</u>	360	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. (AAI) (N04000095)	11-2017	9/2021 (N.A.) {6/2025}	255.69 (N.A.) {255.69}	107.40	77.00
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	361	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. (CPWD EDUCATION) (N42000002)	5-2019	8/2021 (N.A.) {12/2024}	303.90 (N.A.) {390.40}	364.00	99.30
	<u>PETROLEUM</u>	362	UPGRADING IPSHEM TO WORLD CLASS FACILITY OF ONGC, GOA (ONGC) (N16000502)	3-2023	6/2024 (N.A.) {2/2025}	325.53 (N.A.) {325.53}	304.19	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	363	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM. 508.000 TO KM. 513.150 INCLUDING APPROACHES ON N (MoRTH) (N24002181)	4-2023	4/2026 (N.A.) {4/2026}	641.46 (N.A.) {641.46}	0.00	-
GUJARAT	<u>CIVIL AVIATION</u>	364	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT (AAI) (NO4000088)	1-2018	8/2022 (N.A.) {12/2024}	1,405.00 (N.A.) {1,405.00}	1,303.60	100.00
		365	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. (AAI) (NO4000093)	8-2018	2/2021 (N.A.) {3/2025}	353.25 (N.A.) {353.25}	346.11	99.50
		366	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. (AAI) (NO4000099)	6-2022	12/2025 (N.A.) {12/2025}	1,305.00 (1,143.95) {1,143.95}	441.94	45.00
	<u>PETROLEUM</u>	367	REDEVELOPMENT OF SANTHAL FIELD (ONGC) (N16000279)	2-2017	3/2026 (N.A.) {3/2026}	1,162.56 (N.A.) {1,162.56}	1,150.42	93.10
		368	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY (IOCL) (N16000382)	11-2019	5/2023 (N.A.) {3/2025}	5,251.00 (5,894.00) {5,894.00}	4,561.12	99.30
		369	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY (IOCL) (N16000409)	9-2020	8/2024 (N.A.) {12/2025}	18,936.00 (N.A.) {18,936.00}	10,244.46	79.40
		370	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM (IOCL) (N16000411)	10-2020	8/2023 (N.A.) {6/2025}	1,614.00 (N.A.) {1,614.00}	1,076.50	94.21
		371	REDEVELOPMENT OF LINC FIELD (ONGC) (N16000428)	4-2021	3/2025 (N.A.) {7/2025}	631.03 (860.04) {860.04}	313.58	65.60

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		372	REDEVELOPMENT OF SOBHASAN COMPLEX (ONGC) (N16000431)	8-2021	2/2026 (N.A.) {2/2026}	885.63 (1,286.67) {1,286.67}	482.50	60.40
		373	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD (ONGC) (N16000444)	1-2022	11/2024 (N.A.) {11/2025}	621.40 (N.A.) {621.40}	123.10	21.40
		374	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT (IOCL) (N16000454)	1-2022	9/2024 (N.A.) {8/2025}	328.00 (N.A.) {328.00}	42.05	36.10
		375	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT (ONGC) (N16000477)	5-2022	2/2025 (N.A.) {9/2025}	249.43 (N.A.) {249.43}	184.17	90.20
		376	KALOL REDEVELOPMENT PROJECT (ONGC) (N16000481)	8-2022	3/2027 (N.A.) {3/2027}	1,487.41 (N.A.) {1,487.41}	859.39	56.80
		377	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A (ONGC) (N16000483)	7-2021	7/2025 (N.A.) {7/2025}	173.03 (N.A.) {169.84}	136.69	82.50
		378	REVAMPING OF SV STATIONS, GAS TERMINAL AND KRIBHCO TERMINAL (ONGC) (N16000514)	11-2022	8/2026 (N.A.) {8/2026}	837.34 (N.A.) {837.34}	122.28	37.20
POWER		379	GUJARAT 200 MW (GUVNL TENDER) (NTPC) (N18000295)	1-2021	7/2022 (N.A.) {9/2025}	842.27 (N.A.) {842.27}	668.98	30.00
		380	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) (NTPC) (N18000296)	5-2021	9/2022 (N.A.) {3/2025}	674.92 (N.A.) {674.92}	543.04	91.00
		381	Bagodara Solar Power Project (SJVN) (N18000297)	5-2021	10/2022 (N.A.) {12/2025}	339.35 (N.A.) {339.35}	315.95	51.22

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		382	DAYAPAR WIND ENERGY PROJECT 150MW (NTPC) (N18000319)	11-2021	5/2023 (N.A.) {3/2025}	937.80 (N.A.) {937.80}	777.98	98.00
		383	DAYAPAR WIND ENERGY PROJECT 200MW (NTPC) (N18000345)	7-2022	3/2025 (N.A.) {1/2026}	1,316.02 (N.A.) {1,316.02}	302.35	23.00
		384	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) (NTPC) (N18000346)	9-2022	9/2024 (N.A.) {1/2026}	7,179.54 (N.A.) {7,179.54}	3,546.26	61.00
		385	BHUJ SOLAR 300MW (TRANCHE- IV WIND SOLAR HYBRID) (NTPC) (N18000349)	11-2022	3/2024 (N.A.) {9/2026}	1,442.60 (N.A.) {1,442.60}	787.54	2.00
		386	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK (PGCIL) (N18000357)	3-2023	12/2024 (N.A.) {3/2025}	922.30 (N.A.) {922.30}	513.67	83.00
		387	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT (PGCIL) (N18000358)	3-2023	3/2025 (N.A.) {4/2025}	815.12 (N.A.) {815.12}	10.99	72.00
		388	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK (PGCIL) (N18000359)	3-2023	12/2024 (N.A.) {3/2025}	966.79 (N.A.) {966.79}	433.22	82.00
		389	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000360)	3-2023	3/2025 (N.A.) {6/2025}	1,167.55 (N.A.) {1,167.55}	651.14	56.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		390	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000361)	3-2023	3/2025 (N.A.) {6/2025}	2,820.99 (N.A.) {2,820.99}	2,211.46	61.00
		391	KHAVDA 1200MW (4X300MW) IN KHAVDA RE PARK (NTPC) (N18000365)	6-2023	12/2024 (N.A.) {1/2026}	6,283.81 (N.A.) {6,283.81}	1,493.59	16.00
		392	DAYAPAR WIND- III (HYBRID TRANCHE-V) (NTPC) (N18000366)	5-2023	1/2025 (N.A.) {9/2025}	1,095.01 (N.A.) {1,095.01}	325.61	-
		393	TS FOR EVACUATION OF POWER FROM POTENTIAL RE ZONE IN KHAVDA AREA OF GUJARAT UNDER PH-IV PART E3 (PGCIL) (N18000383)	7-2023	7/2025 (N.A.) {7/2025}	334.00 (N.A.) {334.00}	0.00	6.00
		394	TS FOR EVACUATION OF ADDITIONAL 7GW RE POWER FROM KHAVDA RE PARK UNDER PHASE-III PART B [VATAMAN TRA (PGCIL) (N18000384)	12-2023	12/2025 (N.A.) {12/2025}	3,752.00 (N.A.) {3,752.00}	497.02	7.00
		395	TS FOR EVACUATION OF POWER FROM 7GW REZ IN KHAVDA AREA UNDER PHASE-IV PART E2 (PGCIL) (N18000390)	5-2024	5/2026 (N.A.) {5/2026}	679.00 (N.A.) {679.00}	0.00	6.00
		396	AUGMENTATION OF TRANSFORMATION CAPACITY AT JAM KHAMBHALIYA PS [GIS] [SPV NAME POWERGRID JAM KHAMBHAL (PGCIL) (N18000398)	10-2024	7/2026 (N.A.) {7/2026}	329.00 (N.A.) {329.00}	0.00	1.00
		397	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000400)	10-2024	10/2026 (N.A.) {10/2026}	4,766.00 (N.A.) {4,766.00}	65.00	1.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		398	PROVISION OF DYNAMIC REACTIVE COMPENSATION AT KHAVDA POOLING STATION 1 [KPS1] AND KHAVDA POOLING STA (PGCIL) (N18000402)	11-2024	11/2026 (N.A.) {5/2026}	501.00 (N.A.) {501.00}	0.00	6.00
		399	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000405)	11-2024	5/2029 (N.A.) {5/2029}	24,819.00 (N.A.) {24,819.00}	1,340.00	1.00
		400	600 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000406)	4-2022	3/2026 (N.A.) {3/2026}	4,100.45 (N.A.) {4,100.45}	0.69	6.00
	RAILWAYS	401	MIYAGAM-KARJAN-DABHOI- SAMLAYA (GC) (WR) (N22000142)	4-2011	(N.A.) {10/2026}	844.10 (844.10) {844.10}	589.44	41.00
		402	ANAND GODHRA DOUBLING PROJECT 79 KMS (WR) (N22000504)	4-2017	3/2020 (N.A.) {2/2025}	692.25 (692.26) {692.26}	655.49	97.00
		403	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS (WR) (N22000505)	4-2018	3/2024 (N.A.) {10/2024}	537.31 (537.31) {671.91}	844.55	100.00
		404	4TH LINE BETWEEN BAREJADI NANDEJ (GERATPUR)- SANAND (38.20 KM) (AHMEDABAD BYPASS). (WR) (N22000532)	2-2023	3/2027 (N.A.) {2/2027}	961.67 (961.67) {961.67}	88.84	2.50
		405	QUADRUPLING BETWEEN GANDHIDHAM - ADIPUR WITH Y CONNECTION AT ADIPUR FOR PROVIDING DIRECT ENTRY TOWAR (WR) (N22000533)	2-2023	12/2025 (N.A.) {10/2025}	152.44 (152.44) {152.44}	56.82	20.00
		406	RAJKOT-KANALUS (111.20 KM) (WR) (N22000535)	10-2021	10/2026 (N.A.) {3/2026}	1,011.72 (1,080.58) {1,080.58}	1,300.21	65.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		407	HIMMATNAGAR-KHEDBRAHMA (54.83 KM) (WR) (N22000537)	6-2022	2/2030 (N.A.) {6/2025}	354.99 (482.42) {482.42}	770.23	80.00
		408	PETLAD-BHADLAN (22.5 KM) (WR) (N22000538)	5-2022	5/2030 (N.A.) {12/2025}	202.50 (307.12) {307.12}	61.66	7.00
		409	NADIAD-PETLAD (37.26 KM) (WR) (N22000539)	5-2022	6/2030 (N.A.) {12/2025}	335.34 (461.91) {461.91}	73.17	7.00
		410	SAMLAYA-TIMBA ROAD (53.53 KM) (WR) (N22000540)	2-2023	3/2030 (N.A.) {7/2026}	401.48 (670.17) {670.17}	75.62	12.00
		411	SAMNI-JAMBUSAR (24.08 KM) (WR) (N22000541)	5-2022	3/2030 (N.A.) {12/2025}	216.72 (349.93) {349.93}	79.09	25.00
		412	VIJAPUR-AMBLIYASAN (41.53 KM) (WR) (N22000547)	5-2022	3/2030 (N.A.) {6/2025}	309.81 (415.38) {415.38}	527.94	75.00
		413	ADRAJ MOTI-VIAJAPUR (39.75 KM) (WR) (N22000548)	5-2022	5/2030 (N.A.) {5/2030}	296.54 (N.A.) {296.54}	0.00	-
		414	NEW BG LINE BETWEEN NALIYA- JAKHAU PORT (WR) (N22000550)	2-2023	1/2028 (N.A.) {9/2026}	410.46 (410.46) {410.46}	33.59	2.00
		415	NEW BG LINE INTERSECTION (5 NOS) BETWEEN GERATPUR- SANAND & BOTAD-AHMEDABAD (16.51 KM) (PB#29/NR/202 (WR) (N22000551)	10-2022	10/2027 (N.A.) {10/2027}	437.21 (N.A.) {437.21}	0.00	-
		416	TARANGA HILL ABU ROAD VIA AMBAJI NEW LINE (NWR) (N22000592)	7-2022	7/2030 (N.A.) {12/2026}	1,695.82 (N.A.) {2,798.16}	922.90	9.00
		417	JUNAGARH -VISAVADAR (42.28) KM (RVNL) (N22000600)	6-2022	12/2026 (N.A.) {12/2026}	492.83 (N.A.) {492.83}	0.00	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		418	MODASA- SHAMLAJI NEW LINE (MM OF AHMEDABAD- HIMMATNAGAR-UDAIPUR (299.2 KM)) (WR) (N22000622)	9-2012	3/2027 (N.A.) {2/2026}	261.68 (261.68) {261.68}	632.45	45.00
	ROAD TRANSPORT AND HIGHWAYS	419	FOUR LANING OF BHAVNAGAR- TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. (NHAI) (N24000567)	5-2016	8/2019 (N.A.) {6/2024}	998.18 (N.A.) {998.18}	802.34	100.00
		420	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST (NHAI) (N24000569)	5-2016	9/2019 (N.A.) {5/2025}	723.64 (N.A.) {723.64}	561.37	96.35
		421	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU (NHAI) (N24000570)	5-2016	8/2019 (N.A.) {2/2025}	763.08 (N.A.) {763.08}	516.25	96.05
		422	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 (NHAI) (N24000592)	7-2016	7/2020 (N.A.) {2/2025}	829.97 (N.A.) {829.97}	481.13	94.77
		423	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. (NHAI) (N24000649)	1-2017	12/2020 (N.A.) {6/2025}	1,251.11 (1,527.75) {1,527.75}	684.13	83.84
		424	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR (NHAI) (N24000834)	3-2018	10/2021 (N.A.) {4/2025}	1,161.39 (1,738.03) {1,404.00}	518.84	69.48

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		425	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA (MoRTH) (N24000925)	10-2018	11/2020 (N.A.) {9/2024}	400.76 (394.44) {394.44}	287.39	87.00
		426	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT (MoRTH) (N24001427)	6-2020	4/2023 (N.A.) {9/2024}	166.21 (N.A.) {166.21}	98.65	93.00
		427	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 (NHAI) (N24001443)	5-2020	3/2024 (N.A.) {1/2025}	690.30 (929.95) {929.95}	1,193.08	86.40
		428	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION (NHAI) (N24001444)	5-2020	1/2024 (N.A.) {1/2025}	882.00 (N.A.) {882.00}	1,256.69	93.05
		429	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB (NHAI) (N24001445)	5-2020	7/2023 (N.A.) {1/2025}	691.52 (903.85) {903.85}	909.80	93.05
		430	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG (NHAI) (N24001446)	5-2020	12/2023 (N.A.) {1/2025}	894.00 (1,210.06) {1,210.06}	1,025.93	88.84
		431	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 (NHAI) (N24001515)	9-2020	2/2024 (N.A.) {11/2025}	1,542.02 (N.A.) {1,542.02}	922.54	67.24

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		432	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 (NHAI) (N24001516)	9-2020	2/2024 (N.A.) {8/2024}	1,185.69 (N.A.) {1,185.69}	948.23	92.70
		433	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 (NHAI) (N24001518)	11-2019	9/2023 (N.A.) {3/2025}	1,669.56 (N.A.) {1,669.56}	1,013.36	93.50
		434	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 (NHAI) (N24001519)	9-2020	11/2023 (N.A.) {9/2024}	1,198.55 (N.A.) {1,198.55}	894.94	95.70
		435	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 (NHAI) (N24001520)	11-2019	5/2024 (N.A.) {3/2025}	1,604.06 (N.A.) {1,604.06}	1,229.92	95.73
		436	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT (NHAI) (N24001785)	3-2022	6/2025 (N.A.) {6/2025}	1,373.06 (1,085.00) {1,373.06}	532.32	72.26
		437	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU (NHAI) (N24001786)	3-2021	3/2024 (N.A.) {9/2025}	1,259.00 (2,652.24) {1,910.00}	267.96	30.90
		438	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU (NHAI) (N24001788)	7-2020	12/2023 (N.A.) {2/2025}	2,271.86 (3,372.97) {3,916.00}	1,095.02	98.10

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		439	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA (NHAI) (N24001789)	7-2020	8/2023 (N.A.) {3/2025}	1,710.30 (2,665.08) {1,927.00}	709.63	89.20
		440	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ-RGBS-PACKAGE-3) (NHAI) (N24001790)	2-2020	8/2023 (N.A.) {12/2024}	752.30 (N.A.) {766.20}	451.11	98.14
		441	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS-PACKAGE-1) (NHAI) (N24001791)	2-2020	6/2023 (N.A.) {5/2024}	606.51 (N.A.) {657.00}	453.89	98.99
		442	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) (NHAI) (N24001792)	3-2021	9/2022 (N.A.) {2/2025}	536.03 (N.A.) {536.03}	480.77	99.48
		443	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) (NHAI) (N24001793)	3-2021	9/2022 (N.A.) {4/2025}	485.75 (N.A.) {485.75}	387.72	98.17
		444	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4) (NHAI) (N24001794)	2-2020	3/2023 (N.A.) {12/2024}	778.15 (N.A.) {785.67}	547.22	99.70
		445	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE) (NHAI) (N24001827)	3-2022	3/2023 (N.A.) {2/2025}	162.73 (N.A.) {162.73}	131.79	95.30

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		446	UPGRADATION AND STRENGTHENING TO 2 LANE PS FROM KM 95/500 TO KM 129/775 OF NH 168 G IDAR BHILODA SA (MoRTH) (N24002014)	9-2022	12/2023 (N.A.) {12/2025}	237.28 (N.A.) {237.28}	0.59	-
		447	UPGRADATION TO 4L PS DIVIDED CARRIAGEWAY FROM PATAN (NEAR RAJPUR) TO GOJARIYA FROM KM 52.000 TO KM 1 (NHAI) (N24002034)	12-2021	3/2025 (N.A.) {3/2025}	1,181.34 (1,181.00) {1,181.34}	458.32	64.02
		448	WIDENING TO 6L OF EXISTING 4L JETPUR - GONDAL - RAJKOT SECTION FROM KM. 117.600 TO KM. 185.00 ON NH- (NHAI) (N24002035)	9-2023	9/2025 (N.A.) {9/2025}	2,070.44 (N.A.) {2,070.44}	311.22	20.77
		449	UPGRADATION OF DHORAJI JAMKANDORNA KALAVAD SECTION OF NH 927D FROM DESIGN CHAINAGE KM 00 TO KM 58.11 (MoRTH) (N24002117)	10-2022	2/2024 (N.A.) {2/2026}	246.60 (291.00) {291.00}	29.33	15.00
		450	UPGRADATION TO TWO LANE WITH PAVED SHULDER CONFIGURATION FROM KM 00 TO 47 OF NH 351 MAHUA TO BADHA (MoRTH) (N24002118)	12-2022	2/2024 (N.A.) {8/2025}	173.06 (N.A.) {219.00}	0.15	-
		451	WORK OF DEVELOPMENT AND CONSTRUCTION OF ELEVATED CORRIDOR FROM KM 38/660 TO KM 42/690 (ISCON JUNCTION) (MoRTH) (N24002182)	3-2023	3/2026 (N.A.) {3/2026}	530.20 (N.A.) {530.20}	0.00	-
		452	WIDENING 2 LANE TO 4-LANE FROM KM 92/320 TO KM 115/320 (VAV CHOKDI-SATLASANA TO TO VRUNDAVAN CHOKDI, (MoRTH) (N24002183)	3-2022	3/2026 (N.A.) {3/2026}	151.13 (N.A.) {171.00}	0.00	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>URBAN DEVELOPMENT</u>	453	AHMEDABAD METRO RAIL PROJECT PHASE I (AMR) (N28000122)	11-2014	12/2018 (N.A.) {5/2025}	10,773.00 (N.A.) {12,924.55}	12,423.47	99.87
		454	AHMEDABAD METRO RAIL PROJECT PHASE II (AMR) (N28000137)	3-2019	3/2024 (N.A.) {6/2025}	5,384.17 (N.A.) {5,384.17}	3,821.45	81.24
		455	SURAT METRO RAIL PROJECT (AMR) (N28000138)	3-2019	3/2024 (N.A.) {10/2025}	12,020.32 (N.A.) {12,020.32}	6,168.22	59.66
<u>HARYANA</u>	<u>HEALTH AND FAMILY WELFARE</u>	456	ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT MANETHI, HARYANA. (HITES) (N21000032)	3-2019	3/2023 (N.A.) {3/2026}	1,294.34 (1,294.34) {1,294.34}	202.45	11.90
	<u>HOME AFFAIRS</u>	457	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" (CPWD FOR MHA) (N28000147)	1-2020	10/2023 (N.A.) {6/2025}	166.98 (170.23) {170.23}	129.08	94.00
	<u>PETROLEUM</u>	458	R and D CAMPUS II AT FARIDABAD (IOCL) (N16000375)	6-2019	12/2022 (N.A.) {7/2025}	2,281.94 (3,219.94) {3,219.94}	1,678.84	62.40
		459	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA (IOCL) (N16000412)	2-2021	9/2024 (N.A.) {12/2025}	34,627.00 (38,231.00) {38,231.00}	18,355.10	82.30
		460	POLY BUTADIENE RUBBER PLANT AT PANIPAT (IOCL) (N16000458)	3-2022	3/2025 (N.A.) {6/2026}	1,459.00 (2,102.79) {2,102.79}	755.33	57.70
	<u>RAILWAYS</u>	461	DOUBLING BETWEEN BHIWANI- DOBH BAHALI (NWR) (N22000604)	2-2023	2/2028 (N.A.) {12/2025}	471.06 (N.A.) {471.06}	64.45	40.00
		462	DOUBLING BETWEEN REWARI- KATHUWAS (27.73 KM) (NWR) (N22000606)	2-2023	6/2027 (N.A.) {12/2025}	352.41 (N.A.) {352.41}	116.95	30.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	463	CONSTRUCTION OF 4-LANE NH-344P-PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA (NHAI) (N24001532)	11-2021	11/2023 (N.A.) {8/2024}	694.00 (1,918.00) {1,500.00}	1,682.82	100.00
		464	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP (NHAI) (N24001533)	11-2020	12/2023 (N.A.) {3/2025}	1,690.23 (N.A.) {2,010.17}	1,368.33	98.50
		465	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP (NHAI) (N24001534)	12-2020	1/2024 (N.A.) {3/2025}	1,334.04 (N.A.) {1,334.00}	997.01	99.00
		466	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 (NHAI) (N24001535)	7-2020	7/2022 (N.A.) {3/2025}	899.00 (1,882.46) {1,882.46}	1,123.98	93.10
		467	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI (NHAI) (N24001536)	7-2020	7/2022 (N.A.) {3/2025}	817.00 (1,605.00) {1,605.00}	1,025.56	99.00
		468	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F (NHAI) (N24001633)	12-2020	12/2023 (N.A.) {3/2025}	1,430.88 (1,549.23) {1,549.23}	1,120.60	99.60

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		469	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO (NHAI) (N24001634)	1-2021	12/2023 (N.A.) {3/2025}	1,306.95 (1,453.34) {1,453.34}	942.65	98.50
		470	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O (NHAI) (N24001635)	3-2022	2/2025 (N.A.) {2/2025}	1,269.50 (N.A.) {1,269.50}	218.00	49.00
		471	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K (NHAI) (N24001673)	3-2020	3/2023 (N.A.) {3/2025}	510.97 (N.A.) {510.97}	529.00	94.20
		472	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH-352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU (NHAI) (N24001774)	12-2020	11/2023 (N.A.) {6/2024}	1,524.03 (N.A.) {1,524.03}	1,092.84	62.25
		473	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH-11 AS A FEEDER ROUTE IN THE STATE (NHAI) (N24001775)	2-2020	1/2023 (N.A.) {12/2024}	808.31 (N.A.) {958.00}	850.65	99.89
		474	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN (NHAI) (N24001783)	11-2018	9/2021 (N.A.) {3/2025}	2,252.75 (N.A.) {2,252.75}	1,223.07	99.95
		475	UPGRADATION OF EXISTING 4 LANE ISMAILABAD-AMBALA SECTION (KM. 0+000 TO KM 42+500) (PART OF AMBALA-KO (NHAI) (N24002037)	1-2023	12/2025 (N.A.) {3/2026}	609.32 (609.00) {609.00}	148.58	37.40

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		476	CONSTRUCTION OF 6-LANE GREENFIELD KARNAL RING ROAD STARTING FROM NH-44 NEAR VILLAGE SHAMGARH (DESIGN (NHAI) (N24002038)	11-2022	8/2025 (N.A.) {8/2025}	1,691.45 (1,998.00) {1,998.00}	591.18	57.00
		477	CONSTRUCTION OF 6-LANE GREENFIELD AMBALA RING ROAD STARTING FROM JUNCTION WITH SHAMLI- AMBALA SECTION (NHAI) (N24002039)	2-2023	10/2025 (N.A.) {10/2025}	1,088.64 (1,178.00) {1,178.00}	356.69	39.00
		478	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM RANIPUR BARS (SAHARANPUR DISTRICT) TO ADHOYA (NHAI) (N24002040)	4-2022	5/2025 (N.A.) {5/2028}	1,554.21 (N.A.) {1,554.21}	468.42	49.50
		479	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM ADHOYA MUSALMANA (AMBALA DISTRICT) TO SADOPUR (NHAI) (N24002041)	4-2022	5/2025 (N.A.) {5/2025}	1,491.71 (N.A.) {1,491.71}	657.76	42.50
		480	CONSTRUCTION OF 4-LANING OF BHIWANI HANSI ROAD SECTION OF NH 148B (DESIGN LENGTH 42.934 KM) UNDER BH (NHAI) (N24002042)	11-2022	12/2025 (N.A.) {12/2025}	1,322.13 (N.A.) {1,322.13}	312.23	73.13
		481	CONSTRUCTION OF 4-LANE GREENFIELD JALBEHRA - SHAHBAD SECTION OF NH ? 152G FROM KM 0+000 TO KM 22+850 (NHAI) (N24002043)	3-2022	6/2025 (N.A.) {6/2025}	927.22 (N.A.) {927.22}	424.13	75.50
		482	4L AMBALA - KALAAMB FROM KM. -0.800 TO KM. 33.015 OF OLD NH-72 (NHAI) (N24002044)	6-2023	6/2025 (N.A.) {6/2025}	629.16 (N.A.) {629.16}	181.00	78.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		483	CONSTRUCTION OF GREENFIELD CONNECTIVITY TO JEWAR INTERNATIONAL AIRPORT FROM DND FARIDABAD BALLABHGAR (NHAI) (N24002048)	7-2022	6/2025 (N.A.) {6/2025}	2,414.67 (2,898.00) {2,898.00}	1,108.38	40.80
<u>HIMACHAL PRADESH</u>	<u>DEPARTMENT OF HIGHER EDUCATION</u>	484	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR (CPWD EDUCATION) (N42000008)	9-2018	6/2022 (N.A.) {6/2025}	392.51 (N.A.) {446.43}	313.35	90.80
		485	CONSTRUCTION OF PERMANENT CAMPUSES OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND DHARAMSHAL (CPWD) (N42000011)	3-2021	11/2024 (N.A.) {7/2025}	512.37 (300.45) {300.45}	113.41	66.00
	<u>POWER</u>	486	PARBATI HEP (4X200 MW) (NHPC) II (NHPC) (180100210)	9-2002	9/2009 (N.A.) {3/2025}	3,919.59 (N.A.) {12,899.00}	12,744.76	98.73
		487	LUHRI HYDROELECTRIC PROJECT (STAGE1) (SJVN) (N18000279)	11-2020	1/2026 (N.A.) {12/2028}	1,810.56 (N.A.) {3,060.71}	1,675.51	51.02
		488	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) (SJVN) (N18000291)	10-2020	11/2025 (N.A.) {3/2027}	687.97 (N.A.) {1,426.00}	807.53	64.43
		489	SUNNI DAM HYDRO ELECTRIC PROJECT (SJVN) (N18000344)	1-2023	4/2028 (N.A.) {12/2028}	2,614.51 (N.A.) {3,605.30}	891.04	27.92
	<u>RAILWAYS</u>	490	BHANUPALI-BILASPUR BERI NL (RVNL) (N22000273)	4-2008	12/2026 (N.A.) {3/2025}	2,966.99 (N.A.) {6,753.42}	5,369.57	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	491	FOUR LANNING OF NERCHOWK- PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH (NHAI) (N24000613)	9-2016	7/2020 (N.A.) {3/2025}	1,273.71 (N.A.) {1,478.61}	1,439.49	96.02

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		492	FOUR LANING OF SOLAN- KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M (NHAI) (N24000852)	3-2018	5/2021 (N.A.) {12/2024}	478.74 (N.A.) {1,514.46}	1,349.59	83.00
		493	REHABILITATION AND UPGRADATION TO 2-LANE/2- LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA (MoRTH) (N24001381)	8-2020	4/2021 (N.A.) {4/2021}	272.98 (N.A.) {272.98}	140.69	100.00
		494	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA- ASHYARI SECTION (KM 25.000 TO KM 50. (MoRTH) (N24001382)	8-2020	3/2021 (N.A.) {7/2024}	242.80 (N.A.) {242.80}	96.76	87.39
		495	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI- GUMMA SECTION (KM 75 (MoRTH) (N24001383)	8-2020	4/2021 (N.A.) {4/2021}	349.20 (N.A.) {349.20}	239.34	100.00
		496	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI- SHRI KYARI SECTION (KM 50.000 TO K (MoRTH) (N24001422)	2-2021	9/2021 (N.A.) {7/2024}	345.89 (N.A.) {345.89}	152.01	84.08
		497	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR- KARNOHAL SECTION (KM 141.000 TO K (MoRTH) (N24001447)	8-2020	12/2024 (N.A.) {12/2024}	371.93 (N.A.) {371.93}	198.30	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		498	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN- MANDI SECTION (KM 208.950 TO KM 2 (MoRTH) (N24001470)	8-2020	4/2025 (N.A.) {4/2025}	314.32 (N.A.) {314.32}	89.24	-
		499	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF (NHAI) (N24001808)	3-2021	12/2024 (N.A.) {12/2024}	1,322.95 (1,442.47) {1,442.47}	886.72	93.80
		500	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU (NHAI) (N24001809)	5-2022	3/2024 (N.A.) {12/2024}	469.95 (N.A.) {280.00}	299.33	95.75
		501	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP (NHAI) (N24001810)	2-2022	6/2024 (N.A.) {6/2024}	190.60 (N.A.) {163.00}	103.48	100.00
		502	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH-154) (PACKAGE-IB) (NHAI) (N24001811)	4-2021	6/2024 (N.A.) {3/2025}	583.93 (770.00) {770.00}	171.44	98.21
		503	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) (NHAI) (N24001812)	3-2021	5/2024 (N.A.) {12/2025}	1,002.11 (1,361.79) {1,361.76}	189.81	44.43
		504	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A (NHAI) (N24001813)	7-2021	9/2024 (N.A.) {9/2024}	1,692.05 (N.A.) {1,692.05}	942.14	21.60

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		505	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS-5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001915)	3-2021	6/2026 (N.A.) {6/2026}	230.54 (N.A.) {230.54}	20.16	20.16
		506	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS 5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001916)	3-2021	5/2026 (N.A.) {5/2026}	314.67 (N.A.) {314.67}	76.05	44.00
		507	PKG NAME: 4L OF KATHLIGHAT TO SHAKRAL VILLAGE FROM KM 128.835 TO KM 146.300 OF NH- 5 (SHIMLA BYPASS (NHAI) (N24002049)	3-2022	4/2026 (N.A.) {4/2026}	1,703.48 (2,278.00) {2,278.00}	651.98	14.50
		508	REHABILITATION AND UPGRADATION TO 4L CONFIGURATION and STRENGTHENING OF SIHUNI TO RAJOL FROM KM 51.0 (NHAI) (N24002050)	2-2022	9/2025 (N.A.) {9/2025}	696.65 (698.46) {698.46}	346.91	50.10
		509	CONSTRUCTION OF NEW 2 LANE WITH PAVED SHOULDER OF HAMIRPUR BYPASS (PACKAGE IVA) OF NH-88 (NEW NH-103 (NHAI) (N24002051)	7-2022	10/2025 (N.A.) {10/2025}	739.39 (N.A.) {739.39}	307.64	68.50
		510	REHABILITATION AND UP- GRADATION OF EXISTING ROAD TO 2L PS FROM END OF HAMIRPUR BYPASS (NEAR CHILBAHA (NHAI) (N24002052)	2-2022	4/2025 (N.A.) {4/2025}	1,146.19 (N.A.) {1,146.19}	917.42	60.67
		511	REHABILITATION AND UP- GRADATION TO 4L CONFIGURATION AND STRENGTHENING OF THANPURI TO PAROR SECTION F (NHAI) (N24002192)	6-2022	12/2025 (N.A.) {12/2025}	815.69 (815.69) {815.69}	357.11	21.18

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>URBAN DEVELOPMENT</u>	512	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D (CPWD) (N28000154)	4-2022	11/2024 (N.A.) {11/2024}	512.34 (N.A.) {512.34}	0.00	-
<u>JAMMU AND KASHMIR</u>	<u>CIVIL AVIATION</u>	513	JAMMU - CONSTRUCTION OF NEW CIVIL ENCLAVE (AAI) (N04000107)	7-2022	6/2026 (N.A.) {6/2026}	861.37 (N.A.) {861.37}	117.47	24.00
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	514	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) (CPWD EDUCATION) (N28000130)	3-2019	7/2022 (N.A.) {1/2025}	424.93 (N.A.) {500.91}	473.74	96.00
		515	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) (CPWD EDUCATION) (N28000131)	1-2018	4/2023 (N.A.) {2/2025}	676.00 (1,148.68) {1,144.68}	64.75	100.00
	<u>HEALTH AND FAMILY WELFARE</u>	516	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR (CPWD FOR HEALTH) (N21000029)	3-2019	9/2023 (N.A.) {3/2025}	1,404.00 (1,642.00) {1,642.00}	1,460.23	99.80
		517	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR (CPWD FOR HEALTH) (N28000150)	3-2019	9/2025 (N.A.) {11/2025}	1,828.00 (1,577.00) {1,577.00}	1,212.79	62.50
	<u>PETROLEUM</u>	518	SETTING UP A COMMON USER PETROLEUM TERMINAL AT JAMMU FOR RE-SITEMENT OF EXISTING DEPOTS OF PSU OMCS (BPCL) (N16000500)	4-2021	3/2025 (N.A.) {3/2025}	676.89 (N.A.) {676.89}	439.05	67.00
		519	CGD PROJECT AT JAMMU DISTRICTS (IOCL) (N16000527)	3-2022	3/2032 (N.A.) {9/2034}	538.00 (N.A.) {538.00}	3.10	0.40
	<u>POWER</u>	520	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) (CVPPPL) (N18000172)	10-2014	4/2020 (N.A.) {9/2026}	8,112.12 (N.A.) {12,727.76}	5,874.31	65.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		521	KIRU HYDRO ELECTRIC PROJECT (CVPPPL) (N18000278)	3-2019	8/2024 (N.A.) {9/2026}	4,287.59 (N.A.) {5,409.00}	2,286.32	54.10
		522	RATLE HE PROJECT (NHPC) (N18000324)	2-2021	2/2026 (N.A.) {11/2028}	5,281.94 (N.A.) {5,281.94}	884.76	20.01
		523	KWAR HE PROJECT (CVPPPL) (N18000363)	5-2022	11/2026 (N.A.) {12/2027}	4,526.12 (N.A.) {4,526.12}	890.30	19.00
	<u>RAILWAYS</u>	524	UDHAMPUR-SRINAGAR- BARAMULLA (NL),NR (NR) (220100133)	3-1995	11/2002 (N.A.) {12/2024}	2,500.00 (37,012.26) {42,930.00}	42,197.72	100.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	525	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A (NHAI) (N24000488)	12-2015	12/2018 (N.A.) {3/2025}	2,136.97 (2,644.00) {2,644.00}	2,386.12	99.50
		526	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE (NHAI) (N24000717)	12-2017	7/2021 (N.A.) {3/2025}	1,471.75 (1,471.75) {1,903.98}	1,662.19	98.38
		527	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA (NHIDCL) (N24000868)	3-2018	7/2021 (N.A.) {6/2025}	253.44 (N.A.) {253.44}	185.10	80.49
		528	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z- MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D (NHIDCL) (N24001256)	8-2020	9/2026 (N.A.) {9/2026}	6,808.69 (N.A.) {6,808.69}	3,013.84	49.92
		529	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL (NHIDCL) (N24001264)	7-2020	4/2022 (N.A.) {10/2025}	228.39 (N.A.) {228.39}	67.60	87.23

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		530	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K (NHIDCL) (N24001266)	7-2020	4/2022 (N.A.) {6/2025}	210.79 (N.A.) {210.79}	69.67	89.74
		531	KHELLANI-KHANABAL PKG-1 (NHIDCL) (N24001323)	3-2021	9/2022 (N.A.) {3/2025}	486.45 (N.A.) {486.45}	126.73	96.58
		532	KHELLANI-KHANABAL PKG-3 (NHIDCL) (N24001341)	3-2021	12/2022 (N.A.) {3/2025}	398.51 (N.A.) {398.51}	76.47	94.99
		533	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 (NHIDCL) (N24001342)	3-2021	12/2022 (N.A.) {7/2024}	260.40 (N.A.) {260.40}	191.88	93.80
		534	KHELLANI-KHANABAL PKG-2 (NHIDCL) (N24001394)	7-2021	2/2023 (N.A.) {3/2026}	512.43 (N.A.) {512.43}	71.65	50.58
		535	KHELLANI-KHANABAL PKG-4 (NHIDCL) (N24001395)	7-2021	8/2023 (N.A.) {6/2026}	859.67 (N.A.) {859.67}	187.65	43.22
		536	KHELLANI-KHANABAL PKG-5 (NHIDCL) (N24001396)	7-2021	2/2023 (N.A.) {6/2025}	497.09 (N.A.) {497.09}	162.09	80.53
		537	GOHA-KHELLANI PKG-3 (NHIDCL) (N24001397)	2-2021	3/2023 (N.A.) {3/2025}	431.28 (N.A.) {431.28}	351.88	99.45
		538	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA (NHAI) (N24001472)	9-2021	12/2023 (N.A.) {6/2024}	811.19 (N.A.) {811.19}	824.40	99.00
		539	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY (NHAI) (N24001511)	3-2021	2/2024 (N.A.) {10/2025}	2,919.96 (N.A.) {2,919.96}	2,268.89	65.80
		540	FOUR LANING OF JAMMU- AKHNOOR PKG-1 (NHIDCL) (N24001543)	7-2022	1/2025 (N.A.) {4/2025}	245.34 (N.A.) {245.34}	56.99	38.17

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		541	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG- XVI) EXISTING JAKH (VIJAYPUR)- KUNJWANI SECTION OF NH-4 (NHAI) (N24001550)	9-2021	9/2024 (N.A.) {9/2025}	1,821.72 (1,917.32) {1,917.32}	909.88	76.80
		542	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG- XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5 (NHAI) (N24001551)	10-2021	9/2024 (N.A.) {7/2025}	3,044.02 (3,044.02) {3,044.02}	1,482.85	61.52
		543	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B (NHAI) (N24001552)	10-2021	9/2024 (N.A.) {9/2025}	2,714.95 (2,714.95) {2,714.95}	1,626.16	75.45
		544	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- (NHAI) (N24001619)	8-2022	6/2024 (N.A.) {6/2025}	200.05 (200.05) {208.92}	125.20	47.53
		545	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SLIP ZONES AT KM 130.550 TO KM.130.750; KM. (NHAI) (N24001620)	9-2021	10/2023 (N.A.) {12/2025}	442.14 (N.A.) {442.14}	306.30	19.88
		546	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. (NHAI) (N24001621)	7-2021	8/2024 (N.A.) {6/2025}	614.48 (N.A.) {614.48}	182.16	7.00
		547	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX (NHAI) (N24001622)	7-2021	6/2024 (N.A.) {6/2025}	1,401.87 (N.A.) {1,401.87}	667.25	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		548	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350 (NHAI) (N24001623)	1-2020	1/2024 (N.A.) {3/2025}	336.01 (N.A.) {336.01}	222.09	34.00
		549	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI (NHAI) (N24001624)	7-2019	10/2020 (N.A.) {9/2024}	157.05 (N.A.) {157.05}	139.54	100.00
		550	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K (NHAI) (N24001627)	7-2021	2/2025 (N.A.) {5/2026}	1,912.17 (N.A.) {1,912.17}	88.96	-
		551	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B (NHIDCL) (N24001833)	7-2022	3/2025 (N.A.) {8/2025}	198.28 (N.A.) {198.28}	77.06	64.28
		552	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 102 TO KM 13 (BRO) (N24001897)	3-2021	7/2024 (N.A.) {3/2024}	642.24 (N.A.) {642.24}	498.80	95.00
		553	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 30.000 TO K (BRO) (N24001898)	7-2020	11/2024 (N.A.) {11/2024}	272.49 (N.A.) {272.49}	180.48	87.24
		554	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 134.95 TO KM (BRO) (N24001899)	2-2021	7/2024 (N.A.) {3/2025}	395.25 (N.A.) {395.25}	211.75	64.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		555	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 49.150 TO KM (<i>BRO</i>) (<i>N24001900</i>)	3-2020	8/2024 (N.A.) {3/2025}	796.97 (N.A.) {796.97}	468.35	79.00
		556	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 64.535 TO K (<i>BRO</i>) (<i>N24001901</i>)	3-2020	9/2023 (N.A.) {3/2025}	152.93 (N.A.) {152.93}	103.81	78.27
		557	CONSTRUCTION OF TWIN TUBE TUNNELS ON JAMMU KASHMIR RING ROAD (NH-244A) BETWEEN DESIGN CH. 50+600 TO (<i>NHAI</i>) (<i>N24001926</i>)	3-2023	6/2025 (N.A.) {6/2025}	939.86 (N.A.) {939.86}	353.55	55.30
		558	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER FROM (DESIGN CH. 14+200 TO 24+400), (DESIGN CH. 35+300 TO (<i>BRO</i>) (<i>N24001998</i>)	6-2022	8/2025 (N.A.) {8/2025}	832.46 (N.A.) {823.46}	362.09	46.00
		559	2L NH-1 FROM KM 8.660 TO KM 33.775 (SUMBAL TO WAYUL) TO 4L DUAL CARRIAGEWAY NH STANDARD AS PART OF S (<i>NHAI</i>) (<i>N24002059</i>)	9-2022	6/2026 (N.A.) {12/2026}	1,183.60 (N.A.) {1,183.60}	166.86	9.87
		560	DELHI AMRITSAR KATRA EXPRESSWAY (PHASE-II PKG XVIII) DEVELOPMENT AND UPGRADATION OF FOUR LANE ACCESS (<i>NHAI</i>) (<i>N24002060</i>)	3-2023	11/2025 (N.A.) {11/2025}	1,107.00 (N.A.) {975.38}	205.52	30.23
		561	4/6L ACCESS CONTROL EXPRESSWAY FROM DESIGN CHAINAGE KM 515.000 TO 528.300 (KUNJWANI TO SIDHRA SECTIO (<i>NHAI</i>) (<i>N24002061</i>)	8-2022	6/2025 (N.A.) {8/2025}	2,474.47 (N.A.) {2,894.74}	811.55	31.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		562	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM 162.800 TO KM (BRO) (N24002119)	10-2022	1/2026 (N.A.) {1/2026}	562.45 (N.A.) {562.45}	99.06	25.00
		563	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER (PATTAN BYPASS) GREENFIELD BYPASS FROM EXISTING CH. KM 24 (BRO) (N24002179)	3-2023	7/2026 (N.A.) {7/2026}	980.21 (N.A.) {980.21}	300.02	8.00
		564	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 166.100 TO KM (BRO) (N24002180)	9-2021	7/2026 (N.A.) {7/2026}	734.64 (N.A.) {734.64}	19.60	8.00
		565	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDERS (BARAMULLA BYPASS) GREENFIELD BYPASS FROM EXISTING CH. K (BRO) (N24002185)	3-2023	9/2026 (N.A.) {9/2026}	992.43 (N.A.) {992.43}	338.33	-
		566	WIDENING AND STRENGTHENING OF RAFIABAD- KUPWARA-CHOWKIBAL- TANGDHAR-CHAMKOT (NH-701) ROAD FROM DESIGN (BRO) (N24002210)	3-2024	5/2027 (N.A.) {5/2027}	1,404.94 (N.A.) {1,404.94}	0.00	-
JHARKHAND	COAL	567	RAJRAPPA RCE OCP (3.0 MTY) (CCL) (N06000087)	12-2009	3/2016 (N.A.) {3/2027}	510.85 (N.A.) {510.85}	488.57	74.50
		568	MURAI DIH UG TURN-KEY PROJECT (BCCL) (N06000096)	2-2011	4/2014 (N.A.) {1/2026}	339.88 (N.A.) {339.88}	190.48	70.00
		569	MOONIDIH XV SEAM UG (BCCL) (N06000098)	8-2011	3/2019 (N.A.) {2/2026}	1,230.27 (N.A.) {1,230.27}	598.83	80.20
		570	CHITRA EAST (RCE) OCP (ECL) (N06000169)	8-2018	3/2026 (N.A.) {3/2026}	513.98 (N.A.) {513.98}	223.63	51.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		571	TETARIAKHAR EXPANSION OCP (CCL) (N06000186)	11-2019	3/2023 (N.A.) {3/2025}	243.52 (N.A.) {243.52}	44.39	46.60
		572	PACHWARA SOUTH COAL BLOCK (NLC) (N06000193)	7-2013	9/2028 (N.A.) {9/2028}	2,242.92 (2,242.90) {2,242.90}	517.94	44.00
		573	PATHERDIH 2.5 NLW COAL WASHERY (BCCL) (N06000194)	10-2015	4/2018 (N.A.) {3/2026}	334.27 (N.A.) {334.27}	129.81	44.00
		574	REVISED PROJECT REPORT MAGADH EXPANSION OCP (CCL) (N06000216)	8-2020	3/2028 (N.A.) {3/2028}	7,254.37 (N.A.) {7,254.37}	1,418.97	22.00
		575	EXPANSION PROJECT AMRAPALI OCP (CCL) (N06000217)	8-2020	3/2028 (N.A.) {3/2028}	5,136.15 (N.A.) {5,136.15}	998.82	30.00
		576	UCE OF EPR OF NORTH URIMARI OCP (CCL) (N06000218)	7-2021	3/2026 (N.A.) {3/2026}	778.80 (N.A.) {778.80}	693.94	75.00
		577	KOTRE BASANTPUR PACHMO OCP (CCL) (N06000237)	8-2020	3/2032 (N.A.) {3/2032}	625.40 (625.40) {625.40}	441.00	60.00
		578	CHANDRAGUPT OCP (CCL) (N06000238)	8-2020	3/2032 (N.A.) {3/2032}	973.50 (N.A.) {973.50}	339.32	12.40
		579	SIRKA OCP (CCL) (N06000239)	5-2020	3/2025 (N.A.) {3/2025}	222.82 (N.A.) {222.82}	139.31	60.00
		580	JHARKHAND LAIYO OCP (CCL) (N06000240)	8-2020	3/2031 (N.A.) {3/2031}	764.57 (N.A.) {764.57}	145.80	21.00
		581	EPR TAPIN SOUTH OCP (CCL) (N06000241)	11-2020	3/2025 (N.A.) {3/2025}	230.41 (N.A.) {230.41}	20.29	18.30
		582	EPR PUNDI OCP (CCL) (N06000242)	11-2020	3/2027 (N.A.) {3/2027}	713.35 (N.A.) {713.35}	236.57	21.00
		583	EPR ROHINI KARKATA OCP (CCL) (N06000243)	1-2021	3/2028 (N.A.) {3/2028}	1,020.42 (N.A.) {1,020.42}	82.92	11.70
		584	EXPANSION OF KONAR OCP (CCL) (N06000245)	1-2022	3/2032 (N.A.) {3/2032}	799.34 (N.A.) {799.34}	402.47	32.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		585	EXPANSION OF KARO OCP (CCL) (N06000246)	1-2022	3/2026 (N.A.) {3/2026}	908.47 (N.A.) {908.47}	180.72	20.00
		586	EXPANSION OF ASHOK OCP (CCL) (N06000247)	5-2021	3/2028 (N.A.) {3/2028}	2,898.28 (N.A.) {2,898.28}	175.10	20.00
		587	AMALGAMATED NTST KUJAMA OCP 8.5 MTY (BCCL) (N06000273)	1-2023	3/2030 (N.A.) {3/2030}	4,011.85 (N.A.) {4,011.85}	397.65	24.69
		588	HURA C OC (ECL) (N06000275)	8-2022	3/2029 (N.A.) {3/2029}	859.41 (N.A.) {859.41}	438.86	62.00
		589	CHUPERBHITA- SIMLONG OCP (ECL) (N06000280)	12-2023	3/2037 (N.A.) {3/2037}	979.08 (N.A.) {979.08}	0.00	-
		590	BLOCK-E OCP (15 MTY) (BCCL) (N06000287)	3-2024	3/2029 (N.A.) {3/2029}	5,850.83 (N.A.) {5,850.83}	5.36	1.63
	DEPARTMENT OF HIGHER EDUCATION	591	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD (CPWD EDUCATION) (N28000067)	9-2012	3/2016 (N.A.) {3/2016}	171.86 (N.A.) {171.86}	176.08	-
	PETROLEUM	592	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK (ONGC) (N16000239)	12-2015	3/2023 (N.A.) {3/2025}	823.27 (1,137.79) {1,137.79}	1,060.31	83.30
		593	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) (ONGC) (N16000445)	11-2019	1/2024 (N.A.) {3/2025}	431.00 (N.A.) {431.00}	173.22	56.90
		594	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI (IOCL) (N16000480)	3-2023	2/2026 (N.A.) {2/2026}	202.07 (N.A.) {202.07}	47.15	38.68
		595	CGD PROJECT IN BIHAR JHARKHAND (HPCL) (N16000497)	6-2022	6/2030 (N.A.) {6/2030}	1,377.00 (N.A.) {1,377.00}	210.24	20.90
	POWER	596	NORTH KARANPURA STPP (3X660 MW) (NTPC) (N18000177)	2-2014	6/2019 (N.A.) {3/2025}	16,242.90 (N.A.) {16,242.90}	16,605.62	97.00
		597	PATRATU STPP-I (3X800MW) (NTPC) (N18000275)	11-2017	3/2023 (N.A.) {3/2026}	17,112.00 (N.A.) {17,112.00}	15,460.45	79.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		598	BADAM COAL MINING PROJECT (NTPC) (N18000367)	2-2019	10/2024 (N.A.) {6/2025}	501.79 (784.00) {501.79}	281.98	59.79
		599	KERANDARI COAL MINING PROJECT (NTPC) (N18000370)	9-2015	11/2019 (N.A.) {1/2024}	1,553.00 (2,896.64) {2,896.64}	1,976.11	56.00
	<u>RAILWAYS</u>	600	KODERMA-TILAIYA (NL), ECR (ECR) (220100305)	4-2002	(N.A.) {3/2025}	459.91 (1,625.87) {1,700.00}	1,891.00	70.00
		601	BONDAMUNDA RANCHI DOUBLING (SER) (N22000396)	3-2016	3/2021 (N.A.) {6/2026}	1,724.20 (3,029.04) {3,029.04}	2,301.33	82.00
		602	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) (SER) (N22000508)	4-2018	6/2022 (N.A.) {6/2026}	428.65 (N.A.) {472.50}	275.47	2.00
		603	DOUBLING OF PRADHANKHUNTA JN -PATHERDIH BAZAR- BHOJUDIH (ECR) (N22000529)	11-2022	11/2027 (N.A.) {11/2027}	202.00 (349.22) {349.22}	42.89	-
		604	KHARAGPUR-ADITYAPUR - 3RD LINE (132 KM) (RVNL) (N22000595)	12-2015	3/2025 (N.A.) {3/2025}	1,116.00 (N.A.) {3,270.07}	2,899.45	-
		605	3RD LINE BETWEEN DHANBAD SONNAGAR (RVNL) (N22000599)	11-2016	3/2026 (N.A.) {3/2026}	8,975.00 (N.A.) {7,906.38}	4,705.38	-
		606	GARHWA ROAD - RAIL OVER RAIL (ECR) (N22000610)	3-2017	3/2024 (N.A.) {3/2025}	262.71 (N.A.) {262.71}	202.02	73.00
		607	GOMOH - FLYOVER FOR DOWN TRAINS (ECR) (N22000611)	1-2018	12/2025 (N.A.) {12/2025}	487.73 (N.A.) {487.73}	353.78	16.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	608	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION (NHAI) (N24000726)	1-2018	11/2021 (N.A.) {6/2025}	1,155.16 (N.A.) {950.49}	644.97	70.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		609	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I (MoRTH) (N24001216)	12-2016	9/2021 (N.A.) {12/2024}	196.00 (N.A.) {196.00}	164.21	90.00
		610	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 (NHAI) (N24001589)	9-2020	3/2024 (N.A.) {4/2025}	755.26 (N.A.) {1,039.00}	613.83	84.00
		611	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS] (NHAI) (N24001590)	9-2020	10/2023 (N.A.) {1/2025}	748.99 (N.A.) {903.00}	825.10	100.00
		612	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM (NHAI) (N24001594)	2-2022	1/2025 (N.A.) {3/2025}	534.73 (N.A.) {534.73}	125.31	88.00
		613	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH (NHAI) (N24001595)	8-2020	3/2024 (N.A.) {6/2025}	1,034.00 (1,879.55) {1,879.55}	41.50	94.26
		614	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF (NHAI) (N24001596)	11-2021	7/2023 (N.A.) {6/2025}	1,302.72 (1,504.80) {1,504.80}	842.02	74.51
		615	FOUR LANING WITH PAVED SHOULDER OF SECTION FROM KM 53.600 (GOLA ON NH-320) TO KM 81.446 (ORMANJHI ON (NHAI) (N24001854)	6-2023	6/2025 (N.A.) {6/2025}	1,214.93 (1,324.95) {1,324.95}	702.00	65.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		616	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM 0.00 TO 44.00 (KURU-GHAGHRA SECTION) OF NH-143A INCLU (MoRTH) (N24001922)	2-2020	8/2023 (N.A.) {12/2024}	153.01 (N.A.) {153.01}	83.63	96.00
		617	WIDENING AND STRENGTHENING OF EXISTING PAVEEMNT TO TWO LANE WITH PAVED SHOULDERS FROM KM 116.00 TO K (MoRTH) (N24001923)	1-2022	7/2024 (N.A.) {12/2024}	315.21 (N.A.) {315.21}	105.63	80.00
		618	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDER/TWO LANE+ PAVED SHOULDER WITH SERVICE ROA (MoRTH) (N24001924)	3-2022	8/2025 (N.A.) {8/2025}	514.22 (N.A.) {514.22}	10.49	6.00
		619	WIDENING AND STRENGTHENING/RECONSTRUC TION TO TWO LANE WITH PAVED SHOULDER/ TWO LANE WITH PAVED SHOUL (MoRTH) (N24001925)	3-2022	8/2025 (N.A.) {8/2025}	423.18 (N.A.) {423.18}	0.11	-
		620	FOUR LANING OF KHAJURI TO WYNDHAMGANJ FROM KM 219.600 TO KM 260.483 ON NH-75 PKG SEC-V ON HAM (NHAI) (N24002053)	4-2022	9/2025 (N.A.) {9/2025}	1,232.00 (1,343.00) {1,400.00}	606.60	64.00
		621	FOUR LANING OF BHOGU TO SANKHA FROM KM 147.450 TO KM 196.870 ON NH-75 PKG SEC-III (NHAI) (N24002054)	10-2022	11/2025 (N.A.) {11/2025}	1,390.77 (1,391.00) {1,600.00}	296.46	60.51

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		622	FOUR LANING OF BASUKINATH- DEOGHAR SECTION OF NH-114A FROM KM 85.081 TO KM 130.240 UNDER NHDP PHASE-I (NHAI) (N24002055)	3-2023	12/2025 (N.A.) {12/2025}	1,444.94 (N.A.) {1,444.94}	0.00	-
		623	BHARATMALA PARIYOJANA OF BOKARO JAINA MORE - GOLA SECTION OF NH-320 FROM KM. 21.110 TO KM. 53.600 IN (NHAI) (N24002056)	6-2020	6/2025 (N.A.) {6/2025}	964.64 (N.A.) {964.64}	373.92	43.39
		624	FOUR LANING OF MEHGAMA HANSDIHA SECTION OF NH-33 FROM EXISTING KM 41.900 TO 93.000 IN THE STATE OF J (NHAI) (N24002057)	12-2022	5/2025 (N.A.) {5/2025}	1,443.77 (N.A.) {1,443.77}	0.00	-
		625	NEW SINTER PLANT AT BOKARO STEEL PLANT (SAIL) (N12000095)	3-2015	10/2017 (N.A.) {11/2026}	1,034.01 (1,752.30) {1,752.30}	873.69	51.75
	STEEL	626	REVAMPING OF OLD SUB SYSTEM OF BLAST FURNACE 3 AT BOKARO STEEL PLANT (SAIL) (N12000129)	9-2023	7/2025 (N.A.) {7/2025}	513.82 (N.A.) {513.82}	117.18	58.00
		627	REBUILDING OF COKE OVEN BATTERY NO.6 OF BOKARO STEEL PLANT (SAIL) (N12000133)	11-2023	11/2026 (N.A.) {11/2026}	627.31 (N.A.) {627.31}	70.50	32.00
		628	REPLACEMENT OF REMAINING 04 NOS. OF BATTERY CYCLONES WITH 04 NOS. OF ESPS IN SINTER PLANT-1 AT BSL (SAIL) (N12000135)	3-2024	6/2026 (N.A.) {6/2026}	260.37 (N.A.) {260.37}	0.00	5.50
		629	BELAGAVI AIRPORT- EXPANSION OF TERMINAL BUILDING AND ASSOCIATED WORKS (AAI) (N04000105)	6-2023	2/2026 (N.A.) {2/2026}	322.45 (N.A.) {322.45}	72.95	31.00
KARNATAKA	CIVIL AVIATION							

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		630	HUBBALI AIRPORT - CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS (AAI) (N04000108)	6-2023	2/2026 (N.A.) {1/2026}	320.47 (N.A.) {320.47}	40.28	23.50
	DEPARTMENT OF HIGHER EDUCATION	631	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) (CPWD EDUCATION) (N42000006)	7-2019	3/2022 (N.A.) {3/2023}	851.00 (851.00) {851.00}	888.66	-
		632	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL (CPWD) (N42000010)	8-2021	2/2024 (N.A.) {11/2024}	316.25 (N.A.) {316.25}	333.42	94.00
	PETROLEUM	633	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE (HPCL) (N16000369)	12-2018	12/2022 (N.A.) {3/2025}	854.00 (854.00) {854.00}	658.05	93.70
		634	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE (IOCL) (N16000437)	1-2022	7/2025 (N.A.) {12/2025}	463.00 (500.62) {500.62}	211.04	66.00
		635	POWER SYSTEM UPGRADATION PROJECT (MANGALORE REFIN) (N16000509)	10-2023	2/2026 (N.A.) {2/2026}	385.00 (N.A.) {385.00}	76.31	40.46
		636	DEMO PLANT FOR PRODUCTION OF BIO-ATF (MANGALORE REFIN) (N16000536)	3-2024	3/2027 (N.A.) {3/2027}	364.00 (N.A.) {364.00}	8.66	2.20
	POWER	637	TS FOR INTRGRATION OF RE ZONE (PHASE II) IN KOPPAL II (PHASE A and B) AND GADAG II (PHASE A) IN KARN (PGCIL) (N18000385)	12-2023	12/2025 (N.A.) {12/2025}	2,889.00 (N.A.) {2,889.00}	319.00	17.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		638	TS FOR SOLAR ENERGY ZONE IN BIDAR (2500MW), KARNATAKA [BIDAR TRANSMISSION LTD] (PGCIL) (N18000388)	2-2024	2/2026 (N.A.) {2/2026}	2,148.00 (N.A.) {2,148.00}	354.00	30.00
	RAILWAYS	639	TUMKUR-CHITRADURGA- DAVENGERE NL (SWR) (N22000256)	4-2011	(N.A.) {12/2027}	1,801.01 (N.A.) {1,801.01}	488.95	12.00
		640	BAGALKOT-KUDACHI NL (SWR) (N22000258)	4-2010	3/2016 (N.A.) {3/2027}	986.30 (1,378.00) {1,378.00}	601.71	34.00
		641	HOSPET-HUBLI-LONDA- VASCODAGAMA DL (RVNL) (N22000297)	4-2010	3/2023 (N.A.) {12/2026}	2,127.00 (N.A.) {3,692.60}	3,505.49	-
		642	GADAG-WADI NL (SWR) (N22000299)	4-2013	12/2018 (N.A.) {12/2027}	2,841.84 (N.A.) {2,841.84}	1,244.33	28.00
		643	MARIKUPPAM - KUPPAM (SWR) (N22000308)	4-2012	3/2016 (N.A.) {12/2027}	279.54 (296.72) {296.72}	113.20	14.00
		644	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) (SWR) (N22000486)	3-1996	3/2017 (N.A.) {3/2026}	644.78 (825.31) {825.31}	647.90	66.00
		645	BAIYYAPPANAHALLI-HOSUR (48 KM) (NCRTC) (N22000542)	4-2019	3/2026 (N.A.) {3/2026}	375.67 (N.A.) {375.67}	0.00	-
		646	YESHVANTHPUR- CHANNASANDRA (21.7 KM) (NCRTC) (N22000543)	4-2019	3/2026 (N.A.) {3/2026}	169.65 (N.A.) {169.65}	71.75	-
		647	BELGAUM-DHARWAD VIA KITTUR (73.10 KM) (UMBRELLA WORK PB#22/2019-20/NR) (SWR) (N22000557)	9-2020	3/2026 (N.A.) {12/2027}	1,590.80 (927.42) {927.42}	0.69	-
		648	HASSAN (ALUR) - BELUR (32 KM) (UMBRELLA WORK PB#23/2018- 19/NR) (SWR) (N22000558)	6-2019	4/2028 (N.A.) {3/2028}	663.03 (748.85) {748.85}	0.82	1.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		649	SHIMOGA-SHIKARIPURA- RANEBENNUR (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000559)	9-2019	12/2027 (N.A.) {12/2027}	1,453.73 (994.47) {994.47}	67.41	7.00
		650	BANGALORE-WHITEFIELD- BANGALORE CITY- KRISHNARAJAPURAM QUADRUPLING (SWR) (N22000621)	3-2018	3/2025 (N.A.) {6/2025}	492.87 (N.A.) {492.87}	210.66	46.00
	ROAD TRANSPORT AND HIGHWAYS	651	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP (MoRTH) (N24000334)	3-2015	11/2015 (N.A.) {8/2024}	165.67 (N.A.) {165.67}	126.47	99.00
		652	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION (NHAI) (N24000462)	5-2014	8/2016 (N.A.) {3/2025}	1,655.01 (1,990.38) {1,990.38}	1,812.71	97.80
		653	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY (NHAI) (N24000552)	3-2016	3/2019 (N.A.) {6/2025}	701.40 (591.86) {701.40}	526.82	85.00
		654	HOSPET-BELLARY-KARNATAKA AP BORDER (NHAI) (N24000603)	8-2016	3/2019 (N.A.) {5/2025}	1,167.42 (N.A.) {1,224.01}	915.13	86.51
		655	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH- 150A HOSMANE CROSS ? PA (MoRTH) (N24001156)	1-2017	9/2017 (N.A.) {5/2023}	166.67 (N.A.) {264.34}	192.08	100.00
		656	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH (MoRTH) (N24001157)	8-2016	2/2017 (N.A.) {7/2024}	175.50 (N.A.) {241.60}	189.72	90.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		657	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 (MoRTH) (N24001158)	3-2018	6/2019 (N.A.) {12/2023}	159.97 (N.A.) {242.61}	113.15	100.00
		658	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION (MoRTH) (N24001159)	1-2018	7/2018 (N.A.) {3/2022}	159.70 (N.A.) {159.70}	142.88	100.00
		659	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH- 234 BANAVARA-HULIYAR (MoRTH) (N24001160)	9-2017	10/2018 (N.A.) {4/2022}	191.60 (N.A.) {191.60}	112.03	100.00
		660	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- (MoRTH) (N24001161)	12-2017	1/2019 (N.A.) {4/2022}	297.30 (N.A.) {318.28}	280.25	100.00
		661	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN (MoRTH) (N24001162)	3-2018	10/2018 (N.A.) {11/2022}	325.86 (N.A.) {386.41}	356.78	100.00
		662	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN (MoRTH) (N24001164)	10-2016	3/2017 (N.A.) {7/2022}	396.96 (N.A.) {396.96}	329.58	100.00
		663	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT (MoRTH) (N24001165)	11-2016	3/2017 (N.A.) {10/2021}	314.90 (N.A.) {314.90}	233.95	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		664	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH- 218 (218-KNT-2014-15-775) (MoRTH) (N24001166)	3-2015	1/2016 (N.A.) {7/2024}	159.12 (N.A.) {159.12}	127.72	98.00
		665	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT (MoRTH) (N24001168)	5-2018	5/2018 (N.A.) {12/2023}	171.60 (N.A.) {171.60}	134.81	100.00
		666	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U (MoRTH) (N24001172)	1-2017	8/2017 (N.A.) {6/2022}	291.49 (N.A.) {291.49}	238.77	100.00
		667	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI ? JADERCELA SECTION (MoRTH) (N24001173)	2-2017	5/2019 (N.A.) {10/2025}	157.32 (188.00) {187.61}	62.31	60.00
		668	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT (MoRTH) (N24001387)	1-2017	9/2017 (N.A.) {5/2023}	264.34 (N.A.) {264.34}	201.07	100.00
		669	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA (MoRTH) (N24001388)	3-2019	12/2019 (N.A.) {11/2024}	423.15 (N.A.) {423.15}	284.58	82.00
		670	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN (NHAI) (N24001425)	3-2021	11/2021 (N.A.) {8/2025}	1,100.88 (1,687.31) {1,687.31}	1,067.55	76.78

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		671	4L OF ADDAHOLE TO BANTWAL CROSS SECTION (NHAI) (N24001426)	3-2021	10/2021 (N.A.) {3/2025}	317.90 (572.01) {572.01}	360.36	96.86
		672	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) (NHAI) (N24001598)	1-2022	4/2025 (N.A.) {4/2025}	1,388.70 (1,388.70) {1,388.70}	438.61	58.50
		673	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. (NHAI) (N24001599)	3-2018	12/2022 (N.A.) {12/2025}	440.16 (N.A.) {440.16}	329.40	66.09
		674	BANGALORE/TN BORDER TO HOSKOTE (NHAI) (N24001674)	2-2023	2/2025 (N.A.) {2/2025}	1,240.60 (N.A.) {1,240.60}	784.19	77.13
		675	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 (NHAI) (N24001675)	11-2022	5/2025 (N.A.) {5/2025}	1,732.73 (N.A.) {1,732.73}	540.35	97.90
		676	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 (NHAI) (N24001676)	12-2022	6/2025 (N.A.) {6/2025}	2,718.46 (N.A.) {2,718.46}	375.90	45.15
		677	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 (NHAI) (N24001677)	11-2022	5/2024 (N.A.) {5/2024}	226.76 (226.76) {226.76}	80.26	65.87
		678	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 (NHAI) (N24001679)	10-2022	4/2025 (N.A.) {4/2025}	1,479.30 (1,479.30) {1,479.30}	550.20	73.25

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		679	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE (NHAI) (N24001680)	3-2021	10/2024 (N.A.) {12/2025}	1,409.68 (1,808.12) {1,808.12}	953.81	55.35
		680	TUMKUR - NELAMANGALA(6L) (NHAI) (N24001681)	8-2022	8/2025 (N.A.) {3/2027}	2,032.15 (2,032.15) {2,032.15}	176.97	46.77
		681	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA (NHAI) (N24001682)	3-2022	3/2024 (N.A.) {5/2026}	294.62 (309.90) {309.90}	49.92	14.02
		682	AURAD - BIDAR KM 0.00 TO KM 45.878 (NHAI) (N24001683)	9-2021	4/2023 (N.A.) {12/2024}	912.37 (N.A.) {424.16}	330.84	99.10
		683	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION (NHAI) (N24001684)	9-2020	1/2023 (N.A.) {5/2025}	688.00 (602.09) {688.00}	501.74	77.33
		684	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 (NHAI) (N24001686)	3-2021	3/2023 (N.A.) {4/2025}	1,065.06 (1,444.50) {1,444.50}	175.95	93.45
		685	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 (NHAI) (N24001687)	10-2021	10/2023 (N.A.) {8/2025}	1,331.77 (2,082.98) {2,082.98}	378.23	75.64
		686	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN (NHAI) (N24001691)	10-2019	10/2021 (N.A.) {3/2025}	1,225.24 (1,505.85) {1,505.85}	81.36	96.85

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		687	BALANCE WORK OF CONSTRUTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM. 54.370 TO KM. 101.400 (BI (MoRTH) (N24001936)	3-2021	3/2023 (N.A.) {7/2024}	344.79 (N.A.) {344.79}	10.00	90.00
		688	BALANCE WORK OF REHABILITATION AND UPGRADING TO 2LANE/2LANE WITH PAVED SHOULDER CONFIGURATION AND ST (MoRTH) (N24001937)	2-2023	2/2024 (N.A.) {2/2025}	398.48 (N.A.) {398.48}	5.00	50.00
		689	CONSTRUCTION OF ELEVATED CORRIDOR FROM KM. 135.650 TO 136.300 ON 63, FROM KM. 249 TO KM. 250.050 ON (MoRTH) (N24001938)	6-2021	6/2024 (N.A.) {6/2025}	298.00 (N.A.) {298.00}	10.70	52.00
		690	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24001940)	1-2023	1/2026 (N.A.) {9/2025}	166.58 (N.A.) {166.58}	3.54	-
		691	WIDENING TO 4 LANE FROM KM. 133.00 TO 158.04 (DESIGN CHAINAGE KM. 130.88 TO 155.145) (SHIRUR CROSS T (MoRTH) (N24001941)	1-2023	1/2025 (N.A.) {1/2025}	350.69 (N.A.) {350.69}	10.00	56.00
		692	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM. 33.13 TO KM. 40.23 AND KM. 52.00 TO KM. 71.00 (EX (MoRTH) (N24001943)	9-2022	3/2024 (N.A.) {1/2025}	172.98 (N.A.) {172.98}	6.48	65.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		693	WIDENING TO INTERMEDIATE/TWO LANE TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHANAGES KM 112.750 TO (MoRTH) (N24001944)	1-2023	6/2024 (N.A.) {7/2024}	255.88 (N.A.) {255.88}	60.99	78.00
		694	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 116.800 TO 149.070(DSIGN CHANGES) ON HOSADURGA HOL (MoRTH) (N24001945)	8-2022	2/2024 (N.A.) {12/2024}	170.34 (N.A.) {170.34}	4.25	72.00
		695	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM 24.400 TO 27.270, 40.500 TO 41.900, 84.300 TO 88.20 (MoRTH) (N24001946)	11-2022	11/2024 (N.A.) {11/2024}	218.93 (N.A.) {218.93}	10.00	95.00
		696	WIDENING TO EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FROM DESIGN KM 153.00 (MoRTH) (N24001947)	2-2023	2/2025 (N.A.) {2/2025}	177.94 (N.A.) {177.94}	6.66	47.00
		697	WIDENING TO 4 LANE FROM KM 51.60 TO 76.20 (HEBRI TO PARKALA) AND FROM KM 85.20 TO 88.90 (KARAVALI JU (MoRTH) (N24001948)	10-2022	10/2024 (N.A.) {12/2024}	355.72 (N.A.) {355.72}	11.32	60.00
		698	FOUR LANING OF LEFT OVER WORKS OF HOSPET BELLARY KARNATAKA/ AP BORDER FROM KM.280.080 TO KM. 375.450 (NHAI) (N24001989)	3-2023	5/2025 (N.A.) {5/2025}	830.28 (N.A.) {830.28}	521.50	61.19
		699	DEVELOPMENT OF 6 LANE ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KM. 97.000 TO KM. 162.500 MARADGI S (NHAI) (N24001993)	12-2022	10/2025 (N.A.) {10/2025}	1,589.00 (N.A.) {1,589.00}	483.76	56.30

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		700	4/6L OF BANGALORE - PUNE SECTION OF BYPASS CONNECTING DHARWAD - HUBLI FROM KM. 403.80 TO KM. 433.20 (NHAI) (N24001994)	5-2022	3/2023 (N.A.) {9/2025}	1,135.39 (N.A.) {1,135.39}	301.48	56.43
		701	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM 422.000 TO 523.600 (CHITR (MoRTH) (N24002011)	12-2021	6/2024 (N.A.) {12/2024}	516.96 (N.A.) {516.96}	19.93	70.00
		702	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40.00 TO KM 75.00 (EXISTING CHAINAGES) OF MANGALOR (MoRTH) (N24002012)	3-2023	3/2025 (N.A.) {3/2025}	718.52 (N.A.) {718.52}	24.81	23.00
		703	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM KM.0 TO KM. 80 ON NH 548B (VIJAYAPURA-SANKESWAR SE (MoRTH) (N24002013)	3-2021	2/2022 (N.A.) {10/2024}	766.64 (N.A.) {766.64}	13.55	75.00
		704	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24002186)	3-2024	9/2025 (N.A.) {9/2025}	166.58 (N.A.) {166.58}	3.62	-
		705	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM 55.6 TO KM 90.7 (EXISTING CHAINAGES) OF NH-766C ((MoRTH) (N24002187)	2-2024	2/2026 (N.A.) {2/2026}	313.56 (N.A.) {313.56}	53.65	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		706	WIDENING TO 2L+PS FROM KM 71.00 TO 104.00 (EXISTING CHAINAGES) (SARJAPUR TO PATTADKALLU) ON BHANAPUR (MoRTH) (N24002188)	3-2024	3/2026 (N.A.) {3/2026}	445.62 (N.A.) {445.62}	33.24	-
		707	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0.00 (DESIGN CHAINAGE 0.00) TO KM 23.338 (DESIGN C (MoRTH) (N24002189)	9-2024	3/2026 (N.A.) {3/2026}	196.05 (N.A.) {196.05}	2.34	-
	<u>STEEL</u>	708	SCREENING PLANT-II, DONIMALAI (NMDC) (N12000136)	9-2023	8/2026 (N.A.) {8/2026}	1,043.63 (N.A.) {1,043.63}	156.35	7.78
	<u>URBAN DEVELOPMENT</u>	709	BANGALORE METRO RAIL PROJECT PHASE-2 (BMRCL) (N28000058)	2-2014	2/2021 (N.A.) {3/2025}	26,405.14 (N.A.) {26,405.14}	20,936.29	89.00
		710	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B (BMRCL) (N28000151)	6-2021	6/2026 (N.A.) {6/2026}	14,788.10 (N.A.) {14,788.10}	2,424.04	30.00
<u>KERALA</u>	<u>CIVIL AVIATION</u>	711	CALICUT AIRPORT - DEVELOPMENT OF ADDITIONAL RESA ON EITHER END ON RUNWAY 10-28 AT CALICUT AIRPORT (AAI) (N04000111)	6-2023	9/2025 (N.A.) {9/2025}	484.57 (N.A.) {323.98}	18.55	6.00
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	712	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA (CPWD EDUCATION) (N28000140)	7-2019	3/2021 (N.A.) {11/2025}	753.63 (N.A.) {753.63}	412.37	66.00
	<u>HEALTH AND FAMILY WELFARE</u>	713	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST (CPWD FOR HEALTH) (N28000112)	9-2017	3/2020 (N.A.) {11/2024}	150.29 (N.A.) {162.00}	151.92	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	714	REPLACEMENT AND EXTENSION OF JETTY PIPELINES AT KOCHI REFINERY (BPCL) (N16000508)	3-2023	3/2026 (N.A.) {3/2026}	621.87 (N.A.) {621.87}	144.72	75.10
		715	SETTING UP POLYPROPYLENE UNIT AT KOCHI REFINERY (BPCL) (N16000530)	12-2023	10/2027 (N.A.) {10/2027}	4,460.00 (N.A.) {4,460.00}	100.61	8.20
	RAILWAYS	716	TRIVANDRUM-KANYAKUMARI DOUBLING (SR) (N22000399)	2-2015	(N.A.) {12/2027}	1,431.90 (N.A.) {3,785.45}	3,184.42	42.10
		717	ERNAKULAM-KUMBALAM - PATCH DOUBLING (7.71 KM) (SR) (N22000619)	12-2010	3/2028 (N.A.) {12/2026}	600.82 (N.A.) {595.39}	270.57	8.00
		718	KUMBALAM-THURAVUR - PATCH DOUBLING (15.59 KM) (SR) (N22000620)	12-2011	8/2023 (N.A.) {12/2026}	812.85 (N.A.) {802.80}	260.47	7.00
	ROAD TRANSPORT AND HIGHWAYS	719	4-LANNING OF THALSERRY - MAHE BYPASS (NHAI) (N24000704)	9-2017	5/2020 (N.A.) {2/2024}	1,124.11 (1,573.18) {1,573.18}	1,524.17	100.00
		720	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH (NHAI) (N24000784)	2-2018	2/2023 (N.A.) {4/2025}	1,424.77 (2,065.95) {2,065.95}	785.46	86.06
		721	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK (MoRTH) (N24001369)	2-2017	8/2017 (N.A.) {8/2024}	294.28 (296.53) {296.53}	286.80	98.00
		722	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) (MoRTH) (N24001370)	2-2017	9/2017 (N.A.) {8/2024}	380.76 (372.87) {372.87}	347.04	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		723	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE (NHAI) (N24001648)	8-2022	1/2026 (N.A.) {1/2026}	2,429.52 (N.A.) {2,429.52}	908.45	50.82
		724	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 (NHAI) (N24001649)	12-2021	2/2025 (N.A.) {1/2026}	3,273.61 (N.A.) {3,273.61}	597.66	55.14
		725	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54 (NHAI) (N24001650)	12-2021	1/2025 (N.A.) {8/2025}	3,635.64 (N.A.) {3,635.64}	280.92	37.34
		726	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O (NHAI) (N24001651)	9-2021	9/2024 (N.A.) {9/2024}	2,878.97 (N.A.) {2,878.97}	402.61	34.41
		727	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR (NHAI) (N24001652)	3-2020	6/2022 (N.A.) {6/2024}	210.37 (216.94) {216.94}	198.10	100.00
		728	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH ?66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 ((NHAI) (N24001653)	11-2021	4/2025 (N.A.) {4/2025}	3,565.82 (N.A.) {3,064.11}	1,997.05	54.47

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		729	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 (NHAI) (N24001654)	6-2021	3/2025 (N.A.) {12/2025}	2,641.37 (N.A.) {2,641.37}	523.26	71.18
		730	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX (NHAI) (N24001655)	6-2021	2/2025 (N.A.) {11/2025}	3,606.00 (3,946.56) {3,946.56}	3,034.04	64.85
		731	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. (NHAI) (N24001656)	6-2021	3/2025 (N.A.) {12/2025}	2,595.00 (N.A.) {4,009.57}	2,978.98	57.67
		732	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC (NHAI) (N24001657)	6-2021	10/2024 (N.A.) {12/2025}	2,842.14 (N.A.) {2,842.14}	477.69	64.50
		733	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM (NHAI) (N24001658)	1-2021	7/2024 (N.A.) {3/2025}	4,265.42 (N.A.) {4,728.40}	3,472.54	95.39
		734	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH- 66(OLD NH-17) FROM DESIGN CH (NHAI) (N24001659)	2-2021	7/2024 (N.A.) {3/2025}	3,375.31 (3,824.07) {3,824.07}	2,329.23	93.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		735	SIX LANING OF THALIPARAMBHA-MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH (NHAI) (N24001660))	8-2020	2/2024 (N.A.) {12/2025}	2,714.60 (3,557.65) {2,714.60}	1,780.62	67.00
		736	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 (NHAI) (N24001661))	10-2020	4/2024 (N.A.) {12/2025}	3,219.47 (3,898.46) {3,896.46}	2,091.65	51.20
		737	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH (NHAI) (N24001662))	5-2020	5/2024 (N.A.) {3/2025}	1,981.07 (2,627.66) {1,981.07}	1,491.76	86.31
		738	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ (NHAI) (N24001663))	6-2020	4/2024 (N.A.) {12/2025}	3,041.65 (3,799.76) {3,041.65}	2,351.56	75.02
		739	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ (NHAI) (N24001664))	6-2020	4/2024 (N.A.) {11/2025}	1,746.45 (2,377.88) {1,746.45}	1,239.13	75.00
		740	WIDENING/DEVELOPMENT OF EXISTING NH-85 FROM KM 0.000 TO KM 124.636 SECTION TO 2L/@L+PS SECTION IN TH (NHAI) (N24002074))	8-2022	6/2025 (N.A.) {6/2025}	1,231.74 (N.A.) {1,231.74}	226.72	28.90
	URBAN DEVELOPMENT	741	KOCHI METRO RAIL PROJECT PHASE II FROM JLN STADIUM TO INFOPARK VIA KAKKANAD (KMRCL) (N28000158))	7-2018	11/2026 (N.A.) {11/2026}	1,957.05 (N.A.) {1,957.05}	2.81	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		742	KOCHI METRO RAIL PROJECT PHASE IB SECTION FROM S N JUNCTION TO THRIPIUNTHURA (KMRCL) (N28000159)	6-2019	9/2023 (N.A.) {9/2023}	355.70 (448.00) {448.33}	1.64	-
LADAKH	CIVIL AVIATION	743	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT (AAI) (N04000078)	7-2018	9/2021 (N.A.) {10/2025}	480.33 (N.A.) {640.00}	404.97	62.50
	ROAD TRANSPORT AND HIGHWAYS	744	KARGIL-ZANSKR PACKAGE-1 (NHIDCL) (N24001343)	3-2021	1/2023 (N.A.) {11/2025}	384.23 (N.A.) {384.23}	115.95	60.40
		745	KARGIL-ZANSKR PACKAGE-2 (NHIDCL) (N24001344)	3-2021	1/2023 (N.A.) {11/2025}	404.89 (N.A.) {404.89}	190.72	64.36
		746	KARGIL-ZANSKR PACKAGE-3 (NHIDCL) (N24001345)	8-2020	1/2023 (N.A.) {8/2025}	381.01 (N.A.) {381.01}	205.56	74.11
		747	KARGIL-ZANSKR PACKAGE-8 (NHIDCL) (N24001348)	3-2021	1/2023 (N.A.) {8/2025}	398.37 (N.A.) {398.37}	209.68	82.11
		748	CONSTRUCTION OF REALIGNMENT BETWEEN PANDRASS- PASHKYUN (TOTAL LENGTH 27.10 KM) ON ROAD ZOZILA-KARGIL (BRO) (N24001999)	11-2021	6/2025 (N.A.) {6/2025}	426.14 (N.A.) {426.14}	76.75	37.00
MADHYA PRADESH	CIVIL AVIATION	749	UPGRADATION OF JABALPUR AIRPORT (AAI) (N04000087)	6-2016	6/2021 (N.A.) {7/2024}	412.24 (N.A.) {412.24}	402.79	100.00
		750	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 (AAI) (N04000098)	10-2021	8/2023 (N.A.) {8/2024}	446.12 (N.A.) {446.12}	433.09	100.00
	COAL	751	KANCHAN OC EXPANSION (SECL) (N06000125)	12-2014	3/2021 (N.A.) {3/2026}	371.04 (N.A.) {371.04}	135.30	47.00
		752	AMADAND OPENCAST EXPANSION PROJECT (SECL) (N06000148)	3-2016	3/2021 (N.A.) {3/2027}	869.44 (N.A.) {869.44}	267.41	64.00
		753	GANDHIGRAM UG MINE (WCL) (N06000183)	8-2019	3/2026 (N.A.) {3/2026}	414.16 (N.A.) {414.16}	11.75	28.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		754	BLOCK-B EXPANSION OPENCAST PROJECT (NCL) (N06000184)	7-2019	3/2023 (N.A.) {3/2025}	998.71 (N.A.) {998.71}	402.12	28.78
		755	NIGAH I EXPANSION OCP (15 TO 25 MTPA) (NCL) (N06000196)	11-2020	3/2025 (N.A.) {3/2025}	1,729.68 (N.A.) {1,729.68}	731.28	42.65
		756	RAMPUR BATURA OC (4.0 MTY) (SECL) (N06000233)	7-2019	3/2026 (N.A.) {3/2026}	1,248.93 (N.A.) {1,248.93}	481.56	44.00
		757	TAWA III UG MINE (WCL) (N06000250)	12-2021	3/2027 (N.A.) {3/2027}	314.09 (N.A.) {324.25}	0.56	9.00
		758	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) (WCL) (N06000257)	9-2022	3/2027 (N.A.) {3/2027}	399.20 (N.A.) {497.01}	64.13	42.00
		759	VISHNUPURI UG TO OC (WCL) (N06000260)	11-2022	3/2029 (N.A.) {3/2029}	220.62 (N.A.) {227.65}	0.00	7.00
		760	URDHAN OC (WCL) (N06000265)	1-2023	3/2031 (N.A.) {3/2031}	206.88 (N.A.) {228.42}	22.12	9.00
		761	SHARDA UG (WCL) (N06000266)	9-2023	3/2028 (N.A.) {3/2028}	166.25 (N.A.) {200.16}	1.69	11.00
	PETROLEUM	762	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF (BPCL) (N16000518)	5-2023	5/2028 (N.A.) {5/2028}	43,367.00 (N.A.) {43,367.00}	1,276.00	9.90
	POWER	763	SHAJAPUR 325MW SOLAR PV PROJECT (NTPC) (N18000348)	6-2022	3/2024 (N.A.) {3/2025}	1,530.49 (N.A.) {1,530.49}	1,176.06	70.00
		764	TS FOR EVACUATION POWER RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX): PART-C (PGCIL) (N18000392)	8-2024	8/2026 (N.A.) {8/2026}	2,708.00 (N.A.) {2,708.00}	27.00	6.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		765	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-2 5.5GW] [JAISALMER/BARME (PGCIL) (N18000399)	10-2024	10/2026 (N.A.) {10/2026}	3,674.00 (N.A.) {3,674.00}	74.00	1.00
	RAILWAYS	766	RAMGANJMUNDI-BHOPAL (NL),WCR (WCR) (220100314)	4-2001	3/2021 (N.A.) {6/2026}	424.60 (3,032.46) {5,125.16}	3,288.71	68.00
		767	RATLAM-MHOW-KHANDWA- AKOLA (GC) (WR) (N22000120)	4-2008	3/2022 (N.A.) {2/2027}	3,503.69 (5,677.80) {6,203.51}	4,132.14	80.00
		768	KATNI - SINGRAULI DOUBLING PROJECT (WCR) (N22000351)	12-2015	3/2020 (N.A.) {12/2027}	1,763.93 (2,445.30) {4,353.50}	3,052.84	86.00
		769	KATNI GRADE SEPARATOR/BYE PASS (WCR) (N22000416)	8-2016	3/2022 (N.A.) {9/2024}	582.13 (1,247.64) {2,300.00}	1,339.40	-
		770	ANUPPUR-KATNI (SECR) (N22000485)	4-2015	12/2021 (N.A.) {3/2025}	1,370.00 (1,680.00) {2,311.02}	1,801.30	76.00
		771	NIMACH BADI SADRI NEW LINE PROJECT (WR) (N22000503)	4-2017	3/2022 (N.A.) {3/2026}	495.18 (N.A.) {495.18}	239.25	17.00
		772	NIMACH-RATLAM (133 KM) (WR) (N22000536)	10-2021	10/2027 (N.A.) {6/2025}	910.00 (1,095.88) {1,095.88}	946.95	71.00
		773	SATNA - REWA (50 KM) (WCR) (N22000554)	11-2015	3/2026 (N.A.) {3/2026}	500.00 (40.00) {500.00}	1.41	80.00
		774	INDORE BUDNI (INDORE JABALPUR) (RVNL) (N22000601)	9-2018	9/2030 (N.A.) {9/2030}	4,340.00 (N.A.) {7,393.75}	1,004.86	-
	ROAD TRANSPORT AND HIGHWAYS	775	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 (MoRTH) (N24000513)	3-2015	8/2017 (N.A.) {6/2025}	511.83 (N.A.) {511.83}	485.18	93.06

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		776	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN (NHAI) (N24000709)	12-2017	2/2020 (N.A.) {12/2024}	950.27 (N.A.) {786.43}	637.08	99.50
		777	4LBERKHEDI TO GODPEHRA NH- 44 (NHAI) (N24001614)	2-2022	11/2024 (N.A.) {11/2024}	524.84 (N.A.) {524.84}	2,255.47	45.00
		778	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) (NHAI) (N24001615)	3-2021	4/2024 (N.A.) {8/2024}	790.78 (N.A.) {790.78}	1,853.67	70.00
		779	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125 (NHAI) (N24001616)	1-2021	10/2023 (N.A.) {2/2025}	428.04 (N.A.) {428.04}	351.30	98.98
		780	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50 (NHAI) (N24001618)	9-2019	9/2022 (N.A.) {2/2025}	194.40 (235.00) {235.00}	199.66	98.81
		781	4L OF CHANDESARA TO KHEDAKHAJURIYA FROM KM. 0.000 TO (-) 750 AND KM 0.000 TO KM 41.400 OF NH-752D (NHAI) (N24001759)	1-2020	6/2024 (N.A.) {3/2025}	909.84 (N.A.) {909.84}	495.72	93.20
		782	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] (NHAI) (N24001762)	10-2021	1/2024 (N.A.) {12/2024}	1,146.22 (N.A.) {1,146.22}	660.03	90.30
		783	ADDITIONAL WORKS (2VUPS, MR- 10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE-DEWAS SECTION OF N (NHAI) (N24001765)	8-2022	7/2024 (N.A.) {12/2025}	207.77 (N.A.) {207.77}	56.45	59.56

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		784	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] (NHAI) (N24001766)	1-2022	10/2024 (N.A.) {5/2025}	1,011.29 (N.A.) {1,011.29}	232.31	50.25
		785	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND (NHAI) (N24001767)	1-2021	4/2024 (N.A.) {4/2024}	1,001.69 (N.A.) {1,001.69}	507.18	80.67
		786	BALANCE WORK OF 4L OF INDORE-GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF (NHAI) (N24001768)	8-2019	4/2023 (N.A.) {11/2023}	323.51 (N.A.) {323.51}	51.96	100.00
		787	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 (NHAI) (N24001770)	2-2022	3/2024 (N.A.) {3/2025}	417.51 (N.A.) {417.51}	265.77	86.28
		788	2- LANE WITH PAVED SHOULDERS OF HINOTIYA TO MEHULWA FROM DESIGN KM 27+000 90F EXISTING SH-19 KM 26+5 (NHAI) (N24001921)	8-2021	9/2025 (N.A.) {9/2025}	581.65 (592.03) {581.65}	169.81	33.74
		789	CONSTRUCTION OF MIHONA BYPASS, LAHAR BYPASS, DABOH BYPASS and BHANDER BYPASS (TOTAL LENGTH 20.60 KM) (MoRTH) (N24001962)	3-2022	12/2024 (N.A.) {3/2025}	179.19 (N.A.) {179.19}	109.91	96.00
		790	UPGRADATION OF NASRULLAGANI-REHTI-BUDHNI SCCTION TO 2-LANE WITH PAVED SHOULDER FROM KM 0+150 TO KM (MoRTH) (N24001963)	12-2021	10/2024 (N.A.) {9/2025}	305.12 (N.A.) {305.12}	122.88	34.46

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		791	UPGRADATION and WIDENING OF JHARKHEDA- BERASIA - DHOLKHEDI FROM DESIGN KM 0+000 TO KM 87+900 (DESIGN) (MoRTH) (N24001964)	3-2022	5/2025 (N.A.) {5/2025}	365.21 (N.A.) {365.21}	162.23	64.00
		792	REHABILITATION AND UPGRADATION OF KURWAI?MUNGAOLI?CHANDERI ROAD SECTION OF NH-346, FROM DESIGN CHAIN (MoRTH) (N24001965)	3-2022	2/2025 (N.A.) {12/2025}	386.49 (N.A.) {386.49}	119.76	48.77
		793	BALANCE WORK FOR REHABILITATION AND UP-GRADATION OF SIDHI-SINGRAULI FROM KM 82.400 TO KM 187.993 SEC (MoRTH) (N24001966)	12-2020	4/2023 (N.A.) {6/2025}	529.44 (N.A.) {529.44}	222.24	60.01
		794	4L GREENFIELD RUDHI TO DESHGAON (PKG V OF BETUL-KHANDWA/DESHGAON) - N/04015/06003/MP (NHAI) (N24001967)	11-2018	10/2025 (N.A.) {10/2025}	521.21 (N.A.) {521.21}	86.23	34.50
		795	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF JIRAPUR-SUSNER-MP-RJ B (MoRTH) (N24002018)	1-2022	3/2025 (N.A.) {3/2025}	239.72 (232.22) {232.22}	203.70	100.00
		796	UPGRADATION OF DINDORI-SAGARTOLA-KABICHABUTRA (MP-CG BORDER) SECTION OF NH -45 FROM KM 0+00(DESIGN) (MoRTH) (N24002019)	1-2022	9/2025 (N.A.) {9/2025}	329.14 (319.09) {319.09}	167.87	50.12
		797	CONSTRUCTION OF KAITHI-PADARIA KALA BYPASS, PATNA-TAMOLI BYPASS, JASO BYPASS, NAGOD BYPASS (TOTAL L (MoRTH) (N24002020)	3-2022	10/2025 (N.A.) {10/2025}	158.36 (158.00) {158.36}	53.05	30.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		798	BALANCE WORK OF 4L OF NAURADEHI SANCTUARY DE-SCOPED STRETCH OF HIRAN RIVER TO SINDOOR RIVER FROM KM. (NHAI) (N24002067)	1-2021	7/2023 (N.A.) {3/2025}	178.18 (N.A.) {178.18}	161.64	91.73
		799	CONSTRUCTION OF 4-LANE FROM BARELA TO MANEGAON SECTION OF NH-30 FROM DESIGN CH. 2.900 TO DESIGN CH. (NHAI) (N24002068)	12-2022	3/2025 (N.A.) {12/2025}	652.33 (N.A.) {652.33}	322.45	61.66
		800	CONSTRUCTION OF ADDITIONAL 3 LANE WITH PAVED SHOULDER (DESIGN LENGTH 8.87 KM) AS REALIGNMENT OF BAKA (NHAI) (N24002069)	7-2022	12/2024 (N.A.) {12/2024}	209.29 (N.A.) {209.29}	139.51	100.00
		801	INDORE - EDLABAD (PKG-II) [TEJAJINAGAR TO BALWARA] (NHAI) (N24002070)	1-2022	1/2025 (N.A.) {1/2025}	1,162.80 (N.A.) {1,162.80}	479.20	75.06
		802	CONSTRUCTION OF (I) 4-LANE HIGHWAY FROM VIDISHA TO HINOTIYA FROM KM. 0.000 TO KM. 27.000 (LENGTH=27 (NHAI) (N24002077)	9-2022	12/2025 (N.A.) {12/2025}	1,000.63 (N.A.) {1,000.63}	208.37	36.90
		803	FOUR LANING OF RAGHOGARH (DESIGN CH.29.300/EXISTING CH. 29.555) TO NANASA (DESIGN CH.92.971/EXISTING (NHAI) (N24002166)	3-2024	3/2026 (N.A.) {3/2026}	799.20 (N.A.) {799.20}	242.35	22.30
		804	BALANCE WORKS OF 4 LANE DIVIDED CARRIAGEWAY OF MISSING LINK SECTION OF NH-39 (REWA BYPASS) FROM JUNC (NHAI) (N24002200)	4-2024	4/2026 (N.A.) {4/2026}	355.36 (N.A.) {355.36}	11.85	18.33

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>SOCIAL JUSTICE</u>	805	CENTRE FOR DISABILITY SPORTS (CPWD) (N38000001)	2-2019	3/2024 (N.A.) {3/2024}	170.99 (N.A.) {170.99}	73.80	74.00
	<u>URBAN DEVELOPMENT</u>	806	BHOPAL METRO RAIL (MPMRCL) (N28000124)	11-2018	2/2023 (N.A.) {6/2028}	6,941.40 (N.A.) {6,941.40}	2,728.48	39.08
		807	INDORE METRO RAIL (MPMRCL) (N28000125)	11-2018	2/2023 (N.A.) {12/2028}	7,500.80 (N.A.) {7,500.80}	3,462.33	50.52
		808	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT (AAI) (N04000079)	3-2017	4/2021 (N.A.) {12/2023}	475.39 (N.A.) {520.00}	508.22	100.00
		809	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM (AAI) (N04000096)	6-2017	12/2020 (N.A.) {4/2024}	255.68 (N.A.) {270.00}	267.86	100.00
MAHARASHTRA	<u>COAL</u>	810	AMALGAMATED YEKONA-I YEKONA-II (WCL) (N06000132)	8-2015	3/2025 (N.A.) {3/2025}	727.28 (N.A.) {727.28}	530.02	86.00
		811	UKNI DEEP OC (WCL) (N06000179)	1-2019	3/2021 (N.A.) {3/2025}	237.06 (N.A.) {318.14}	163.86	91.00
		812	GHONSA EXPANSION DEEP OC (WCL) (N06000205)	3-2021	3/2028 (N.A.) {3/2029}	184.71 (N.A.) {241.72}	9.25	6.00
		813	SASTI EXPANSION OC (WCL) (N06000206)	8-2020	3/2026 (N.A.) {3/2026}	319.04 (N.A.) {371.59}	68.64	24.00
		814	DHUPTALA OC(SASTI UG TO OC) (WCL) (N06000209)	10-2021	3/2028 (N.A.) {3/2028}	711.00 (N.A.) {720.87}	159.15	33.00
		815	ADASA UG TO OC (1.50 MTY) (WCL) (N06000219)	11-2018	3/2024 (N.A.) {3/2025}	316.00 (N.A.) {333.43}	208.20	78.00
		816	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) (WCL) (N06000222)	2-2020	3/2027 (N.A.) {3/2027}	822.88 (N.A.) {1,184.33}	578.89	48.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		817	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) (WCL) (N06000226)	9-2018	3/2024 (N.A.) {3/2025}	235.90 (N.A.) {313.34}	116.46	87.00
		818	SAONER UG MINE I EXPANSION (WCL) (N06000251)	1-2022	3/2028 (N.A.) {3/2028}	228.64 (N.A.) {253.51}	118.34	27.00
		819	SINGHORI DEEP OC (WCL) (N06000252)	5-2022	3/2029 (N.A.) {3/2029}	335.75 (N.A.) {421.84}	22.01	16.00
		820	MAKARDHOKDA I EXPANSION OC (WCL) (N06000253)	6-2022	3/2026 (N.A.) {3/2026}	361.87 (N.A.) {497.06}	33.90	12.00
		821	BHATADI EXPANSION OC (WCL) (N06000254)	5-2022	3/2028 (N.A.) {3/2028}	580.60 (N.A.) {729.86}	61.33	17.00
		822	NEW MAJARI UG TO OC (3.0 MTY) (WCL) (N06000255)	9-2022	3/2027 (N.A.) {3/2027}	402.27 (N.A.) {496.38}	47.99	27.00
		823	BHANEGAON OC (1.15MTY) (WCL) (N06000256)	9-2022	3/2028 (N.A.) {3/2028}	405.20 (N.A.) {494.60}	10.21	7.00
		824	GOKUL EXPANSION OC (WCL) (N06000264)	4-2021	3/2026 (N.A.) {3/2026}	309.58 (N.A.) {456.95}	3.65	7.00
		825	KOLGAON EXPANSION (DEEP) OC (WCL) (N06000267)	9-2023	3/2027 (N.A.) {3/2027}	198.71 (N.A.) {206.19}	0.55	5.00
		826	AMALGAMATED GAURI PAUNI EXPANSION OC (WCL) (N06000271)	3-2024	3/2030 (N.A.) {3/2030}	1,225.21 (N.A.) {1,428.25}	52.83	17.00
		827	GAURI CENTRAL OCM (WCL) (N06000278)	6-2024	3/2030 (N.A.) {3/2030}	973.07 (N.A.) {1,015.07}	0.00	-
		828	BALLARPUR NORTHWEST OC MINE (WCL) (N06000282)	12-2022	3/2029 (N.A.) {3/2029}	360.18 (N.A.) {360.18}	0.00	-
		829	NORTHERN EXTENSION OF MUNGOLI NIRGUDA DEEP OC (WCL) (N06000283)	6-2024	3/2029 (N.A.) {3/2029}	1,024.91 (N.A.) {1,184.44}	0.00	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		830	AMALGAMATED GONDEGAON - GHATROHAN EXPANSION OCM (WCL) (N06000284)	9-2024	3/2029 (N.A.) {3/2029}	668.54 (N.A.) {871.59}	0.00	-
	DEPARTMENT OF HIGHER EDUCATION	831	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI (CPWD EDUCATION) (N28000117)	1-2018	7/2020 (N.A.) {2/2024}	223.37 (275.00) {230.00}	141.16	100.00
	HEALTH AND FAMILY WELFARE	832	500 BEDDED HOSPITAL INCLUDING 50 SUPERSPECIALITY BEDS FOR ESIC AT PUNE (CPWD) (N21000033)	7-2022	9/2025 (N.A.) {9/2025}	429.25 (N.A.) {429.25}	99.08	-
	PETROLEUM	833	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS (ONGC) (N16000213)	12-2015	4/2018 (N.A.) {6/2025}	3,190.69 (3,375.90) {3,375.90}	2,967.37	88.10
		834	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV (ONGC) (N16000358)	4-2019	3/2022 (N.A.) {2/2025}	3,228.80 (3,976.67) {3,976.67}	3,957.65	100.00
		835	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND (GAIL) (N16000430)	5-2019	4/2025 (N.A.) {10/2025}	8,797.00 (11,256.00) {11,256.00}	5,826.33	80.65
		836	PIPELINE REPLACEMENT PROJECT - VII (ONGC) (N16000436)	1-2022	5/2024 (N.A.) {3/2025}	3,183.58 (N.A.) {3,645.23}	3,417.00	99.50
		837	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL (BPCL) (N16000442)	4-2021	6/2024 (N.A.) {4/2025}	1,164.69 (N.A.) {1,164.69}	739.99	71.30
		838	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY (IOCL) (N16000446)	9-2021	10/2023 (N.A.) {5/2024}	378.00 (N.A.) {378.00}	120.07	39.08

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		839	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI (BPCL) (N16000452)	5-2022	3/2024 (N.A.) {9/2024}	423.39 (N.A.) {423.39}	217.90	73.00
		840	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) (IOCL) (N16000456)	9-2022	8/2025 (N.A.) {3/2026}	165.00 (N.A.) {165.00}	62.45	59.59
		841	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK (ONGC) (N16000470)	6-2022	10/2025 (N.A.) {2/2026}	4,144.41 (6,406.90) {6,406.90}	2,037.17	58.20
		842	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS (IOCL) (N16000487)	3-2022	3/2030 (N.A.) {9/2031}	865.00 (N.A.) {865.00}	52.47	1.90
		843	ANDHERI RESIDENTIAL TOWERS MUMBAI (IOCL) (N16000503)	6-2017	5/2025 (N.A.) {6/2026}	281.35 (389.67) {389.67}	211.52	48.00
		844	CONSTRUCTION OF ADDITIONAL TANKAGES AND ALLIED FACILITIES AT JNPT TERMINAL (IOCL) (N16000504)	4-2022	10/2024 (N.A.) {8/2026}	341.43 (436.14) {436.14}	228.19	40.90
		845	INSTALLATION OF INDEPENDENT DE- AROMATIZED SOLVENTS PRODUCTION FACILITIES AT MUMBAI REFINERY (BPCL) (N16000507)	3-2023	7/2025 (N.A.) {7/2025}	405.00 (N.A.) {405.00}	143.94	66.10
		846	PART REPLACEMENT PIPELINE PROJECT (PRPP) (ONGC) (N16000515)	11-2022	5/2024 (N.A.) {3/2025}	1,219.48 (N.A.) {1,145.10}	477.49	65.40
		847	POL AND LOBS INSTALLATIONS WITH RECEIPT PIPELINES AT RASAYANI (BPCL) (N16000519)	5-2023	5/2026 (N.A.) {5/2026}	2,585.00 (N.A.) {2,585.00}	339.72	48.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		848	MHN TCPP PGC BGC PROJECT (MTPBP) (ONGC) (N16000526)	2-2024	5/2026 (N.A.) {5/2026}	2,329.45 (N.A.) {2,354.23}	272.30	23.40
		849	PRP-VIII GROUP B (NH AND BS ASSET) (ONGC) (N16000533)	6-2024	5/2026 (N.A.) {2/2026}	2,379.84 (N.A.) {2,379.84}	222.56	24.40
		850	HP TDAE UNIT IN MUMBAI REFINERY (HPCL) (N16000534)	6-2024	4/2026 (N.A.) {4/2026}	240.00 (N.A.) {240.00}	19.91	19.80
		851	INTEGRATED DEVELOPMENT OF 4 CONTRACT AREAS UNDER DSF2 (ONGC) (N16000537)	5-2023	4/2027 (N.A.) {4/2027}	6,183.79 (N.A.) {6,183.79}	0.00	8.60
		852	LUBE MODERNIZATION AND BOTTOM UPGRADATION PROJECT (HPCL) (N16000540)	12-2024	3/2028 (N.A.) {3/2028}	4,679.00 (N.A.) {4,679.00}	148.87	3.20
	POWER	853	BIKANER SOLAR POWER PROJECT (SJVN) (N18000335)	4-2022	5/2024 (N.A.) {9/2025}	5,491.89 (532.00) {5,491.89}	3,285.48	67.72
		854	TS FOR EVACUATION OF 7GW RE INJECTION AT KHAVDA PS UNDER PHASE-IV PART E4 (PGCIL) (N18000377)	11-2023	7/2025 (N.A.) {7/2025}	224.00 (N.A.) {224.00}	0.00	3.00
	RAILWAYS	855	AHMEDNAGAR-PARLI VAIJNATH(NL) CR (CR) (220100181)	2-1997	3/2021 (N.A.) {12/2025}	2,271.50 (N.A.) {4,909.82}	4,651.86	91.00
		856	MUMBAI URBAN TRANSPORT PROJECT PHASE-II (MRTP) (N22000092)	4-2008	3/2014 (N.A.) {3/2014}	5,300.00 (N.A.) {918.53}	7,135.77	77.30
		857	WARDHA-NANDED MAHARASHTRA (CR) (N22000231)	4-2008	3/2023 (N.A.) {1/2026}	3,168.29 (N.A.) {3,445.34}	2,918.89	47.00
		858	KALYAN-KASARA 3RD LINE (CR) (N22000233)	4-2011	3/2021 (N.A.) {12/2025}	792.89 (N.A.) {1,432.61}	831.24	50.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		859	WARDHA-SEWAGRAM NGP 3RD LINE (CR) (N22000250)	4-2012	3/2022 (N.A.) {5/2025}	540.02 (N.A.) {540.02}	692.36	72.00
		860	WARDHA-BALHARSHAH - 3RD LINE (132 KM) (CR) (N22000356)	2-2015	3/2022 (N.A.) {8/2025}	1,272.19 (N.A.) {1,384.72}	1,400.09	67.00
		861	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) (CR) (N22000358)	2-2015	3/2023 (N.A.) {3/2027}	2,449.91 (N.A.) {2,449.91}	1,608.87	48.00
		862	PUNE-MIRAJ-LONDA (467 KM) (CR) (N22000359)	2-2015	3/2024 (N.A.) {3/2025}	3,627.47 (3,627.00) {6,463.49}	4,415.59	84.00
		863	DAUND - MANMAD (236 KM) (CR) (N22000360)	2-2016	3/2023 (N.A.) {9/2025}	1,876.00 (N.A.) {2,081.27}	2,556.05	87.00
		864	MANMAD - JALGAON - 3RD LINE (160 KM) (CR) (N22000361)	2-2016	3/2022 (N.A.) {3/2026}	1,035.16 (N.A.) {1,552.24}	1,552.35	80.00
		865	WARDHA - NAGPUR - 4TH LINE (76 KM) (CR) (N22000362)	2-2016	3/2023 (N.A.) {5/2025}	637.95 (N.A.) {637.95}	900.89	70.00
		866	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) (SECR) (N22000420)	9-2016	3/2023 (N.A.) {12/2025}	1,908.51 (N.A.) {3,544.25}	2,979.85	90.00
		867	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (WR) (N22000434)	3-2010	(N.A.) {3/2024}	265.88 (N.A.) {311.36}	0.00	-
		868	WADSA-GADHCHIROLI NEW LINE (52.36 KM) (SECR) (N22000480)	6-2018	12/2021 (N.A.) {12/2026}	229.00 (N.A.) {1,880.61}	674.63	22.00
		869	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (N22000511)	8-2022	8/2027 (N.A.) {3/2029}	955.00 (N.A.) {2,093.82}	71.75	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		870	SOLAPUR-TULJAPUR- OSMANABAD (UMBRELLA WORK) (CR) (N22000513)	1-2019	3/2028 (N.A.) {10/2027}	904.92 (N.A.) {3,295.74}	1,093.34	5.00
		871	DHULE (BORVIHIR)-NARDANA (UMBRELLA WORK) (CR) (N22000514)	1-2019	3/2026 (N.A.) {9/2027}	492.76 (N.A.) {1,170.83}	176.04	5.00
		872	KALYAN-MURBAD VIA ULHASNAGAR (UMBRELLA WORK) (CR) (N22000515)	2-2023	3/2027 (N.A.) {3/2027}	836.12 (N.A.) {836.12}	9.23	-
		873	BARAMATI - LONAND (CR) (N22000615)	2-1999	3/2027 (N.A.) {2/2026}	736.44 (N.A.) {1,843.90}	639.48	50.00
		874	MUMBAI URBAN TRANSPORT PROJECT IIIA (MRVC) (N22000627)	4-2019	3/2025 (N.A.) {12/2027}	33,690.00 (N.A.) {33,690.00}	846.83	-
		875	NAGPUR- NAGBHIR RAILWAY LINE GAUGE CONVERSION PROJECT (MRIDC) (N22000629)	10-2019	6/2024 (N.A.) {3/2025}	1,400.00 (N.A.) {1,400.00}	6.81	78.00
	ROAD TRANSPORT AND HIGHWAYS	876	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM (MoRTH) (N24000332)	1-2015	(N.A.) {}	225.81 (N.A.) {225.81}	167.96	96.00
		877	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN (NHAI) (N24000442)	12-2015	3/2019 (N.A.) {3/2025}	649.50 (N.A.) {649.50}	601.24	91.23
		878	NAGPUR RING ROAD PACKAGE-2 (NHAI) (N24000560)	3-2016	7/2019 (N.A.) {3/2025}	591.66 (N.A.) {591.66}	624.24	97.69
		879	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000584)	3-2016	(N.A.) {12/2023}	1,142.62 (1,907.03) {1,142.62}	1,056.08	95.17

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		880	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000585)	3-2016	(N.A.) {}	1,101.58 (N.A.) {1,101.58}	608.53	-
		881	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) (NHAI) (N24000656)	3-2017	3/2020 (N.A.) {12/2025}	744.64 (N.A.) {1,007.00}	467.65	92.50
		882	4-LANNING OF WARANGA- MAHAGAON SECTION(KM 253.7000 TO 320.580) (NHAI) (N24000659)	3-2017	3/2017 (N.A.) {10/2024}	1,059.73 (1,071.00) {1,071.00}	878.19	82.04
		883	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF (NHAI) (N24000851)	3-2018	7/2021 (N.A.) {6/2025}	1,162.92 (1,182.87) {1,182.87}	371.48	58.12
		884	SARSAM TO KOTHARI (MoRTH) (N24001002)	2-2016	7/2019 (N.A.) {12/2023}	545.64 (N.A.) {545.64}	232.64	93.68
		885	AKOLA TO AKOT (MoRTH) (N24001003)	1-2017	6/2019 (N.A.) {12/2023}	313.95 (N.A.) {313.95}	270.26	99.00
		886	DIGRAS DARWAH KARANJA (MoRTH) (N24001013)	1-2017	6/2019 (N.A.) {12/2023}	391.06 (391.00) {391.06}	287.60	93.00
		887	DAHEGAON TO KUHI (MoRTH) (N24001017)	1-2017	6/2019 (N.A.) {12/2023}	228.89 (229.00) {228.89}	154.82	99.00
		888	BHANDARA TO GHOTITOK (MoRTH) (N24001018)	1-2017	6/2019 (N.A.) {6/2019}	392.83 (393.00) {392.83}	274.75	100.00
		889	AMD I TO SAONER (MoRTH) (N24001021)	1-2017	6/2019 (N.A.) {12/2023}	396.91 (397.00) {396.91}	289.79	98.69
		890	WADI TO ASOLA (MoRTH) (N24001022)	1-2017	9/2019 (N.A.) {12/2023}	363.82 (364.00) {363.82}	154.65	93.00
		891	SHAHPUR PATGAON SECTION I (MoRTH) (N24001027)	1-2018	12/2019 (N.A.) {3/2024}	150.79 (N.A.) {150.79}	81.14	70.66

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		892	JINTUR TO PARBHANI (MoRTH) (N24001039)	1-2017	(N.A.) {12/2023}	356.66 (N.A.) {356.66}	209.48	80.48
		893	RALEGAON TO RAMTIRTH (MoRTH) (N24001046)	1-2017	7/2019 (N.A.) {8/2023}	210.81 (N.A.) {210.81}	210.81	96.50
		894	VITA TO NAGAJ (MoRTH) (N24001050)	3-2018	12/2019 (N.A.) {12/2023}	304.58 (305.00) {304.58}	154.68	68.39
		895	KARAD PATAN CHIPLUN GUHAGAR (MoRTH) (N24001057)	2-2017	6/2019 (N.A.) {10/2023}	407.19 (407.00) {407.19}	323.02	89.97
		896	KARWANDI TO RAJURI (MoRTH) (N24001058)	3-2018	12/2019 (N.A.) {3/2024}	276.95 (277.00) {276.95}	160.94	92.06
		897	PALPHATA TO PHULAMBARI (MoRTH) (N24001060)	3-2018	12/2019 (N.A.) {12/2023}	227.19 (227.00) {227.19}	141.92	95.00
		898	NANDED TO JALKOT (MoRTH) (N24001069)	12-2017	9/2019 (N.A.) {9/2019}	456.93 (457.00) {456.93}	278.22	-
		899	PUNE TO MALE VILLAGE (MoRTH) (N24001078)	3-2018	12/2019 (N.A.) {12/2023}	228.31 (N.A.) {228.31}	100.97	93.89
		900	ARDHAPUR TO HIMAYATNAGAR (MoRTH) (N24001079)	12-2017	6/2020 (N.A.) {12/2023}	426.06 (426.00) {426.06}	271.40	96.25
		901	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER (MoRTH) (N24001080)	3-2018	12/2019 (N.A.) {10/2023}	256.15 (N.A.) {256.15}	126.62	98.00
		902	HIMAYATNAGAR TO PHULSAWANGI (MoRTH) (N24001081)	3-2018	12/2019 (N.A.) {12/2023}	294.87 (295.00) {294.87}	183.17	89.99
		903	PUNE RAIGARH DISTRICT BORDER TO MANGAON (MoRTH) (N24001082)	3-2018	12/2019 (N.A.) {12/2023}	223.46 (N.A.) {223.46}	123.46	100.00
		904	KOLDE TO KHETIYA (MoRTH) (N24001090)	1-2017	7/2019 (N.A.) {12/2023}	509.18 (N.A.) {509.18}	283.13	94.81
		905	SATARA TO MHASWAD (MoRTH) (N24001092)	1-2017	7/2019 (N.A.) {12/2023}	653.46 (N.A.) {653.46}	369.62	77.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		906	SATARA MURVAD PILLOV PANDHARPUR (MoRTH) (N24001095)	1-2017	(N.A.) {6/2024}	388.44 (N.A.) {388.44}	240.05	88.16
		907	SELDOH TO PANVAR (MoRTH) (N24001097)	7-2018	5/2020 (N.A.) {5/2020}	404.33 (404.00) {404.33}	140.65	64.00
		908	MHASWAD TO TEMBHURNI (MoRTH) (N24001099)	1-2017	7/2019 (N.A.) {12/2023}	488.60 (N.A.) {488.60}	279.42	76.50
		909	KURUDWADI TO PANDHARPUR (MoRTH) (N24001101)	1-2017	7/2019 (N.A.) {11/2023}	307.63 (N.A.) {307.63}	232.57	96.27
		910	PANDHARPUR TO SANGOLA (MoRTH) (N24001102)	7-2017	7/2019 (N.A.) {12/2023}	218.38 (N.A.) {218.38}	182.63	99.78
		911	PEN TO KHOPOLI (MoRTH) (N24001106)	3-2018	3/2018 (N.A.) {1/2024}	301.39 (302.00) {301.39}	170.12	82.07
		912	PANCHARAL TO MANDANGHAR (MoRTH) (N24001107)	7-2018	5/2020 (N.A.) {5/2020}	381.08 (302.00) {381.08}	45.66	-
		913	KOLHA TO NASRATPUR (MoRTH) (N24001111)	4-2016	4/2019 (N.A.) {8/2024}	281.78 (282.00) {281.78}	77.83	86.77
		914	NASRATPUR TO BARASGAON (MoRTH) (N24001112)	7-2016	9/2019 (N.A.) {3/2024}	406.54 (407.00) {406.54}	274.30	80.07
		915	INDAPUR TO VADPALE (MoRTH) (N24001114)	1-2017	12/2019 (N.A.) {3/2024}	1,202.52 (1,656.94) {1,202.52}	1,450.82	61.42
		916	PAITHAN TO SHIRUR (MoRTH) (N24001122)	3-2017	6/2019 (N.A.) {3/2024}	341.80 (N.A.) {341.80}	226.19	78.60
		917	SHIRUR TO KHARDA (MoRTH) (N24001123)	2-2017	6/2019 (N.A.) {12/2023}	381.77 (N.A.) {381.77}	199.48	83.93
		918	AURANGABAD TO SILLIOD (MoRTH) (N24001124)	2-2017	6/2019 (N.A.) {12/2023}	456.32 (541.93) {456.32}	355.54	94.07
		919	SILLIOD TO FARDAPUR (MoRTH) (N24001125)	2-2017	6/2019 (N.A.) {12/2023}	337.46 (432.98) {337.46}	335.30	91.56
		920	KUMBHARI PHTA TO DEULGAON RAJA (MoRTH) (N24001127)	2-2017	6/2019 (N.A.) {2/2024}	406.51 (N.A.) {406.51}	340.26	87.84

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		921	BHOGAN KHURD TO KASHEDI (MoRTH) (N24001132)	9-2017	6/2021 (N.A.) {12/2023}	743.21 (743.00) {743.21}	911.64	88.69
		922	KANTE TO WAKED (MoRTH) (N24001134)	3-2016	11/2019 (N.A.) {12/2024}	1,230.02 (1,230.00) {1,230.02}	791.80	-
		923	PARLI PIMPLA DAHIGUDA (MoRTH) (N24001138)	2-2017	6/2019 (N.A.) {8/2023}	205.72 (206.00) {205.72}	85.71	100.00
		924	UPGRADATION OF ADHALGAON- JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH (MoRTH) (N24001448)	11-2021	2/2022 (N.A.) {2/2022}	223.35 (N.A.) {223.35}	209.36	87.88
		925	REPANPALLI TO SIRONCHA (MoRTH) (N24001468)	3-2022	6/2022 (N.A.) {6/2024}	282.07 (N.A.) {282.07}	34.65	-
		926	TUNNEL AT KHAMBATKI GHAT SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 (NHAI) (N24001486)	2-2019	2/2022 (N.A.) {10/2025}	493.00 (N.A.) {493.00}	386.52	75.13
		927	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL-ALANDI SECTION (NHAI) (N24001488)	9-2021	9/2023 (N.A.) {4/2025}	618.45 (N.A.) {618.45}	606.34	94.40
		928	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) (NHAI) (N24001493)	12-2022	12/2024 (N.A.) {12/2024}	1,749.86 (N.A.) {1,749.86}	1,807.94	64.34
		929	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 ((NHAI) (N24001495)	11-2022	11/2024 (N.A.) {11/2024}	930.00 (N.A.) {930.00}	325.19	74.90

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		930	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001502)	9-2021	9/2023 (N.A.) {5/2025}	624.45 (580.15) {580.15}	409.76	2.00
		931	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001503)	9-2021	9/2023 (N.A.) {3/2025}	667.66 (666.21) {666.21}	598.65	3.00
		932	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) (NHAI) (N24001504)	5-2022	5/2024 (N.A.) {1/2025}	1,260.00 (N.A.) {1,260.00}	608.72	93.22
		933	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) (NHAI) (N24001505)	3-2022	3/2024 (N.A.) {5/2025}	1,549.02 (N.A.) {1,549.02}	537.10	65.79
		934	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) (NHAI) (N24001506)	2-2022	2/2024 (N.A.) {6/2025}	2,747.00 (N.A.) {2,747.00}	929.38	71.49
		935	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) (NHAI) (N24001507)	11-2022	5/2024 (N.A.) {6/2025}	1,124.00 (N.A.) {1,124.00}	360.76	57.63
		936	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) (NHAI) (N24001508)	11-2022	10/2024 (N.A.) {6/2025}	1,450.00 (N.A.) {1,450.00}	638.66	78.49

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		937	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE) (NHAI) (N24001521)	11-2022	10/2024 (N.A.) {4/2025}	990.00 (N.A.) {990.00}	352.70	64.00
		938	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) (NHAI) (N24001546)	1-2023	1/2025 (N.A.) {1/2025}	1,025.20 (N.A.) {1,025.20}	734.54	42.71
		939	BALANCE WORKS OF 4L PANVEL- INDAPUR SECTION OF NH-66 (OLD NH-17) FROM KM 42.300 (KASU) TO KM 84.600 ((NHAI) (N24001607)	10-2022	5/2024 (N.A.) {12/2025}	332.00 (N.A.) {332.00}	240.77	59.64
		940	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) (NHAI) (N24001608)	9-2021	7/2025 (N.A.) {7/2025}	2,208.68 (N.A.) {2,208.68}	488.60	70.02
		941	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH-66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO (NHAI) (N24001609)	1-2023	12/2023 (N.A.) {3/2025}	151.26 (N.A.) {151.26}	141.21	75.51
		942	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL ? ALANDI S (NHAI) (N24001610)	1-2022	5/2024 (N.A.) {3/2025}	1,833.73 (N.A.) {1,833.73}	524.86	92.11
		943	FOUR LANING OF AURANGABAD- PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA . (NHAI) (N24001795)	10-2022	7/2024 (N.A.) {12/2024}	490.40 (N.A.) {289.00}	275.78	89.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		944	4L OF RAJURA-KORPANA- ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B (NHAI) (N24001796)	3-2022	10/2024 (N.A.) {4/2025}	1,013.33 (1,013.33) {1,111.33}	355.07	62.01
		945	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 (NHAI) (N24001797)	10-2021	1/2024 (N.A.) {3/2025}	815.77 (N.A.) {815.77}	689.51	96.18
		946	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH-53 (NHAI) (N24001798)	2-2021	11/2023 (N.A.) {3/2025}	540.21 (N.A.) {540.21}	433.66	98.98
		947	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J (NHAI) (N24001799)	2-2021	10/2023 (N.A.) {3/2025}	1,166.96 (N.A.) {1,251.00}	1,065.17	80.82
		948	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) (NHAI) (N24001804)	12-2019	9/2022 (N.A.) {6/2025}	1,654.07 (N.A.) {980.00}	835.19	95.53
		949	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG ? II) (NHAI) (N24001834)	5-2023	5/2025 (N.A.) {5/2025}	839.00 (N.A.) {839.00}	433.13	45.75
		950	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG?III) (NHAI) (N24001835)	5-2023	5/2025 (N.A.) {5/2025}	986.00 (N.A.) {986.00}	387.44	46.10
		951	REHABILITATION AND UP- GRADATION TO 4 LANE ROAD WITH PAVED SHOULDER CONFIGURATION OF SECTION FROM UND (MoRTH) (N24001880)	3-2022	7/2025 (N.A.) {7/2025}	778.18 (N.A.) {778.18}	135.78	27.35

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		952	CONSTRUCTION OF NEW FOUR LANE BYPASS TO PARBHANI CITY (PARWA TO ASOLA) KM 463/265 TO KM 481/180 (DES (MoRTH) (N24001882)	3-2022	10/2024 (N.A.) {10/2024}	496.64 (N.A.) {496.64}	0.00	8.00
		953	CONSTRUCTION OF 4 LANE FLYOVER AT NAGPUR RTO CHOWK TO NAGPUR UNIVERSITY CAMPUS FROM CH 2/250 TO 5/10 (MoRTH) (N24001883)	3-2021	3/2024 (N.A.) {4/2024}	478.83 (N.A.) {478.83}	233.48	65.00
		954	REHABILITATION AND UPGRADATION OF SATANA TO MANGRUL (CHANDWAD) SECTION OF NH752 G DESIGN CH: KM 64.0 (MoRTH) (N24001884)	3-2023	5/2025 (N.A.) {5/2025}	428.80 (N.A.) {428.80}	54.11	30.69
		955	REHABILITATION AND UP- GRADATION OF JINTUR- SHIRAD SHAHAPUR SECTION KM 258.300 TO KM 306.300 [DESIGN (MoRTH) (N24001885)	2-2023	12/2024 (N.A.) {12/2024}	414.81 (N.A.) {414.81}	0.00	-
		956	DEVELOPMENT/WIDENING OF TALEGAON ? CHAKAN ? SHIKRAPUR ? NHAVARA SECTION OF NH 548DG (NHAVARA TO CHOU (MoRTH) (N24001886)	10-2022	8/2024 (N.A.) {8/2024}	304.68 (N.A.) {304.68}	97.09	58.78
		957	REHABILITATION AND UPGRADATION OF BHOKARDAN TO KUMBHARI FATA DESIGN CH. (KM 13+500 TO 17+00) AND RAJ (MoRTH) (N24001887)	8-2022	6/2024 (N.A.) {6/2024}	291.37 (N.A.) {291.37}	102.94	78.44
		958	UP-GRADATION OF TIRORA- GONDIA, STATE HIGHWAY FROM EXISTING KM 163+213 (ON SH- 335, TIRORA) TO KM 191+ (MoRTH) (N24001888)	8-2021	4/2023 (N.A.) {5/2024}	288.14 (N.A.) {288.14}	63.01	46.31

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		959	2 LANE + PS PIMPLNER TO SATANA -[DESIGN CHAINAGE KM 21.427 TO 64.00] OF NH-752G] (MoRTH) (N24001889)	9-2019	7/2021 (N.A.) {12/2023}	277.81 (N.A.) {277.81}	148.68	90.00
		960	REHABILITATION AND UPGRADATION OF PARLI TO SIRSALA SECTION OF NH-361F (KM 136+700 TO 115+000) (LENGT (MoRTH) (N24001890)	2-2023	12/2024 (N.A.) {12/2024}	261.82 (N.A.) {261.82}	70.59	46.00
		961	BALANCE WORK OF REHABILITATION AND UP-GRADATION TO NH-166F FROM MAHAD JUNCTION (AT KM 123/400 ON NH- (MoRTH) (N24001891)	7-2021	11/2023 (N.A.) {3/2024}	256.54 (N.A.) {256.54}	80.10	59.66
		962	REHABILITATION AND UPGRADATION OF SHIRAPUR JUNCTION TO SHIVAJI CHOWK (DESIGN CHAINAGE KM. 130+00 TO (MoRTH) (N24001892)	2-2023	12/2024 (N.A.) {12/2024}	245.61 (N.A.) {245.61}	43.39	32.50
		963	2 LANE + PS ASTHAMODE - TIVATYAL [DESIGN CH. KM 24.300 - 62.00] [KM 134.98-172.95 OF NH-63] (MoRTH) (N24001894)	9-2019	7/2021 (N.A.) {12/2023}	228.82 (N.A.) {228.82}	144.54	95.44
		964	REHABILITATION AND UPGRADATION TO TWO LANES WITH PAVED SHOULDER CONFIGURATION FROM WATUR TO CHARTHANA (MoRTH) (N24001895)	11-2021	9/2023 (N.A.) {12/2023}	228.01 (N.A.) {228.01}	103.01	99.00
		965	UPGRADATION AND REHABILITATION OF SECTION OF NH 361 F FROM PARLI (00/000) TO GANGAKHED (30/400) TO (MoRTH) (N24001896)	11-2021	9/2023 (N.A.) {4/2024}	224.44 (N.A.) {224.44}	75.34	45.63

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		966	REHABILITATION AND UP-GRADATION OF SABALKHED TO ASHTI SECTION FROM KM 37+900 TO KM 55+100 AND CHINCH (MoRTH) (N24001902)	12-2022	9/2024 (N.A.) {9/2024}	213.32 (N.A.) {213.32}	20.00	34.00
		967	REHABILITATION AND UP-GRADATION OF MUDKHED TO NANDED SECTION FROM KM. 372+000 TO KM 388+400 OF NH 16 (MoRTH) (N24001903)	8-2022	4/2025 (N.A.) {4/2025}	206.54 (N.A.) {206.54}	21.36	-
		968	KOPARGAON TO SAVALI VIHIR SECTION (MoRTH) (N24001904)	9-2022	7/2024 (N.A.) {7/2024}	195.38 (N.A.) {195.38}	29.59	19.76
		969	CONSTRUCTION OF MAJOR BRIDGE ACROSS MANJRA RIVER NEAR YESGI VILLAGE @ KM, 166/500 ON NH 63 TQ BILOLI (MoRTH) (N24001905)	10-2021	8/2023 (N.A.) {12/2023}	188.69 (N.A.) {188.69}	111.26	95.80
		970	UP-GRADATION TO 4 LANING OF DAULTABAD T-POINT TO MALIWADA [FROM DESIGN KM.0.000 TO KM 4.000] AND UPG (MoRTH) (N24001906)	8-2022	3/2024 (N.A.) {3/2024}	185.59 (N.A.) {185.59}	63.56	48.00
		971	CONSTRUCTION OF SIX LANE FLYOVER AT KATRAJ JUNCTION AT KM, 3/880 OF NH 548-DD (VADGAON - KATRAJ - KO (MoRTH) (N24001907)	6-2021	2/2024 (N.A.) {3/2024}	169.15 (N.A.) {169.15}	36.94	35.96
		972	UPGRADATION OF EXHISTING 2 LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDERS RIGID PAVEMENT FROM DESI (MoRTH) (N24001908)	12-2021	5/2024 (N.A.) {5/2024}	167.97 (N.A.) {167.97}	35.28	36.76

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		973	STRENGTHING AND WIDINING OF EXISTING CARRIAGEWAY TO 10 M IN KM, 156/160 TO 229/160 (TEMBHURNI - KUSL (MoRTH) (N24001909)	11-2021	6/2024 (N.A.) {6/2024}	157.72 (N.A.) {157.72}	55.38	90.41
		974	REHABILITATION AND UPGRADATION OF JAMKHEDE TO SAUTADA SECTION OF NH548 D (FROM KM 195.375 TO KM 208.7 (MoRTH) (N24001910)	9-2022	7/2024 (N.A.) {7/2024}	157.62 (N.A.) {157.62}	13.86	17.03
		975	PANGAON TO DHARMAPURI AND PARALI TO INJEGAON 2L+PS (MoRTH) (N24001911)	3-2018	7/2024 (N.A.) {12/2023}	152.03 (N.A.) {152.03}	81.35	98.00
		976	4L OF INDORA CHOWK TO PACHPAOLI AND AGRASEN CHOWK - ASHOKA CHOWK (NHAI) (N24002071)	3-2023	6/2026 (N.A.) {6/2026}	998.27 (N.A.) {998.27}	263.13	36.01
		977	IMPROVEMENT OF EXISTING ALIGNMENT OF PANDHARPUR TOWN PART BYPASSED SECTION FROM WAKHARI TO LORD VITT (NHAI) (N24002072)	7-2022	10/2025 (N.A.) {10/2025}	150.21 (150.21) {150.21}	20.08	2.00
		978	STRENGTHENING OF 6-LANE PIMPALGAON-NASHIK-GONDE (KM. 380 - KM. 440) SECTION OF NH-3 IN MAHARASHTRA U (NHAI) (N24002137)	2-2024	3/2025 (N.A.) {3/2025}	175.00 (N.A.) {175.00}	144.18	95.00
		979	REHABILITATION/UPGRADATION OF EXISTING HIGHWAY TO 2L+PS/4 LANE OF DHAWALI TO RAJOLI FROM DESIGN KM.1 (MoRTH) (N24002169)	3-2022	9/2025 (N.A.) {9/2025}	316.44 (N.A.) {316.44}	0.00	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		980	REHABILITATION/ UPGRADATION OF EXISTING HIGHWAY TO FOUR LANE STANDARDS IN KURKHEDA TOWN FROM (KM.413 (MoRTH) (N24002170)	3-2022	5/2025 (N.A.) {5/2025}	163.86 (N.A.) {163.86}	0.00	-
		981	REHABILITATION & UP- GRADATION FOR TALERE A?? GAGANBAWDAA?? KOLHAPUR ROAD (NH-166G) STRETCHES START F (MoRTH) (N24002171)	2-2023	4/2025 (N.A.) {4/2025}	249.13 (N.A.) {249.13}	0.00	-
		982	UP-GRADATION TO 4 LANE CONFIGURATION FOR THE WORK OF PETH NAKA TO SANGLI ROAD, NH-166H, FROM KM 0+00 (MoRTH) (N24002172)	2-2023	12/2025 (N.A.) {12/2025}	856.82 (N.A.) {856.82}	0.00	-
		983	REHABILITATION AND UP- GRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF MAHUD SANGOLA ROAD NH (MoRTH) (N24002173)	2-2023	4/2025 (N.A.) {4/2025}	253.78 (N.A.) {253.78}	0.00	-
		984	UP-GRADATION TO FOUR LANE/ TWO LANE WITH PAVED SHOULDERS CONFIGURATION OF KALYAN - MURBAD - MALSHI (MoRTH) (N24002174)	2-2023	8/2026 (N.A.) {8/2026}	984.07 (N.A.) {984.07}	0.00	-
		985	CONSTRUCTION OF FOUR-LANE CONCRETE ROAD FROM POLICE HEADQUARTER GONDIA CITY TO RAWANWADI VILLAGE (BI (MoRTH) (N24002175)	2-2023	8/2025 (N.A.) {8/2025}	328.11 (N.A.) {328.11}	0.00	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		986	REHABILITATION/UP GRADATION OF KARANJA ? KHERDA - MURTIZAPUR SECTION TO 4LANE+PAVED SHOULDER STANDA (MoRTH) (N24002176)	3-2023	2/2026 (N.A.) {2/2026}	594.44 (N.A.) {594.44}	0.00	-
		987	REHABILITATION / UPGRADATION TO 4 LANE WITH PAVED SHOULDER OF EXISTING SECTION IN SILLOD TOWN WITH D (MoRTH) (N24002177)	3-2023	7/2025 (N.A.) {7/2025}	153.79 (N.A.) {153.79}	0.00	-
		988	REHABILITATION, UPGRADATION & WIDENING OF EXISTING HIGHWAY TO RIGID PAVEMENT 2 LANE WITH PAVED SHOUL (MoRTH) (N24002178)	2-2023	7/2026 (N.A.) {7/2026}	723.13 (N.A.) {723.13}	0.00	-
	URBAN DEVELOPMENT	989	MUMBAI METRO LINE 3 (COLABA- BANDRA-SEEPZ) (MMRCL) (N28000086)	7-2013	3/2020 (N.A.) {12/2023}	23,136.00 (N.A.) {37,276.00}	23,687.33	87.20
		990	PUNE METRO RAIL PROJECT (PHASE 1) (MMRC) (N28000121)	12-2016	11/2021 (N.A.) {9/2024}	11,420.00 (13,656.22) {13,656.22}	12,944.30	100.00
		991	NAGPUR METRO RAIL PROJECT PHASE II (NMRCL) (N28000155)	12-2022	12/2027 (N.A.) {12/2027}	6,708.00 (N.A.) {6,708.00}	599.66	18.36
		992	PCMC NIGDI PROJECT EXTENSION OF CORRIDOR 1 OF PUNE METRO PHASE 1 (MMRC) (N28000157)	10-2023	1/2027 (N.A.) {1/2027}	910.18 (N.A.) {910.18}	55.14	10.34
		993	PUNE METRO PHASE-1 EXTENSION FROM SWARGATE TO KATRAJ (MMRC) (N28000160)	9-2024	3/2029 (N.A.) {3/2029}	2,954.53 (N.A.) {2,954.53}	12.99	1.00
MANIPUR	CIVIL AVIATION	994	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (N.A.) {3/2026}	499.00 (N.A.) {499.00}	134.58	38.16

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>RAILWAYS</u>	995	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	3/2011 (N.A.) {12/2028}	4,454.17 (12,274.06) {19,517.70}	15,096.58	81.50
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	996	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (N.A.) {5/2025}	292.24 (N.A.) {292.24}	127.86	88.64
		997	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (N.A.) {5/2025}	365.53 (N.A.) {365.53}	156.31	77.36
		998	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (N.A.) {5/2025}	167.95 (204.12) {167.95}	88.05	69.89
		999	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (N.A.) {5/2025}	177.76 (N.A.) {177.76}	89.67	80.53
		1000	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (N.A.) {6/2025}	379.39 (N.A.) {379.39}	198.61	57.91
		1001	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (N.A.) {5/2025}	226.32 (N.A.) {226.32}	96.41	73.82
		1002	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (N.A.) {3/2025}	188.36 (N.A.) {188.36}	126.71	99.02
		1003	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3-2021	12/2022 (N.A.) {3/2026}	195.14 (N.A.) {195.14}	61.81	50.79
		1004	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (N.A.) {5/2025}	234.08 (N.A.) {234.08}	139.45	90.69

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1005	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (N.A.) {5/2025}	211.70 (N.A.) {211.70}	68.35	60.24
		1006	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (N.A.) {7/2025}	467.00 (N.A.) {467.00}	188.84	76.37
		1007	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (N.A.) {1/2025}	185.80 (N.A.) {185.80}	114.69	100.00
		1008	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (N.A.) {5/2025}	483.87 (N.A.) {483.87}	278.89	92.43
		1009	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (N.A.) {3/2025}	198.77 (N.A.) {198.77}	115.53	97.54
		1010	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (N.A.) {5/2025}	673.27 (N.A.) {673.27}	376.21	77.71
		1011	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (N.A.) {6/2025}	477.86 (N.A.) {477.86}	239.80	83.92
		1012	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (N.A.) {4/2025}	311.18 (N.A.) {311.18}	175.90	78.27
		1013	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (N.A.) {2/2025}	467.41 (N.A.) {467.41}	264.24	100.00
		1014	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (N.A.) {7/2025}	579.63 (N.A.) {579.63}	157.89	63.65
		1015	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (N.A.) {3/2025}	310.76 (N.A.) {310.76}	129.15	90.86
		1016	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (N.A.) {10/2025}	410.68 (N.A.) {410.68}	124.31	61.42

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1017	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (N.A.) {9/2025}	504.76 (N.A.) {504.76}	148.02	67.30
		1018	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (N.A.) {3/2025}	152.11 (N.A.) {152.11}	66.00	95.98
		1019	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (N.A.) {9/2025}	315.56 (N.A.) {315.56}	110.91	74.92
		1020	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (N.A.) {12/2025}	760.16 (N.A.) {760.16}	102.90	46.30
		1021	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (N.A.) {3/2026}	578.98 (N.A.) {578.98}	106.92	56.70
		1022	MARREM KHULLEN TO JESSAMI SECTION IMPHAL- UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	0.00	4.00
		1023	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	0.00	9.88
MEGHALAYA	DEPARTMENT OF HIGHER EDUCATION	1024	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (N.A.) {7/2025}	484.32 (429.70) {429.70}	292.55	81.00
	ROAD TRANSPORT AND HIGHWAYS	1025	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (N.A.) {3/2025}	553.51 (610.09) {553.51}	383.57	78.99

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1026	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM ((NHIDCL) (N24001313)	11-2020	12/2023 (N.A.) {10/2025}	351.12 (N.A.) {351.12}	264.92	45.57
		1027	IMPROVEMENT/WIDENING TO 2-L LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	406.62	22.29
		1028	IMPROVEMENT/WIDENING TO 2-L LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	200.09	17.10
		1029	IMPROVEMENT/WIDENING TO 2-L LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	73.87	12.15
		1030	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI- RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (N.A.) {2/2025}	157.86 (146.92) {157.86}	149.62	100.00
		1031	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3-2021	12/2022 (N.A.) {2/2025}	260.21 (N.A.) {260.21}	232.62	99.63
		1032	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (N.A.) {3/2025}	302.88 (N.A.) {302.88}	224.39	95.20

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1033	REHABILITATION AND UP GRADATION OF NONGSTOIN- RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (N.A.) {12/2025}	359.86 (N.A.) {359.86}	224.90	82.99
		1034	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11-2021	6/2024 (N.A.) {3/2025}	283.50 (N.A.) {283.50}	225.92	87.52
		1035	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	185.32	16.55
		1036	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	255.10	16.00
		1037	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	284.57	16.59
<u>MIZORAM</u>	<u>RAILWAYS</u>	1038	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,774.22	94.52
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1039	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {3/2025}	519.09 (N.A.) {785.65}	658.71	95.75
		1040	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {5/2024}	640.07 (N.A.) {1,286.35}	1,192.26	98.90

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1041	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4-2017	6/2023 (N.A.) {3/2024}	642.96 (N.A.) {988.23}	720.30	99.34
		1042	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {3/2025}	473.18 (N.A.) {688.25}	525.62	92.01
		1043	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {3/2025}	537.82 (N.A.) {789.05}	753.11	95.16
		1044	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {3/2025}	518.53 (N.A.) {906.76}	826.22	95.15
		1045	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {3/2025}	404.29 (N.A.) {750.32}	613.21	93.57
		1046	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {3/2025}	428.11 (N.A.) {746.39}	578.81	91.25

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1047	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL- TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9-2020	10/2022 (N.A.) {4/2025}	275.02 (N.A.) {247.25}	231.64	81.30
		1048	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH- 06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	262.50	99.37
		1049	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH- 06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {6/2025}	292.24 (N.A.) {331.17}	287.30	93.15
		1050	DULTE- KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355)	3-2021	12/2022 (N.A.) {3/2024}	374.39 (N.A.) {318.92}	286.49	100.00
		1051	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (N.A.) {12/2025}	233.25 (N.A.) {233.25}	172.09	64.55
		1052	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	449.15	52.84
		1053	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	343.91	50.60
		1054	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (N.A.) {5/2024}	492.94 (N.A.) {492.94}	344.85	86.80
		1055	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWLRAWG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	303.25	60.68
		1056	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	210.02	58.76

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1057	ZORINPUI- HMAWNGBU- LONGMASU (NH-502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	33.56	0.30
MULTI STATE	COAL	1058	NILJAI EXPANSION (DEEP) OC (3.5 MTY) (WCL) (N06000154)	8-2016	3/2022 (N.A.) {3/2025}	319.76 (319.76) {319.76}	183.67	98.00
		1059	BINA KAKRI AMALGAMATION OCP 14 MTPA (NCL) (N06000192)	8-2020	3/2024 (N.A.) {3/2025}	836.42 (N.A.) {836.42}	715.70	57.03
	DPIIT	1060	NATIONAL INDUSTRIAL CORRIDOR PROJECT (DMIC FOR DPIIT) (N40000001)	9-2011	3/2027 (N.A.) {3/2032}	20,084.00 (26,684.00) {26,684.00}	11,217.21	50.99
	PETROLEUM	1061	KOCHI-KOOTTANAD-BANGALORE- MANGALORE PIPELINE PHASE-II (GAIL) (N16000285)	6-2009	12/2012 (N.A.) {3/2026}	2,915.00 (5,909.00) {5,909.00}	4,160.90	93.50
		1062	SRIKAKULAM ANGUL PIPELINE PROJECT (GAIL) (N16000388)	9-2019	7/2022 (N.A.) {6/2025}	2,658.34 (N.A.) {2,658.34}	2,104.80	93.90
		1063	DHAMRA HALDIA PIPELINE PROJECT (GAIL) (N16000391)	3-2020	11/2022 (N.A.) {12/2025}	1,030.65 (N.A.) {1,030.65}	810.40	85.60
		1064	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT (GAIL) (N16000398)	6-2020	5/2023 (N.A.) {6/2025}	7,844.25 (N.A.) {7,844.25}	6,111.90	92.60
		1065	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS (IOCL) (N16000426)	6-2019	12/2029 (N.A.) {3/2030}	169.00 (N.A.) {169.00}	75.14	20.00
		1066	NORTH EAST GAS GRID (IGGL) (N16000439)	11-2020	3/2024 (N.A.) {3/2027}	9,265.00 (9,265.00) {9,265.00}	5,746.93	84.00
		1067	GURDASPUR JAMMU PIPELINE (GAIL) (N16000531)	7-2023	7/2026 (N.A.) {7/2026}	521.92 (521.92) {521.92}	100.20	27.30

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	1068	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P (PGCIL) (N18000249)	12-2014	12/2018 (N.A.) {3/2025}	4,754.42 (9,129.32) {9,129.32}	7,009.75	79.50
		1069	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES (PGCIL) (N18000250)	12-2014	12/2018 (N.A.) {6/2025}	5,111.33 (6,700.00) {6,700.00}	5,066.06	95.60
		1070	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM (PGCIL) (N18000328)	2-2022	4/2025 (N.A.) {4/2025}	318.12 (N.A.) {318.12}	157.75	94.00
		1071	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM (PGCIL) (N18000330)	3-2022	12/2024 (N.A.) {7/2025}	288.71 (N.A.) {288.71}	143.79	48.00
		1072	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000331)	2-2022	9/2023 (N.A.) {5/2025}	359.47 (N.A.) {359.47}	290.16	94.00
		1073	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000332)	5-2022	11/2023 (N.A.) {5/2025}	1,666.00 (N.A.) {1,666.00}	1,442.62	86.00
		1074	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B (PGCIL) (N18000337)	7-2022	6/2023 (N.A.) {6/2025}	4,546.26 (N.A.) {4,546.26}	2,624.35	87.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1075	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C (PGCIL) (N18000338)	7-2022	3/2025 (N.A.) {3/2025}	186.19 (N.A.) {186.19}	70.53	91.00
		1076	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION (PGCIL) (N18000343)	10-2022	10/2025 (N.A.) {10/2025}	307.87 (N.A.) {307.87}	163.31	80.00
		1077	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART- A PART B (PGCIL) (N18000352)	3-2023	11/2024 (N.A.) {5/2025}	3,546.94 (N.A.) {3,546.94}	2,000.14	84.00
		1078	ER WR TRANSMISSION LIMITED (PGCIL) (N18000353)	3-2023	3/2025 (N.A.) {3/2025}	281.16 (N.A.) {281.16}	99.14	84.00
	RAILWAYS	1079	NANGALDAM-TALWARA(NL),NR (NR) (220100188)	3-1981	7/2012 (N.A.) {1/2027}	450.00 (N.A.) {2,017.96}	1,544.51	70.00
		1080	LALITPUR-SATNA-REWA- SINGRULI NL, (NCR) (WCR) (220100232)	9-1998	5/2008 (N.A.) {3/2025}	247.66 (63.57) {8,248.50}	2,520.04	43.00
		1081	CHHAPRA-BALLIA UP (NER) (N22000134)	3-2013	1/2019 (N.A.) {12/2025}	295.00 (954.00) {1,025.00}	999.78	95.00
		1082	CHOTTAUDEPUR-DHAR(NL) (WR) (N22000138)	4-2007	3/2022 (N.A.) {12/2027}	1,347.26 (1,793.63) {1,793.63}	1,586.58	58.00
		1083	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) (WR) (N22000139)	4-2007	3/2022 (N.A.) {2/2027}	1,640.04 (1,873.10) {2,873.11}	2,679.75	58.00
		1084	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) (NCR) (N22000148)	4-2011	3/2022 (N.A.) {12/2024}	2,912.96 (N.A.) {3,845.60}	1,024.32	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1085	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR (NCR) (N22000158)	4-2010	(N.A.) {12/2026}	2,030.50 (746.83) {746.83}	152.47	31.00
		1086	NEW BONGAIGAON-RANGIA- KAMAKGHYA DOUBLING (NFR) (N22000183)	4-2013	3/2019 (N.A.) {10/2024}	1,798.00 (N.A.) {2,832.35}	3,536.27	99.50
		1087	NEW BG LINE FROM BALURGHAT TO HILLY NFR (NFR) (N22000206)	4-2010	3/2020 (N.A.) {3/2027}	242.22 (N.A.) {1,206.60}	396.23	5.00
		1088	NEW BG LINE FROM JAGBANI TO BIRATNAGAR (NFR) (N22000207)	4-2010	(N.A.) {12/2026}	241.52 (485.96) {485.96}	365.14	86.21
		1089	MURKONGSELEK-PASIGHAT NL (NFR) (N22000208)	4-2011	3/2020 (N.A.) {11/2025}	414.84 (N.A.) {1,252.49}	687.63	43.00
		1090	PIRPAINTI-JASIDIH (ER) (N22000219)	4-2013	3/2022 (N.A.) {3/2028}	915.98 (N.A.) {2,610.84}	857.40	45.00
		1091	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION (SCR) (N22000261)	4-2012	3/2023 (N.A.) {3/2025}	1,856.95 (N.A.) {1,952.68}	1,601.49	-
		1092	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL (NR) (N22000274)	4-2007	(N.A.) {}	336.91 (N.A.) {791.39}	572.99	-
		1093	RAYADURGA-TUMKUR NL (SWR) (N22000279)	4-2007	(N.A.) {2/2028}	2,062.30 (2,495.59) {2,495.59}	1,598.00	60.00
		1094	HOTGI-KUDGI-GADAG (SWR) (N22000333)	3-2015	3/2019 (N.A.) {2/2026}	1,614.59 (1,877.81) {2,458.87}	2,477.19	89.00
		1095	KAZIPET-BALHRSHA (SCR) (N22000367)	4-2015	3/2021 (N.A.) {1/2025}	2,063.03 (N.A.) {2,909.00}	2,743.71	-
		1096	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT (NHSRCL) (N22000463)	12-2015	12/2023 (N.A.) {8/2027}	108,000.00 (N.A.) {108,000.00}	72,257.00	49.80

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1097	WESTERN DEDICATED FREIGHT CORRIDOR (DFCC) (N22000464)	11-2007	3/2020 (N.A.) {3/2020}	16,592.00 (51,101.00) {51,101.00}	47,476.00	83.00
		1098	CHANDIGARH-BADDI (NR) (N22000467)	4-2007	3/2023 (N.A.) {7/2026}	328.14 (1,540.14) {1,540.14}	932.77	23.00
		1099	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) (SER) (N22000506)	3-2019	5/2023 (N.A.) {6/2026}	1,866.31 (N.A.) {1,866.31}	1,819.98	58.00
	ROAD TRANSPORT AND HIGHWAYS	1100	VARANASI-AURANGABAD KM.786 TO KM.978.40 (NHAI) (N24000182)	9-2011	3/2014 (N.A.) {9/2024}	2,848.00 (N.A.) {3,241.56}	3,901.66	88.10
		1101	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 (NHAI) (N24001628)	11-2021	2/2025 (N.A.) {8/2025}	2,155.95 (N.A.) {2,155.95}	1,262.48	60.28
		1102	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O (NHAI) (N24001629)	4-2022	11/2024 (N.A.) {3/2025}	796.65 (N.A.) {796.65}	382.42	78.15
	SHIPPING AND PORTS	1103	JAL MARG VIKAS PROJECT (IWAI) (N25000072)	1-2018	3/2023 (N.A.) {12/2025}	5,369.18 (5,061.15) {5,061.15}	3,314.48	66.01
	TELECOMMUNICA TIONS	1104	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (N26000114)	3-2020	6/2021 (N.A.) {6/2025}	461.42 (461.42) {461.42}	165.04	81.00
		1105	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (IPMPLS) NETWORK and (BSNL) (N26000115)	3-2023	3/2024 (N.A.) {3/2025}	239.60 (N.A.) {239.60}	174.71	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1106	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (N26000116)	5-2023	8/2024 (N.A.) {3/2025}	645.13 (N.A.) {645.13}	330.56	85.63
		1107	PLANNIN ENGINEERING SUPPLY INSTALLATION TESTING COMMISSIONING INTEGARTION and ANNUAL MAINTENANCE OF (BSNL) (N26000117)	6-2023	6/2025 (N.A.) {6/2025}	24,556.35 (24,544.55) {24,544.55}	6,822.97	82.92
		1108	OPTICAL TRANSPORT NETWORK (OTN) PH-4 IN BSNL (BSNL) (N26000118)	2-2024	8/2025 (N.A.) {8/2025}	810.99 (N.A.) {810.99}	425.00	80.32
	<u>URBAN DEVELOPMENT</u>	1109	DELHI GHAZIABAD MEERUT RRTS CORRIDOR (NCRTC) (N28000134)	3-2019	6/2025 (N.A.) {6/2025}	30,274.00 (N.A.) {30,274.00}	24,182.03	83.40
<u>NAGALAND</u>	<u>PETROLEUM</u>	1110	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	2.90	15.50
	<u>RAILWAYS</u>	1111	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	4,250.21	66.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1112	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (N.A.) {2/2025}	373.07 (534.41) {534.41}	382.50	99.81
		1113	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (N.A.) {9/2025}	429.52 (794.74) {794.74}	311.07	88.39

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1114	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (N.A.) {3/2025}	387.00 (688.12) {688.12}	388.86	99.64
		1115	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (N.A.) {3/2025}	500.09 (698.81) {698.81}	373.62	98.05
		1116	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3-2018	9/2022 (N.A.) {7/2024}	285.68 (N.A.) {285.68}	193.90	99.90
		1117	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (N.A.) {8/2025}	215.79 (N.A.) {215.79}	123.39	58.37
		1118	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (N.A.) {9/2025}	323.98 (N.A.) {323.98}	106.68	44.38
		1119	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3-2017	11/2020 (N.A.) {2/2023}	217.35 (N.A.) {217.35}	214.18	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1120	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3-2019	12/2022 (N.A.) {1/2023}	237.51 (N.A.) {237.51}	215.47	100.00
		1121	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (N.A.) {6/2026}	277.44 (N.A.) {277.44}	166.31	65.92
		1122	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (N.A.) {6/2025}	159.85 (342.29) {159.85}	89.88	23.30
		1123	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (N.A.) {2/2025}	202.36 (N.A.) {202.36}	73.20	27.78
		1124	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9-2020	4/2022 (N.A.) {12/2025}	315.63 (N.A.) {315.63}	95.84	74.23
		1125	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	62.50
		1126	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (N.A.) {6/2023}	278.95 (N.A.) {278.95}	166.29	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1127	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (N.A.) {11/2025}	330.80 (N.A.) {330.80}	141.88	84.76
		1128	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (N.A.) {11/2026}	232.29 (350.88) {232.29}	65.36	11.52
		1129	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3-2020	6/2022 (N.A.) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.40
		1130	PEREN-DIMAPUR SECTION PKG- 2 (NHIDCL) (N24001406)	7-2021	3/2023 (N.A.) {9/2025}	258.52 (N.A.) {258.52}	80.21	71.80
		1131	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	56.25	48.48
		1132	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (N.A.) {6/2026}	252.19 (N.A.) {252.19}	11.80	10.38
		1133	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (N.A.) {3/2025}	297.24 (N.A.) {297.24}	121.54	73.15
		1134	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (N.A.) {3/2025}	226.44 (N.A.) {226.44}	136.74	98.71

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1135	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3-2022	12/2024 (N.A.) {1/2025}	605.36 (N.A.) {605.36}	269.26	100.00
		1136	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (N.A.) {6/2025}	192.93 (N.A.) {192.93}	94.72	83.42
		1137	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {6/2025}	177.77 (199.02) {199.02}	38.12	51.33
		1138	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO- AVANGKHU SECTION OF NH- 202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	62.60	40.26
		1139	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO- AVANGKHU SECTION OF NH- 202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	25.94	18.29
		1140	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO- AVANGKHU SECTION OF NH- 202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	121.55	49.22
ODISHA	COAL	1141	BASUNDHARA (WEST) OC EXTN(7.00 MTY) (MCL) (N06000112)	5-2014	3/2019 (N.A.) {3/2027}	479.15 (N.A.) {479.15}	267.05	62.00
		1142	SIARMAL OCP (40.00MTY) (MCL) (N06000113)	2-2021	3/2029 (N.A.) {3/2029}	5,194.96 (N.A.) {5,194.96}	3,430.66	42.80
		1143	INTEGRATED LAKHANPUR- BELPAHAR-LILARI OCP (MCL) (N06000167)	5-2018	3/2027 (N.A.) {3/2027}	2,434.75 (N.A.) {2,434.75}	1,877.25	55.10

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1144	REORGANISATION OF BHARATPUR OCP EXPANSION (MCL) (N06000171)	11-2018	3/2029 (N.A.) {3/2029}	2,838.87 (N.A.) {2,838.87}	1,736.10	44.60
		1145	TALABIRA II AND III OCP (NLC) (N06000189)	7-2017	1/2027 (N.A.) {1/2027}	2,401.07 (N.A.) {2,401.07}	1,494.91	58.00
		1146	NAINI COAL MINE (SCCL) (N06000203)	3-2020	3/2024 (N.A.) {3/2026}	494.30 (N.A.) {494.30}	491.33	70.00
		1147	GOPALJI-KANIHA OCP (MCL) (N06000229)	4-2022	3/2028 (N.A.) {3/2028}	6,107.87 (N.A.) {6,107.87}	1,653.60	16.80
		1148	BALARAM EXPANSION OCP (MCL) (N06000230)	8-2020	3/2029 (N.A.) {3/2029}	3,504.21 (N.A.) {3,504.21}	985.17	49.90
		1149	SUBHADRA OCP (MCL) (N06000249)	5-2021	3/2029 (N.A.) {3/2029}	1,693.81 (N.A.) {1,693.81}	1,172.21	39.20
		1150	NLC TALABIRA THERMAL POWER PROJECT (PHASE-1: 3 X 800 MW) (NLC) (N06000270)	1-2024	5/2029 (N.A.) {3/2030}	27,213.00 (N.A.) {27,213.00}	1,437.76	1.55
		1151	RPR OF HINGULA EXPANSION OCP (MCL) (N06000285)	11-2022	3/2029 (N.A.) {3/2029}	1,561.85 (N.A.) {1,561.85}	0.00	3.57
		1152	BHUBANESWARI EXPANSION OCP (MCL) (N06000286)	3-2024	3/2031 (N.A.) {3/2031}	5,366.28 (N.A.) {5,366.28}	0.00	3.39
		1153	BALABHADRA OCP (MCL) (N06000288)	4-2023	3/2030 (N.A.) {3/2030}	978.44 (N.A.) {978.44}	208.37	1.00
		1154	INTEGRATED KULDA GARJANBAHAL OCP (MCL) (N06000289)	4-2023	3/2030 (N.A.) {3/2030}	3,563.50 (N.A.) {3,563.50}	4.92	1.00
	DEPARTMENT OF HIGHER EDUCATION	1155	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR (CPWD EDUCATION) (N28000126)	1-2019	3/2022 (N.A.) {6/2025}	790.79 (N.A.) {790.79}	685.13	95.00
	MINES	1156	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT (NALCO) (N10000010)	12-2014	4/2021 (N.A.) {9/2025}	4,103.00 (5,677.40) {5,677.40}	3,533.19	71.39

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1157	UTKAL D AND E COAL BLOCK (NALCO) (N10000011)	5-2016	1/2020 (N.A.) {3/2024}	534.00 (N.A.) {1,021.97}	773.15	84.50
		1158	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (NALCO) (N10000012)	12-2015	11/2020 (N.A.) {8/2027}	355.00 (581.00) {581.00}	130.79	12.60
		1159	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN (NALCO) (N10000013)	11-2017	4/2021 (N.A.) {5/2025}	483.00 (483.00) {483.00}	372.43	88.22
		1160	POTTANGI BAUXITE MINES (NALCO) (N10000016)	5-2018	12/2024 (N.A.) {5/2025}	1,437.00 (N.A.) {1,381.00}	649.96	50.70
		1161	CONSTRUCTION OF RED MUD POND - II AT NALCO DAMANJODI ODISHA (NALCO) (N10000017)	9-2019	3/2023 (N.A.) {5/2024}	225.79 (N.A.) {270.66}	5.00	100.00
	PETROLEUM	1162	ADDITIONAL STORAGE TANKS AT PARADIP (IOCL) (N16000361)	11-2018	9/2021 (N.A.) {3/2025}	462.30 (552.44) {552.44}	493.72	97.40
		1163	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY (IOCL) (N16000396)	7-2020	1/2024 (N.A.) {4/2025}	13,805.00 (N.A.) {13,805.00}	7,123.18	88.10
	POWER	1164	EASTERN REGION EXPANSION SCHEME XXIX (PGCIL) (N18000351)	3-2023	11/2025 (N.A.) {11/2025}	524.04 (N.A.) {524.04}	329.97	84.00
		1165	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) (NTPC) (N18000364)	8-2022	5/2027 (N.A.) {12/2027}	11,844.00 (N.A.) {12,539.00}	2,638.09	19.70

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	1166	KHURDA ROAD- BOLANGIR(NL)ECOR (ECOR) (220100284)	4-1994	3/2009 (N.A.) {12/2026}	2,923.13 (3,791.66) {5,089.37}	4,485.68	83.00
		1167	TALCHER- BIMALAGARH(NL)(ECOR) (ECOR) (220100328)	4-2005	6/2021 (N.A.) {3/2026}	810.78 (N.A.) {1,928.07}	1,571.33	40.00
		1168	BHADRAK - NERGUNDI 3RD LINE (ECOR) (N22000316)	3-2013	10/2020 (N.A.) {10/2025}	843.04 (1,284.39) {1,284.39}	1,200.57	75.00
		1169	JAGADALPUR-KORAPUT DOUBLING (ECOR) (N22000376)	4-2015	3/2022 (N.A.) {3/2022}	1,547.38 (N.A.) {1,547.38}	1,246.26	92.00
		1170	KORAPUT - SINGAPUR ROAD DOUBLING (ECOR) (N22000379)	4-2015	3/2022 (N.A.) {3/2026}	2,361.74 (2,361.74) {2,361.74}	1,690.94	75.00
		1171	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE (ECOR) (N22000380)	4-2015	11/2018 (N.A.) {8/2026}	701.61 (N.A.) {810.02}	548.68	-
		1172	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. (ECOR) (N22000381)	4-2015	12/2018 (N.A.) {11/2025}	1,172.92 (N.A.) {2,022.75}	1,837.45	75.00
		1173	VIZIANAGARAM - SAMABALPUR 3RD LINE (RVNL) (N22000409)	1-1991	12/2024 (N.A.) {12/2026}	2,335.67 (N.A.) {4,803.16}	4,691.52	-
		1174	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL (IRCON) (N22000418)	4-2016	3/2020 (N.A.) {12/2025}	5,200.00 (N.A.) {5,200.00}	0.00	17.40
		1175	JEYPORE MALKANGIRI NEW LINE (ECOR) (N22000516)	2-2018	7/2033 (N.A.) {7/2033}	642.69 (N.A.) {642.69}	200.33	0.10
		1176	JEYPORE NABARANGPUR NEWLINE (ECOR) (N22000517)	7-2017	7/2028 (N.A.) {7/2028}	499.99 (N.A.) {747.91}	0.00	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1177	TALCHER - ANGUL NEW LINE WITH Y CONNECTION AT TALCHER (ECOR) (N22000518)	7-2018	12/2026 (N.A.) {12/2026}	278.96 (495.00) {494.62}	29.50	-
		1178	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (ECOR) (N22000519)	8-2022	8/2027 (N.A.) {8/2027}	190.90 (N.A.) {190.90}	10.00	-
		1179	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION (ECOR) (N22000520)	9-2022	9/2027 (N.A.) {7/2027}	189.93 (N.A.) {189.93}	5.19	-
		1180	BRUNDAMAL-JHARSUGUDA- FLYOVER CONNECTION FOR JOINING DN LINE (ECOR) (N22000521)	12-2009	12/2026 (N.A.) {12/2026}	48.44 (N.A.) {297.00}	295.90	10.00
		1181	BAGHUAPAL FLY OVER (20 KM) (ECOR) (N22000522)	8-2019	8/2027 (N.A.) {8/2027}	183.00 (257.97) {257.97}	0.60	-
		1182	ROURKELA-BONDAMUNDA A- CABIN 5TH LINE (10 KM) (UMBRELLA WORK PB#57/2019- 20/NR) (SER) (N22000571)	9-2022	9/2026 (N.A.) {2/2026}	209.75 (N.A.) {244.99}	55.28	10.00
	ROAD TRANSPORT AND HIGHWAYS	1183	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S (NHAI) (N24000619)	9-2016	8/2019 (N.A.) {3/2025}	2,510.04 (N.A.) {2,510.04}	1,104.98	99.00
		1184	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO (NHAI) (N24000715)	12-2017	7/2020 (N.A.) {3/2025}	686.65 (565.00) {686.65}	574.26	95.00
		1185	REHABILITATION AND UP- GRADATION OF EXISTING 2- LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE ((NHAI) (N24000733)	1-2018	8/2022 (N.A.) {6/2025}	633.68 (492.83) {633.68}	560.38	84.34

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1186	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG (NHAI) (N24000734)	1-2018	8/2021 (N.A.) {3/2025}	614.48 (503.30) {757.12}	664.48	99.00
		1187	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON (NHAI) (N24000736)	1-2018	9/2020 (N.A.) {3/2025}	686.65 (504.09) {1,015.16}	435.85	92.50
		1188	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141) (NHAI) (N24000738)	1-2018	9/2021 (N.A.) {3/2025}	999.00 (1,152.70) {1,152.70}	498.82	79.92
		1189	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) ((NHAI) (N24000739)	1-2018	6/2021 (N.A.) {3/2025}	503.88 (609.03) {609.03}	536.89	96.69
		1190	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. (MoRTH) (N24000912)	8-2016	2/2017 (N.A.) {4/2025}	287.70 (N.A.) {293.66}	274.88	98.66
		1191	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA (MoRTH) (N24000914)	12-2016	8/2018 (N.A.) {4/2025}	223.50 (N.A.) {223.50}	220.50	92.00
		1192	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA (MoRTH) (N24000917)	3-2018	8/2018 (N.A.) {4/2025}	199.16 (N.A.) {199.16}	155.44	98.00
		1193	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 (NHAI) (N24001647)	8-2020	3/2022 (N.A.) {3/2025}	200.00 (154.73) {154.73}	137.04	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1194	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 (NHAI) (N24001665)	12-2021	10/2024 (N.A.) {10/2025}	1,592.00 (1,592.00) {1,592.00}	1,022.21	73.22
		1195	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE-OD (NHAI) (N24001666)	12-2021	9/2024 (N.A.) {8/2025}	714.00 (714.00) {714.00}	525.87	85.08
		1196	6L GREENFIELD KALIAGURA ? BAUNSAGUAR SECTION OF NH- 130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG (NHAI) (N24001667)	9-2021	5/2024 (N.A.) {10/2025}	1,734.00 (1,734.00) {1,734.00}	1,165.28	81.35
		1197	6L OF BADAKUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130-CD (PACKAGE ? OD-3) (NHAI) (N24001668)	3-2021	4/2024 (N.A.) {6/2025}	1,249.00 (N.A.) {1,249.00}	462.56	80.16
		1198	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH-130-CD (PACKAGE ? OD-1) (NHAI) (N24001669)	2-2021	3/2024 (N.A.) {6/2025}	586.00 (N.A.) {586.00}	213.49	75.20
		1199	6L OF KARKI ? KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH-130-CD (PACKAGE ? OD-4) (NHAI) (N24001670)	2-2021	3/2024 (N.A.) {3/2025}	593.00 (N.A.) {593.00}	282.15	90.45
		1200	6L OF HATIBENA - BADAKUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE ? OD-2) (NHAI) (N24001671)	2-2021	3/2024 (N.A.) {3/2025}	925.00 (N.A.) {925.00}	445.07	94.91

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1201	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE ? (NHAI) (N24001678)	8-2021	6/2024 (N.A.) {8/2025}	1,460.00 (1,460.00) {1,460.00}	902.44	85.08
		1202	CONSTRUCTION OF ROAD FROM KM 0/0 TO 72/0 OF NH-26 SUCH AS 4 LANE FROM KM 0/0 TO 21/0 (BARGARH TO BAR (MoRTH) (N24001857)	6-2020	12/2023 (N.A.) {5/2025}	414.24 (N.A.) {414.24}	287.48	97.00
		1203	WIDENING AND STRENGTHENING TO 2L+PS INCLUDING LA OF KANDARPUR- BALIKUDA FROM KM 277/500 TO 318/970 OF (MoRTH) (N24001858)	3-2022	6/2025 (N.A.) {6/2025}	499.79 (N.A.) {499.79}	262.85	36.83
		1204	CONSTRUCTION OF BYPASS ON NH-59 FROM KM 336/350 TO 349/910 (13.56 KM) NEAR BERHAMPUR TOWN INCLUDING (MoRTH) (N24001859)	3-2021	3/2024 (N.A.) {5/2025}	196.94 (N.A.) {196.94}	66.09	15.00
		1205	CONSTRUCTION OF BYPASS TO NAYAGARH TOWN FROM KM 235.469 TO 252.482 OF NH-57 INCLUDING LAND ACQUISITI (MoRTH) (N24001860)	1-2022	4/2025 (N.A.) {5/2025}	300.33 (N.A.) {300.33}	188.27	50.00
		1206	CONSTRUCTION OF BYPASS TO KHORDHA TOWN FROM KM 294/000 TO 300/300 ON NH-57 INCLUDING LA IN THE STATE (MoRTH) (N24001861)	2-2022	11/2024 (N.A.) {5/2025}	157.49 (N.A.) {157.49}	63.33	31.74
		1207	CONSTRUCTION OF BYPASS ROAD TO BALANGIR TOWN FROM KM 72/400 (DESING KM 0/0) TO KM 79/800 (DESIGN KM (MoRTH) (N24001862)	2-2022	10/2025 (N.A.) {11/2025}	238.78 (N.A.) {238.78}	28.40	12.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1208	CONSTRUCTION OF 5 HL BRIDGES AT KM 379/000 (PANGAM), KM 439/400 (POTTERU), KM 444/237 (KONGURUKONDA) (MoRTH) (N24001863)	3-2021	6/2024 (N.A.) {6/2025}	154.05 (N.A.) {154.05}	47.47	25.00
		1209	CONSTRUCTION OF FOUR LANE ROB AND ITS APPROACHES IN LIEU OF EXISTING LEVEL CROSSING NO. RV-71 AT KM (MoRTH) (N24001864)	11-2021	6/2025 (N.A.) {6/2025}	154.49 (N.A.) {154.49}	56.36	17.00
		1210	CONSTRUCTION OF 4 LANE ROB WITH APPROACHES IN LIEU OF LC NO. RV-172 AT KM 176.00 OF NH-201 (PRESENT (MoRTH) (N24001865)	12-2021	5/2025 (N.A.) {5/2025}	324.09 (N.A.) {324.09}	84.60	20.00
		1211	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM. (NHAI) (N24002078)	12-2023	12/2025 (N.A.) {12/2025}	711.00 (N.A.) {711.00}	111.90	37.10
		1212	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002079)	12-2023	12/2025 (N.A.) {12/2025}	742.25 (N.A.) {742.25}	186.00	41.65
		1213	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002080)	12-2023	12/2025 (N.A.) {12/2025}	762.75 (N.A.) {762.75}	186.57	41.65
		1214	3L MAJOR BRIDGE OVER RIVER BRAHMANI AT KM. 401.250 (DUBURI CHANDIKHOLE SECTION) OF NH 200 (NEW NH 5 (NHAI) (N24002081)	8-2022	1/2025 (N.A.) {7/2025}	153.61 (N.A.) {153.61}	14.22	34.49

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1215	WIDENING AND STRENGTHENING TO 2L+PS FROM KM 0.000 TO 40.000 (DHAUGAON- PODAMARI SECTION) OF NH 326 I (MoRTH) (N24002135)	3-2022	2/2026 (N.A.) {2/2026}	186.52 (N.A.) {186.52}	41.20	12.00
		1216	WIDENING AND STRENGTHENING TO 4L+PS/2L+PS FROM KM 0.000 TO 35.800 (KUAKHIA - MANGALPUR SECTION) OF N (MoRTH) (N24002136)	3-2022	2/2026 (N.A.) {2/2026}	636.10 (N.A.) {636.10}	229.90	22.73
	STEEL	1217	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY (SAIL) (N12000122)	11-2020	5/2023 (N.A.) {3/2025}	377.18 (N.A.) {377.18}	432.35	95.29
		1218	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP (SAIL) (N12000125)	1-2022	5/2025 (N.A.) {7/2025}	970.18 (N.A.) {970.18}	625.31	80.89
PUNJAB	DEPARTMENT OF HIGHER EDUCATION	1219	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. (CPWD EDUCATION) (N28000142)	10-2019	5/2022 (N.A.) {6/2025}	348.24 (N.A.) {348.24}	280.97	90.00
	PETROLEUM	1220	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB (HPCL) (N16000402)	5-2020	2/2023 (N.A.) {3/2025}	1,421.46 (N.A.) {1,421.46}	1,119.17	95.50
		1221	BHATINDA SANGRUR PIPELINE (HPCL) (N16000440)	11-2021	5/2024 (N.A.) {6/2025}	367.00 (397.00) {397.00}	310.83	87.90
		1222	CGD PROJECT AT PATHANKOT DISTRICT (IOCL) (N16000488)	3-2022	3/2030 (N.A.) {9/2033}	151.00 (N.A.) {151.00}	7.83	1.50

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	1223	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI (NR) (N22000502)	6-2009	8/2016 (N.A.) {8/2025}	404.00 (N.A.) {404.00}	190.00	100.00
		1224	LUDHIANA MULLANPUR DOUBLING (NR) (N22000589)	9-2020	3/2025 (N.A.) {3/2025}	82.99 (N.A.) {235.00}	0.00	-
		1225	FEROZPUR - PATTI (25.72 KM) (NR) (N22000614)	4-2017	3/2027 (N.A.) {3/2027}	299.74 (N.A.) {299.74}	0.00	-
	ROAD TRANSPORT AND HIGHWAYS	1226	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL- BUDHLADA (MoRTH) (N24000907)	3-2018	8/2020 (N.A.) {7/2024}	293.10 (N.A.) {315.00}	306.60	100.00
		1227	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 (MoRTH) (N24000909)	10-2017	10/2019 (N.A.) {12/2025}	1,069.59 (N.A.) {1,069.59}	739.08	62.00
		1228	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 (MoRTH) (N24000910)	3-2018	11/2020 (N.A.) {6/2024}	170.57 (192.48) {150.00}	104.98	79.00
		1229	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES (MoRTH) (N24000941)	3-2018	8/2020 (N.A.) {8/2020}	293.64 (N.A.) {293.64}	295.46	100.00
		1230	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO (NHAI) (N24001415)	12-2020	4/2024 (N.A.) {7/2024}	881.00 (N.A.) {881.00}	882.83	89.33

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1231	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI (NHAI) (N24001416)	12-2020	1/2024 (N.A.) {3/2025}	989.66 (N.A.) {989.66}	324.77	31.08
		1232	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO (NHAI) (N24001417)	12-2020	4/2024 (N.A.) {9/2025}	1,234.40 (N.A.) {1,234.40}	792.35	57.84
		1233	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO (NHAI) (N24001418)	12-2020	4/2024 (N.A.) {9/2025}	1,094.46 (N.A.) {1,094.46}	802.93	61.96
		1234	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- (NHAI) (N24001419)	2-2021	4/2024 (N.A.) {11/2024}	1,269.96 (N.A.) {1,269.96}	585.86	43.45
		1235	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA- SRIHARGOBINDPUR- (NHAI) (N24001420)	2-2021	4/2024 (N.A.) {12/2025}	853.66 (N.A.) {853.66}	132.99	15.33
		1236	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA (NHAI) (N24001630)	7-2021	2/2025 (N.A.) {2/2025}	1,501.02 (N.A.) {1,501.02}	345.00	80.00
		1237	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD (NHAI) (N24001631)	3-2021	10/2024 (N.A.) {10/2024}	1,525.31 (N.A.) {1,525.31}	333.00	78.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1238	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM (NHAI) (N24001632)	1-2021	5/2024 (N.A.) {4/2025}	1,741.86 (2,086.91) {2,086.91}	1,238.81	94.00
		1239	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA ? RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR (NHAI) (N24001636)	5-2021	12/2024 (N.A.) {10/2026}	1,368.91 (1,368.91) {1,368.91}	163.58	15.31
		1240	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K (NHAI) (N24001637)	3-2021	1/2025 (N.A.) {1/2025}	1,754.84 (N.A.) {1,754.84}	1,082.62	32.50
		1241	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 (NHAI) (N24001638)	11-2021	7/2024 (N.A.) {4/2025}	646.42 (646.42) {646.42}	481.67	95.00
		1242	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE (NHAI) (N24001639)	5-2020	12/2024 (N.A.) {8/2025}	864.23 (864.23) {864.23}	434.88	50.00
		1243	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N (NHAI) (N24001640)	3-2021	11/2024 (N.A.) {11/2024}	1,229.38 (N.A.) {1,229.38}	729.77	36.41

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1244	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR (NHAI) (N24001641)	3-2021	10/2024 (N.A.) {12/2025}	1,641.75 (N.A.) {1,641.75}	179.85	25.06
		1245	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI (NHAI) (N24001642)	2-2021	8/2024 (N.A.) {12/2025}	1,474.77 (N.A.) {1,474.77}	422.91	69.24
		1246	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I (NHAI) (N24001643)	12-2020	6/2024 (N.A.) {6/2025}	857.91 (N.A.) {857.91}	127.71	38.50
		1247	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV (NHAI) (N24001644)	12-2020	9/2023 (N.A.) {9/2025}	524.88 (416.58) {416.58}	157.14	70.00
		1248	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION OF NH-354 SECTION ARIFKES-FEROZEPUR- MUKTS (MoRTH) (N24001960)	3-2021	10/2023 (N.A.) {4/2025}	263.19 (N.A.) {220.00}	94.08	42.00
		1249	WORK OF WIDENING/UPGRADATION OF 2- LANE WITH PAVED SHOULDER OF SRI MUKTSAR SAHIB TO MALOUT ROAD FROM (MoRTH) (N24001961)	3-2022	10/2023 (N.A.) {4/2025}	152.58 (N.A.) {152.58}	81.25	69.00
		1250	6L OF JODHPUR ROMANA (BATHINDA) - MANDI DABWALI (PUNJAB HARYANA BORDER) SECTION OF NH-54 FROM KM. 0. (NHAI) (N24002075)	12-2020	8/2025 (N.A.) {8/2025}	757.13 (757.00) {757.00}	246.51	95.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1251	6L AMRITSAR-BATHINDA GREENFIELD SECTION FROM JN. WITH BHAGTA BHAI KA- BHADAUR ROAD NEAR DYALPURA BHAI (NHAI) (N24002076)	3-2021	10/2025 (N.A.) {6/2026}	2,029.17 (2,029.00) {2,029.00}	84.23	36.00
		1252	6L ACCESS CONTROLLED LUDHIANA-BATHINDA GREENFIELD HIGHWAY FROM JN. WITH AMRITSAR-BATHINDA GREENFIELD (NHAI) (N24002091)	6-2021	9/2025 (N.A.) {5/2026}	906.51 (906.51) {906.51}	221.31	44.53
		1253	6-LANE AMRITSAR-BATHINDA GREENFIELD SECTION OF NH- 754A FROM JUNCTION WITH MOGA JALANDHAR ROAD (NH-70 (NHAI) (N24002092)	3-2021	10/2025 (N.A.) {10/2025}	1,801.37 (N.A.) {1,801.37}	969.94	34.79
		1254	6L OF AMBALA-CHANDIGARH GREENFIELD SECTION FROM KM. 0.000 TO KM. 25.000 WITH 4L SPUR TO LALRU FROM K (NHAI) (N24002098)	3-2022	10/2025 (N.A.) {10/2025}	1,641.66 (N.A.) {1,641.66}	126.00	39.00
		1255	4L OF EXISTING BEAS ? BABA BAKALA - DERA BABA NANAK SECTION FROM START OF BATALA BYPASS TILL INTERSE (NHAI) (N24002100)	10-2021	6/2025 (N.A.) {6/2025}	1,003.38 (N.A.) {1,003.38}	257.71	66.77
		1256	4L OF BEAS-MEHTA-BATALA- DERA BABA NANAK FROM INTERSECTION WITH JALANDHAR-AMRITSAR HIGHWAY (NH-3) NEA (NHAI) (N24002101)	8-2021	6/2025 (N.A.) {12/2025}	809.51 (N.A.) {809.51}	179.00	44.02
		1257	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I SPUR-I) FROM JN. WITH KAPURTHALA - SULTANPUR LODHI ROAD (NH (NHAI) (N24002102)	1-2020	4/2026 (N.A.) {4/2027}	2,165.23 (N.A.) {2,165.23}	152.41	17.53

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
RAJASTHAN	CIVIL AVIATION	1258	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT (AAI) (N04000101)	5-2022	11/2024 (N.A.) {6/2025}	480.00 (N.A.) {480.00}	184.82	66.00
		1259	UDAIPUR AIRPORT- CONSTRUCTION OF NEW INTEGRATED PASSENGER TERMINAL BUILDING (AAI) (N04000104)	6-2023	3/2026 (N.A.) {9/2026}	887.00 (N.A.) {887.00}	230.27	51.66
	COAL	1260	NLCIL 300 MW SOLAR POWER PROJECT (PART OF 510 MW CPSU SCHEME) (NLC) (N06000269)	3-2023	9/2024 (N.A.) {3/2025}	1,813.00 (N.A.) {1,813.00}	482.28	59.00
	PETROLEUM	1261	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE (IOCL) (N16000435)	12-2021	10/2024 (N.A.) {12/2025}	9,028.00 (N.A.) {9,028.00}	6,333.97	75.97
		1262	CGD PROJECT IN TONK, SAWAI MADHOPUR, DAUSA, KARALI (HPCL) (N16000496)	3-2022	3/2030 (N.A.) {3/2030}	1,751.00 (N.A.) {1,751.00}	212.55	22.80
		1263	SETTING UP OF PETROCHEMICAL EVACUATION MARKETING TERMINAL (PEMT) AT BARMER (HPCL) (N16000512)	12-2023	12/2026 (N.A.) {12/2026}	461.05 (N.A.) {461.05}	59.64	34.30
		1264	RAJASTHAN REFINERY PROJECT (HPCLRRL(JV)) (N16000513)	10-2017	10/2022 (N.A.) {3/2025}	43,129.00 (72,937.00) {72,937.00}	54,535.00	85.20
		1265	CGD PROJECTS AT FAZILKA (EXCEPT AREA ALREADY AUTHORIZED) GANGANAGAR AND HANUMANGARH DISTRICTS (BPCL) (N16000520)	12-2022	6/2030 (N.A.) {6/2030}	3,207.00 (N.A.) {3,207.00}	242.33	17.90
	POWER	1266	SAMBHU KI BHURJ-II SOLAR 300MW (NTPC) (N18000286)	3-2020	9/2021 (N.A.) {3/2025}	1,782.00 (12.00) {1,782.00}	1,357.88	95.00
		1267	BHENSARA 320 MW (NTPC) (N18000293)	1-2021	7/2022 (N.A.) {3/2025}	1,221.73 (1,521.00) {1,221.73}	1,021.45	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1268	NOKH PLOT-1 SOLAR PV PROJECT 245MW (NTPC) (N18000320)	3-2022	8/2023 (N.A.) {3/2025}	1,352.71 (N.A.) {1,352.71}	969.36	45.00
		1269	NOKH PLOT-2 SOLAR PV PROJECT 245MW (NTPC) (N18000321)	3-2022	8/2023 (N.A.) {3/2025}	1,409.52 (N.A.) {1,409.52}	1,367.38	95.00
		1270	NOKH PLOT-3 SOLAR PV PROJECT 245MW (NTPC) (N18000322)	3-2022	8/2023 (N.A.) {3/2025}	1,426.94 (N.A.) {1,426.94}	1,122.68	80.00
		1271	BHADLA-II 500MW SOLAR PV PROJECT (NTPC) (N18000347)	6-2022	3/2024 (N.A.) {7/2025}	2,598.92 (N.A.) {2,598.92}	1,469.07	12.00
		1272	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART (PGCIL) (N18000356)	3-2023	9/2024 (N.A.) {5/2025}	1,433.28 (N.A.) {1,433.28}	811.47	87.00
		1273	300 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000368)	5-2022	11/2023 (N.A.) {8/2025}	1,677.12 (N.A.) {1,677.12}	805.32	80.00
		1274	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III, PART E1 (PGCIL) (N18000373)	8-2023	2/2025 (N.A.) {4/2025}	688.74 (N.A.) {688.74}	315.00	87.00
		1275	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART H (PGCIL) (N18000374)	10-2023	4/2025 (N.A.) {5/2025}	2,211.00 (N.A.) {2,211.00}	905.63	49.00
		1276	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART C1 (PGCIL) (N18000375)	10-2023	4/2025 (N.A.) {10/2025}	1,796.00 (N.A.) {1,796.00}	787.48	56.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1277	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART B1 (PGCIL) (N18000376)	9-2023	4/2025 (N.A.) {6/2025}	2,191.00 (N.A.) {2,191.00}	895.26	58.00
		1278	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART J (PGCIL) (N18000378)	12-2022	3/2025 (N.A.) {3/2026}	331.00 (N.A.) {331.00}	8.66	26.00
		1279	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART E2 (PGCIL) (N18000379)	11-2023	6/2025 (N.A.) {6/2025}	428.00 (N.A.) {428.00}	0.00	6.00
		1280	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART A [BIKANER III N (PGCIL) (N18000386)	12-2023	12/2025 (N.A.) {12/2025}	2,998.00 (N.A.) {2,998.00}	420.98	35.00
		1281	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART D [NEEMRANA II B (PGCIL) (N18000387)	12-2023	12/2025 (N.A.) {12/2025}	2,056.00 (N.A.) {2,056.00}	542.00	33.00
		1282	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PH-III PART D [SIKAR KHETRI TRANSMISSI (PGCIL) (N18000389)	2-2024	8/2025 (N.A.) {8/2025}	2,000.00 (N.A.) {2,000.00}	535.00	43.00
		1283	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) PART-B (JAISALMER/BARMER COMPLEX) (PGCIL) (N18000391)	8-2024	8/2026 (N.A.) {8/2026}	3,279.00 (N.A.) {3,279.00}	43.00	7.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1284	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-C (PGCIL) (N18000393)	8-2024	8/2026 (N.A.) {8/2026}	2,227.00 (N.A.) {2,227.00}	66.00	9.00
		1285	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-E (PGCIL) (N18000394)	8-2024	8/2026 (N.A.) {8/2026}	3,251.00 (N.A.) {3,251.00}	75.00	7.00
		1286	ADDITIONAL TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM BHADLA-III PS AS PART OF RAJASTHAN REZ P (PGCIL) (N18000396)	8-2024	2/2026 (N.A.) {2/2026}	369.00 (N.A.) {369.00}	0.00	1.00
		1287	TRANSMISSION SYSTEM STRENGTHENING FOR INTERCONNECTIONS OF BHADLA-III AND BIKANER III COMPLEX [SPV NA (PGCIL) (N18000397)	8-2024	8/2026 (N.A.) {8/2026}	1,382.00 (N.A.) {1,382.00}	0.00	1.00
		1288	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BAR (PGCIL) (N18000401)	11-2024	11/2026 (N.A.) {11/2026}	2,735.00 (N.A.) {2,735.00}	0.00	-
		1289	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6GW)] [BIKANER COMPLEX (PGCIL) (N18000403)	11-2024	11/2026 (N.A.) {11/2026}	5,969.00 (N.A.) {5,969.00}	0.00	-
		1290	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6 GW)] [BIKANER COMPLE (PGCIL) (N18000404)	11-2024	11/2026 (N.A.) {11/2026}	5,357.00 (N.A.) {5,357.00}	0.00	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	1291	AGRA FORT-BANDIKUI (NCR) (N22000553)	6-2022	6/2027 (N.A.) {5/2026}	1,389.81 (N.A.) {987.83}	42.46	12.00
		1292	GUDHA THATHANA MITHRI TEST TRACK FOR RDSO (NWR) (N22000593)	4-2019	3/2025 (N.A.) {3/2025}	528.48 (N.A.) {500.85}	339.59	73.00
		1293	DEDICATED TEST TRACK FOR RDSO (PHASE II) (NWR) (N22000594)	11-2021	11/2026 (N.A.) {12/2025}	466.42 (N.A.) {466.22}	668.43	75.00
		1294	DOUBLING BETWEEN CHURU- RATANGARH (42.81 KM) (NWR) (N22000605)	2-2023	2/2028 (N.A.) {5/2025}	422.60 (N.A.) {422.60}	168.42	72.00
		1295	SAWAIMADHOPUR - BYPASS LINE (6.98 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NWR) (N22000607)	12-2022	6/2026 (N.A.) {1/2026}	304.00 (239.54) {239.54}	96.67	21.00
		1296	GC OF NATHDWARA - DEVGARH MADARIYA (82.5KM) (NWR) (N22000608)	1-2023	6/2028 (N.A.) {12/2026}	968.92 (N.A.) {968.92}	323.01	28.00
	ROAD TRANSPORT AND HIGHWAYS	1297	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA (NHAI) (N24000795)	2-2018	4/2021 (N.A.) {3/2025}	741.86 (649.00) {649.00}	672.53	96.00
		1298	4L+PS OF NH -58 FROM BEAWAR- GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. (MoRTH) (N24001411)	12-2020	10/2023 (N.A.) {12/2025}	379.23 (N.A.) {379.23}	233.62	96.10
		1299	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR (MoRTH) (N24001527)	12-2021	5/2024 (N.A.) {6/2025}	411.40 (N.A.) {411.40}	183.61	60.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1300	WIDENING OF PACHPADRA-BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE (MoRTH) (N24001528)	1-2022	12/2024 (N.A.) {6/2025}	194.88 (N.A.) {194.88}	104.69	75.46
		1301	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH-68) IN THE STATE OF RAJASTHAN ON EPC M (MoRTH) (N24001529)	12-2021	8/2024 (N.A.) {3/2025}	451.66 (N.A.) {451.66}	401.78	97.00
		1302	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN-LALSOT-KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH (MoRTH) (N24001530)	12-2021	9/2024 (N.A.) {7/2025}	150.11 (N.A.) {150.11}	65.83	75.00
		1303	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR (NHAI) (N24001557)	3-2022	11/2024 (N.A.) {3/2025}	1,636.15 (N.A.) {1,636.15}	725.69	86.00
		1304	4L OF KARWAR (KM. 281.980 OF NH-62 NAGPUR ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) (NHAI) (N24001558)	11-2021	8/2024 (N.A.) {3/2025}	736.75 (N.A.) {736.75}	234.95	89.10
		1305	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE -0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK (NHAI) (N24001559)	9-2021	6/2024 (N.A.) {3/2025}	672.35 (N.A.) {672.35}	392.56	99.00
		1306	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) (NHAI) (N24001563)	10-2019	8/2023 (N.A.) {3/2025}	846.59 (N.A.) {846.59}	155.11	97.80

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1307	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7) (NHAI) (N24001564)	10-2019	7/2023 (N.A.) {3/2025}	662.08 (N.A.) {662.08}	121.41	96.50
		1308	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA (NHAI) (N24001567)	11-2019	10/2022 (N.A.) {6/2025}	1,272.97 (N.A.) {1,272.97}	627.05	85.02
		1309	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N (NHAI) (N24001568)	11-2019	5/2023 (N.A.) {3/2025}	1,119.35 (N.A.) {1,119.35}	1,447.42	99.80
		1310	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M (NHAI) (N24001573)	11-2019	12/2022 (N.A.) {3/2025}	1,658.06 (N.A.) {1,658.06}	180.53	99.90
		1311	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH (NHAI) (N24001612)	7-2020	1/2024 (N.A.) {12/2025}	1,788.69 (N.A.) {1,788.69}	896.22	73.93
		1312	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FOR FATEHPUR BYPASS, MANDAWA BYPASS AND JHUNJHUNU BYPAS (MoRTH) (N24001866)	3-2022	8/2024 (N.A.) {6/2025}	186.29 (N.A.) {186.29}	142.69	78.00
		1313	UPGRADATION OF TWO LANE PAVED SHOULDER FROM SHAHPURA TO THANAGAZI OF NH-248A ON EPC MODE IN THE STAT (MoRTH) (N24001867)	3-2022	7/2024 (N.A.) {6/2025}	174.34 (N.A.) {174.34}	104.08	80.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1314	Sagwara Bypass and Garhi- Partapur Bypass of NH-927A in the State of Rajasthan. (MoRTH) (N24001868)	3-2022	8/2025 (N.A.) {6/2025}	187.65 (N.A.) {187.65}	106.57	75.45
		1315	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF GHAGARIYA- MUNABAO SECTION FROM KM (MoRTH) (N24001869)	12-2022	8/2025 (N.A.) {8/2025}	235.15 (N.A.) {235.15}	152.69	94.00
		1316	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FROM CHARBHUJA AT DESIGN KM 0.00 (EXISTING KM 150.00) TO (MoRTH) (N24001927)	2-2022	9/2025 (N.A.) {9/2025}	838.43 (N.A.) {838.43}	295.87	72.00
		1317	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER NORTHERN BYPASS PHASE-II OF KOTA CITY FROM DESIGN CHAINAG (MoRTH) (N24001928)	3-2022	4/2025 (N.A.) {12/2025}	317.74 (N.A.) {317.74}	136.23	11.00
		1318	ADDITIONAL STRUCTURES ON 6LGURGAON-JAIPUR SECTION OF NH-48 BETWEEN KM 42.700 TO KM 273.00 (NHAI) (N24002058)	8-2022	6/2024 (N.A.) {3/2025}	409.64 (N.A.) {409.64}	214.75	72.45
		1319	UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF HANUMANGARH TO KENCHIYAN OF NH 54 ON EPC MODE IN THE ST (MoRTH) (N24002167)	3-2024	10/2026 (N.A.) {10/2026}	334.64 (N.A.) {334.64}	68.00	20.00
		1320	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM NEECHLI ODEN (NATHDWARA) AT DESIGN KM 88.800 TO BHATE (MoRTH) (N24002168)	3-2023	10/2026 (N.A.) {10/2026}	606.61 (N.A.) {606.61}	46.00	6.50

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
SIKKIM	<u>CIVIL AVIATION</u>	1321	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	17.83	9.25
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1322	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Unversi) (N44000002)	8-2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	157.24	54.00
	<u>POWER</u>	1323	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,126.44	65.28
		1324	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,394.69	84.55
	<u>RAILWAYS</u>	1325	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	12/2015 (N.A.) {12/2027}	1,339.48 (11,972.96) {11,972.96}	8,068.38	72.50
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1326	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (N.A.) {12/2023}	375.80 (N.A.) {375.80}	287.54	96.55
		1327	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11-2017	10/2020 (N.A.) {4/2024}	290.05 (N.A.) {290.05}	218.36	100.00
		1328	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {3/2025}	402.94 (N.A.) {402.94}	243.64	76.54
		1329	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (N.A.) {3/2025}	295.97 (N.A.) {295.97}	245.22	94.64

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1330	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	-
		1331	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {4/2025}	311.00 (N.A.) {273.78}	256.55	94.63
		1332	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (N.A.) {4/2025}	345.38 (395.59) {395.59}	362.13	90.23
		1333	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (N.A.) {12/2025}	183.31 (439.56) {439.56}	351.80	49.88
		1334	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (N.A.) {12/2025}	262.84 (414.20) {414.20}	220.26	46.47
		1335	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (N.A.) {12/2025}	292.80 (N.A.) {292.80}	195.37	55.85

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1336	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (N.A.) {6/2025}	230.45 (244.91) {244.91}	204.72	80.32
		1337	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (N.A.) {7/2025}	493.42 (478.79) {478.79}	284.66	46.12
		1338	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (N.A.) {12/2025}	816.79 (786.60) {786.60}	308.77	49.32
		1339	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1-2021	9/2023 (N.A.) {12/2025}	332.20 (N.A.) {348.92}	149.38	41.04
		1340	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (N.A.) {6/2025}	410.60 (379.30) {379.30}	221.02	69.79
		1341	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (N.A.) {1/2026}	385.15 (N.A.) {385.15}	170.32	80.00
TAMIL NADU	CIVIL AVIATION	1342	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI (AAI) (N04000074)	6-2018	2/2022 (N.A.) {3/2026}	2,467.00 (N.A.) {2,467.00}	1,542.89	69.50
		1343	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI (AAI) (N04000075)	8-2018	10/2021 (N.A.) {12/2023}	951.28 (1,112.49) {1,112.49}	1,112.49	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1344	DEVELOPMENT OF TUTICORIN AIRPORT (AAI) (N04000090)	6-2019	3/2022 (N.A.) {3/2025}	380.87 (N.A.) {455.99}	347.58	98.50
	COAL	1345	JAWAHAR KHANI OPENCAST (JK OC) MINE (SCCL) (N06000259)	12-2021	3/2025 (N.A.) {3/2025}	297.88 (N.A.) {297.88}	45.19	20.00
		1346	50 MW SOLAR POWER PROJECT - NEYVELI MINED OUT AREA (NLC) (N06000279)	5-2023	6/2025 (N.A.) {4/2025}	218.03 (N.A.) {218.03}	297.33	37.00
	FINANCE	1347	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI (CPWD FOR FINANC) (N28000109)	11-2017	11/2021 (N.A.) {11/2022}	348.77 (N.A.) {348.77}	223.39	100.00
	MINES	1348	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (NALCO) (N10000014)	9-2017	6/2019 (N.A.) {12/2024}	166.62 (163.17) {163.17}	135.63	65.00
	PETROLEUM	1349	IRUGUR-DEVANGONTHI POL PIPELINE (BPCL) (N16000234)	11-2012	2/2017 (N.A.) {10/2025}	678.00 (1,732.00) {1,732.00}	536.25	50.70
		1350	CBR 9 MMTPA PROJECT (CPCL) (N16000434)	1-2021	6/2025 (N.A.) {6/2025}	31,580.00 (31,580.00) {36,354.00}	1,311.86	10.20
		1351	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI (IOCL) (N16000438)	1-2022	7/2024 (N.A.) {6/2025}	827.00 (887.71) {887.71}	549.21	81.60
		1352	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) (IOCL) (N16000455)	1-2022	7/2024 (N.A.) {5/2026}	829.00 (N.A.) {829.00}	229.90	57.15
		1353	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS (IOCL) (N16000486)	3-2022	3/2030 (N.A.) {12/2030}	501.00 (N.A.) {501.00}	103.98	5.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1354	CGD PROJECTS AT THE NILGIRIS AND ERODE DISTRICTS (BPCL) (N16000521)	12-2022	3/2030 (N.A.) {3/2030}	3,685.00 (N.A.) {3,685.00}	164.57	8.20
	RAILWAYS	1355	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP (MRTPT) (N22000028)	4-2006	6/2013 (N.A.) {5/2025}	495.74 (N.A.) {734.01}	632.33	98.00
		1356	TIDIVANAM-NAGARI (NL) (SR) (N22000085)	9-2006	(N.A.) {3/2028}	582.83 (3,631.34) {3,631.34}	826.84	12.00
		1357	CHENNAI BEACH-CHENNAI EGMORE (4.3 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SR) (N22000568)	3-2022	3/2026 (N.A.) {3/2025}	359.60 (274.20) {274.20}	248.04	95.00
		1358	MORAPPUR-DHARMAPURI (SR) (N22000618)	2-2019	3/2028 (N.A.) {3/2027}	358.95 (N.A.) {358.95}	38.37	1.00
		1359	KARAIKAL PERALAM(23KM)-NEW LINE PROJECT (SR) (N22000625)	1-2019	3/2026 (N.A.) {3/2025}	304.22 (N.A.) {373.42}	266.40	80.00
		1360	NAGAPATTINAM THIRUTURAIPUNDI (38KM)- NEW LINE PROJECT (SR) (N22000626)	7-2008	3/2026 (N.A.) {3/2027}	677.12 (N.A.) {788.05}	142.44	19.00
	ROAD TRANSPORT AND HIGHWAYS	1361	FOUR LANNING OF CHOLOPURAM-THANJAVUR (NHAI) (N24000697)	8-2017	9/2020 (N.A.) {3/2025}	1,176.37 (N.A.) {1,176.37}	1,325.06	99.50
		1362	4-LANNING OF STHIYATHOPU- CHOLOPURAM (NHAI) (N24000708)	9-2017	8/2020 (N.A.) {5/2025}	1,227.87 (N.A.) {1,227.87}	1,391.60	95.20
		1363	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 (NHAI) (N24000826)	3-2018	10/2022 (N.A.) {3/2025}	505.35 (N.A.) {837.69}	376.61	99.75

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1364	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON (NHAI) (N24001428)	3-2018	11/2021 (N.A.) {12/2024}	998.70 (1,358.32) {1,358.32}	924.02	98.26
		1365	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER (NHAI) (N24001429)	3-2018	11/2021 (N.A.) {12/2024}	1,294.47 (1,588.40) {1,588.40}	860.53	98.65
		1366	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM (NHAI) (N24001430)	3-2018	1/2022 (N.A.) {12/2024}	2,120.40 (2,565.63) {2,565.63}	1,579.60	99.80
		1367	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN (NHAI) (N24001431)	3-2018	10/2020 (N.A.) {8/2025}	1,872.68 (2,661.51) {2,756.09}	1,291.81	59.20
		1368	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 (MoRTH) (N24001455)	2-2022	8/2022 (N.A.) {3/2025}	191.33 (207.97) {207.97}	185.78	96.00
		1369	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) (NHAI) (N24001600)	10-2020	5/2023 (N.A.) {3/2025}	434.12 (N.A.) {434.12}	258.89	99.30
		1370	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 (NHAI) (N24001601)	1-2019	1/2023 (N.A.) {6/2025}	1,051.69 (N.A.) {1,051.69}	574.70	79.82

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1371	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001602)	1-2019	12/2022 (N.A.) {11/2025}	1,409.38 (N.A.) {1,409.38}	653.27	90.23
		1372	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001603)	1-2019	10/2022 (N.A.) {3/2025}	1,518.53 (N.A.) {1,607.54}	915.40	100.00
		1373	4-LANING OF MELUR - PILLAYARPATTI - KARAUKUDI SECTION OF NH-338, NH-36, NH- 383 (NHAI) (N24001605)	6-2018	3/2022 (N.A.) {5/2025}	1,103.86 (N.A.) {1,103.86}	461.32	72.00
		1374	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH- 744A (MADURAI RING ROAD) (NHAI) (N24001606)	12-2018	3/2022 (N.A.) {7/2025}	854.94 (N.A.) {854.94}	369.07	70.00
		1375	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS (NHAI) (N24001692)	1-2022	9/2024 (N.A.) {6/2025}	467.99 (N.A.) {468.00}	22.34	62.15
		1376	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 (NHAI) (N24001693)	9-2021	10/2024 (N.A.) {10/2024}	1,751.18 (N.A.) {1,757.27}	49.69	-
		1377	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM (NHAI) (N24001694)	2-2019	12/2023 (N.A.) {12/2024}	1,243.57 (N.A.) {1,243.57}	171.63	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1378	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460 (NHAI) (N24001696)	2-2019	8/2023 (N.A.) {12/2024}	1,291.37 (N.A.) {1,291.37}	215.02	-
		1379	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM (NHAI) (N24001716)	7-2022	8/2023 (N.A.) {12/2024}	186.50 (242.40) {242.40}	17.15	100.00
		1380	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K (NHAI) (N24001717)	11-2020	8/2024 (N.A.) {3/2026}	1,155.49 (1,525.10) {1,525.10}	485.62	53.06
		1381	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 (NHAI) (N24001718)	12-2020	7/2024 (N.A.) {7/2025}	843.48 (1,068.60) {1,068.60}	431.31	90.21
		1382	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT (NHAI) (N24001719)	2-2021	7/2024 (N.A.) {8/2025}	2,948.31 (3,605.73) {3,605.73}	728.20	72.67
		1383	BANGALORE CHENNAI EXPRESSWAY PHASE-III ? PACKAGE I (GUDIPALA TO WALAJHPET) FROM KM 156.000 TO KM 1 (NHAI) (N24001720)	10-2020	5/2024 (N.A.) {6/2025}	1,023.91 (1,438.62) {1,438.62}	574.44	80.47
		1384	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 (NHAI) (N24001721)	2-2019	5/2024 (N.A.) {3/2026}	1,008.99 (1,360.53) {1,360.53}	196.13	43.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1385	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH (NHAI) (N24001722)	11-2021	2/2023 (N.A.) {2/2025}	463.44 (463.07) {463.44}	331.22	99.00
		1386	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 (NHAI) (N24001723)	10-2018	2/2021 (N.A.) {4/2025}	707.90 (766.51) {766.51}	487.51	86.30
		1387	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 (NHAI) (N24001725)	1-2019	5/2021 (N.A.) {1/2025}	819.89 (1,314.82) {922.85}	394.75	57.32
		1388	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 ? 29/250 INCLUDING LA AND SHIFTING OF NH-234 (MoRTH) (N24001828)	1-2022	11/2024 (N.A.) {3/2025}	221.03 (243.95) {243.95}	149.75	80.00
		1389	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU (MoRTH) (N24001829)	10-2022	11/2024 (N.A.) {3/2025}	172.15 (N.A.) {172.15}	140.39	96.00
		1390	CONSTRUCTION OF STRR (WEST SIDE)-NH948A- BALAGONDAPALLI (TAMIL NADU) TO KARNATAKA/TAMIL NADU BORDER F (NHAI) (N24001968)	4-2022	5/2025 (N.A.) {5/2025}	1,260.74 (N.A.) {1,260.74}	487.46	44.95
		1391	4L OF THIRUMANGALAM TO VADUGAPATTI SECTION FROM KM 0.000 TO KM 36.000 OF NH- 744 (NHAI) (N24002084)	3-2022	2/2025 (N.A.) {6/2025}	1,076.97 (N.A.) {1,076.97}	482.18	81.25

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1392	CONSTRUCTION OF NEW DOUBLE TIER 4 LANE ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI (NHAI) (N24002107)	3-2023	5/2026 (N.A.) {5/2026}	1,382.00 (N.A.) {1,382.00}	0.00	-
		1393	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002108)	3-2023	5/2026 (N.A.) {5/2026}	1,618.96 (N.A.) {1,618.96}	0.00	-
		1394	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002109)	3-2023	5/2026 (N.A.) {5/2026}	1,301.37 (N.A.) {1,301.37}	0.00	-
		1395	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002110)	3-2023	5/2026 (N.A.) {5/2026}	1,207.40 (N.A.) {1,207.40}	0.00	-
		1396	FOUR LANING OF MUGAIYUR TO MARAKKANAM SECTION OF NH- 332A FROM KM 31.000 TO KM 62.000 (NHAI) (N24002111)	2-2019	12/2025 (N.A.) {12/2025}	825.94 (1,116.13) {1,116.13}	235.33	33.34
		1397	SIX LANING OF TUTICORIN PORT ROAD SECTION OF NH-7A (NEW NH-138) FROM KM 0.000 TO KM 6.140 [EFFECTIVE (NHAI) (N24002112)	3-2023	7/2024 (N.A.) {5/2025}	200.30 (N.A.) {200.30}	72.69	72.50
		1398	4L OF LEFT-OVER WORKS INCLUDING ADDITIONAL STRUCTURES FROM KERALA/TAMIL NADU BORDER TO KANYAKUMARI S (NHAI) (N24002113)	3-2023	8/2025 (N.A.) {8/2025}	1,141.78 (N.A.) {1,141.78}	337.04	33.52

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1399	4L OF VADUGAPATTI TO THERKUVENGANALLUR (RAJAPALYAM) SECTION FROM KM 36.000 TO KM 71.600 OF NH744 UND (NHAI) (N24002114)	2-2022	4/2025 (N.A.) {4/2025}	1,097.59 (N.A.) {1,317.06}	665.46	93.12
		1400	WIDENING TO 4L/4L+PS AND STRENGTHENING IN SELECTED STRETCHES FROM KM 0/8 TO 50/570 OF NH 532 INCLUD (MoRTH) (N24002151)	3-2022	1/2024 (N.A.) {7/2025}	257.14 (294.70) {294.70}	185.85	68.00
		1401	WIDENING FROM 2L+PS TO 4L/4L+PS AND IMPROVEMENTS THE SELECTED STRETHCES FROM KM 26/5 - 81/2 INCLU (MoRTH) (N24002152)	3-2023	11/2023 (N.A.) {11/2025}	274.84 (N.A.) {274.84}	206.02	92.00
		1402	STRENGTHENING OF 2L+PS FROM KM 17/8 ? 18/2, CONSTRUCTION OF 2L+PS FROM KM 18/2 TO KM 20/0 AND CONSTR (MoRTH) (N24002153)	3-2023	2/2024 (N.A.) {8/2025}	169.68 (N.A.) {169.68}	72.62	52.00
		1403	CONSTRUCTION OF BYPASS TO MADURAI - ACHAMBATHU - VIRATIPATHU IN KM 6/850 - 10/382 OF NH 49 EXTN. (NE (MoRTH) (N24002165)	3-2022	8/2026 (N.A.) {8/2026}	238.97 (260.07) {260.07}	68.06	21.00
TELANGANA	CIVIL AVIATION	1404	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD (AAI) (N04000086)	5-2020	5/2022 (N.A.) {6/2023}	353.61 (N.A.) {353.61}	303.22	100.00
	COAL	1405	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 (SCCL) (N06000161)	3-2017	3/2022 (N.A.) {3/2025}	413.84 (N.A.) {413.84}	382.88	79.00
		1406	GODAVARIKHANI COAL MINE (SCCL) (N06000202)	7-2019	3/2023 (N.A.) {3/2025}	438.98 (N.A.) {438.98}	169.89	70.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1407	VENKATESH KHANI COAL MINE (SCCL) (N06000204)	10-2020	3/2023 (N.A.) {3/2026}	484.51 (N.A.) {484.51}	281.16	30.00
		1408	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT (SCCL) (N06000210)	11-2015	3/2023 (N.A.) {3/2025}	489.62 (N.A.) {489.62}	405.54	70.00
		1409	RCE OF INDARAM OPENCAST PROJECT (SCCL) (N06000211)	8-2017	3/2021 (N.A.) {3/2025}	349.28 (N.A.) {424.81}	402.64	80.00
		1410	RCE OF KALYANIKHANI OPENCAST PROJECT (SCCL) (N06000213)	3-2016	3/2020 (N.A.) {3/2025}	384.32 (N.A.) {384.32}	248.21	75.00
		1411	RCE OF KAKATHIYAKHANI OC - 2 PROJECT (SCCL) (N06000214)	8-2017	3/2020 (N.A.) {3/2025}	442.42 (N.A.) {442.42}	201.29	63.00
		1412	GOLETI OPENCAST MINE (SCCL) (N06000258)	7-2021	3/2026 (N.A.) {3/2026}	345.60 (N.A.) {345.60}	66.07	20.00
	<u>HEALTH AND FAMILY WELFARE</u>	1413	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR (HITES) (N21000031)	12-2018	7/2024 (N.A.) {3/2025}	1,110.55 (N.A.) {1,110.55}	700.42	80.87
		1414	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD (CPWD FOR HEALTH) (N28000098)	10-2016	3/2020 (N.A.) {1/2025}	209.84 (281.05) {281.05}	252.40	98.50
	<u>RAILWAYS</u>	1415	MANOHARABAD-KOTHPALL NEW LINE(SCR) (SCR) (N22000032)	4-2006	3/2010 (N.A.) {3/2025}	1,160.48 (N.A.) {3,014.00}	1,464.78	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1416	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT (MoRTH) (N24000245)	1-2014	3/2016 (N.A.) {9/2019}	270.00 (N.A.) {270.00}	0.00	72.15

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1417	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR (MoRTH) (N24000247)	10-2014	2/2017 (N.A.) {3/2025}	295.47 (N.A.) {295.47}	224.42	99.00
		1418	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM (MoRTH) (N24000248)	3-2015	1/2017 (N.A.) {12/2023}	153.21 (N.A.) {153.21}	101.15	93.00
		1419	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON (MoRTH) (N24000980)	10-2016	2/2019 (N.A.) {8/2024}	298.32 (N.A.) {298.32}	178.47	98.00
		1420	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ (MoRTH) (N24000981)	10-2016	3/2019 (N.A.) {8/2024}	248.83 (N.A.) {248.83}	173.82	100.00
		1421	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE (MoRTH) (N24000982)	1-2017	5/2019 (N.A.) {8/2019}	244.54 (N.A.) {244.54}	176.32	100.00
		1422	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH (MoRTH) (N24000983)	1-2017	10/2019 (N.A.) {2/2024}	196.52 (N.A.) {196.52}	125.53	96.00
		1423	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI (MoRTH) (N24000984)	1-2017	12/2019 (N.A.) {12/2019}	283.00 (N.A.) {283.00}	259.15	99.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1424	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION (MoRTH) (N24000986)	1-2017	5/2019 (N.A.) {1/2024}	300.00 (N.A.) {300.00}	243.36	96.00
		1425	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD- SAMSHABAD SECTION OF NH (MoRTH) (N24000987)	1-2018	5/2020 (N.A.) {8/2024}	283.15 (N.A.) {283.15}	279.54	93.00
		1426	WIDENING AND STRENGTHENING OF EXISTING 2- LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 (MoRTH) (N24000988)	1-2018	12/2019 (N.A.) {11/2020}	230.03 (N.A.) {230.03}	232.00	100.00
		1427	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 (MoRTH) (N24000989)	2-2018	6/2020 (N.A.) {1/2021}	206.13 (N.A.) {206.13}	192.73	98.00
		1428	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT (MoRTH) (N24000990)	2-2018	11/2019 (N.A.) {1/2024}	294.13 (N.A.) {294.13}	203.07	87.00
		1429	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC (MoRTH) (N24000993)	3-2018	9/2020 (N.A.) {6/2023}	322.81 (N.A.) {322.81}	325.47	98.00
		1430	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES (MoRTH) (N24000994)	3-2018	7/2020 (N.A.) {2/2026}	626.76 (N.A.) {626.76}	282.78	44.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1431	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR) (MoRTH) (N24000996)	1-2017	10/2019 (N.A.) {6/2021}	605.08 (N.A.) {605.08}	416.45	100.00
		1432	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL ? MALLAMPALLY SECTION OF NH-365 (MoRTH) (N24000997)	3-2018	7/2019 (N.A.) {8/2024}	192.67 (N.A.) {192.67}	178.95	92.00
		1433	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR (MoRTH) (N24000998)	1-2019	(N.A.) {8/2024}	193.19 (249.72) {249.72}	230.79	95.00
		1434	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM (NHAI) (N24001482)	8-2022	10/2024 (N.A.) {10/2024}	772.11 (N.A.) {772.11}	466.27	74.30
		1435	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUDEM V (NHAI) (N24001483)	2-2022	9/2024 (N.A.) {9/2024}	637.11 (N.A.) {637.11}	334.20	74.80
		1436	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUDEM VILLAGE TO RECHERLA (NHAI) (N24001484)	9-2022	2/2024 (N.A.) {12/2024}	804.69 (N.A.) {804.69}	464.67	78.05

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1437	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 (NHAI) (N24001522)	1-2021	1/2024 (N.A.) {12/2024}	1,307.95 (N.A.) {1,307.95}	641.28	99.79
		1438	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, (NHAI) (N24001555)	3-2022	1/2025 (N.A.) {1/2025}	955.49 (N.A.) {955.49}	217.22	35.80
		1439	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 (NHAI) (N24001556)	12-2021	7/2024 (N.A.) {7/2024}	521.53 (N.A.) {521.53}	234.98	47.85
		1440	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 (NHAI) (N24001625)	1-2022	1/2025 (N.A.) {7/2025}	1,227.57 (N.A.) {1,227.57}	288.58	41.24
		1441	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM (NHAI) (N24001626)	2-2022	1/2025 (N.A.) {1/2025}	972.06 (N.A.) {972.06}	408.48	55.24
		1442	WIDENING AND STRENGTHENING OF EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FRO (MoRTH) (N24002000)	3-2021	7/2024 (N.A.) {8/2024}	317.19 (N.A.) {317.19}	164.72	67.00
		1443	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF MEDAK - SIDDIPET SECTION FROM KM 0/0 TO KM 69/978 OF NH- (MoRTH) (N24002001)	1-2022	1/2025 (N.A.) {6/2025}	882.18 (N.A.) {882.18}	291.30	66.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1444	WIDENING AND IMPROVEMENT OF EXISTING CARRIAGE WAY TO 2 LANE WITH PAVED SHOULDERS FROM KM. 86/160 TO (MoRTH) (N24002002)	1-2022	12/2024 (N.A.) {12/2024}	423.48 (N.A.) {423.48}	209.98	69.00
		1445	REHABILITATION AND UP- GRADATION OF VALIGONDA TO THORRUR SECTION TO TWO LANE WITH PAVED SHOULDERS FRO (MoRTH) (N24002003)	1-2022	12/2024 (N.A.) {3/2025}	549.28 (N.A.) {549.28}	196.96	64.00
		1446	REHABILITATION AND UPGRADATION OF LB-NAGAR TO MALKAPUR SECTION TO 6-LANE MAIN CARRIAGEWAY WITH SERVI (MoRTH) (N24002004)	3-2021	7/2024 (N.A.) {6/2025}	545.11 (N.A.) {545.11}	305.02	73.00
		1447	WIDENING TO TWO LANE WITH PAVED SHOULDERS OF 'BODHAN BASAR BHAINSA ' SECTION FROM KM 38/900 TO 95/3 (MoRTH) (N24002005)	3-2022	3/2025 (N.A.) {6/2025}	644.45 (N.A.) {644.45}	258.65	76.00
		1448	ONSTRUCTION OF 4-LANE FLYOVER AT AMBERPET-X ROAD, HYDERABAD ON NH-202 IN THE STATE OF TELANGANA (MoRTH) (N24002006)	10-2017	6/2023 (N.A.) {12/2024}	186.71 (N.A.) {186.71}	184.20	88.00
		1449	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/000 TO KM 79/300 OF KALWAKURTHY - KOLLAPUR SECTI (MoRTH) (N24002007)	3-2022	7/2025 (N.A.) {7/2025}	886.69 (N.A.) {886.69}	168.83	50.00
		1450	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF SIDDIPET-ELKATHURTHY SECTION FROM KM 69/978 TO KM 133/6 (MoRTH) (N24002008)	1-2022	12/2024 (N.A.) {12/2024}	578.85 (N.A.) {578.85}	196.36	78.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1451	WIDENING AND STRENGTHENING TO 2/4 LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR ? CHINCHOLI SECTION FROM (MoRTH) (N24002009)	1-2022	1/2025 (N.A.) {7/2025}	703.68 (N.A.) {703.68}	276.18	59.00
		1452	WIDENING AND STRENGTHENING TO 4 LANE / 2-LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR-CHINCHOLI SECTION (MoRTH) (N24002010)	3-2022	3/2024 (N.A.) {10/2025}	631.49 (N.A.) {631.49}	58.81	22.00
		1453	IMPROVEMENT OF GEOMETRICS OF THONDUPALLY TO KOTHUR FROM KM 22.300 TO KM 34.14 OF NH-44-RCW (NHAI) (N24002082)	2-2022	9/2024 (N.A.) {1/2026}	541.58 (N.A.) {541.58}	27.77	-
		1454	FOUR LANING OF KARIMNAGAR-WARANGAL SECTION OF NH-563 FROM DESIGN CH.48.860 KM NEAR SH-1 CH.170.400 K (NHAI) (N24002083)	3-2022	7/2025 (N.A.) {7/2025}	2,146.86 (2,413.00) {2,414.46}	916.67	66.64
		1455	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM-VIJAYAWADA) (NHAI) (N24002190)	3-2023	8/2026 (N.A.) {8/2026}	983.00 (N.A.) {983.00}	0.00	5.67
TRIPURA	PETROLEUM	1456	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (N.A.) {9/2025}	656.00 (N.A.) {656.00}	379.44	76.20

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1457	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (N.A.) {12/2024}	277.50 (302.02) {302.02}	256.89	99.94
		1458	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (N.A.) {11/2024}	159.13 (171.50) {171.50}	84.33	100.00
		1459	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {3/2025}	201.99 (N.A.) {287.47}	144.07	98.12
		1460	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (N.A.) {12/2025}	354.79 (N.A.) {354.79}	34.08	59.09
		1461	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (N.A.) {5/2025}	456.88 (N.A.) {456.88}	106.10	45.80
		1462	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {9/2025}	195.95 (N.A.) {195.95}	21.95	27.34
		1463	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	8.33	5.53
		1464	REHABILITATION AND UP- GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGTH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	3.60	8.51
		1465	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	26.01	21.84

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1466	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	8.31	-
		1467	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	-
		1468	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	28.16	8.80
UTTAR PRADESH	CIVIL AVIATION	1469	CCS INTERNATIONAL AIRPORT , LUCKNOW (AAI) (N04000077)	6-2018	9/2021 (N.A.) {10/2026}	1,383.00 (1,938.00) {3,291.81}	2,609.59	79.28
		1470	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 (AAI) (N04000094)	3-2021	12/2022 (N.A.) {3/2025}	242.14 (328.00) {358.00}	339.44	99.90
		1471	PRAYAGRAJ AIRPORT - CONSTRUCTION OF NEW TERMINAL BUILDING, SECOND LINK TAXI TRACK, APRON EXPANSION, (AAI) (N04000102)	5-2023	11/2024 (N.A.) {6/2025}	185.75 (274.38) {274.38}	166.78	85.00
		1472	AGRA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT AGRA AIRPORT. (AAI) (N04000113)	6-2024	7/2026 (N.A.) {7/2026}	579.00 (N.A.) {579.00}	24.92	10.00
		1473	VARANASI: DEVELOPMENT OF LAL BAHADUR SHASTRI INTERNATIONAL AIRPORT, VARANASI. (AAI) (N04000114)	7-2024	7/2027 (N.A.) {7/2027}	2,869.65 (N.A.) {2,869.65}	71.08	7.80
	COAL	1474	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW (NLC) (N06000152)	7-2016	11/2021 (N.A.) {6/2025}	17,237.00 (21,780.94) {21,780.94}	19,431.56	88.71

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1475	KHADIA EXPANSION OCP (NCL) (N06000208)	6-2021	3/2025 (N.A.) {3/2025}	491.67 (N.A.) {491.67}	102.99	8.61
	HOME AFFAIRS	1476	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI (CPWD FOR MHA) (N45000003)	5-2019	1/2022 (N.A.) {3/2023}	199.31 (N.A.) {199.31}	86.49	85.00
	PETROLEUM	1477	60 KTA POLYPROPYLENE PROJECT (GAIL) (N16000429)	3-2019	4/2024 (N.A.) {6/2025}	910.56 (1,299.02) {1,299.02}	928.40	94.20
		1478	AUGMENTATION OF FACILITIES AT MATHURA BITUMEN PLANT (IOCL) (N16000505)	4-2022	4/2025 (N.A.) {12/2026}	260.12 (N.A.) {260.12}	1.03	22.80
		1479	GRASS-ROOT TERMINAL AT MIRZAPUR UTTAR PRADESH (IOCL) (N16000506)	9-2022	6/2026 (N.A.) {11/2026}	980.45 (N.A.) {980.45}	172.76	44.20
		1480	CITY GAS DISTRIBUTION PROJECTS AT LAKHIMPUR KHERI, SITAPUR, BAHAICH, SHRAVASTI, BALRAMPUR, (BPCL) (N16000525)	12-2022	6/2030 (N.A.) {6/2030}	16,654.00 (N.A.) {16,654.00}	414.20	7.20
	POWER	1481	KHURJA SUPER THERMAL POWER PROJECT (THDCIL) (N18000272)	3-2019	9/2023 (N.A.) {6/2025}	11,089.42 (N.A.) {13,276.16}	11,980.68	94.50
		1482	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III (2X800 MW) (NTPC) (N18000382)	3-2024	2/2030 (N.A.) {2/2030}	17,195.31 (N.A.) {17,195.31}	1,114.00	0.50
	RAILWAYS	1483	VARANASI-MODHOSINGH- ALLAHABAD DOUBLING (RVNL) (N22000401)	4-2015	3/2022 (N.A.) {12/2024}	943.60 (N.A.) {2,018.23}	1,780.22	-
		1484	RAMNA - SINGRAULI DOUBLING (ECR) (N22000417)	8-2015	3/2020 (N.A.) {9/2024}	2,436.21 (2,880.40) {2,880.40}	3,050.81	90.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1485	KARAILA ROAD - SHAKTINAGAR DOUBLING (<i>ECR</i>) (N22000419)	8-2015	3/2019 (N.A.) {8/2024}	528.57 (762.97) {762.97}	804.73	90.00
		1486	BURHWAL - GONDA - 3RD RUNNING LINE. (<i>NER</i>) (N22000468)	4-2016	(N.A.) {9/2025}	602.50 (N.A.) {1,069.29}	1,012.63	50.00
		1487	SHAHGANJ-BHATNI-PHEPHNA- INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. (<i>NER</i>) (N22000470)	4-2016	12/2019 (N.A.) {3/2025}	1,177.96 (N.A.) {2,050.00}	2,036.35	80.50
		1488	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING (<i>NCR</i>) (N22000495)	3-2018	3/2023 (N.A.) {3/2027}	4,329.53 (N.A.) {4,329.53}	1,702.93	35.00
		1489	JHANSI BINA DOUBLING (<i>NCR</i>) (N22000496)	9-2016	3/2021 (N.A.) {3/2027}	2,001.00 (N.A.) {2,001.00}	1,699.31	85.00
		1490	MATHURA-JHANSI-3RD LINE (273.80 KM) (<i>RVNL</i>) (N22000501)	6-2016	12/2023 (N.A.) {12/2024}	3,677.76 (N.A.) {5,190.26}	5,046.07	-
		1491	SURFACE TRIANGLE LINE BETWEEN BHADURA STATION AND NEW CROSSING STN KARMA DOUBLING (<i>ECR</i>) (N22000525)	10-2022	10/2027 (N.A.) {10/2027}	199.96 (N.A.) {199.96}	55.09	-
		1492	MUGHALSARAI - ALLAHABAD - 3RD LINE (<i>NCR</i>) (N22000544)	8-2019	12/2026 (N.A.) {12/2026}	2,390.00 (N.A.) {2,390.00}	83.10	55.00
		1493	ALIGARH-HARDUAGANJ FLYOVER (22 KM) (<i>NCR</i>) (N22000545)	4-2020	6/2026 (N.A.) {6/2026}	1,456.89 (1,244.13) {1,456.89}	10.14	8.00
		1494	LALITPUR - BIRARI WITH FLYOVER AT LALITPUR (<i>NCR</i>) (N22000546)	3-2017	12/2024 (N.A.) {6/2025}	260.00 (356.00) {356.00}	181.47	55.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1495	ALIGARH-DAUD KHAN - 3RD LINE 6.9 KM AND CONSTRUCTION OF FLYOVER AT DAUD KHAN (NCR) (N22000562)	4-2019	12/2025 (N.A.) {12/2025}	451.99 (779.49) {779.49}	95.56	37.00
		1496	ALLAHABAD-BAMHRAULI - 4TH LINE (10 KM) WITH FLY-OVER AT SUBEDARGANJ (NCR) (N22000563)	4-2019	3/2026 (N.A.) {3/2026}	494.11 (N.A.) {494.11}	42.61	42.00
		1497	BHANDAI - FLYOVER FOR ETAWAH BOUND DOWN TRAINS (NCR) (N22000564)	4-2019	12/2025 (N.A.) {3/2026}	187.21 (N.A.) {250.17}	2.72	8.00
		1498	SAHJANWA - DOHRIGHAT (NER) (N22000565)	8-2019	3/2029 (N.A.) {12/2027}	371.77 (N.A.) {1,319.75}	544.30	2.50
		1499	BAHRAICH - NANPARA - NEPALGANJ (56.15 KM) (NER) (N22000566)	7-2020	12/2024 (N.A.) {6/2025}	950.00 (N.A.) {341.66}	267.18	20.00
		1500	BAHRAICH SRAVASTI BALRAMPUR (TULSIPUR) (NER) (N22000569)	10-2018	10/2030 (N.A.) {12/2026}	1,600.00 (N.A.) {4,939.78}	1,025.83	6.00
		1501	JANGHAI PRATAPGARH AMETHI DOUBLING (NR) (N22000583)	11-2017	3/2025 (N.A.) {12/2025}	701.98 (N.A.) {1,100.00}	21.80	60.00
		1502	BARABANKI MALHAUR 3RD AND 4TH LINE (32.84 KM) (NR) (N22000590)	1-2019	3/2025 (N.A.) {12/2025}	323.85 (N.A.) {407.00}	3.60	55.00
		1503	DOUBLING BETWEEN JAUNPUR JN-ZAFFARABAD (6.28 KM) (NR) (N22000591)	3-2023	12/2026 (N.A.) {12/2026}	177.33 (N.A.) {177.33}	0.00	-
		1504	JANGHAI-PHAPHAMAU - DOUBLING WITH ELECTRIFICATION (46.79 KM) (RVNL) (N22000596)	11-2018	3/2025 (N.A.) {3/2025}	357.48 (N.A.) {409.38}	362.09	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1505	BHATNI - AUNRIHAR WITH ELECTRIFICATION (125 KM) (EXCL INDARA - MAU (116.95 KM)) (RVNL) (N22000598)	5-2018	3/2024 (N.A.) {2/2025}	1,177.96 (N.A.) {2,529.46}	1,636.33	-
		1506	MATHURA - VRINDAVAN (11 KM) (NCR) (N22000612)	8-2022	6/2025 (N.A.) {6/2025}	402.88 (N.A.) {402.88}	0.00	-
		1507	DOMINGARH - GORAKHPUR - GORAKHPUR CANTT - KUSUMHI - 3RD RUNNING LINE (21.15 KM) (NER) (N22000613)	11-2016	6/2024 (N.A.) {7/2025}	186.85 (N.A.) {470.47}	458.41	85.00
	ROAD TRANSPORT AND HIGHWAYS	1508	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B (MoRTH) (N24000331)	12-2019	4/2022 (N.A.) {4/2025}	282.41 (N.A.) {319.96}	274.17	88.00
		1509	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 (NHAI) (N24000556)	3-2016	4/2019 (N.A.) {3/2025}	899.00 (1,633.98) {1,633.98}	1,143.19	96.42
		1510	4-LANNING OF HARIDWAR- NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 (NHAI) (N24000564)	3-2016	7/2020 (N.A.) {5/2025}	1,408.00 (1,659.12) {1,659.12}	1,263.59	85.60
		1511	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO (NHAI) (N24000796)	3-2018	12/2021 (N.A.) {7/2024}	1,117.84 (N.A.) {1,203.92}	1,198.22	99.76
		1512	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA (NHAI) (N24000798)	3-2018	11/2021 (N.A.) {6/2025}	2,140.93 (N.A.) {2,140.93}	2,065.57	98.56

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1513	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN (NHAI) (N24001306)	10-2020	3/2023 (N.A.) {5/2024}	724.60 (N.A.) {724.60}	569.96	95.20
		1514	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD (MoRTH) (N24001421)	7-2018	2/2024 (N.A.) {8/2025}	1,948.25 (N.A.) {1,948.25}	1,063.05	72.00
		1515	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH- 24A INCLUDING RETAINING W (MoRTH) (N24001424)	3-2021	9/2023 (N.A.) {1/2025}	185.09 (269.81) {269.81}	263.39	100.00
		1516	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM (MoRTH) (N24001456)	4-2020	2/2024 (N.A.) {1/2025}	199.39 (212.96) {199.39}	186.47	100.00
		1517	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH-730C F (MoRTH) (N24001457)	4-2020	7/2024 (N.A.) {4/2025}	172.50 (169.56) {172.50}	95.76	70.00
		1518	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP (MoRTH) (N24001461)	4-2020	3/2024 (N.A.) {4/2025}	236.47 (N.A.) {236.47}	132.09	86.00
		1519	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP (MoRTH) (N24001462)	4-2020	7/2024 (N.A.) {4/2025}	211.09 (N.A.) {211.09}	136.60	95.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1520	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 (MoRTH) (N24001464)	3-2021	8/2023 (N.A.) {4/2025}	264.86 (N.A.) {264.86}	112.75	79.00
		1521	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO (MoRTH) (N24001469)	11-2021	5/2024 (N.A.) {4/2025}	307.11 (N.A.) {307.11}	187.10	86.00
		1522	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH-730C FROM KM.0.00 TO 52.770 UNDER GNHCP (MoRTH) (N24001471)	4-2020	11/2024 (N.A.) {4/2025}	325.24 (340.16) {325.24}	249.71	95.00
		1523	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) (MoRTH) (N24001479)	3-2021	5/2024 (N.A.) {6/2025}	395.62 (392.03) {395.62}	273.44	66.00
		1524	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH-334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW (MoRTH) (N24001480)	10-2021	4/2024 (N.A.) {3/2025}	227.06 (N.A.) {227.06}	141.81	100.00
		1525	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO(NEAR MOHAND) OF GANESHPUR ? DEHRADUN SECTION FROM K (NHAI) (N24001523)	3-2021	10/2023 (N.A.) {3/2025}	836.24 (N.A.) {836.24}	782.55	98.85

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1526	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR ? DEHRADUN SECTION FROM (NHAI) (N24001524)	3-2021	10/2023 (N.A.) {3/2025}	990.28 (N.A.) {990.28}	997.62	98.78
		1527	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF (MoRTH) (N24001587)	3-2020	9/2024 (N.A.) {4/2025}	262.37 (343.77) {343.77}	261.37	80.00
		1528	4L SPUR OF SHAMLI- MUZZAFARNAGAR CONNECTING NH-709AD (PANIPAT-SHAMLI- MUZAFFARNAGAR) AND NH-58 (MEERUT (NHAI) (N24001726)	1-2023	8/2024 (N.A.) {8/2024}	391.26 (N.A.) {391.26}	14.12	80.30
		1529	IMPROVEMENT AND UP- GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B (NHAI) (N24001727)	3-2022	2/2025 (N.A.) {2/2025}	762.62 (N.A.) {762.62}	491.62	83.35
		1530	IMPROVEMENT AND UP- GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO (NHAI) (N24001728)	12-2021	7/2025 (N.A.) {7/2025}	1,138.81 (N.A.) {1,138.81}	440.25	99.82
		1531	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT ? SHAMLI ? MUZAFFARNAGAR) AND NH-709A (KARN (NHAI) (N24001729)	8-2022	4/2024 (N.A.) {4/2025}	326.79 (N.A.) {329.79}	105.11	93.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1532	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) (NHAI) (N24001730)	12-2021	1/2025 (N.A.) {3/2025}	1,384.79 (N.A.) {1,384.79}	657.94	97.98
		1533	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 (NHAI) (N24001731)	12-2021	5/2025 (N.A.) {5/2025}	2,470.64 (N.A.) {2,335.00}	613.44	80.16
		1534	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS (NHAI) (N24001732)	12-2021	10/2024 (N.A.) {4/2025}	540.97 (N.A.) {540.97}	253.70	76.57
		1535	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.-MAVIKALAN) TO VILL.-LOHADDA FROM K (NHAI) (N24001733)	3-2022	8/2024 (N.A.) {4/2025}	1,602.48 (N.A.) {1,602.48}	395.79	85.00
		1536	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-LOHADDA TO VILL.-KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. (NHAI) (N24001734)	3-2022	8/2024 (N.A.) {4/2025}	1,335.45 (N.A.) {1,335.45}	397.39	74.00
		1537	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-KHYAWARI TO VILL.-LATIFPUR AT SAHARANPUR BYPASS FROM KM (NHAI) (N24001735)	3-2022	8/2024 (N.A.) {4/2025}	1,428.19 (N.A.) {1,428.19}	472.63	80.00
		1538	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-KARAUNDA MAHAJAN TO VILL.-KHYAWARI FROM KM. 56.500 TO K (NHAI) (N24001736)	1-2022	8/2024 (N.A.) {4/2025}	1,159.96 (N.A.) {1,159.96}	510.48	98.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1539	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III (NHAI) (N24001737)	11-2021	4/2024 (N.A.) {4/2024}	923.15 (N.A.) {923.15}	455.61	97.92
		1540	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV (NHAI) (N24001738)	9-2021	10/2023 (N.A.) {12/2024}	300.79 (N.A.) {300.79}	122.56	64.36
		1541	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U (NHAI) (N24001739)	10-2019	11/2023 (N.A.) {12/2024}	1,779.83 (N.A.) {2,200.00}	1,066.00	99.80
		1542	4L OF SHAMLI BYAPSS-SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II (NHAI) (N24001744)	5-2019	11/2022 (N.A.) {3/2025}	779.17 (N.A.) {779.17}	54.69	96.45
		1543	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N (NHAI) (N24001745)	12-2021	7/2025 (N.A.) {7/2025}	1,972.10 (N.A.) {1,936.00}	431.50	57.55
		1544	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR (NHAI) (N24001746)	3-2021	4/2024 (N.A.) {6/2025}	364.47 (N.A.) {364.47}	174.61	87.29
		1545	4 LANING OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74 (NHAI) (N24001753)	2-2022	6/2024 (N.A.) {3/2025}	570.98 (578.02) {578.02}	371.14	93.05

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1546	SPUR OF MEERUT-GARH-MUKTESHWAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN (NHAI) (N24001754)	1-2022	10/2024 (N.A.) {10/2024}	953.79 (N.A.) {953.79}	384.66	52.10
		1547	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH (NHAI) (N24001755)	10-2019	3/2023 (N.A.) {12/2024}	1,936.68 (N.A.) {2,458.03}	1,380.90	98.80
		1548	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR (NHAI) (N24001772)	8-2021	3/2024 (N.A.) {12/2024}	1,147.26 (N.A.) {1,147.26}	81.34	51.00
		1549	4L BYPASSES FOR JAGATPUR, B4ABUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA (NHAI) (N24001815)	12-2022	11/2024 (N.A.) {11/2024}	1,699.00 (1,078.00) {1,699.00}	64.39	98.00
		1550	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 (NHAI) (N24001826)	2-2019	2/2022 (N.A.) {12/2024}	927.77 (N.A.) {1,603.00}	1,202.77	79.45
		1551	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 (NHAI) (N24001830)	6-2020	11/2023 (N.A.) {12/2024}	2,002.79 (N.A.) {2,002.79}	1,989.85	99.00
		1552	4L FROM MATHURA BYPASS (START) AT EXISTING KM. 154.20 OF NH-44 TO GAJU VILLAGE AT KM 32.982 OF NH-53 (NHAI) (N24001851)	1-2022	3/2025 (N.A.) {3/2025}	1,738.20 (N.A.) {1,738.20}	742.13	65.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1553	6L OF AGRA BYPASS (NORTHERN) CONNECTING KM. 174.500 OF NH-2 (NEW NH-19) TO KM. 141.000 OF YAMUNA EXP (NHAI) (N24001852)	10-2021	2/2025 (N.A.) {2/2025}	957.62 (N.A.) {957.62}	832.80	86.00
		1554	CONSTRUCTION OF LEFT OUT PORTION OF AGRA INNER RING ROAD CONNECTING VILLAGE DEORI TO NH-44 VILLAGE B (NHAI) (N24001853)	10-2021	9/2024 (N.A.) {3/2025}	772.05 (N.A.) {772.05}	593.39	67.50
		1555	CONSTRUCTION OF 4-LANE GREEN FIELD HIGHWAY FROM KM. 35.000 TO KM. 49.155 OF NH- 731A WITH PAVED SHOUL (MoRTH) (N24001929)	1-2022	10/2025 (N.A.) {10/2025}	697.66 (N.A.) {697.66}	281.64	80.00
		1556	BALANCE WORKS OF 4-LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 (NEW NH NO. 09) FROM KM. 0.000 (KM 1 (NHAI) (N24001992)	8-2022	2/2024 (N.A.) {3/2025}	199.31 (199.38) {199.38}	130.59	77.02
		1557	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER HIGHWAY FROM DESIGN CH.0.000 TO CH.49.200 OF NH- 731B ON (MoRTH) (N24001996)	3-2022	11/2025 (N.A.) {11/2025}	640.18 (602.76) {602.76}	424.36	63.00
		1558	CONSTRUCTION OF SHOHRATGARH BYPASS ON NH- 730 UNDER EPC MODE IN THE STATE OF UTTAR PRADESH (MoRTH) (N24001997)	10-2022	5/2025 (N.A.) {5/2025}	189.31 (N.A.) {189.31}	52.61	15.00
		1559	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 90.00 TO (MoRTH) (N24002015)	11-2021	6/2025 (N.A.) {6/2025}	403.36 (328.49) {403.36}	117.95	47.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1560	CONSTRUCTION OF PRATAPGARH BYPASS (EXTENSION) CONNECTING NH-31 TO NH-330 (MoRTH) (N24002016)	10-2022	6/2025 (N.A.) {6/2025}	225.17 (N.A.) {225.17}	95.68	50.00
		1561	WIDENING TO FOUR LANE WITH PAVED SHOULDER FROM DESIGN KM.49.200 TO KM.89.285 OF NH-731B ON EPC MODE (MoRTH) (N24002029)	3-2022	1/2026 (N.A.) {1/2026}	917.91 (956.30) {917.91}	548.89	34.00
		1562	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM EXISTING KM.0.000 TO KM.55.610 (DESIGN KM. 0.000 T (MoRTH) (N24002031)	12-2021	2/2026 (N.A.) {2/2026}	840.93 (773.58) {840.93}	449.58	29.00
		1563	CONSTRUCTION OF 4-LANE HIGHWAY WITH PAVED SHOULDERS FROM KM 49.155 TO KM 74.700 OF NH-731A ON HYBRID (MoRTH) (N24002032)	1-2022	1/2026 (N.A.) {1/2026}	1,156.72 (N.A.) {1,156.72}	286.10	40.00
		1564	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM GOGWAN JALALPUR (SHAMLI DISTRICT) TO RANIPUR (NHAI) (N24002036)	4-2022	5/2025 (N.A.) {5/2025}	1,843.59 (N.A.) {1,843.59}	814.70	41.00
		1565	GARHMUKTESHWAR (KM. 83.200 OF NH-24) TO MEERUT (KM. 9.860 OF NH-235) INCLUDING CONNECTOR TO NH-119 (NHAI) (N24002073)	10-2019	10/2023 (N.A.) {6/2025}	2,068.99 (2,171.00) {2,171.00}	209.60	53.08
		1566	WIDENING OF RAEBARELI TO PRAYAGRAJ SECTION FROM KM. 82.650 TO KM. 161.450 OF NH-30 AND LINK ROAD FRO (NHAI) (N24002085)	11-2023	3/2025 (N.A.) {3/2025}	1,470.93 (N.A.) {1,470.93}	69.56	99.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1567	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002086)	10-2022	7/2025 (N.A.) {7/2025}	1,706.47 (N.A.) {1,706.47}	719.13	63.07
		1568	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002087)	10-2022	10/2025 (N.A.) {10/2025}	1,493.14 (N.A.) {1,493.14}	93.30	49.50
		1569	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002088)	10-2022	8/2025 (N.A.) {8/2025}	1,493.50 (N.A.) {1,493.50}	492.86	41.00
		1570	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER GREENFIELD SECTION OF N (NHAI) (N24002089)	10-2022	6/2025 (N.A.) {6/2025}	617.87 (N.A.) {617.88}	106.20	58.00
		1571	CONSTRUCTION OF FOUR-LANE ?WESTERN SIDE SPUR OF RAMPUR-RUDRAPUR SECTION CONNECTING NH-24 TO NH-87 BY (NHAI) (N24002090)	3-2021	11/2024 (N.A.) {4/2025}	646.27 (N.A.) {646.27}	45.38	34.57
		1572	IMPROVEMENT , UP-GRADATION OF NH-734 SECTION OF MORADABAD - THAKURDWARA - KASHIPUR: ?PACKAGE-I: MORA (NHAI) (N24002093)	10-2022	9/2025 (N.A.) {9/2025}	1,841.92 (N.A.) {1,841.92}	334.38	43.30
		1573	IMPROVEMENT AND UP- GRADATION OF EXISTING ROAD TO 4L PS FROM KM 123.650 TO 175.080, FROM START OF SHA (NHAI) (N24002094)	9-2022	11/2025 (N.A.) {11/2025}	1,212.26 (N.A.) {1,212.26}	329.01	23.15

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1574	FOUR LANING OF SONAULI GORAKHPUR SECTION OF NH 29E (NEW NH 24) FROM DESIGN CH. 0.000 TO DESIGN CH. 7 (NHAI) (N24002095)	12-2021	3/2025 (N.A.) {3/2025}	2,555.50 (N.A.) {2,555.50}	866.10	48.53
		1575	CONSTRUCTION OF 4 LANE GREEN FIELD NORTHERN EAST SIDE GORAKHPUR BYPASS (26.616 KMS) STARTING FROM NH (NHAI) (N24002096)	2-2023	1/2026 (N.A.) {1/2026}	1,973.98 (N.A.) {1,973.98}	736.14	36.37
		1576	STRENGTHENING OF EXISTING 4L AYODHYA BYPASS SECTION FROM DESIGN KM.121.600 TO KM. 144.020 OF NH 28 ((NHAI) (N24002097)	2-2023	9/2025 (N.A.) {8/2025}	526.45 (N.A.) {526.45}	195.61	77.00
		1577	CONSTRUCTION OF RING ROAD AROUND KANPUR FROM KM.000 TO KM. 23.325 (CHACHENDI SACHENDI I TO MAHARAJPU (NHAI) (N24002104)	1-2023	6/2026 (N.A.) {6/2026}	1,754.00 (N.A.) {1,754.00}	284.77	25.00
		1578	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS (PHASE-I) FROM DESIGN KM 43+200 (AT MAHUWARI VI (NHAI) (N24002105)	8-2023	6/2026 (N.A.) {6/2026}	1,378.36 (N.A.) {739.00}	174.00	19.65
		1579	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS FROM DESIGN KM 50.860 (NABABA URF NIBI KALA UPA (NHAI) (N24002106)	8-2023	3/2025 (N.A.) {5/2025}	993.77 (N.A.) {349.48}	343.31	84.50
		1580	CONSTRUCTION OF MARIAHU BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION (KM.53.540 TO KM.59.200) (MoRTH) (N24002115)	3-2023	8/2025 (N.A.) {2/2026}	438.24 (362.39) {438.24}	186.82	20.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1581	REHABILITATION AND UPGRADATION FROM KM 51.600 TO KM 75.700 OF NH-321G (NUHKHAS TO ETAH SECTION) TO T (MoRTH) (N24002116)	1-2022	8/2025 (N.A.) {8/2025}	343.54 (N.A.) {343.54}	55.83	33.00
		1582	CONSTRUCTION OF JASRA BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION FROM KM. 379.670 ON NH-76 () (MoRTH) (N24002120)	2-2023	9/2025 (N.A.) {9/2025}	274.06 (N.A.) {274.06}	110.36	80.00
		1583	IMPROVEMENT AND UP- GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM. 420.00 (MoRTH) (N24002121)	1-2022	9/2025 (N.A.) {9/2025}	509.65 (N.A.) {509.65}	150.06	18.00
		1584	REHABILITATION AND UP- GRADATION FROM KM. 0.000 TO KM. 40.390 OF NH-730S (MAHARAJGANJ ? NICHLOUL ? TH (MoRTH) (N24002134)	3-2023	12/2025 (N.A.) {12/2025}	809.25 (N.A.) {809.25}	211.36	20.00
		1585	CONSTRUCTION OF FOUR LANE HIGHWAY WITH PAVED SHOULDER FROM KM.74.700 TO KM.112.950 OF NH-731A (I/C Y (MoRTH) (N24002138)	3-2022	6/2026 (N.A.) {6/2026}	1,141.67 (N.A.) {1,141.67}	348.70	28.00
		1586	CONSTRUCTION OF BALRAMPUR BYPASS WITH 2L FLEXIBLE PAVEMENT CONFIGURATION FROM KM.223.000 OF NH-330 T (MoRTH) (N24002150)	12-2022	2/2026 (N.A.) {2/2026}	515.69 (N.A.) {515.69}	146.84	13.00
		1587	WIDENING TO 4L RIGID PAVEMENT CONFIGURATION FROM KM 90.00 TO KM 100.800 OF NH-96 (KM 42.0 TO KM 53.3 (MoRTH) (N24002199)	12-2022	11/2026 (N.A.) {11/2026}	309.63 (N.A.) {309.63}	3.62	15.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1588	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER/FOUR LANE CONFIGURATION FROM EXISTING K (MoRTH) (N24002201)	1-2022	5/2027 (N.A.) {5/2027}	974.19 (N.A.) {974.19}	556.73	-
		1589	REHABILITATION AND UPGRADATION TO FOUR LANE ROAD FROM KM 70.500 TO KM 78.600 OF NH-92 UNDER EPC MODE (MoRTH) (N24002211)	1-2022	1/2027 (N.A.) {1/2027}	296.02 (N.A.) {296.02}	24.72	-
		1590	WIDENING AND STRENGTHENING FROM DESIGN KM. 67.280 TO KM. 88.622 OF NH-727A (SALEMPUR-MAIRWA ROAD) TO (MoRTH) (N24002212)	3-2023	7/2026 (N.A.) {7/2026}	371.89 (N.A.) {371.89}	105.34	-
		1591	REHABILITATION and UP-GRADATION TO 2L+PS FROM KM. 0.0 TO KM. 7.80 AND KM. 35.400 TO KM. 52.345 (DESI (MoRTH) (N24002213)	3-2023	7/2026 (N.A.) {7/2026}	701.02 (N.A.) {701.02}	233.83	-
		1592	CONSTRUCTION OF AMETHI BYPASS (PART-II) AT KM.30.050 OF NH-931 UNDER EPC MODE IN THE STATE OF UTTAR (MoRTH) (N24002214)	12-2022	2/2027 (N.A.) {2/2027}	283.86 (N.A.) {283.86}	58.89	-
URBAN DEVELOPMENT		1593	KANPUR METRO RAIL PROJECT (LMRCL) (N28000144)	5-2019	3/2024 (N.A.) {12/2026}	11,076.48 (N.A.) {11,076.48}	8,344.03	71.50
		1594	AGRA METRO RAIL PROJECT (LMRCL) (N28000145)	5-2019	3/2024 (N.A.) {12/2026}	8,379.62 (N.A.) {8,379.62}	4,527.78	51.50

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>WATER RESOURCES</u>	1595	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH (UPJalNigam) (N30000021)	1-2019	12/2021 (N.A.) {12/2024}	231.79 (234.03) {234.03}	141.79	96.00
		1596	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH (UPJalNigam) (N30000024)	2-2019	6/2022 (N.A.) {12/2025}	681.78 (N.A.) {690.71}	13.34	13.00
UTTARAKHAND	<u>CIVIL AVIATION</u>	1597	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN (AAI) (N04000085)	7-2018	9/2020 (N.A.) {9/2024}	456.86 (500.00) {500.00}	483.86	100.00
	<u>POWER</u>	1598	TEHRI PUMPED STORAGE PLANT(1000MW) (THDCIL) (N18000010)	7-2006	2/2016 (N.A.) {7/2025}	1,657.00 (4,825.60) {7,877.81}	7,716.13	97.95
		1599	TAPOVAN-VISHNUGAD HEP (4X130MW) (NTPC) (N18000014)	11-2006	3/2013 (N.A.) {4/2029}	2,978.48 (N.A.) {10,907.00}	6,679.38	72.40
		1600	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT (THDCIL) (N18000042)	8-2008	6/2013 (N.A.) {12/2026}	2,491.58 (3,860.35) {6,630.60}	4,473.90	69.50
		1601	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW (NTPC) (N18000142)	7-2012	8/2017 (N.A.) {8/2017}	1,527.00 (N.A.) {1,527.00}	149.93	9.80
	<u>RAILWAYS</u>	1602	RISHIKESH - KARNAPRAYAG NEW LINE (RVNL) (N22000406)	4-2011	12/2024 (N.A.) {3/2025}	16,216.00 (N.A.) {24,659.00}	18,820.04	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1603	4-LANING OF KASHIPUR- SITARGANJ SECTION (AMR) (N24000465)	11-2012	8/2016 (N.A.) {8/2016}	605.84 (N.A.) {605.84}	0.00	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1604	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 (NHAI) (N24000559)	3-2016	10/2019 (N.A.) {3/2025}	720.00 (1,150.00) {1,150.00}	666.15	97.22
		1605	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 (NHIDCL) (N24000741)	3-2018	11/2020 (N.A.) {3/2024}	274.31 (N.A.) {274.31}	251.61	97.31
		1606	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI (NHIDCL) (N24000742)	3-2018	11/2020 (N.A.) {3/2024}	403.36 (N.A.) {403.36}	337.72	98.93
		1607	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA (NHIDCL) (N24000743)	3-2018	11/2020 (N.A.) {3/2024}	417.24 (N.A.) {417.24}	344.20	99.88
		1608	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000772)	12-2017	12/2019 (N.A.) {12/2019}	257.34 (N.A.) {257.34}	232.69	100.00
		1609	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000773)	12-2017	12/2019 (N.A.) {12/2019}	200.34 (253.43) {200.34}	227.98	100.00
		1610	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 (MoRTH) (N24000774)	12-2017	12/2019 (N.A.) {12/2019}	248.22 (N.A.) {248.22}	236.80	100.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1611	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000775)	6-2017	6/2019 (N.A.) {3/2023}	282.08 (N.A.) {282.08}	234.97	100.00
		1612	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG (MoRTH) (N24000776)	11-2017	11/2019 (N.A.) {11/2019}	232.81 (N.A.) {232.81}	201.58	100.00
		1613	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION (MoRTH) (N24000777)	11-2017	11/2019 (N.A.) {11/2019}	283.51 (N.A.) {283.51}	278.51	100.00
		1614	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000778)	11-2017	11/2019 (N.A.) {11/2019}	266.52 (N.A.) {266.52}	250.34	100.00
		1615	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR (MoRTH) (N24000779)	2-2018	2/2020 (N.A.) {3/2023}	418.88 (N.A.) {418.88}	339.71	94.00
		1616	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K (MoRTH) (N24000780)	2-2018	(N.A.) {4/2023}	293.68 (N.A.) {293.68}	244.25	100.00
		1617	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN (MoRTH) (N24000781)	5-2018	5/2020 (N.A.) {12/2023}	248.00 (N.A.) {248.00}	120.50	65.56

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1618	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 (MoRTH) (N24000782)	3-2018	(N.A.) {}	460.73 (N.A.) {461.00}	0.00	-
		1619	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) (NHIDCL) (N24000855)	3-2018	7/2022 (N.A.) {1/2026}	1,383.78 (N.A.) {1,383.78}	687.14	62.99
		1620	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER (MoRTH) (N24001130)	8-2016	12/2017 (N.A.) {12/2017}	234.88 (273.49) {234.88}	237.19	100.00
		1621	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR ? DEHRADUN SECTION FROM KM. (NHAI) (N24001525)	3-2021	3/2024 (N.A.) {3/2025}	169.08 (N.A.) {169.08}	95.77	99.99
		1622	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF (NHAI) (N24001526)	8-2021	10/2024 (N.A.) {8/2025}	1,377.79 (1,384.11) {1,377.79}	679.10	47.31
		1623	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) (NHAI) (N24001553)	3-2022	2/2025 (N.A.) {3/2025}	1,092.90 (1,092.90) {1,092.90}	463.92	75.07
		1624	4L POANTA SAHEB?MEDNIPUR FROM KM. 435.65 TO KM. 458.65 OF NH-07(PKG-1) (NHAI) (N24001990)	6-2022	5/2025 (N.A.) {5/2025}	524.54 (683.26) {683.26}	76.94	70.80

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1625	ACCESS ROAD/BRIDGE CONNECTIVITY FROM NH-09 AT KM.40 NEAR JAGBUDA BRIDGE (INDIA) TO BOUNDARY PILLAR (NHAI) (N24001991)	5-2022	9/2024 (N.A.) {5/2025}	314.31 (N.A.) {314.31}	169.85	64.40
		1626	CONSTRUCTION FOR MITIGATION MEASURES KM 368.00-UTTARAKHAND-TO KM 433.00 ON NH-07-PKG-1 (NHIDCL) (N24002163)	12-2023	12/2025 (N.A.) {12/2025}	216.88 (N.A.) {216.88}	15.09	44.58
		1627	CONSTRUCTION FOR MITIGATION MEASURES KM 450.00-UTTARAKHAND-TO KM 468.00 ON NH-07-PKG-3 (NHIDCL) (N24002164)	12-2023	12/2025 (N.A.) {12/2025}	250.33 (N.A.) {250.33}	18.41	43.00
		1628	CONSTRUCTION FOR MITIGATION MEASURES PKG-2 (NHIDCL) (N24002206)	12-2023	6/2026 (N.A.) {6/2026}	259.64 (N.A.) {259.64}	0.00	-
<u>WEST BENGAL</u>	<u>CIVIL AVIATION</u>	1629	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA (AAI) (N04000080)	1-2016	3/2020 (N.A.) {12/2023}	458.00 (N.A.) {458.00}	246.68	100.00
		1630	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA (AAI) (N04000081)	1-2019	11/2021 (N.A.) {5/2023}	389.71 (N.A.) {397.00}	396.57	100.00
		1631	NSCBI AIRPORT KOLKATA: RE- CONSTRUCTION OF RIGID POSITIONS OF SECONDARY RUNWAY, 'K' AND 'A' TAXIWAY (AAI) (N04000109)	4-2023	10/2025 (N.A.) {10/2025}	328.30 (N.A.) {328.30}	74.64	36.00
		1632	BAGDOGRA AIRPORT: DEVELOPMENT OF NEW CIVIL ENCLAVE AT BAGDOGRA AIRPORT. SUB-HEAD : CONSTRUCTION OF N (AAI) (N04000115)	8-2024	3/2027 (N.A.) {3/2027}	1,549.00 (N.A.) {1,549.00}	87.37	5.50

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	COAL	1633	RANIGANJ MASTER PLAN (ECL) (N06000163)	8-2009	8/2019 (N.A.) {8/2024}	2,661.73 (N.A.) {5,146.48}	774.85	42.00
		1634	SIDULI MINE (OC AND UG) (ECL) (N06000165)	5-2018	3/2027 (N.A.) {3/2027}	535.18 (N.A.) {535.17}	4.39	14.00
		1635	NAKRAKONDA KUMARDIH B OCP (ECL) (N06000170)	8-2018	3/2029 (N.A.) {3/2029}	502.68 (N.A.) {502.67}	65.97	25.50
		1636	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT (ECL) (N06000191)	4-2020	3/2026 (N.A.) {3/2026}	483.65 (N.A.) {483.65}	51.73	12.00
		1637	2.0 MTPA BHOJUDIH NLW WASHERY (BCCL) (N06000195)	12-2015	9/2020 (N.A.) {3/2025}	341.22 (341.22) {341.22}	342.18	96.60
		1638	SONEPUR BAZARI EXPANSION OC (ECL) (N06000220)	7-2021	3/2029 (N.A.) {3/2029}	5,365.88 (5,366.00) {5,365.88}	530.13	17.00
		1639	EXPANSION PR OF JHANJRA UG (5.00 MTY) (ECL) (N06000223)	4-2020	3/2029 (N.A.) {3/2029}	1,210.12 (N.A.) {1,210.12}	468.56	38.00
		1640	MOHANPUR EXPANSION OC PHASE II (ECL) (N06000236)	11-2020	3/2026 (N.A.) {3/2026}	888.99 (N.A.) {888.99}	62.79	30.00
		1641	BONJEMEHARI EXPANSION OCP (ECL) (N06000244)	8-2021	3/2026 (N.A.) {3/2026}	570.12 (N.A.) {570.11}	80.23	16.00
		1642	ITAPARA OC (ECL) (N06000272)	12-2023	3/2030 (N.A.) {3/2030}	929.10 (N.A.) {929.10}	60.66	7.00
		1643	UCE OF TILABONI UG (ECL) (N06000276)	1-2023	3/2029 (N.A.) {3/2029}	749.07 (N.A.) {749.07}	51.46	10.00
		1644	UCE OF PARASEA BELBAID REORGANISATION UG (ECL) (N06000277)	1-2023	3/2029 (N.A.) {3/2028}	389.10 (N.A.) {389.10}	130.56	16.00
		1645	PARASCOLE JAMBAD OCP (ECL) (N06000281)	11-2024	3/2037 (N.A.) {3/2037}	1,193.55 (N.A.) {1,193.55}	0.00	-

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1646	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED (CPWD EDUCATION) (N28000146)	3-2020	6/2020 (N.A.) {5/2024}	193.83 (N.A.) {193.83}	185.75	-
	<u>HOME AFFAIRS</u>	1647	NSG AT KOLKATA (CPWD FOR MHA) (N28000104)	10-2014	4/2018 (N.A.) {8/2025}	162.88 (210.83) {210.83}	189.72	90.75
	<u>MINES</u>	1648	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA (CPWD) (N10000015)	4-2019	4/2022 (N.A.) {8/2026}	255.37 (N.A.) {255.37}	66.26	32.00
	<u>PETROLEUM</u>	1649	DURGAPUR-HALDIA PIPELINE PROJECT (GAIL) (N16000275)	3-2017	12/2020 (N.A.) {12/2025}	1,740.00 (2,433.15) {2,433.15}	2,117.50	88.60
		1650	CITY GAS DISTRIBUTION IN WEST BENGAL (HPCL) (N16000392)	3-2019	3/2031 (N.A.) {3/2029}	5,830.20 (N.A.) {5,830.20}	844.59	28.00
		1651	HALDIA PANAGARH PIPELINE PROJECT (HPCL) (N16000478)	11-2022	11/2025 (N.A.) {11/2025}	1,010.00 (N.A.) {1,010.00}	382.99	70.80
		1652	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS (IOCL) (N16000491)	3-2022	3/2030 (N.A.) {6/2031}	609.00 (N.A.) {609.00}	58.81	1.60
		1653	CGD PROJECT IN WEST BENGAL 11TH ROUND (HPCL) (N16000498)	6-2022	6/2030 (N.A.) {6/2030}	2,628.00 (N.A.) {2,628.00}	181.10	20.50
		1654	CITY GAS DISTRIBUTION PROJECTS AT ALIPURDUAR AND COOCH BEHAR (BPCL) (N16000522)	12-2022	3/2030 (N.A.) {3/2030}	1,017.00 (N.A.) {1,017.00}	134.42	25.20
	<u>POWER</u>	1655	RAMMAM-III HEPP (3X40 MW) (NTPC) (N18000178)	9-2014	9/2019 (N.A.) {3/2029}	1,381.84 (N.A.) {1,803.00}	1,119.24	43.68

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	1656	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER (ER) (220100272)	4-2000	3/2019 (N.A.) {2/2026}	1,188.91 (N.A.) {2,582.49}	1,174.10	75.00
		1657	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA- BARASAI VIA BIMANBANDER (MTP) (KOMRCL) (N22000108)	4-2010	3/2016 (N.A.) {3/2016}	2,397.72 (N.A.) {2,397.72}	197.20	17.00
		1658	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) (RVNL) (N22000109)	4-2010	3/2014 (N.A.) {12/2025}	2,298.42 (N.A.) {2,733.86}	392.98	-
		1659	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) (RVNL) (N22000110)	4-2010	3/2016 (N.A.) {3/2026}	3,951.98 (N.A.) {8,964.35}	7,387.40	-
		1660	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. (RVNL) (N22000111)	4-2010	3/2016 (N.A.) {12/2026}	2,913.51 (N.A.) {4,834.54}	3,918.86	-
		1661	PURULIA TO KOTSHILA DOUBLING (39.1 KM) (SER) (N22000510)	4-2018	6/2022 (N.A.) {3/2025}	338.00 (N.A.) {393.83}	280.67	85.00
		1662	AZIMGANJ-MURSHIDABAD (JIYAGANJ) INCL. RLY. BRIDGE OVER RIVER BHAGIRATHI (ER) (N22000609)	10-2001	2/2024 (N.A.) {2/2024}	164.33 (N.A.) {187.05}	159.40	100.00
		1663	NAHATI - RANAGHAT 3RD LINE (MM OF KALINARAYANPUR - KRISHNANAGAR) (ER) (N22000624)	7-2015	3/2025 (N.A.) {3/2026}	283.54 (N.A.) {283.54}	163.55	44.00

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1664	EAST WEST METRO CORRIDOR KOLKATA (KOMRCL) (N22000628)	2-2009	9/2016 (N.A.) {6/2024}	4,874.58 (8,575.00) {10,442.41}	0.00	-
		1665	KALIPAHARI - BAKHTARNAGAR 5TH LINE (17.61 KM) (ER) (N22000630)	4-2024	6/2027 (N.A.) {6/2027}	350.46 (N.A.) {350.46}	0.00	-
		1666	SITARAMPUR BYE - PASS LINE (6.59 KM) (ER) (N22000631)	2-2023	3/2027 (N.A.) {3/2027}	461.64 (N.A.) {461.64}	0.34	-
	ROAD TRANSPORT AND HIGHWAYS	1667	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI () KM 0.00 TO KM . 83.785) (NHAI) (N24000463)	12-2015	6/2018 (N.A.) {8/2023}	1,083.00 (1,414.01) {1,414.01}	1,080.05	100.00
		1668	SIX-LANING OF BARWA ADDA- PANAGARH (NHAI) (N24000515)	4-2014	9/2016 (N.A.) {3/2025}	1,665.00 (N.A.) {4,949.67}	4,949.67	94.50
		1669	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU (NHAI) (N24000788)	3-2018	9/2022 (N.A.) {12/2025}	841.57 (708.30) {708.30}	9,766.24	94.20
		1670	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H (MoRTH) (N24000874)	3-2016	11/2018 (N.A.) {3/2025}	271.17 (291.20) {291.20}	193.15	79.89
		1671	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. (MoRTH) (N24000880)	2-2018	9/2020 (N.A.) {2/2025}	426.18 (426.18) {426.18}	364.92	100.00
		1672	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 (NHAI) (N24001747)	3-2020	9/2024 (N.A.) {9/2024}	2,193.23 (2,314.00) {2,314.00}	2,048.00	90.83

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1673	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA (NHAI) (N24001748)	3-2021	9/2024 (N.A.) {6/2025}	2,200.93 (N.A.) {2,616.06}	2,616.06	96.28
		1674	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE (NHAI) (N24001749)	8-2021	8/2023 (N.A.) {4/2025}	557.55 (N.A.) {567.31}	472.82	91.41
		1675	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA (NHAI) (N24001750)	8-2018	12/2021 (N.A.) {6/2025}	622.04 (N.A.) {622.04}	539.44	86.25
		1676	DEVELOPMENT TO 4/6-LANNING OF NH-31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 (MoRTH) (N24001850)	3-2022	9/2025 (N.A.) {9/2025}	995.04 (995.04) {995.04}	338.00	40.00
		1677	CONSTRUCTION OR 4 LANE RANIGANJ BYPASS OF LENGTH 5 261 KM ON NH 60 NEW NH 14 FROM KM 273 00 OF NH (MoRTH) (N24002184)	3-2023	3/2026 (N.A.) {3/2026}	410.83 (N.A.) {410.83}	135.00	23.15
		1678	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF LEVEL CROSSING NO 10 B T AT KM 307 050 OF NH 60 B (MoRTH) (N24002191)	3-2016	8/2025 (N.A.) {8/2025}	155.87 (N.A.) {155.87}	17.00	8.27
	STEEL	1679	REBUILDING OF COKE OVEN BATTERY NO.4 OF DURGAPUR STEEL PLANT (SAIL) (N12000132)	11-2023	12/2026 (N.A.) {12/2026}	916.78 (N.A.) {916.78}	72.10	4.50

Table:-7. Project List: Ongoing Projects as of 28th February 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>WATER RESOURCES</u>	1680	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA (KMDA) (N30000032)	5-2018	2/2022 (N.A.) {3/2025}	198.43 (224.69) {286.97}	75.85	90.00
		1681	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA (KMDA) (N30000034)	8-2017	9/2022 (N.A.) {12/2026}	307.12 (N.A.) {653.67}	0.00	-
		1682	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY- CHINSURAH (KMDA) (N30000042)	5-2018	2/2022 (N.A.) {3/2025}	160.00 (154.73) {154.73}	87.35	89.00
			Total			2,582,886.62 (913,344.42) {3,110,752.73}	16,67,903.28	

Abbreviations used in the Report

AGENCY_NAME	AGENCY_NAME_SHORT
AIRPORT AUTHORITY OF INDIA LIMITED	AAI
ARTIFICIAL LIMBS MANUFACTURING CORPM. OF INDIA	ALIMCO
BHARAT ALUMINUM CORPORATION	BALCO
BHABHA ATOMIC RESEARCH CENTRE	BARC
BHARAT COKING COAL LIMITED	BCCL
BRAHMAPUTRA CRECKER & POLYMER LTD.	BCPL
BHAVINI LIMITED	BHAVNI
BHARAT HEAVY ELECTRICALS LIMITED	BHEL
BANGALORE METRO RAIL CORPORATION LIMITED	BMRCL
BOKARO STEEL PLANT	BOKARO STEEL PL
BRAHMAPUTRA BOARD	BPB
BHARAT PETROLEUM CORPORATION LIMITED	BPCL
BORDER ROAD ORGANISATION	BRO
BONGAIGAON REFINERY PETROLEUM LIMITED	BRPL
BHARAT SANCHAR NIGAM LIMITED	BSNL
Bihar Urban Infrastructure Development Corporation Ltd	BUIDCO
BRAHMAPUTRA VALLY FERTILISER CORPORATION	BVFC
CENTRE FOR DEVELOPMENT OF TELEMATICS, TELECOM, TECHNOLOGY	C-DOT
CENTRAL COAL FIELDS LIMITED	CCL
CONTAINER CORPORATION OF INDIA	CCOI
CHENAB VALLEY POWER CORPORATION LIMITED	CHENAB VALLEY P
CHENNAI METRO RAIL LTD	CMRL
CHENNAI PETROLEUM CORPORATION LIMITED	CPCL
CENTRAL PUBLIC WORKS DEPARTMENT	CPWD
CPWD OF HIGHER EDUCATION	CPWD EDUCATION
CPWD FOR DEFENCE	CPWD FOR DEFENC
CPWD FOR FINANCE	CPWD FOR FINANC
CPWD FOR HEALTH	CPWD FOR HEALTH
CPWD FOR MHA	CPWD FOR MHA
CPWD FOR POWER	CPWD FOR POWER
CPWD FOR RURAL	CPWD FOR RURAL
CPWD FOR TELECOM	CPWD FOR TELECO
CPWD FOR RENEWABLE ENERGY	CPWD R ENERGY
CENTRAL RAILWAYS	CR
COCHIN REFINERY LIMITED	CRL
COCHIN SHIPYARD LTD	CSL
CHENAB VELLEY POWER PROJECTS [P] LIMITED	CVPPPL
DUMMY AGENCY	DA
DEDICATED FREIGHT CORRIDOR CORPORATION OF INDIA LTD	DFCC
DIRECTORATE GENERAL OF CIVIL AVIATION	DGCA
Delhi Jal Board	DJB
Delhi Mumbai Industrial Corridor	DMIC
DMIC FOR DPIIT	DMIC FOR DPIIT
DELHI METRO RAIL CORPORATION	DMRC
DEPARTMENT OF TELECOMMUNICATION	DOT
Department for Promotion of Industry and Internal Trade	DPIIT
DAMODAR VALLEY CORPORATION	DVC
EASTERN COAL FIELDS LIMITED	ECL
EAST COAST RAILWAY	ECOR
EAST CENTRAL RAILWAYS	ECR

AGENCY_NAME	AGENCY_NAME_SHORT
EDCIL(India) Limited	EDCIL
ENNORE PORT LTD.	ENNORE PORT LTD
ENNORE TANK TERMINAL PVT.LTD.	ENNORE TANK
EASTERN RAILWAYS	ER
FERTILISER AND CHEMICAL TRIVANCORE	FACT
FREIGHT OPERATION INFORMATION SYSTEM	FOIS
SETTING UP FILM AND TELEVISION INSTITUTE	FTI
GAS AUTHORITY OF INDIA LIMITED	GAIL
GOA SHIPYARD LIMITED	GSL
HEALTH & FAMILY WELFARE	H&FW
HINDUSTAN AERONAUTICS LTD	HAL
HINDUSTAN COPPER LIMITED	HCL
HALDIA FERTILISER CORPORATION	HFC
HLL Infra Tech Services Limited	HITES
HYDERABAD METRO RAIL LTD	HMRL
HINDUSTAN PETROLEUM CORPORATION LIMITED	HPCL
HPCL Rajasthan Refinery Limited(JV)	HPCLRRL(JV)
HPOIL Gas Pvt. Ltd	HPOIL(JV)
HOSPITAL SERVICES CONSULTANCY CORPORATION LTD	HSCC
HINDUSTAN STEELWORK CONSTRUCTION LIMITED	HSCL
HINDUSTHAN STEELWORKS CONSTRUCTION LIMITED	HSCL
HSCL FOR DONER	HSCL FOR DONER
HSCL FOR RURAL	HSCL FOR RURAL
HSCL FOR WATER	HSCL FOR WATER
INDIAN FARMERS FERTILISER CORPORATION	IFFCO
INDIRA GANDHI CENTRE FOR ATOMIC RESEARCH	IGCAR
INDRADHANUSH GAS GRID LTD	IGGL
India International Convention and Expo Centre	IICC
IICC FOR DPIIT	IICC FOR DPIIT
INDIAN IRON STEEL COMPANY	IISCO
Indian Institute of Technology, Kharagpur	IITKGP
INDIAN OIL CORPORATION LIMITED	IOCL
INDIAN PETRO-CHEMICAL CORPORATION LIMITED	IPCL
Indian Railway Construction Company Limited	IRCON
INDIAN STRATEGIC PETROLEUM RESERVES LTD	ISPRL
INDIAN TELEPHONE INDUSTRY	ITI
Inland Waterways Authority of India	IWAI
INLAND WATER TRANSPORT	IWT
JAWAHAR LAL NEHRU NATIONAL URBAN RENEWAL MISSION	JNNURM
JWAAHARLAL NEHRU PORT TRUST	JNPT
Jharkhand Urban Infrastructure Development Company Ltd	JUIDCO
Kolkata Metropolitan Development Authority	KMDA
KOCHI METRO RAIL CORPORATION LTD	KMRCL
KOLKATA METRO RAIL CORPORATION LIMITED	KOMRCL
KAMARAJAR PORT LIMITED	KPL
KONKAN RAILWAY	KR
Rail Infrastructure Development Company	KRIDE
KOCHI REFINERIES LIMITED	KRL
Kochi Salem Pipeline Private Limited(JV)	KSPPL(JV)
LINE DOUBLING	LD
LUCKNOW METRO RAIL CORPORATION LIMITED	LMRCL
MANGALORE REFINERY AND PETROCHEMICALS LIMITED	MANGALORE REFIN

AGENCY_NAME	AGENCY_NAME_SHORT
MAHANADI COAL FIELDS LIMITED	MCL
MECON LIMITED	MECON LIMITED
AHMEDABAD METRO RAIL	MEGA
MADRAS FERTILISER LIMITED	MFL
Munitions India Limited	MIL
MAHARASTRA METRO RAIL CORPORATION LTD.	MMRC
MUMBAI METRO RAIL CORPORATION LTD	MMRCL
MINISTRY OF WATER RESOURCES	MOWR
Madhya Pradesh Metro Rail Co Limited	MPMRCL
Maharashtra Rail Infrastructure Development Corporation Limited	MRIDC
MANGALORE REFINARY LIMITED	MRL
METROPOLITAN RAPID TRANSPORT PROJECTS	MRTP
Mumbai Railway Vikas Corporation	MRVC
MAHANAGAR TELEPHONE NIGAM LIMITED	MTNL
MUMBAI PORT TRUST	MUMBAI PORT TRU
Armoured Vehicles Nigam Limited	MVNL
MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)	MoRTH
NATIONAL ALUMINUM COMPANY LIMITED (NALCO)	NALCO
NATRIIP IMPLEMENTATION SOCIETY	NATIS
NATIONAL BUILDING CONSTRUCTION CORPORATION LTD	NBCC
NBCC FOR COMMERCE	NBCC FOR COMMER
NBCC FOR HEALTH	NBCC FOR HEALTH
NORTHERN COAL FIELDS LIMITED	NCL
NORTH CENTRAL RAILWAY	NCR
NATIONAL CAPITAL REGION TRANSPORT CORP	NCRTC
NATIONAL CENTRE OF EXCELLENCE	NCoE
NORTH EAST ELECTRIC POWER CORPORATION	NEEPCO
NORTH EAST GAS GRID	NEGG
NORTH EASTERN RAILWAY	NER
National Film Archive of India	NFAI
NUCLEAR FUEL CORPORATION	NFC
NATIONAL FERTILISER LIMITED	NFL
NORTH EAST FRONTIER RAILWAY	NFR
NATIONAL HIGHWAYS AUTHORITY OF INDIA	NHAI
NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.	NHIDCL
NATIONAL HYDRO-ELECTRIC POWER CORPORATION	NHPC
National High Speed Rail Corporation Limited	NHSRCL
NEW LINE	NL
NEYVELI LIGNITE CORPORATION	NLC
NATIONAL MISSION FOR CLEAN GANGA	NMCG
NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)	NMDC
NAGPUR METRO RAIL CORPORATION LTD	NMRCL
NATIONAL PROJECTS CONSTRUCTION CORPORATION LIMITED	NPCC
NUCLEAR POWER CORPORATION OF INDIA LIMITED	NPCIL
NORTHERN RAILWAY	NR
NUMALIGARH REFINERY LIMITED	NRL
SETTING UP OF NEW RAILWAY ZONES	NRZ
NATIONAL THERMAL POWER CORPORATION	NTPC
NORTH WESTERN RAILWAY	NWR
OIL INDIA LIMITED	OIL
OIL & NATURAL GAS CORPORATION LIMITED	ONGC
PATNA METRO RAIL CORPORATION	PATNA METRO RAI

AGENCY_NAME	AGENCY_NAME_SHORT
PAWAN HANS HELICOPTERTERS LTD.	PAWAN HANS HELI
POWER GRID CORPORATION OF INDIA LIMITED	PGCIL
PORT TRUST	PORT TRUST
Polavaram Project Authority	PPA
RASHTRIYA CHEMICAL & FERTILISER LIMITED	RCF
RAILWAY ELECTRIFICATION	RE
RASTRIYA ISPAT NIGAM LIMITED	RINL
RAIL INDIA TECHNICAL AND ECONOMIC SERVICE	RITES
rites OF HIGHER EDUCATION	rites OF HIGHER
RAIL VIKAS NIGAM LTD.	RVNL
SIGNALLING & TELECOMMUNICATIONS	S&T
STEEL AUTHORITY OF INDIA LIMITED (SAIL)	SAIL
SINGARENI COLLIERS COMPANY LIMITED	SCCL
SOUTH CENTRAL RAILWAY	SCR
SOUTH-EASTERN COAL FIELDS LIMITED	SECL
SOUTH EAST CENTRAL RAILWAY	SECR
SOUTH EASTERN RAILWAY	SER
SER(GC) GAUGE CONVERSION	SER(GC
SHIPPING CRP. OF INDIA	SHIPP.
SATLUJ JAL VIDYUT NIGAM LIMITED	SJVN
SOUTHERN RAILWAY	SR
SOUTH WESTERN RAILWAY	SWR
Sikkim University	Sikkim Universi
THDC INDIA LIMITED	THDCIL
TUTICORIN PORT TRUST	TUTICORIN
URANIUM CORPORATION OF INDIA LIMITED	UCIL
URBAN DEVELOPMENT	UD
Uttarakhand Pey Jal Nigam	UKJalNigam
Uttar Pradesh Jal Nigam	UPJalNigam
VISAKHAPATNAM PORT TRUST	VPT
Varanasi Smart City	Varanasi Smart
WAPCOS	WAPCOS
WESTERN COAL FIELDS LIMITED	WCL
WEST CENTRAL RAILWAY	WCR
WESTERN RAILWAY	WR
WORKSHOPS & PRODUCTION UNIT	WS&PU



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
