



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation

IMPLEMENTATION STATUS REPORT

**COSTING
RS. 150 CRORE & ABOVE**

QUARTERLY PROJECT



**Quarter-1 FY 2025-26
(April-June)**









CONTENTS

Synopsis	1-2
List of Tables	3-252
Table:-1. Overview of Ongoing Projects: Sector-wise Distribution.....	3-4
Table:-2. Overview of Ongoing Projects: State-wise Distribution.....	5-7
Table:-3. Project List: Completed during 1 st Quarter (April-June), 2025-26	8-21
Table:-4. Project List: Added during 1 st Quarter (April-June), 2025-26.....	22-27
Table:-5. Project List: Frozen/Deleted during 1 st Quarter (April-June), 2025-26.....	28-29
Table:-6. Project List: Ongoing Projects of North-East Region.....	30-54
Table:-7. Project List: Ongoing Projects during 1 st Quarter (April-June), 2025-26.....	55-252




SYNOPSIS

Quarterly Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above

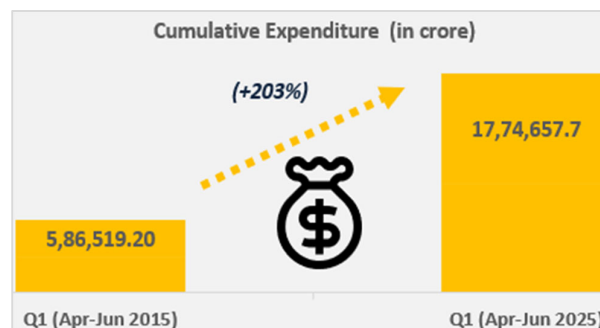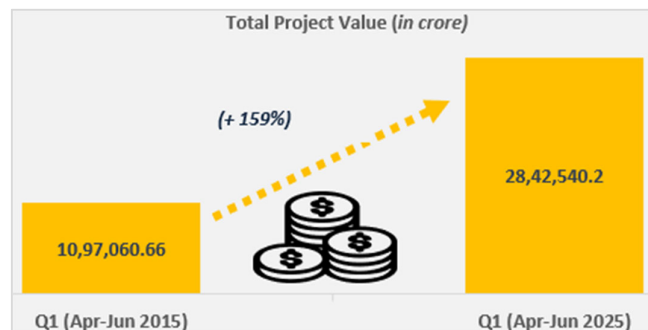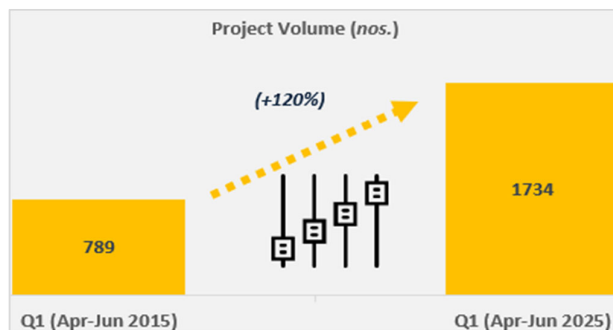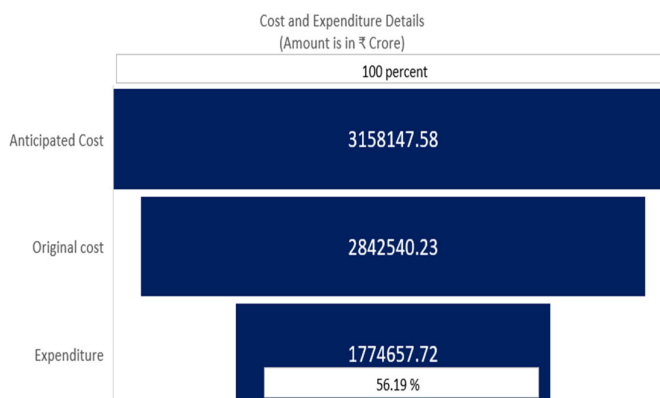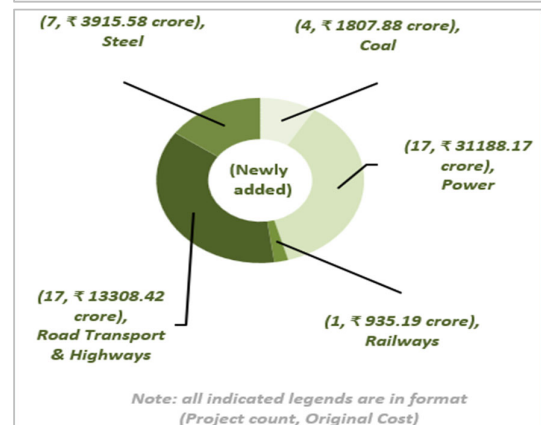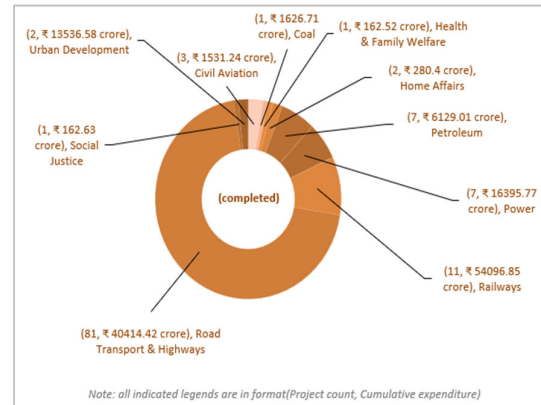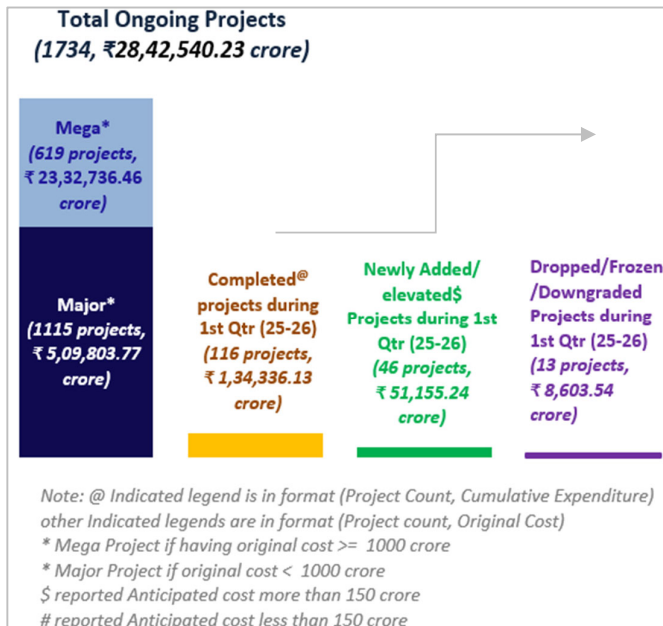


Sectoral Comparison : Major Sectors (as per count)
[Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

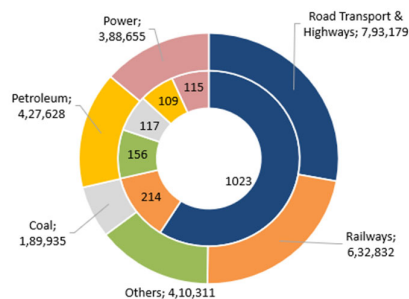


*Others include Water Resources, Civil Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Atomic energy, Home Affairs, Finance, DPIIT, DONER, Renewable Energy, Shipping & Ports, and Social Justice

State Comparison : Major States (as per count)
[Outer Ring:Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

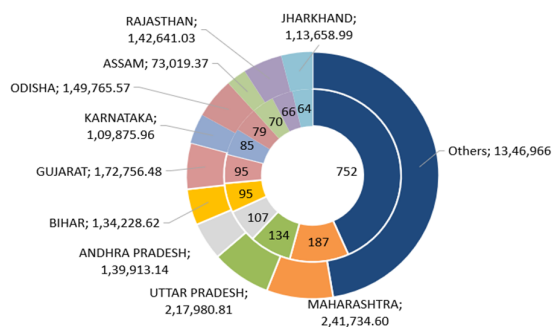

*Others include Tamilnadu, Madhya Pradesh, Delhi, Chhattisgarh, Haryana, Jammu & Kashmir, West Bengal, Kerala, Arunachal Pradesh, Punjab, Telangana, Uttarakhand, Himachal Pradesh, Manipur, Sikkim, Nagaland, Mizoram, Meghalaya, Tripura, Goa, A&N Island, Ladakh and Multistate

Sectoral Distribution of total 765 projects with reported Physical Progress between 80-100%

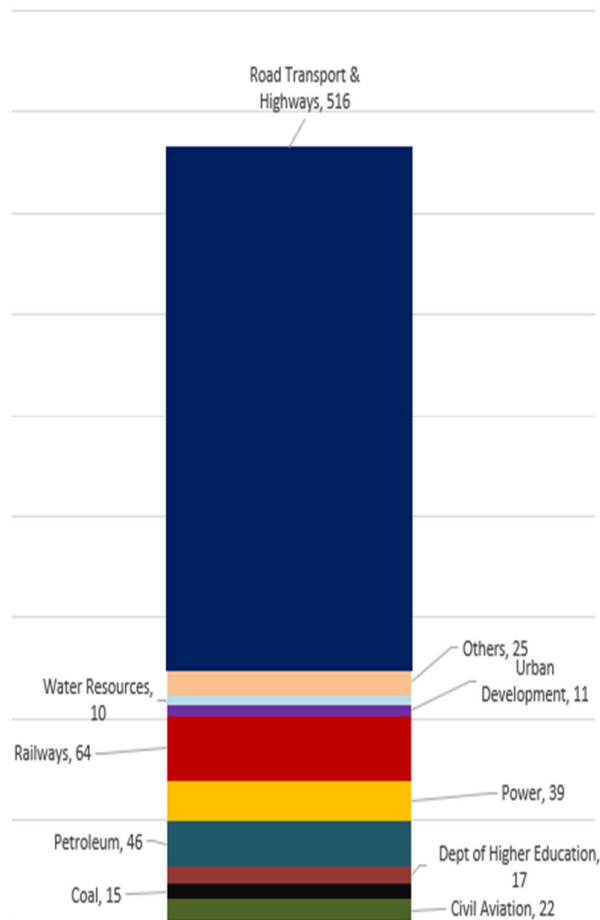



LIST OF TABLES

**Table:-1. Overview of Ongoing Projects: Sector-wise Distribution during 1st Quarter
(April-June),2025-26**

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	CIVIL AVIATION	41	28,200.17 (29,521.45) {32,130.66}	19,569.62
2	COAL	117	189,934.94 (194,478.98) {199,308.23}	69,601.23
3	DEPARTMENT OF HIGHER EDUCATION	20	9,680.92 (10,072.78) {10,271.25}	7,214.67
4	DPIIT	2	24,857.00 (31,457.00) {32,085.00}	16,231.95
5	FINANCE	2	577.27 (577.27) {569.04}	399.67
6	HEALTH AND FAMILY WELFARE	8	7,301.27 (7,609.40) {7,356.19}	5,137.01
7	HOME AFFAIRS	5	2,025.73 (2,949.25) {2,949.25}	2,489.50
8	MINES	8	7,559.78 (9,356.73) {9,845.57}	6,076.89
9	PETROLEUM	109	427,628.10 (479,675.67) {489,828.88}	2,53,857.11
10	POWER	115	388,655.20 (411,996.48) {476,127.63}	2,50,456.46
11	RAILWAYS	214	632,832.03 (622,151.48) {659,838.53}	4,59,488.42
12	ROAD TRANSPORT AND HIGHWAYS	1023	793,179.02 (825,135.87) {836,967.98}	4,33,508.00
13	SHIPPING AND PORTS	1	5,369.18 (5,061.15) {5,061.15}	3,472.54
14	SOCIAL JUSTICE	1	170.99 (170.99) {170.99}	162.63
15	STEEL	20	16,297.20 (20,228.73) {20,228.73}	8,030.85
16	TELECOMMUNICATIONS	6	26,961.69 (26,949.89) {26,949.89}	9,777.17

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution during 1st Quarter
(April-June),2025-26

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
17	URBAN DEVELOPMENT	27	265,881.46 (272,720.33) {286,578.30}	2,01,738.62
18	WATER RESOURCES	15	15,428.28 (15,429.03) {61,880.31}	27,445.38
	Total	1734	2842540.23 (2965542.48) {3158147.58}	1774657.72

***Either Revised or Original Cost**

**Table:-2. Overview of Ongoing Projects: State-wise Distribution during 1st Quarter
(April-June),2025-26**

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ANDAMAN AND NICOBAR ISLANDS	10	2,956.02 (3,029.18) {3,010.04}	1,817.30
2	ANDHRA PRADESH	107	139,913.14 (140,412.47) {188,264.34}	1,04,918.01
3	ARUNACHAL PRADESH	17	46,277.92 (46,427.82) {66,154.50}	31,192.12
4	ASSAM	70	73,019.37 (73,503.24) {80,974.64}	51,299.26
5	BIHAR	95	134,228.62 (146,243.18) {158,856.89}	1,03,365.01
6	CHHATTISGARH	54	76,728.88 (80,618.31) {81,093.37}	36,942.43
7	DELHI	21	90,609.18 (96,063.03) {94,869.54}	76,898.76
8	GOA	3	1,201.05 (1,201.05) {1,287.55}	485.92
9	GUJARAT	95	172,756.48 (180,000.53) {181,454.95}	93,756.29
10	HARYANA	29	67,288.90 (78,084.81) {78,136.40}	41,872.43
11	HIMACHAL PRADESH	31	41,877.88 (42,907.56) {51,017.13}	33,014.11
12	JAMMU AND KASHMIR	55	112,603.25 (113,914.62) {126,963.34}	79,819.42
13	JHARKHAND	64	113,658.99 (117,419.60) {116,571.41}	67,421.35
14	KARNATAKA	85	109,875.96 (111,585.92) {110,313.91}	53,826.52
15	KERALA	32	64,106.75 (69,729.34) {70,321.90}	36,735.08
16	LADAKH	6	2,474.97 (2,634.64) {2,634.64}	1,349.63

**Table:-2. Overview of Ongoing Projects: State-wise Distribution during 1st Quarter
(April-June),2025-26**

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
17	MADHYA PRADESH	59	113,890.17 (113,291.57) {119,925.74}	42,660.81
18	MAHARASHTRA	187	241,734.60 (246,273.58) {271,281.09}	1,48,854.13
19	MANIPUR	35	26,343.72 (24,331.16) {34,255.53}	19,856.68
20	MEGHALAYA	16	7,087.27 (7,078.29) {7,097.47}	3,689.98
21	MIZORAM	19	15,437.36 (13,931.36) {19,781.78}	16,974.82
22	MULTI STATE	52	334,099.78 (339,652.77) {353,659.76}	2,57,093.50
23	NAGALAND	31	15,684.24 (17,032.92) {16,731.89}	9,458.18
24	ODISHA	79	149,765.57 (151,845.86) {154,533.92}	68,650.28
25	PUNJAB	39	38,037.49 (38,498.05) {38,937.45}	15,572.84
26	RAJASTHAN	66	142,641.03 (172,792.36) {172,386.55}	98,554.11
27	SIKKIM	22	21,037.80 (25,537.19) {26,380.76}	18,940.39
28	TAMIL NADU	64	93,038.36 (99,694.67) {104,811.51}	28,908.67
29	TELANGANA	53	29,478.09 (29,815.44) {31,802.96}	15,701.33
30	TRIPURA	14	7,910.17 (7,947.06) {8,032.54}	1,403.56
31	UTTAR PRADESH	134	217,980.81 (225,694.48) {230,674.16}	1,18,832.83
32	UTTARAKHAND	31	58,781.06 (63,526.61) {63,474.70}	45,356.01

**Table:-2. Overview of Ongoing Projects: State-wise Distribution during 1st Quarter
(April-June), 2025-26**

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
33	WEST BENGAL	59	80,015.35 (84,823.81) {92,455.22}	49,435.96
	Total	1734	2842540.23 (2965542.48) {3158147.58}	1774657.72

***Either Revised or Original Cost**

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
CIVIL AVIATION					
	1	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD (TELANGANA) (N04000086) (AAI)	353.61	05-2022	303.22
	2	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI (TAMIL NADU) (N04000075) (AAI)	951.28	10-2021	1084.94
	3	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT (ANDHRA PRADESH) (N04000089) (AAI)	177.1	02-2020	143.08
COAL					
	4	TALABIRA II AND III OCP (ODISHA) (N06000189) (NLC)	2401.07	01-2027	1626.71
HEALTH AND FAMILY WELFARE					
	5	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST (KERALA) (N28000112) (CPWD FOR HEALTH)	150.29	03-2020	162.52
HOME AFFAIRS					
	6	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI (UTTAR PRADESH) (N45000003) (CPWD FOR MHA)	199.31	01-2022	86.49
	7	NSG AT KOLKATA (WEST BENGAL) (N28000104) (CPWD FOR MHA)	162.88	04-2018	193.91
PETROLEUM					
	8	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS (MULTI STATE) (N16000426) (IOCL)	169	12-2029	71

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	9	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV (MAHARASHTRA) (N16000358) (ONGC)	3228.8	03-2022	3867.19
	10	REVAMPING OF FACILITIES AT VIZAG TERMINAL (ANDHRA PRADESH) (N16000343) (IOCL)	355	04-2022	249
	11	ADDITIONAL STORAGE TANKS AT PARADIP (ODISHA) (N16000361) (IOCL)	462.3	09-2021	493.72
	12	CITY GAS DISTRIBUTION IN WEST BENGAL (WEST BENGAL) (N16000392) (HPCL)	5830.2	03-2031	875.27
	13	CGD PROJECT IN TONK, SAWAI MADHOPUR, DAUSA, KARAUULI (RAJASTHAN) (N16000496) (HPCL)	1751	03-2030	301.39
	14	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT (CHHATTISGARH) (N16000413) (HPCL)	456	03-2024	271.44
POWER					
	15	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C (MULTI STATE) (N18000338) (PGCIL)	186.19	03-2025	91.53
	16	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME-XXVIII AND XXIX (CHHATTISGARH) (N18000355) (PGCIL)	260.3	03-2025	197.79
	17	BHENSARA 320 MW (RAJASTHAN) (N18000293) (NTPC)	1221.73	07-2022	1139.42

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	18	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) (GUJARAT) (N18000296) (NTPC)	674.92	09-2022	572.53
	19	PARBATI HEP (4X200 MW) (NHPC) II (HIMACHAL PRADESH) (180100210) (NHPC)	3919.59	09-2009	12832.59
	20	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII (CHHATTISGARH) (N18000354) (PGCIL)	271.69	09-2024	192.03
	21	SAMBHU KI BHURJ-II SOLAR 300MW (RAJASTHAN) (N18000286) (NTPC)	1782	09-2021	1369.88
RAILWAYS					
	22	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS (GUJARAT) (N22000505) (WR)	537.31	03-2024	944.55
	23	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR (JAMMU AND KASHMIR) (220100133) (NR)	37012	08-2024	42328.83
	24	MANSABHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI (PUNJAB) (N22000502) (NR)	404	08-2016	190
	25	DARBHANGA - BYPASS LINE CONNECTING SHISHO HALT AND KAKARGHATI EXCL DARBHANGA YARD (7.64 KM) (BIHAR) (N22000523) (ECR)	983.62	06-2025	417.57
	26	KARAILA ROAD - SHAKTINAGAR DOUBLING (UTTAR PRADESH) (N22000419) (ECR)	762.97	08-2024	808.96

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	27	KARAIKAL PERALAM(23KM)-NEW LINE PROJECT (TAMIL NADU) (N22000625) (SR)	304.22	03-2026	292.65
	28	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL (ODISHA) (N22000418) (IRCON)	5200	03-2020	389
	29	2880.4 (UTTAR PRADESH) (N22000417) (ECR)	2880.4	08-2024	3074.78
	30	AZIMGANJ-MURSHIDABAD (JIYAGANJ) INCL. RLY. BRIDGE OVER RIVER BHAGIRATHI (WEST BENGAL) (N22000609) (ER)	164.33	02-2024	160.82
	31	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING (UTTAR PRADESH) (N22000401) (RVNL)	2018.23	12-2024	1780.22
	32	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING (MULTI STATE) (N22000183) (NFR)	2047.51	08-2024	3709.47
ROAD TRANSPORT AND HIGHWAYS					
	33	PUNE TO MALE VILLAGE (MAHARASHTRA) (N24001078) (MoRTH)	228.31	12-2019	113.29
	34	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI- AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP (HARYANA) (N24001533) (NHAI)	1690.23	12-2023	1462.45
	35	2 LANE WITH PAVED SHOULDER CONFIGURATION FROM SEETHARAMAPURAM TO DUTTALURU SECTION OF NH-167 BG FROM (ANDHRA PRADESH) (N24002141) (MoRTH)	364.07	07-2025	227.21

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	36	REHABILITATION AND UPGRADATION OF BHOKARDAN TO KUMBHARI FATA DESIGN CH. (KM 13+500 TO 17+00) AND RAJ (MAHARASHTRA) (N24001887) (MoRTH)	291.37	06-2024	157.59
	37	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES (PUNJAB) (N24000941) (MoRTH)	293.64	08-2020	295.46
	38	CONSTRUCTION OF MAJOR BRIDGE ACROSS MANJRA RIVER NEAR YESGI VILLAGE @ KM, 166/500 ON NH 63 TQ BILOLI (MAHARASHTRA) (N24001905) (MoRTH)	188.69	08-2023	111.25
	39	UP-GRADATION OF TIRORA-GONDIA, STATE HIGHWAY FROM EXISTING KM 163+213 (ON SH-335, TIRORA) TO KM 191+ (MAHARASHTRA) (N24001888) (MoRTH)	288.14	04-2023	72.78
	40	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (ASSAM) (N24001451) (NHIDCL)	215.27	07-2024	105.4
	41	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 (KARNATAKA) (N24001675) (NHAI)	1732.73	05-2025	754.79
	42	AMD I TO SAONER (MAHARASHTRA) (N24001021) (MoRTH)	396.91	06-2019	253.59
	43	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO (UTTAR PRADESH) (N24001728) (NHAI)	1138.81	07-2025	528.1

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	44	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) (MAHARASHTRA) (N24000659) (NHAI)	1059.73	03-2017	928.19
	45	NH167B FROM KM.143.320 MALAKONDA TO 189.050 SINGARAYAKONDA ON NH 16 TO TWO LANE WITH PAVED SHOULDERS (ANDHRA PRADESH) (N24001950) (MoRTH)	369.81	02-2025	303.78
	46	KUMBHARI PHTA TO DEULGAON RAJA (MAHARASHTRA) (N24001127) (MoRTH)	406.51	06-2019	340.26
	47	CONSTRUCTION OF 4-LANE NH-344P-PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA (HARYANA) (N24001532) (NHAI)	694	11-2023	1466.82
	48	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS-PACKAGE-1) (GUJARAT) (N24001791) (NHAI)	606.51	06-2023	453.89
	49	WIDENING OF RAEBARELI TO PRAYAGRAJ SECTION FROM KM. 82.650 TO KM. 161.450 OF NH-30 AND LINK ROAD FRO (UTTAR PRADESH) (N24002085) (NHAI)	1470.93	03-2025	1088.3
	50	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125 (MADHYA PRADESH) (N24001616) (NHAI)	428.04	10-2023	351.97
	51	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER (MAHARASHTRA) (N24001080) (MoRTH)	256.15	12-2019	115.53
	52	2 LANE + PS PIMPLNER TO SATANA -[DESIGN CHAINAGE KM 21.427 TO 64.00] OF NH-752G] (MAHARASHTRA) (N24001889) (MoRTH)	277.81	07-2021	155.01

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	53	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (MIZORAM) (N24000859) (NHIDCL)	642.96	06-2023	686.42
	54	HIMAYATNAGAR TO PHULSAWANGI (MAHARASHTRA) (N24001081) (MoRTH)	294.87	12-2019	183.17
	55	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (MEGHALAYA) (N24001339) (NHIDCL)	157.86	04-2022	152.95
	56	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM (MAHARASHTRA) (N24000332) (MoRTH)	225.81	N.A.	118.84
	57	ADDITIONAL WORKS (2VUPS, MR-10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE-DEWAS SECTION OF N (MADHYA PRADESH) (N24001765) (NHAI)	207.77	07-2024	147.24
	58	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 (KARNATAKA) (N24001686) (NHAI)	1065.06	03-2023	736.55
	59	2 LANE + PS ASTHAMODE - TIVATYAL [DESIGN CH. KM 24.300 - 62.00] [KM 134.98-172.95 OF NH-63] (MAHARASHTRA) (N24001894) (MoRTH)	228.82	07-2021	145.5
	60	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 (UTTARAKHAND) (N24000741) (NHIDCL)	274.31	11-2020	253.61

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	61	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP (HARYANA) (N24001534) (NHAI)	1334.04	01-2024	1048.12
	62	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN (MADHYA PRADESH) (N24000709) (NHAI)	950.27	02-2020	643.9
	63	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU (GUJARAT) (N24000570) (NHAI)	763.08	08-2019	520.19
	64	RANIKOR-MAHESKHOLA- BAGHMARA (RMB) PKG-3 (MEGHALAYA) (N24001360) (NHIDCL)	260.21	12-2022	239.35
	65	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (ARUNACHAL PRADESH) (N24001391) (NHIDCL)	294.04	04-2022	147.13
	66	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NAGALAND) (N24001389) (NHIDCL)	206.53	06-2022	119.25
	67	BALANCE WORK OF 4L OF INDORE-GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF (MADHYA PRADESH) (N24001768) (NHAI)	323.51	04-2023	246.27
	68	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (NAGALAND) (N24001180) (MoRTH)	237.51	12-2022	215.47
	69	KEIFANG - TUVAI PKG-1 (MIZORAM) (N24001440) (NHIDCL)	492.94	05-2023	365.86

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	70	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO (UTTAR PRADESH) (N24000796) (NHAI)	1117.84	12-2021	1960.91
	71	KURUDWADI TO PANDHARPUR (MAHARASHTRA) (N24001101) (MoRTH)	307.63	07-2019	208.22
	72	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN (HARYANA) (N24001783) (NHAI)	2252.75	09-2021	1223.07
	73	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (SIKKIM) (N24001254) (NHIDCL)	242.97	06-2022	246.91
	74	4 LANING OF BATHALAPALLI TO MUDIGUBBA SECTION (DESIGN CHAINAGE KM. 96.300 TO 129.300) INCLUDING BATH (ANDHRA PRADESH) (N24001931) (MoRTH)	536	02-2025	334.06
	75	AJANTHA TO BULDHANA (ANDAMAN AND NICOBAR ISLANDS) (N24001008) (MoRTH)	401	07-2019	246.39
	76	SHAHPUR PATGAON SECTION I (MAHARASHTRA) (N24001027) (MoRTH)	150.79	12-2019	81.14
	77	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (ARUNACHAL PRADESH) (N24000948) (NHIDCL)	568.92	12-2019	508.65
	78	SELDOH TO PANVAR (MAHARASHTRA) (N24001097) (MoRTH)	404.33	05-2020	140.65

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	79	AURAD - BIDAR KM 0.00 TO KM 45.878 (KARNATAKA) (N24001683) (NHAI)	912.37	04-2023	255.94
	80	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY (KARNATAKA) (N24000552) (NHAI)	701.4	03-2019	923.99
	81	PARLI PIMPLA DAHIGUDA (MAHARASHTRA) (N24001138) (MoRTH)	205.72	06-2019	813.5
	82	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM (TAMIL NADU) (N24001430) (NHAI)	2120.4	01-2022	1588.35
	83	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 (BIHAR) (N24001708) (NHAI)	2156.22	06-2024	1397.72
	84	KOLDE TO KHETIYA (MAHARASHTRA) (N24001090) (MoRTH)	509.18	07-2019	246.83
	85	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (NAGALAND) (N24001179) (MoRTH)	217.35	11-2020	214.18
	86	4-LANNING OF THALSERRY -MAHE BYPASS (KERALA) (N24000704) (NHAI)	1124.11	05-2020	1527.28
	87	4L BYPASSES FOR JAGATPUR, B4ABUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA (UTTAR PRADESH) (N24001815) (NHAI)	1699	11-2024	1033.72

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	88	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NAGALAND) (N24001475) (NHIDCL)	605.36	12-2024	273.21
	89	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 (MIZORAM) (N24001277) (NHIDCL)	275.02	10-2022	237.68
	90	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH- 702 (PKG-I) (NAGALAND) (N24001286) (NHIDCL)	278.95	06-2022	166.29
	91	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI (HARYANA) (N24001536) (NHAI)	817	07-2022	986.08
	92	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) (TAMIL NADU) (N24001600) (NHAI)	434.12	05-2023	268.92
	93	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. (GUJARAT) (N24000567) (NHAI)	998.18	08-2019	802.89
	94	AKOLA TO AKOT (MAHARASHTRA) (N24001003) (MoRTH)	313.95	06-2019	270.02
	95	REHABILITATION AND UPGRADATION TO TWO LANES WITH PAVED SHOULDER CONFIGURATION FROM WATUR TO CHARTHANA (MAHARASHTRA) (N24001895) (MoRTH)	228.01	09-2023	106.11
	96	KOLHA TO NASRATPUR (MAHARASHTRA) (N24001111) (MoRTH)	281.78	04-2019	77.83

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	97	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (SIKKIM) (N24000768) (NHIDCL)	290.05	10-2020	218.36
	98	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH (ANDHRA PRADESH) (N24000301) (MoRTH)	271.45	10-2015	240.23
	99	STRENGTHING AND WIDINING OF EXISTING CARRIAGEWAY TO 10 M IN KM, 156/160 TO 229/160 (TEMBHURNI - KUSL) (MAHARASHTRA) (N24001909) (MoRTH)	157.72	06-2024	80.37
	100	ARDHAPUR TO HIMAYATNAGAR (MAHARASHTRA) (N24001079) (MoRTH)	426.06	06-2020	268.96
	101	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON (TAMIL NADU) (N24001428) (NHAI)	998.7	11-2021	975.74
	102	STRENGTHENING OF 6-LANE PIMPALGAON-NASHIK-GONDE (KM. 380 - KM. 440) SECTION OF NH-3 IN MAHARASHTRA U (MAHARASHTRA) (N24002137) (NHAI)	175	03-2025	201
	103	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) (TAMIL NADU) (N24001603) (NHAI)	1518.53	10-2022	915.4
	104	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU (GUJARAT) (N24001788) (NHAI)	2271.86	12-2023	2655.78

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	105	PANDHARPUR TO SANGOLA (MAHARASHTRA) (N24001102) (MoRTH)	218.38	07-2019	176.99
	106	SATARA MURVAD PILLOV PANDHARPUR (MAHARASHTRA) (N24001095) (MoRTH)	388.44	N.A.	240.05
	107	NH167B FROM KM 99.103 CS PURAM TO KM 143.320 MALAKONDA TO 2LPS (ANDHRA PRADESH) (N24001949) (MoRTH)	277.3	03-2024	206.25
	108	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN (KARNATAKA) (N24001691) (NHAI)	1225.24	10-2021	1043
	109	BHANDARA TO GHOTITOK (MAHARASHTRA) (N24001018) (MoRTH)	392.83	06-2019	264.35
	110	JINTUR TO PARBHANI (MAHARASHTRA) (N24001039) (MoRTH)	356.66	N.A.	209.48
	111	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF GHAGARIYA- MUNABAO SECTION FROM KM (RAJASTHAN) (N24001869) (MoRTH)	235.15	08-2025	159.69
	112	RALEGAON TO RAMTIRTH (MAHARASHTRA) (N24001046) (MoRTH)	210.81	07-2019	132
	113	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G (BIHAR) (N24001711) (NHAI)	939.43	03-2023	1030.75
SOCIAL JUSTICE					

Table:-3. Project List: Completed during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	114	CENTRE FOR DISABILITY SPORTS (MADHYA PRADESH) (N38000001) (CPWD)	170.99	03-2024	162.63
URBAN DEVELOPMENT					
	115	KOCHI METRO RAIL PROJECT PHASE IB SECTION FROM S N JUNCTION TO THRIPIUNITHURA (KERALA) (N28000159) (KMRC)	355.7	09-2023	448.39
	116	PUNE METRO RAIL PROJECT (PHASE 1) (MAHARASHTRA) (N28000121) (MMRC)	11420	11-2021	13088.19
		Total	139796.75		134336.13

Table:-4. Project List: Added during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
<u>COAL</u>	1	50 MW WIND POWER PROJECT PART OF 150 MW SECI HYBRID (NLC) (N06000292) (GUJARAT)	7-2022	383.84 (383.84) {383.84}	6/2025 (01-01-2026) {1/2026}
	2	WAGHODA UG (WCL) (N06000293) (MAHARASHTRA)	1-2025	379.30 (379.30) {379.30}	3/2030 (N.A.) {3/2030}
	3	KOLARPIMPRI EXPANSION OCM (2.50 MTY) (WCL) (N06000294) (MAHARASHTRA)	2-2025	630.37 (630.37) {630.37}	3/2030 (N.A.) {3/2030}
	4	JARANGDIH OCP (CCL) (N06000295) (JHARKHAND)	2-2020	414.37 (414.37) {414.37}	3/2029 (N.A.) {3/2029}
<u>POWER</u>	5	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-4: 3.5 GW): PART A (PGCIL) (N18000407) (UTTAR PRADESH)	12-2024	5,846.00 (5,846.00) {5,846.00}	12/2026 (N.A.) {12/2026}
	6	TRANSMISSION SYSTEM UNDER ISTS FOR EVACUATION OF POWER FROM KUDANKULAM UNIT - 3 AND 4 (2X1000 MW) (PGCIL) (N18000408) (TAMIL NADU)	1-2025	548.00 (548.00) {548.00}	7/2028 (N.A.) {7/2028}
	7	SYSTEM STRENGTHENING AT KOPPAL-II AND GADAG-II FOR INTEGRATION OF RE GENERATION PROJECTS (PGCIL) (N18000409) (KARNATAKA)	1-2025	1,354.00 (1,354.00) {1,354.00}	1/2027 (N.A.) {1/2027}
	8	AUGMENTATION OF TRANSFORMATION CAPACITY AT BIDAR PS (PGCIL) (N18000410) (KARNATAKA)	2-2025	288.00 (288.00) {288.00}	2/2027 (N.A.) {2/2027}
	9	AUGMENTATION OF TRANSFORMATION CAPACITY AT KPS2 AND KPS2 (PGCIL) (N18000411) (GUJARAT)	3-2025	466.00 (466.00) {466.00}	3/2027 (N.A.) {3/2027}

Table:-4. Project List: Added during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	10	AUGMENTATION OF BANASKANTHA (RAGHANESDA) PS (GIS) (PGCIL) (N18000412) (GUJARAT)	3-2025	172.00 (172.00) {172.00}	3/2027 (N.A.) {3/2027}
	11	TRANSMISSION SYSTEM FOR INTEGRATION OF KURNOOL-IV REZ PHASE-I (FOR 4.5 GW) (PGCIL) (N18000413) (ANDHRA PRADESH)	3-2025	5,000.00 (5,000.00) {5,000.00}	3/2027 (N.A.) {3/2027}
	12	RAJASTHAN REZ PH-V (PART-1: 4 GW) [SIROHI/NAGAU] COMPLEX (PGCIL) (N18000414) (RAJASTHAN)	3-2025	5,028.00 (5,028.00) {5,028.00}	3/2027 (N.A.) {3/2027}
	13	AUGMENTATION AT FATEHGARH-II PS, FATEHGARH-IV PS (SECTION-II) AND BARMER-I (PGCIL) (N18000415) (RAJASTHAN)	3-2025	404.00 (404.00) {428.00}	12/2026 (N.A.) {12/2026}
	14	TRANSMISSION SYSTEM STRENGTHENING AT KURNOOL- III PS FOR INTEGRATION OF ADDITIONAL RE GENERATION PRO (PGCIL) (N18000416) (ANDHRA PRADESH)	3-2025	2,886.00 (2,886.00) {2,886.00}	3/2027 (N.A.) {3/2027}
	15	TRANSMISSION SCHEME FOR EVACUATION OF POWER FROM RATLE HEP (850 MW) AND KIRU (624 MW): PART B (PGCIL) (N18000417) (JAMMU AND KASHMIR)	3-2025	219.00 (219.00) {219.00}	3/2027 (N.A.) {3/2027}
	16	NOKH SOLAR PV PROJECT 735 MW (NTPC) (N18000418) (RAJASTHAN)	3-2022	4,189.17 (4,378.17) {4,378.17}	4/2024 (01-07-2025) {7/2025}
	17	TRANSMISSION SCHEME FOR INTEGRATION OF DAVANAGERE / CHITRADURGA AND BELLARY REZ IN KARNATAKA (PGCIL) (N18000419) (KARNATAKA)	3-2025	3,453.00 (3,453.00) {3,453.00}	3/2027 (N.A.) {3/2027}
	18	IMPLEMENTATION OF LILO OF BOTH CIRCUITS OF 400KV VIDHYACHAL PS TO SASAN D/C LINE AT HINDALCO SWITCHY (PGCIL) (N18000420) (HARYANA)	2-2025	370.00 (370.00) {370.00}	12/2026 (N.A.) {12/2026}

Table:-4. Project List: Added during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	19	EASTERN REGION EXPANSION SCHEME: 43 [ERES: 43] (PGCIL) (N18000421) (BIHAR)	5-2025	343.00 (343.00) {343.00}	5/2026 (N.A.) {5/2026}
	20	EASTERN REGION EXPANSION SCHEME: 44 [ERES: 44] (PGCIL) (N18000422) (BIHAR)	5-2025	409.00 (409.00) {409.00}	5/2026 (N.A.) {5/2026}
	21	TRANSMISSION SYSTEM FOR STRENGTHENING TO FACILITATE EVACUATION OF POWER FROM BHADLA/BIKANER COMPLEX (PGCIL) (N18000423) (UTTAR PRADESH)	12-2024	213.00 (213.00) {213.00}	6/2026 (N.A.) {6/2026}
RAILWAYS	22	MURARAI - BARHARWA 3RD LINE (48.90 KM) (ER) (N22000632) (WEST BENGAL)	5-2025	935.19 (935.19) {935.19}	5/2028 (N.A.) {5/2028}
ROAD TRANSPORT AND HIGHWAYS	23	BILASIPURA- GUWAHATI ROAD PKG-2 (NHIDCL) (N24002229) (ASSAM)	11-2023	1,338.61 (1,338.61) {1,338.61}	6/2027 (N.A.) {6/2027}
	24	BADARPUR ? CHURABARI PKG-6 (NHIDCL) (N24002230) (ASSAM)	3-2024	870.00 (870.00) {870.00}	3/2027 (N.A.) {3/2027}
	25	KARIMGANI - SUTARKANDI SECTION ON SILCHAR-CHURABARI PKG-7 (NHIDCL) (N24002231) (ASSAM)	2-2024	791.79 (791.79) {791.79}	2/2027 (N.A.) {2/2027}
	26	IMPHAL-KOHIMA ROAD PKG-5A (NHIDCL) (N24002232) (MANIPUR)	9-2020	228.97 (228.97) {228.97}	8/2026 (N.A.) {8/2026}
	27	DAINADUBI-DARUGIRI PKG-1B (NHIDCL) (N24002233) (MEGHALAYA)	3-2023	705.83 (705.83) {705.83}	3/2027 (N.A.) {3/2027}
	28	WIDENING TO 4L FROM KM.108.50 TO 139.00 OF NH-135A PKG-II (JAUNPUR TO AKBARPUR SECTION) ON HAM IN TH (MoRTH) (N24002234) (UTTAR PRADESH)	3-2023	1,511.57 (1,511.57) {1,511.57}	3/2027 (N.A.) {3/2027}

Table:-4. Project List: Added during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	29	CONSTRUCTION OF RAEBARELI RING ROAD (PHASE-2) WITH FOUR LANE CONFIGURATION FOR RAEBARELI CITY IN THE (MoRTH) (N24002235) (UTTAR PRADESH)	3-2022	1,273.72 (1,273.72) {1,273.72}	5/2027 (N.A.) {5/2027}
	30	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM - VIJAYAWADA (NHAI) (N24002236) (TELANGANA)	3-2023	832.62 (832.62) {832.62}	3/2025 (N.A.) {3/2027}
	31	CONSTRUCTION OF 4 LANE GAURIPUR BYPASS ON NH-17 IN THE STATE OF ASSAM (MoRTH) (N24002237) (ASSAM)	3-2024	421.15 (421.15) {421.15}	10/2026 (N.A.) {10/2026}
	32	CONSTRUCTION OF 2 LANE BARPETA BYPASS FROM KM 77+900(BARADI) TO KM 86+150(DEURIKUCHI) (LENGTH=8.25K (MoRTH) (N24002238) (ASSAM)	3-2023	173.65 (173.65) {173.65}	8/2026 (N.A.) {8/2026}
	33	IMPROVEMENT AND WIDENING TWO LANNIG WITH PAVED SHOULDER OF NATIONAL HIGHWAY 127B FROM KM 31.500 (GOE (MoRTH) (N24002239) (MEGHALAYA)	12-2023	504.00 (504.00) {504.00}	5/2027 (N.A.) {5/2027}
	34	IMPROVEMENT AND UP-GRADATION OF NH-227B (84 KOSI PARIKRAMA MARG) PACKAGE ?I, FROM KM 228.920 (JAGARN (MoRTH) (N24002240) (UTTAR PRADESH)	3-2022	912.50 (912.50) {912.50}	11/2026 (N.A.) {11/2026}
	35	IMPROVEMENT AND UP-GRADATION OF NH-227B (84 KOSI PARIKRAMA MARG) PACKAGE ?III, FROM KM.47.800 (GOSAI (MoRTH) (N24002241) (UTTAR PRADESH)	3-2022	587.97 (587.97) {587.97}	11/2026 (N.A.) {11/2026}
	36	CHOITHAR TO MARREM KHULLEN SECTION IMPHAL- UKHRUL - JESSAMI PKG-5 (NHIDCL) (N24002242) (MANIPUR)	3-2023	564.05 (564.05) {564.05}	3/2027 (N.A.) {3/2027}

Table:-4. Project List: Added during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	37	SILCHAR- CHURAIBARI PKG-5 (NHIDCL) (N24002243) (ASSAM)	2-2024	1,258.13 (1,258.13) {1,258.13}	10/2027 (N.A.) {10/2027}
	38	IMPHAL - KHONGSANG - JIRIBAM PKG-2 (NHIDCL) (N24002244) (MANIPUR)	3-2021	195.14 (195.14) {195.14}	3/2026 (N.A.) {3/2026}
	39	CONSTRUCTION OF BASTI RING ROAD (PHASE-I) WITH 4L CONFIGURATION FOR BASTI CITY IN THE STATE OF UTTAR (MoRTH) (N24002245) (UTTAR PRADESH)	12-2022	1,138.72 (1,138.72) {1,138.72}	6/2027 (N.A.) {6/2027}
STEEL	40	REPLACEMENT OF HOT LEVELLER-1 OF PLATE MILL AT BHILAI STEEL PLANT (SAIL) (N12000137) (CHHATTISGARH)	7-2024	198.62 (198.62) {198.62}	7/2026 (N.A.) {7/2026}
	41	INSTALLATION OF NEW BAR MILL AT DURGAPUR STEEL PLANT (SAIL) (N12000138) (WEST BENGAL)	9-2024	2,115.44 (2,115.44) {2,115.44}	6/2027 (N.A.) {6/2027}
	42	UP-GRADATION OF BLAST FURNACE NO. 3 AT DURGAPUR STEEL PLANT (SAIL) (N12000139) (WEST BENGAL)	9-2024	758.09 (758.09) {758.09}	6/2026 (N.A.) {6/2026}
	43	REVAMPING OF AIR POLLUTION CONTROL SYSTEMS OF SP-1 AT DURGAPUR STEEL PLANT (SAIL) (N12000140) (WEST BENGAL)	11-2024	196.40 (196.40) {196.40}	5/2026 (N.A.) {5/2026}
	44	THIRD LADLE FURNACE IN SECONDARY REFINERY UNIT AT IISCO STEEL PLANT (SAIL) (N12000141) (WEST BENGAL)	11-2024	227.96 (227.96) {227.96}	7/2026 (N.A.) {7/2026}
	45	REPLACEMENT OF EXISTING GRINDERS IN CRM-I & II AT BOKARO STEEL PLANT (SAIL) (N12000142) (JHARKHAND)	1-2025	211.94 (211.94) {211.94}	1/2027 (N.A.) {1/2027}

Table:-4. Project List: Added during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	46	SECONDARY EMISSION CONTROL IN CONVERTERS OF SMS-II AT BOKARO STEEL PLANT (SAIL) (N12000143) (JHARKHAND)	1-2025	207.13 (207.13) {207.13}	10/2026 (N.A.) {10/2026}
<u>Grand Total</u>				51155.24 (51344.24) {51368.24}	

Table:-5. Project List: Frozen/Deleted during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
POWER					
	1	NOKH PLOT-2 SOLAR PV PROJECT 245MW (NATIONAL THERMAL POWER CORPORATION) (N18000321) (RAJASTHAN)	1,409.52	08/2023	1,403.89
	2	NOKH PLOT-3 SOLAR PV PROJECT 245MW (NATIONAL THERMAL POWER CORPORATION) (N18000322) (RAJASTHAN)	1,426.94	08/2023	1,170.29
	3	NOKH PLOT-1 SOLAR PV PROJECT 245MW (NATIONAL THERMAL POWER CORPORATION) (N18000320) (RAJASTHAN)	1,352.71	08/2023	1,057.36
ROAD TRANSPORT AND HIGHWAYS					
	4	BALANCE WORK FOR REHABILITATION AND UP-GRADATION OF SIDHI-SINGRAULI FROM KM 82.400 TO KM 187.993 SEC (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) (N24001966) (MADHYA PRADESH)	529.44	04/2023	378.40
	5	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) (N24001259) (NAGALAND)	315.63	04/2022	116.70
	6	HOSPET-BELLARY-KARNATAKA AP BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) (N24000603) (KARNATAKA)	1,167.42	03/2019	1,028.39
	7	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) (N24002026) (ASSAM)	643.42	12/2025	69.47
	8	RISHI BORDER- ROLEP- MENLA PKG- 2A (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) (N24001361) (SIKKIM)	332.20	09/2023	149.38

Table:-5. Project List: Frozen/Deleted during 1st Quarter (April-June),2025-26

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	9	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) (N24000686) (NAGALAND)	373.07	09/2019	382.50
	10	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) (N24001272) (MANIPUR)	167.95	06/2022	88.05
	11	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) (N24001273) (MANIPUR)	177.76	08/2022	89.67
	12	IMPHAL - KHONGSANG PKG-2 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) (N24001353) (MANIPUR)	195.14	12/2022	61.81
URBAN DEVELOPMENT					
	13	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D (CENTRAL PUBLIC WORKS DEPARTMENT) (N28000154) (HIMACHAL PRADESH)	512.34	11/2024	-
		Total	8603.54		5995.91

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ARUNACHAL PRADESH	CIVIL AVIATION	1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (01-07-2025) {7/2025}	645.63 (732.00) {732.00}	694.26	99.89
	POWER	2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	24,484.77	96.6
		3	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,380.24	15.81
	ROAD TRANSPORT AND HIGHWAYS	4	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	398.18	95.84
		5	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	194.62	44.56
		6	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (01-08-2024) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		7	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8-2020	4/2022 (01-02-2024) {9/2024}	294.04 (N.A.) {294.04}	147.13	100
		8	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (01-02-2024) {7/2025}	184.88 (N.A.) {184.88}	99.32	97.42
		9	HUNLI TO HAYULIANG PKG-1 (NHIDCL) (N24002222)	2-2024	2/2028 (N.A.) {2/2028}	1,262.43 (N.A.) {1,262.43}	12.12	2.76

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		10	HUNLI TO ITHUN BRIDGE SECTION (NHIDCL) (N24002223)	2-2024	1/2027 (N.A.) {1/2027}	275.50 (N.A.) {275.50}	7.61	7.88
		11	PANGO TO JORGING ROAD PKG-1 (NHIDCL) (N24002224)	1-2024	7/2027 (N.A.) {7/2027}	898.19 (N.A.) {898.19}	16.01	4.25
		12	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (01-03-2024) {12/2024}	180.57 (244.10) {180.57}	160.46	96.62
		13	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (01-06-2025) {12/2025}	1,718.59 (1,718.59) {1,718.59}	742.36	73.84
		14	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9-2016	12/2019 (01-08-2024) {9/2024}	568.92 (568.92) {568.92}	508.65	100
		15	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (01-05-2023) {3/2025}	256.66 (N.A.) {256.66}	-	63.59
		16	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA- HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (01-04-2025) {4/2025}	301.06 (N.A.) {301.06}	205.71	100
		17	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO (NHIDCL) (N24001245)	9-2020	5/2022 (01-10-2022) {3/2024}	353.90 (N.A.) {353.90}	41.82	25.38

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ASSAM	<u>CIVIL AVIATION</u>	18	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (01-09-2025) {9/2025}	1,142.00 (N.A.) {2,333.00}	1,948.45	89.66
	<u>COAL</u>	19	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	81.45	0
		20	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	105.59	0
	<u>HEALTH AND FAMILY WELFARE</u>	21	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (01-04-2023) {6/2025}	875.00 (873.92) {860.00}	796.74	99.62
	<u>PETROLEUM</u>	22	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.52	27.3
		23	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	97.22	92
		24	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	255.51	55
		25	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	208.56	46.3
		26	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (01-06-2025) {12/2025}	543.91 (726.93) {726.93}	491.56	93.98
		27	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	16,357.82	74.92

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		28	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,579.31	85.1
		29	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (01-05-2026) {5/2026}	412.00 (595.20) {595.20}	396.15	83.4
		30	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (01-09-2026) {9/2026}	277.00 (N.A.) {277.00}	181.63	67.67
		31	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (01-07-2025) {10/2025}	860.00 (N.A.) {860.00}	535.46	97.5
		32	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (01-06-2025) {12/2025}	430.76 (N.A.) {430.76}	320.71	83.94
		33	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	101.15	34.6
		34	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (01-07-2027) {7/2027}	156.36 (156.36) {156.36}	44.33	35.4
		35	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (01-07-2027) {7/2027}	384.04 (N.A.) {384.04}	97.54	44
	RAILWAYS	36	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2026 (N.A.) {3/2027}	4,059.65 (N.A.) {4,962.40}	3,668.09	92.31

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	37	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	217.31	97.76
		38	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {7/2025}	437.39 (N.A.) {437.39}	586.89	97.43
		39	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	517.62	78.19
		40	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH- 52 (NHIDCL) (N24000431)	1-1991	6/2019 (01-06-2019) {7/2025}	520.01 (N.A.) {520.01}	306.13	98.42
		41	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (01-07-2021) {12/2025}	289.99 (N.A.) {289.99}	233.23	88.03
		42	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {7/2025}	294.17 (N.A.) {294.17}	396.49	98.4
		43	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {7/2025}	252.00 (N.A.) {330.30}	242.97	95.42
		44	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (01-06-2025) {8/2025}	216.49 (241.52) {216.49}	114.38	87.02
		45	CONSTRUCTION OF 4 LANE GAURIPUR BYPASS ON NH-17 IN THE STATE OF ASSAM (MoRTH) (N24002237)	3-2024	10/2026 (N.A.) {10/2026}	421.15 (N.A.) {421.15}	-	0

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		46	CONSTRUCTION OF 2 LANE BARPETA BYPASS FROM KM 77+900(BARADI) TO KM 86+150(DEURIKUCHI) (LENGTH=8.25K (MoRTH) (N24002238)	3-2023	8/2026 (N.A.) {8/2026}	173.65 (N.A.) {173.65}	-	0
		47	SILCHAR- CHURAI BARI PKG-5 (NHIDCL) (N24002243)	2-2024	10/2027 (N.A.) {10/2027}	1,258.13 (N.A.) {1,258.13}	-	0
		48	BILASIPURA- GUWAHATI ROAD PKG-1 (NHIDCL) (N24002225)	2-2024	8/2027 (N.A.) {8/2027}	1,081.15 (N.A.) {1,081.15}	33.93	2.76
		49	SILCHAR-JIRIBAM PKG-1 (NHIDCL) (N24002226)	1-2024	1/2028 (N.A.) {1/2028}	957.95 (N.A.) {957.95}	-	21.98
		50	BILASIPURA- GUWAHATI ROAD PKG-2 (NHIDCL) (N24002229)	11-2023	6/2027 (N.A.) {6/2027}	1,338.61 (N.A.) {1,338.61}	0.50	0
		51	BADARPUR ? CHURAI BARI PKG-6 (NHIDCL) (N24002230)	3-2024	3/2027 (N.A.) {3/2027}	870.00 (N.A.) {870.00}	-	5.86
		52	KARIMGANI - SUTARKANDI SECTION ON SILCHAR-CHURAI BARI PKG-7 (NHIDCL) (N24002231)	2-2024	2/2027 (N.A.) {2/2027}	791.79 (N.A.) {791.79}	-	1.02
		53	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	409.15	68.26
		54	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	417.17	68.6

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		55	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	467.83	65.56
		56	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	323.24	98.48
		57	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	303.89	99.06
		58	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	551.88	47.5
		59	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	308.11	29.01
		60	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	425.17	27.99
		61	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	242.92	75.51
		62	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	134.02	18.15
		63	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3-2023	12/2025 (N.A.) {12/2026}	643.42 (N.A.) {643.42}	69.47	0

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		64	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	290.90	43.16
		65	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	213.67	50.88
		66	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.87	100
		67	SILCHAR VAIRENGTE SAIRANG ROAD PKG- 1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	539.19	40.36
		68	SILCHAR VAIRENGTE SAIRANG ROAD PKG- 2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	989.94	64.56
		69	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	297.70	54.97
		70	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	407.11	68.95
		71	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (1,019.17) {925.47}	192.50	30.65
		72	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	344.27	67.85

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		73	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {5/2025}	625.64 (N.A.) {625.64}	556.44	100
		74	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3-2022	7/2024 (N.A.) {10/2024}	215.27 (N.A.) {215.27}	105.40	100
		75	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {7/2025}	204.10 (N.A.) {204.10}	143.66	96.8
		76	FOUR LANING OF SRIRAMPUR-DHUBRI PKG- 2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	532.44	100
		77	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (01-09-2024) {6/2024}	175.00 (N.A.) {175.00}	209.02	100
		78	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	683.00	78.92
		79	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {5/2025}	457.72 (N.A.) {457.72}	366.34	100
		80	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	110.76	35.77
		81	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {11/2025}	458.59 (N.A.) {458.59}	205.87	66.12

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		82	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {3/2026}	535.03 (N.A.) {535.03}	102.23	34.54
		83	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.78	100
		84	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG- 7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	159.30	82.9
		85	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (01-05-2025) {12/2025}	261.13 (N.A.) {261.13}	70.08	57.5
		86	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (01-04-2025) {12/2025}	217.50 (N.A.) {217.50}	89.21	68.03
		87	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,464.49	62.82
MANIPUR	CIVIL AVIATION	88	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (01-12-2025) {12/2025}	499.00 (N.A.) {499.00}	154.47	40.82
	RAILWAYS	89	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	12/2026 (01-03-2028) {3/2028}	14,322.79 (12,274.06) {22,234.60}	15,485.02	69.2
	ROAD TRANSPORT AND HIGHWAYS	90	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (01-06-2025) {12/2025}	379.39 (N.A.) {379.39}	218.03	70.94

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		91	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8-2020	4/2022 (N.A.) {8/2026}	228.97 (N.A.) {228.97}	-	4.6
		92	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (01-03-2025) {12/2025}	226.32 (N.A.) {226.32}	105.78	74.48
		93	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (01-01-2025) {9/2025}	188.36 (N.A.) {188.36}	126.71	99.02
		94	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3-2021	12/2022 (01-03-2025) {3/2026}	195.14 (N.A.) {195.14}	61.81	0
		95	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (01-09-2024) {11/2025}	234.08 (N.A.) {234.08}	139.45	92.82
		96	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (01-01-2026) {3/2026}	410.68 (N.A.) {410.68}	152.34	70.11
		97	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (01-09-2025) {12/2025}	504.76 (N.A.) {504.76}	190.26	78.25
		98	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (01-02-2025) {3/2025}	152.11 (N.A.) {152.11}	73.48	100
		99	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (01-07-2025) {12/2025}	579.63 (N.A.) {579.63}	180.72	72.5
		100	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (01-01-2025) {1/2026}	477.86 (N.A.) {477.86}	246.09	84.87

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		101	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (01-11-2024) {12/2025}	311.18 (N.A.) {311.18}	190.96	83.78
		102	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (01-10-2024) {2/2025}	467.41 (N.A.) {467.41}	264.83	100
		103	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (01-05-2025) {10/2025}	211.70 (N.A.) {211.70}	83.79	71.06
		104	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (01-03-2025) {10/2025}	467.00 (N.A.) {467.00}	193.81	79.81
		105	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (01-01-2025) {1/2025}	185.80 (N.A.) {185.80}	117.78	100
		106	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (01-01-2025) {12/2025}	483.87 (N.A.) {483.87}	278.89	92.94
		107	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (01-02-2025) {3/2025}	198.77 (N.A.) {198.77}	127.86	100
		108	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (01-03-2025) {12/2025}	673.27 (N.A.) {673.27}	382.37	80.28
		109	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (01-03-2026) {3/2026}	578.98 (N.A.) {578.98}	153.92	71.25
		110	MARREM KHULLEN TO JESSAMI SECTION IMPHAL- UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	17.79	15

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		111	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	13.14	18.04
		112	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (01-03-2025) {7/2025}	310.76 (N.A.) {310.76}	129.15	96.77
		113	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (01-12-2025) {3/2026}	760.16 (N.A.) {760.16}	157.48	62.92
		114	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (01-08-2025) {8/2025}	315.56 (N.A.) {315.56}	137.81	88.74
		115	IMPHAL-KOHIMA ROAD PKG-5A (NHIDCL) (N24002232)	9-2020	8/2026 (N.A.) {8/2026}	228.97 (N.A.) {228.97}	-	10.13
		116	JESSAMI TO LAYNEN BRIDGE UKHRUL - JESSAMI PKG-7 (NHIDCL) (N24002227)	3-2023	6/2026 (N.A.) {6/2026}	164.89 (N.A.) {164.89}	3.83	9.78
		117	IMPHAL - KHONGSANG - JIRIBAM PKG-2 (NHIDCL) (N24002244)	3-2021	3/2026 (N.A.) {3/2026}	195.14 (N.A.) {195.14}	4.42	11.53
		118	CHOITHAR TO MARREM KHULLEN SECTION IMPHAL- UKHRUL - JESSAMI PKG-5 (NHIDCL) (N24002242)	3-2023	3/2027 (N.A.) {3/2027}	564.05 (N.A.) {564.05}	-	0
		119	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (01-06-2025) {9/2025}	292.24 (N.A.) {292.24}	130.66	90.69
		120	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (01-06-2025) {10/2025}	365.53 (N.A.) {365.53}	156.31	77.69

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA		121	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (01-01-2025) {12/2025}	167.95 (204.12) {167.95}	88.05	69.89
		122	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (01-02-2025) {12/2025}	177.76 (N.A.) {177.76}	89.67	80.53
	DEPARTMENT OF HIGHER EDUCATION	123	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (01-07-2025) {7/2025}	484.32 (429.70) {494.52}	270.55	84
	ROAD TRANSPORT AND HIGHWAYS	124	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (01-06-2025) {6/2025}	553.51 (610.09) {553.51}	438.16	88.07
		125	IMPROVEMENT AND WIDENING TWO LANNIG WITH PAVED SHOULDER OF NATIONAL HIGHWAY 127B FROM KM 31.500 (GOE (MoRTH) (N24002239)	12-2023	5/2027 (N.A.) {5/2027}	504.00 (N.A.) {504.00}	-	0
		126	DAINADUBI-DARUGIRI PKG-1B (NHIDCL) (N24002233)	3-2023	3/2027 (N.A.) {3/2027}	705.83 (N.A.) {705.83}	0.32	2.13
		127	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (01-06-2024) {2/2025}	157.86 (146.92) {157.86}	152.95	100
		128	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (01-05-2026) {5/2026}	359.86 (N.A.) {359.86}	233.26	60.81
		129	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	222.26	30

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		130	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	293.36	25.52
		131	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	297.91	25.27
		132	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (N.A.) {7/2025}	302.88 (N.A.) {302.88}	228.68	96
		133	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11-2021	6/2024 (01-12-2024) {5/2025}	283.50 (N.A.) {283.50}	257.26	100
		134	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	214.34	30.3
		135	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	107.86	24
		136	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3-2021	12/2022 (01-06-2024) {2/2025}	260.21 (N.A.) {260.21}	239.35	100
		137	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM () (NHIDCL) (N24001313)	11-2020	12/2023 (01-10-2025) {10/2025}	351.12 (N.A.) {351.12}	299.22	63
		138	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	434.50	32

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MIZORAM	RAILWAYS	139	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2025 (N.A.) {6/2025}	6,527.45 (5,021.45) {8,071.30}	8,066.76	97
	ROAD TRANSPORT AND HIGHWAYS	140	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL- TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9-2020	10/2022 (N.A.) {4/2025}	275.02 (N.A.) {247.25}	237.68	100
		141	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	265.38	100
		142	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {10/2024}	292.24 (N.A.) {331.17}	294.78	94.4
		143	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (01-04-2024) {4/2024}	233.25 (N.A.) {233.25}	172.09	100
		144	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	502.24	63.7
		145	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	373.89	61
		146	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (N.A.) {5/2024}	492.94 (N.A.) {492.94}	365.86	100
		147	ZORINPUI- HMAWNGBU-LONGMASU (NH- 502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	33.77	3
		148	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	279.44	75.4

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		149	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWLRAING SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	379.40	95.31
		150	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {4/2025}	519.09 (N.A.) {785.65}	670.91	97.51
		151	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {5/2024}	640.07 (N.A.) {1,286.35}	1,195.84	98.9
		152	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4-2017	6/2023 (N.A.) {3/2024}	642.96 (N.A.) {988.23}	686.42	100
		153	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {4/2025}	473.18 (N.A.) {688.25}	541.04	95
		154	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {4/2025}	537.82 (N.A.) {789.05}	779.37	99.88
		155	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {5/2025}	518.53 (N.A.) {906.76}	849.68	97.9
		156	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {5/2025}	404.29 (N.A.) {750.32}	666.58	100

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		157	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {5/2025}	428.11 (N.A.) {746.39}	613.69	99.82
NAGALAND	PETROLEUM	158	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	6.62	19
	RAILWAYS	159	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2026 (N.A.) {12/2029}	6,663.20 (6,663.20) {6,663.20}	4,942.71	74
	ROAD TRANSPORT AND HIGHWAYS	160	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (01-11-2022) {5/2025}	373.07 (534.41) {534.41}	382.50	99.81
		161	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (01-09-2025) {9/2025}	429.52 (794.74) {794.74}	321.40	92.46
		162	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (01-02-2023) {4/2025}	387.00 (688.12) {688.12}	392.01	100
		163	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (01-08-2024) {4/2025}	500.09 (698.81) {698.81}	393.53	100
		164	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (01-08-2022) {8/2025}	215.79 (N.A.) {215.79}	132.93	80.38

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		165	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (01-06-2023) {9/2025}	323.98 (N.A.) {323.98}	119.94	60.11
		166	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3-2017	11/2020 (01-02-2023) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
		167	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3-2019	12/2022 (01-01-2023) {1/2023}	237.51 (N.A.) {237.51}	215.47	100
		168	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (01-09-2024) {6/2026}	277.44 (N.A.) {277.44}	169.46	67.91
		169	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (01-06-2025) {12/2025}	159.85 (342.29) {159.85}	108.15	33.55
		170	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (01-04-2023) {8/2025}	202.36 (N.A.) {202.36}	75.39	32.67
		171	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9-2020	4/2022 (01-05-2024) {12/2025}	315.63 (N.A.) {315.63}	116.70	0
		172	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	100.51	58.57

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		173	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	50.60	28.05
		174	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	168.20	66.03
		175	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3-2022	12/2024 (N.A.) {1/2025}	605.36 (N.A.) {605.36}	273.21	100
		176	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	65.19	73.34
		177	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (01-09-2025) {9/2025}	258.52 (N.A.) {258.52}	89.46	81.4
		178	PEREN-DIMAPUR PKG-5 (NHIDCL) (N24001407)	2-2021	3/2023 (N.A.) {3/2023}	207.33 (N.A.) {207.33}	-	0
		179	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (01-06-2026) {6/2026}	252.19 (N.A.) {252.19}	14.33	20.27
		180	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (01-12-2025) {12/2025}	297.24 (N.A.) {297.24}	150.10	80.31
		181	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (01-03-2025) {3/2025}	226.44 (N.A.) {226.44}	140.24	100

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		182	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (01-09-2025) {9/2025}	192.93 (N.A.) {192.93}	112.09	93.38
		183	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {12/2025}	177.77 (199.02) {199.02}	46.94	63.33
		184	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3-2020	6/2022 (01-09-2022) {1/2025}	206.53 (N.A.) {206.53}	119.25	100
		185	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	119.20	65.06
		186	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (01-10-2022) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		187	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (01-11-2025) {11/2025}	330.80 (N.A.) {330.80}	171.89	92.44
		188	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (01-11-2026) {11/2026}	232.29 (350.88) {232.29}	79.69	17.31
SIKKIM	CIVIL AVIATION	189	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	29.68	12.5
	DEPARTMENT OF HIGHER EDUCATION	190	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim University) (N44000002)	8-2020	1/2025 (N.A.) {1/2025}	314.06 (N.A.) {303.55}	157.24	80

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	191	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,424.21	68.17
		192	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,524.17	89.45
	RAILWAYS	193	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	5/2015 (01-12-2027) {12/2027}	7,876.92 (11,963.43) {11,963.43}	8,743.57	79.5
	ROAD TRANSPORT AND HIGHWAYS	194	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (01-10-2023) {12/2025}	292.80 (N.A.) {292.80}	202.92	61.41
		195	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (01-10-2023) {12/2025}	183.31 (439.56) {439.56}	355.31	51.85
		196	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (01-08-2024) {12/2025}	262.84 (414.20) {414.20}	221.86	49.2
		197	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1-2021	9/2023 (01-04-2025) {12/2025}	332.20 (348.92) {348.92}	149.38	0
		198	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (01-12-2025) {12/2025}	410.60 (379.30) {379.30}	238.13	74.82
		199	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (01-10-2024) {3/2026}	230.45 (244.91) {244.91}	206.95	82.8

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		200	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (01-07-2025) {3/2026}	493.42 (478.79) {478.79}	308.18	59.49
		201	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (01-06-2025) {12/2026}	816.79 (786.60) {786.60}	332.24	45.9
		202	SPECIAL PROTECTION WORK ON REHABILITATION AND RESTORATION OF SLIDING AND SINKING ZONE FROM RANGPO TO (NHIDCL) (N24001913)	3-2017	6/2022 (N.A.) {6/2022}	165.56 (N.A.) {165.56}	-	71.74
		203	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (01-03-2026) {3/2026}	385.15 (N.A.) {385.15}	175.16	83.3
		204	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {10/2025}	311.00 (N.A.) {273.78}	257.86	95.12
		205	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (01-08-2024) {10/2025}	345.38 (395.59) {395.59}	362.61	89.81
		206	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {10/2025}	402.94 (N.A.) {402.94}	247.12	76.54
		207	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (01-11-2024) {10/2025}	295.97 (N.A.) {295.97}	249.97	95.71

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
TRIPURA		208	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100
		209	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (01-05-2022) {12/2023}	375.80 (N.A.) {375.80}	288.56	96.55
		210	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11-2017	10/2020 (01-08-2023) {4/2024}	290.05 (N.A.) {290.05}	218.36	100
	PETROLEUM	211	GRASS ROOT RAIL FED DEPOT AT SEKEREKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (01-09-2025) {9/2025}	656.00 (N.A.) {656.00}	427.77	83.17
	ROAD TRANSPORT AND HIGHWAYS	212	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (01-02-2024) {12/2024}	277.50 (302.02) {302.02}	262.91	99.94
		213	KHOWAI ? TELIAMURA-AMARPUR-HARINA-SABROOM SECTION PKG-4 (NHIDCL) (N24002228)	1-2024	12/2026 (N.A.) {12/2026}	726.90 (N.A.) {726.90}	7.36	3.85
		214	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	81.54	24.56
		215	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	26.34	8.82
		216	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGTH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	9.54	16.61

**Table:-6. Project List: Ongoing Projects of North-East Region during 1st Quarter
(April-June),2025-26**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		217	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	52.82	34.61
		218	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	95.71	32.85
		219	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	3.81	3.05
		220	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {12/2025}	195.95 (N.A.) {195.95}	46.46	45.42
		221	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (01-05-2025) {5/2025}	456.88 (N.A.) {456.88}	122.67	50.18
		222	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (N.A.) {12/2025}	354.79 (N.A.) {354.79}	34.08	0
		223	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {4/2025}	201.99 (N.A.) {287.47}	148.22	100
		224	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (01-10-2023) {11/2024}	159.13 (171.50) {171.50}	84.33	100
			Total			212797.85 (-) {259409.11}	152814.99	

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDAMAN AND NICOBAR ISLANDS	CIVIL AVIATION	1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR (AAI) (N04000073)	10-2013	9/2018 (01-06-2023) {6/2023}	417.23 (707.73) {707.73}	698.80	100
	RAILWAYS	2	LUDHIANA KILA RAIPUR (19 KMS) WITH FREIGHT LINE AT GILL STATION ON LDH-JHL SECTION (NR) (N22000584)	3-2019	3/2025 (01-08-2025) {3/2026}	235.72 (N.A.) {235.72}	59.78	55
	ROAD TRANSPORT AND HIGHWAYS	3	MAJOR BRIDGE OVER MIDDLE STRAIT CREEK (NHIDCL) (N24002207)	12-2024	2/2026 (N.A.) {2/2026}	371.80 (207.99) {207.99}	-	5.23
		4	PACKAGE-3A (NHIDCL) (N24002208)	2-2018	9/2025 (01-03-2024) {9/2025}	207.54 (154.01) {154.01}	16.21	39.27
		5	PACKAGE-3B (NHIDCL) (N24002209)	2-2018	11/2025 (N.A.) {11/2025}	183.47 (N.A.) {183.47}	18.36	34.01
		6	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N (NHIDCL) (N24000745)	3-2017	12/2019 (01-03-2023) {6/2025}	409.85 (N.A.) {409.85}	214.23	95.23
		7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O (NHIDCL) (N24000749)	3-2018	9/2020 (01-11-2022) {7/2025}	234.27 (N.A.) {234.27}	126.50	83
		8	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 (MoRTH) (N24000820)	11-2017	11/2019 (N.A.) {11/2019}	237.80 (N.A.) {238.00}	222.13	98.23
		9	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000821)	11-2017	11/2019 (N.A.) {11/2019}	257.34 (N.A.) {238.00}	214.90	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		10	AJANTHA TO BULDHANA (MoRTH) (N24001008)	2-2017	7/2019 (N.A.) {12/2023}	401.00 (401.00) {401.00}	246.39	96.75
ANDHRA PRADESH	CIVIL AVIATION	11	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT (AAI) (N04000089)	8-2017	2/2020 (01-12-2021) {1/2024}	177.10 (N.A.) {177.10}	143.08	100
		12	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT (AAI) (N04000091)	4-2020	3/2023 (01-08-2025) {8/2025}	611.80 (N.A.) {611.80}	449.66	75.25
		13	RAJAHMUNDY AIRPORT: CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUD (AAI) (N04000103)	12-2022	8/2025 (N.A.) {8/2025}	347.15 (347.15) {347.15}	76.86	46
		14	KADAPPA AIRPORT- CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUDING MA (AAI) (N04000106)	3-2023	1/2026 (01-03-2026) {3/2026}	265.91 (265.91) {265.91}	39.54	29
		15	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE (CPWD EDUCATION) (N42000005)	2-2019	6/2020 (N.A.) {6/2020}	655.34 (N.A.) {655.34}	366.21	95
		16	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC (CPWD EDUCATION) (N42000007)	9-2019	9/2022 (N.A.) {6/2024}	588.72 (656.39) {656.39}	630.55	100
	PETROLEUM	17	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT (ONGC) (N16000247)	3-2016	6/2020 (01-03-2025) {6/2025}	34,012.00 (N.A.) {34,012.00}	33,167.16	96.4
		18	REVAMPING OF FACILITIES AT VIZAG TERMINAL (IOCL) (N16000343)	4-2018	4/2022 (01-03-2025) {3/2025}	355.00 (N.A.) {355.00}	249.00	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		19	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY (HPCL) (N16000432)	9-2021	6/2024 (01-03-2026) {3/2026}	160.00 (220.00) {220.00}	75.86	59.4
		20	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS (IOCL) (N16000485)	3-2022	3/2030 (N.A.) {3/2030}	1,420.00 (N.A.) {1,420.00}	153.86	6.2
		21	MULTI-PRODUCT PIPELINE FROM KRISHNAPATNAM COASTAL INSTALLATION TO THE PROPOSED INSTALLATION AT HYDER (BPCL) (N16000499)	9-2019	3/2025 (N.A.) {10/2025}	1,932.00 (N.A.) {1,932.00}	1,498.21	94.3
		22	HP TRIJET UNIT IN VR (HPCL) (N16000535)	7-2024	7/2027 (N.A.) {7/2027}	193.00 (N.A.) {193.00}	0.43	23
		23	CONSTRUCTION OF AVIATION FUEL FARM FACILITIES AT BHOGAPURAM AIRPORT (HPCL) (N16000538)	8-2024	3/2026 (N.A.) {3/2026}	240.00 (N.A.) {240.00}	22.34	42.8
		24	VISAKHA RAIPUR PIPELINE PROJECT (HPCL) (N16000539)	9-2024	9/2027 (N.A.) {9/2027}	2,212.00 (N.A.) {2,212.00}	8.32	6.03
	POWER	25	TRANSMISSION SCHEME FOR SOLAR ENERGY ZONE IN ANANTHPURAM (2500MW) AND KURNOOL (1000MW) (PGCIL) (N18000380)	9-2023	3/2025 (N.A.) {9/2025}	1,249.00 (N.A.) {1,249.00}	761.69	67.5
		26	AUGMENTATION OF 1500MVA 3RD 765/400KV TRANSFORMATION CAPACITY AT KURNOOL NEW SUBSTATION (PGCIL) (N18000395)	5-2023	9/2025 (N.A.) {9/2025}	164.00 (N.A.) {164.00}	60.00	33
		27	TRANSMISSION SYSTEM FOR INTEGRATION OF KURNOOL-IV REZ PHASE-I (FOR 4.5 GW) (PGCIL) (N18000413)	3-2025	3/2027 (N.A.) {3/2027}	5,000.00 (N.A.) {5,000.00}	20.00	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		28	TRANSMISSION SYSTEM STRENGTHENING AT KURNOOL- III PS FOR INTEGRATION OF ADDITIONAL RE GENERATION PRO (PGCIL) (N18000416)	3-2025	3/2027 (N.A.) {3/2027}	2,886.00 (N.A.) {2,886.00}	20.20	0
	RAILWAYS	29	KOTLPALLI-NARASAPUR (NL) (SCR) (SCR) (220100265)	12-2001	3/2028 (N.A.) {3/2027}	2,500.98 (N.A.) {2,500.98}	1,141.44	18
		30	NADIKUDE-SRI KALAHASTI (SCR) (N22000286)	4-2011	5/2027 (N.A.) {5/2027}	2,312.00 (N.A.) {3,122.35}	1,977.09	0
		31	GUNTUR-GUNTAKAL (SCR) (N22000368)	4-2016	12/2025 (N.A.) {12/2025}	3,733.37 (N.A.) {3,887.48}	3,606.85	0
		32	VIJAYAWADA-GUDUR (RVNL) (N22000369)	4-2015	11/2024 (N.A.) {12/2024}	6,654.00 (N.A.) {6,238.67}	5,883.89	0
		33	KOTTAVALSA - KORAPUT DOUBLING (ECOR) (N22000377)	4-2015	3/2022 (N.A.) {3/2022}	2,499.71 (N.A.) {2,499.71}	1,965.11	70
		34	PENUKONDA-DHARMAVARAM, EXCL. DHARMAVARAM (41.5 KM) (SWR) (N22000555)	4-2019	3/2026 (N.A.) {12/2025}	294.67 (307.66) {307.66}	213.03	60
		35	MALUGUR-PALASAMUDRAM (17.98 KM) (PB#29/NR/2022-23) (SWR) (N22000556)	9-2022	12/2025 (N.A.) {12/2026}	323.14 (342.41) {342.41}	46.89	12
		36	DOUBLING BETWEEN GOOTY-PENDAKALLU (29.225) (SCR) (N22000585)	3-2023	3/2027 (N.A.) {3/2027}	351.83 (N.A.) {351.83}	-	0
		37	VIJAYAWADA KAZIPET BYEPASS LINE (SCR) (N22000586)	4-2016	12/2025 (N.A.) {12/2025}	647.37 (N.A.) {226.72}	261.07	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		38	RENIGUNTA WADI GOOTY - BYPASS (SCR) (N22000587)	4-2016	12/2025 (N.A.) {12/2025}	302.00 (N.A.) {302.00}	226.67	50
	ROAD TRANSPORT AND HIGHWAYS	39	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) (NHAI) (N24001301)	11-2019	1/2024 (N.A.) {7/2024}	1,601.10 (N.A.) {1,601.10}	1,445.67	92.34
		40	REHABILITATION AND UPGRADATION TO 2- LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT (MoRTH) (N24001386)	8-2020	3/2021 (N.A.) {6/2025}	222.61 (N.A.) {222.61}	183.91	95
		41	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI (NHAI) (N24001476)	9-2021	9/2022 (01-09-2024) {7/2025}	517.05 (N.A.) {655.06}	543.03	94.5
		42	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP (NHAI) (N24001477)	9-2021	9/2022 (01-09-2024) {6/2025}	622.00 (N.A.) {817.91}	541.73	75.96
		43	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 (NHAI) (N24001817)	2-2019	3/2023 (01-10-2024) {10/2024}	757.45 (N.A.) {757.45}	711.37	99.61
		44	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) (NHAI) (N24001818)	2-2021	1/2025 (N.A.) {1/2025}	818.73 (N.A.) {1,105.00}	564.03	25.32
		45	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) (NHAI) (N24001819)	3-2021	1/2025 (N.A.) {1/2025}	1,102.63 (N.A.) {1,303.00}	1,171.71	97.26
		46	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) (NHAI) (N24001820)	2-2021	12/2024 (N.A.) {12/2024}	1,484.83 (N.A.) {1,768.00}	1,544.65	93.29

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		47	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP) (NHAI) (N24001821)	11-2020	10/2024 (N.A.) {10/2024}	1,137.74 (N.A.) {1,289.00}	1,256.44	97.43
		48	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE) (NHAI) (N24001822)	12-2020	10/2024 (N.A.) {10/2024}	1,075.27 (N.A.) {1,307.00}	1,132.36	85.89
		49	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A (NHAI) (N24001823)	1-2022	1/2025 (01-01-2023) {1/2025}	1,852.12 (N.A.) {1,787.00}	777.18	93
		50	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP (NHAI) (N24001824)	3-2020	1/2024 (01-12-2024) {12/2024}	1,863.09 (N.A.) {2,238.00}	1,227.61	98.76
		51	6L KANTAKAPALLE ? SABBAVARAM SECTION OF NH-130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4) (NHAI) (N24001836)	2-2021	10/2024 (N.A.) {3/2026}	824.29 (N.A.) {924.00}	521.51	76.13
		52	6L JAKKUVA ? KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) (NHAI) (N24001837)	2-2021	3/2024 (01-07-2024) {12/2025}	663.60 (N.A.) {768.00}	464.74	98.84
		53	6L ALURU - JAKKUVA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) (NHAI) (N24001838)	2-2021	3/2024 (N.A.) {12/2025}	922.50 (N.A.) {1,128.68}	534.51	84.38
		54	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA (NHAI) (N24001841)	12-2022	9/2025 (N.A.) {2/2026}	912.94 (N.A.) {912.94}	238.84	59.65
		55	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 (NHAI) (N24001842)	12-2022	11/2025 (N.A.) {11/2025}	750.81 (N.A.) {750.81}	145.15	50.78

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		56	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH (NHAI) (N24001843)	12-2022	11/2025 (N.A.) {11/2025}	992.89 (N.A.) {992.89}	197.36	47
		57	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. (NHAI) (N24001844)	12-2022	10/2025 (N.A.) {10/2025}	1,058.90 (N.A.) {1,058.90}	251.41	47.64
		58	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 (NHAI) (N24001845)	2-2023	10/2025 (N.A.) {10/2025}	1,253.24 (N.A.) {1,253.24}	197.29	23.2
		59	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. (NHAI) (N24001846)	2-2023	10/2025 (N.A.) {10/2025}	1,200.42 (N.A.) {1,200.42}	98.82	8.9
		60	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA (NHAI) (N24001847)	1-2023	11/2025 (N.A.) {11/2025}	956.14 (N.A.) {956.14}	215.17	43.11
		61	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTLA 196.000 KM. PACK (NHAI) (N24001848)	2-2023	10/2025 (N.A.) {10/2025}	909.02 (N.A.) {909.02}	161.56	23.44
		62	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 (NHAI) (N24001849)	5-2022	7/2025 (N.A.) {9/2025}	1,063.72 (N.A.) {1,063.72}	467.94	82.1
		63	CONSTRUCTION OF 4-LANE HIGHWAY FROM SAMARLAKOTA TO ACHAMPETA JUNCTION (FROM KM. 0.000 TO KM. 12.250 (NHAI) (N24001856)	5-2023	8/2025 (N.A.) {8/2025}	648.75 (N.A.) {648.75}	253.96	64.67

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		64	4 LANING OF BATHALAPALLI TO MUDIGUBBA SECTION (DESIGN CHAINAGE KM. 96.300 TO 129.300) INCLUDING BATH (MoRTH) (N24001931)	3-2022	2/2025 (N.A.) {2/2025}	536.00 (N.A.) {536.00}	334.06	100
		65	2L+PS FROM KM. 0+000 TO KM. 32+000 (MUDIGUBBA TO PUTTAPARTHI) OF NH-342 (MoRTH) (N24001932)	3-2022	9/2024 (N.A.) {6/2025}	401.72 (N.A.) {401.72}	190.74	80
		66	NH440 RAYACHOTY TOVEMPALLI 2LPS (MoRTH) (N24001934)	12-2021	5/2024 (N.A.) {7/2025}	439.82 (N.A.) {439.82}	174.96	0
		67	4 LANE WITH PAVED SHOULDER FROM KM 0.000 TO KM 51.119 OF TADIPATRI TO MUDDANUR OF NH67 (MoRTH) (N24001935)	3-2022	8/2025 (N.A.) {8/2025}	724.17 (N.A.) {724.17}	464.48	0
		68	NH165 FROM KM 0.000 TO KM 64.020 PAMARRU TO AKIVEEDU SECTION TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001939)	3-2020	9/2023 (N.A.) {12/2026}	529.24 (N.A.) {529.24}	353.88	62.7
		69	2LPS FROM KM36.400 TO KM. 107.224 OF NH167BG FROM DUTTALUR TO KAVALI SECTION (MoRTH) (N24001942)	3-2021	7/2024 (N.A.) {6/2026}	423.67 (N.A.) {423.67}	222.39	83.59
		70	NH167B FROM KM 99.103 CS PURAM TO KM 143.320 MALAKONDA TO 2LPS (MoRTH) (N24001949)	12-2021	3/2024 (N.A.) {1/2025}	277.30 (N.A.) {277.30}	206.25	100
		71	NH167B FROM KM.143.320 MALAKONDA TO 189.050 SINGARAYAKONDA ON NH 16 TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001950)	3-2021	2/2025 (N.A.) {2/2025}	369.81 (N.A.) {369.81}	303.78	100
		72	NH167AD FROM MACHERLA TO DACHEPALLI FROM KM.0.000 TO 43.659 TO 2LPS (MoRTH) (N24001951)	1-2022	1/2025 (N.A.) {1/2025}	403.22 (N.A.) {403.22}	296.69	98.82

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		73	NH 167 B KADAPA NELLORE BORDER TO CSPURAM I.E. FROM KM 58.635 TO KM 99.409 (MoRTH) (N24001952)	3-2022	8/2025 (N.A.) {8/2025}	285.50 (N.A.) {285.50}	204.29	95
		74	NH-30-BHADRACHALAM TO KONTA SECTION 2LPS (MoRTH) (N24001953)	12-2021	9/2024 (N.A.) {9/2025}	388.71 (N.A.) {388.71}	242.09	89.6
		75	WIDENING TO 2LPS OF RAMPACHODAVARAM - KOYYURU SECTION OF NH516E FROM KM.43.700 TO KM 113.820 (MoRTH) (N24001954)	3-2022	1/2025 (N.A.) {1/2025}	568.12 (N.A.) {568.12}	350.64	91.05
		76	GUDIWADA TOWN 2 LANE ROB AND ROAD IMPROVEMENT OF NH165 IN REPLACEMENT OF LC NO 3ESPL3 AT KM 231.700 (MoRTH) (N24001955)	3-2022	5/2025 (N.A.) {5/2025}	317.22 (N.A.) {317.22}	190.90	80
		77	2LPS FROM GONDIGUDA TO ARAKU BHALLAGUDA KM 27.480 TO KM 51.772 SECTION OF NH 516E (MoRTH) (N24001956)	8-2020	9/2023 (N.A.) {12/2024}	296.66 (N.A.) {296.66}	246.11	87.49
		78	2LPS OF KOYYURU TO CHAPRATHIPALEM SECTION OF NH 516E (MoRTH) (N24001957)	8-2020	7/2024 (N.A.) {7/2024}	349.29 (N.A.) {349.29}	216.90	0
		79	2LPS OF CHAPRATHIPALEM TO LAMBASINGI SECTION OF NH 516E (MoRTH) (N24001958)	8-2020	10/2024 (N.A.) {6/2025}	311.22 (N.A.) {311.22}	151.24	72
		80	4 LANE FROM KM 56.400 TO KM 120.300 FROM B.KOTHAPALLI JUNCTION TO GORANTLA OF NH 716G (MoRTH) (N24001959)	3-2022	9/2025 (N.A.) {9/2025}	839.98 (N.A.) {839.98}	418.51	0
		81	4L GREENFIELD ROAD CONNECTING NORTH AND SOUTH INDUSTRIAL CLUSTER OF KHANDALERU CREEK NEAR KRISHNAPAT (NHAI) (N24001979)	8-2022	9/2025 (N.A.) {9/2025}	609.43 (N.A.) {609.43}	25.24	56.7

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		82	4 LANING OF NH 544D FROM EXISTING KM 346.300 OF NH 44 (DESIGN CHAINAGE KM 0.000) TO KM 39.380 (DESIG (NHAI) (N24001980)	10-2022	7/2025 (N.A.) {7/2025}	907.76 (N.A.) {907.76}	388.70	84.29
		83	CONSTRUCTION OF SIX LANING OF NAIDUPETA JUNCTION - TURPUKANUPUR SECTION FROM KM.57+046 TO KM.91+927 (NHAI) (N24001981)	7-2022	10/2025 (N.A.) {10/2025}	1,398.84 (N.A.) {1,398.84}	58.68	19.1
		84	4L PS FROM KURNOOL (EXISTING KM. 5.400 OF NH-40/DESIGN KM.0.000) TO MANDLEM (EXISTING KM.38.000/DESI (NHAI) (N24001982)	3-2023	10/2025 (N.A.) {10/2025}	827.39 (N.A.) {827.39}	333.88	99.65
		85	4 LANING FROM EXISTING KM 39.380 (DESIGN CH. 37.000) TO KM 74.450 (DESIGN CH. 69.000) OF MUCHUKOTA ? (NHAI) (N24001983)	10-2022	8/2025 (N.A.) {8/2025}	972.63 (N.A.) {1,055.23}	310.77	54.96
		86	4L PS FROM MANDLEM (EXISTING KM. 38.000/DESIGN KM.30.600) TO ATMAKUR (EXISTING KM.73.000/DESIGN KM 6 (NHAI) (N24001984)	3-2023	10/2025 (N.A.) {10/2025}	887.28 (N.A.) {887.28}	297.95	89.2
		87	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-II) FROM KM.96.000 TO KM 127.000 (BAIREDDYPALLE TO BANGAR (NHAI) (N24001985)	3-2021	6/2025 (N.A.) {6/2025}	1,942.94 (2,171.00) {2,171.00}	1,736.95	64.5
		88	4L OF PILERU TO KALUR SECTION FROM KM 55.900 TO KM 92.800 AND KM 94.500 TO KM 95.717 (NHAI) (N24001986)	10-2023	4/2025 (N.A.) {4/2025}	1,047.32 (N.A.) {1,047.32}	301.20	93
		89	CONSTRUCTION OF 1 NOS ROB, 2 NOS VUPS, SERVICE ROADS, PROVISION OF LIGHTING AND CONSTRUCTION OF OTHE (NHAI) (N24001987)	6-2023	12/2024 (N.A.) {12/2024}	152.05 (N.A.) {152.05}	139.12	76.83

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		90	6L OF CHITTOOR TO THATCHUR FROM KUMARAJAPET TO VEERA KAVERI RAJA PURAM FROM KM 43.800 TO KM 61.380 O (NHAI) (N24001988)	2-2021	10/2025 (N.A.) {10/2025}	591.99 (703.00) {703.00}	506.67	70.95
		91	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED HIGHWAY FROM CHILLAKURU CROSS ROAD TO TURPUKANUPUR KM 0+000 (NHAI) (N24002033)	7-2022	12/2025 (N.A.) {12/2025}	909.47 (N.A.) {909.47}	97.03	32.3
		92	COMPLETION OF BALANCE WORKS PENDING IN BIT AND PIECES (INCOMPLETE STRETCH AT 7 LOCATIONS) AND LISTED (NHAI) (N24002103)	9-2022	1/2025 (N.A.) {6/2025}	166.52 (N.A.) {166.52}	60.34	98
		93	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NARAYANMPET (CH. 203+500) TO CHANDRASEKHARPURAM (CH. 22 (NHAI) (N24002122)	2-2024	2/2026 (N.A.) {2/2026}	813.66 (N.A.) {813.66}	91.93	24.2
		94	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM CHANDRASEKHARAPURAM (CH. 228+000) TO POLAVARAM (CH. 260 (NHAI) (N24002123)	2-2024	2/2026 (N.A.) {2/2026}	1,292.65 (N.A.) {1,292.65}	135.27	18.96
		95	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM POLAVARAM (CH. 260+000) TO MARRIPUDI (CH. 285+500) OF [(NHAI) (N24002124)	2-2024	2/2026 (N.A.) {2/2026}	747.29 (N.A.) {747.29}	142.65	32.02
		96	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MARRIPUDI (CH. 285+500) TO SOMAVARAPPADU (CH. 314+600) (NHAI) (N24002125)	2-2024	2/2026 (N.A.) {2/2026}	976.40 (N.A.) {976.40}	229.68	43.6
		97	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM SOMAVARAPPADU (CH.314.600) TO MUPPAVARAM (CH.343+240) O (NHAI) (N24002126)	2-2024	2/2026 (N.A.) {2/2026}	1,103.89 (N.A.) {1,103.89}	133.89	15.98

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		98	4-LANE WITH PAVED SHOULDERS FROM KM 32/0 TO KM 79/650 (DESIGN CHAINAGE KM 32+000 TO KM 78+760) PUTTA (MoRTH) (N24002139)	3-2023	12/2025 (N.A.) {11/2025}	1,318.57 (N.A.) {1,318.57}	424.42	0
		99	SOMAYAJULAPALLI ? DHONE SECTION OF NH ? 340B FROM KM.0/0 TO 56/200 [DESIGN CH. KM 0/00 TO KM 53/33] (MoRTH) (N24002140)	4-2023	12/2025 (N.A.) {12/2025}	629.73 (N.A.) {629.73}	369.43	0
		100	2 LANE WITH PAVED SHOULDER CONFIGURATION FROM SEETHARAMAPURAM TO DUTTALURU SECTION OF NH-167 BG FROM (MoRTH) (N24002141)	6-2023	7/2025 (N.A.) {7/2025}	364.07 (N.A.) {364.07}	227.21	100
		101	2-LANE WITH PAVED SHOULDER CONFIGURATION OF LAMBASINGI TO PADERU SECTION (KM 205+000 TO KM 253+974) (MoRTH) (N24002142)	8-2023	11/2025 (N.A.) {11/2025}	361.24 (N.A.) {361.24}	63.54	0
		102	BYPASS ROAD TO ADONI TOWN CONNECTING NH-167 (HAGARI - JADCHARLA ROAD) FROM KM.62/700 TO 71/400 IN KU (MoRTH) (N24002143)	8-2023	2/2026 (N.A.) {2/2026}	361.24 (N.A.) {361.24}	109.65	56
		103	VODAREVU-CHILAKALURIPET SECTION (DESIGN CHAINAGE 0+00 TO 47+000) OF NH-167A (PACKAGE-I) (MoRTH) (N24002144)	8-2023	2/2026 (N.A.) {2/2026}	1,064.24 (N.A.) {1,064.24}	584.25	0
		104	TADIPATRI BYPASS (KM 0+000 TO KM 6+285) OF 4-LANE ON NH-67 IN ANANTAPURAMU (MoRTH) (N24002145)	11-2023	3/2026 (N.A.) {3/2026}	159.66 (N.A.) {159.66}	60.51	63.5
		105	KURNOOL/KADAPA BORDER-JAMMALAMADUGU SECTION OF NH-167K I.E. DESIGN CH. KM 248+010 TO KM 269+900 (MoRTH) (N24002146)	11-2023	11/2025 (N.A.) {11/2025}	292.63 (N.A.) {292.63}	81.57	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		106	DORNALA TO KUNTA JUNCTION FROM DESIGN CHAINAGE KM 244+000 TO 267+990 SECTION OF NH-765 (PACKAGE-2) (MoRTH) (N24002147)	12-2022	1/2024 (N.A.) {3/2026}	244.83 (N.A.) {244.83}	111.65	0
		107	PADERU BYPASS (KM 0+000 TO KM 13+000) OF 2- LANE WITH PAVED SHOULDER ON NH-516E (MoRTH) (N24002148)	3-2023	3/2024 (N.A.) {2/2026}	244.43 (N.A.) {244.43}	23.40	0
		108	DAVUALAPALLY TO MALLAPALEM SECTION (DESIGN CH. KM 133+922 TO KM 154+216 (EXISTING CH. KM 133+922 TO (MoRTH) (N24002149)	1-2024	2/2024 (N.A.) {2/2026}	393.61 (N.A.) {393.61}	135.13	0
		109	DEVELOPMENT OF SIX LANE ACCESS CONTROLLED GREEN FIELD HIGHWAY FROM KAVULAKUNTALA (KM.196+000) TO NARA (NHAI) (N24002215)	2-2023	2/2027 (N.A.) {2/2027}	1,092.18 (N.A.) {1,092.18}	0.14	0
		110	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TN/AP BORDER (DESIGN CHAINAGE KM 61+51 (NHAI) (N24002217)	12-2024	12/2026 (N.A.) {12/2026}	1,346.82 (N.A.) {1,346.82}	37.35	8.2
		111	REHABILITATION AND UPGRADATION OF NH- 219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES (MoRTH) (N24000301)	3-2015	10/2015 (N.A.) {}	271.45 (N.A.) {271.45}	240.23	100
		112	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 (NHAI) (N24000811)	3-2018	12/2020 (01-12-2022) {12/2024}	314.43 (N.A.) {348.72}	85.61	71.49
		113	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 (MoRTH) (N24000931)	11-2016	5/2017 (N.A.) {11/2024}	290.15 (N.A.) {236.16}	205.03	90

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		114	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG (MoRTH) (N24000937)	3-2018	8/2018 (N.A.) {11/2024}	289.67 (290.00) {285.29}	256.60	98.5
		115	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD (MoRTH) (N24000964)	8-2016	1/2017 (N.A.) {5/2025}	350.61 (N.A.) {411.18}	390.28	98.2
		116	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 (MoRTH) (N24000969)	1-2017	9/2017 (N.A.) {6/2025}	263.45 (N.A.) {263.45}	265.51	85
	<u>WATER RESOURCES</u>	117	POLAVARAM IRRIGATION PROJECT (PPA) (N30000002)	2-2009	3/2020 (01-03-2027) {12/2027}	10,151.04 (N.A.) {55,548.87}	23,775.68	76
	<u>ARUNACHAL PRADESH</u>	118	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (01-07-2025) {7/2025}	645.63 (732.00) {732.00}	694.26	99.89
	<u>POWER</u>	119	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	24,484.77	96.6
		120	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,380.24	15.81
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	121	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	398.18	95.84

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		122	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	194.62	44.56
		123	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (01-08-2024) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		124	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8-2020	4/2022 (01-02-2024) {9/2024}	294.04 (N.A.) {294.04}	147.13	100
		125	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (01-02-2024) {7/2025}	184.88 (N.A.) {184.88}	99.32	97.42
		126	HUNLI TO HAYULIANG PKG-1 (NHIDCL) (N24002222)	2-2024	2/2028 (N.A.) {2/2028}	1,262.43 (N.A.) {1,262.43}	12.12	2.76
		127	HUNLI TO ITHUN BRIDGE SECTION (NHIDCL) (N24002223)	2-2024	1/2027 (N.A.) {1/2027}	275.50 (N.A.) {275.50}	7.61	7.88
		128	PANGO TO JORGING ROAD PKG-1 (NHIDCL) (N24002224)	1-2024	7/2027 (N.A.) {7/2027}	898.19 (N.A.) {898.19}	16.01	4.25
		129	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (01-03-2024) {12/2024}	180.57 (244.10) {180.57}	160.46	96.62
		130	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING- HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (01-06-2025) {12/2025}	1,718.59 (1,718.59) {1,718.59}	742.36	73.84

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		131	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9-2016	12/2019 (01-08-2024) {9/2024}	568.92 (568.92) {568.92}	508.65	100
		132	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (01-05-2023) {3/2025}	256.66 (N.A.) {256.66}	-	63.59
		133	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (01-04-2025) {4/2025}	301.06 (N.A.) {301.06}	205.71	100
		134	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO (NHIDCL) (N24001245)	9-2020	5/2022 (01-10-2022) {3/2024}	353.90 (N.A.) {353.90}	41.82	25.38
ASSAM	CIVIL AVIATION	135	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (01-09-2025) {9/2025}	1,142.00 (N.A.) {2,333.00}	1,948.45	89.66
	COAL	136	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	81.45	0
		137	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	105.59	0
	HEALTH AND FAMILY WELFARE	138	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (01-04-2023) {6/2025}	875.00 (873.92) {860.00}	796.74	99.62
	PETROLEUM	139	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (01-06-2025) {12/2025}	543.91 (726.93) {726.93}	491.56	93.98

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		140	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	16,357.82	74.92
		141	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,579.31	85.1
		142	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (01-05-2026) {5/2026}	412.00 (595.20) {595.20}	396.15	83.4
		143	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (01-09-2026) {9/2026}	277.00 (N.A.) {277.00}	181.63	67.67
		144	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (01-07-2025) {10/2025}	860.00 (N.A.) {860.00}	535.46	97.5
		145	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (01-06-2025) {12/2025}	430.76 (N.A.) {430.76}	320.71	83.94
		146	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	101.15	34.6
		147	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (01-07-2027) {7/2027}	156.36 (156.36) {156.36}	44.33	35.4
		148	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (01-07-2027) {7/2027}	384.04 (N.A.) {384.04}	97.54	44

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		149	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	97.22	92
		150	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	255.51	55
		151	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	208.56	46.3
		152	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.52	27.3
	RAILWAYS	153	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2026 (N.A.) {3/2027}	4,059.65 (N.A.) {4,962.40}	3,668.09	92.31
	ROAD TRANSPORT AND HIGHWAYS	154	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,464.49	62.82
		155	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (01-05-2025) {12/2025}	261.13 (N.A.) {261.13}	70.08	57.5
		156	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (01-04-2025) {12/2025}	217.50 (N.A.) {217.50}	89.21	68.03
		157	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.78	100
		158	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	159.30	82.9

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		159	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (1,019.17) {925.47}	192.50	30.65
		160	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	344.27	67.85
		161	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {5/2025}	625.64 (N.A.) {625.64}	556.44	100
		162	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3-2022	7/2024 (N.A.) {10/2024}	215.27 (N.A.) {215.27}	105.40	100
		163	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {7/2025}	204.10 (N.A.) {204.10}	143.66	96.8
		164	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	532.44	100
		165	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (01-09-2024) {6/2024}	175.00 (N.A.) {175.00}	209.02	100
		166	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION-HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	683.00	78.92
		167	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {5/2025}	457.72 (N.A.) {457.72}	366.34	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		168	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	110.76	35.77
		169	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {11/2025}	458.59 (N.A.) {458.59}	205.87	66.12
		170	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {3/2026}	535.03 (N.A.) {535.03}	102.23	34.54
		171	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	409.15	68.26
		172	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	417.17	68.6
		173	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	467.83	65.56
		174	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	323.24	98.48
		175	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	303.89	99.06

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		176	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	551.88	47.5
		177	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	308.11	29.01
		178	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	425.17	27.99
		179	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	242.92	75.51
		180	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	134.02	18.15
		181	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3-2023	12/2025 (N.A.) {12/2026}	643.42 (N.A.) {643.42}	69.47	0
		182	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.87	100
		183	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	539.19	40.36
		184	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	989.94	64.56

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		185	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	297.70	54.97
		186	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	407.11	68.95
		187	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	290.90	43.16
		188	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	213.67	50.88
		189	BILASIPURA- GUWAHATI ROAD PKG-1 (NHIDCL) (N24002225)	2-2024	8/2027 (N.A.) {8/2027}	1,081.15 (N.A.) {1,081.15}	33.93	2.76
		190	SILCHAR-JIRIBAM PKG-1 (NHIDCL) (N24002226)	1-2024	1/2028 (N.A.) {1/2028}	957.95 (N.A.) {957.95}	-	21.98
		191	BILASIPURA- GUWAHATI ROAD PKG-2 (NHIDCL) (N24002229)	11-2023	6/2027 (N.A.) {6/2027}	1,338.61 (N.A.) {1,338.61}	0.50	0
		192	BADARPUR ? CHURABARI PKG-6 (NHIDCL) (N24002230)	3-2024	3/2027 (N.A.) {3/2027}	870.00 (N.A.) {870.00}	-	5.86
		193	KARIMGANI - SUTARKANDI SECTION ON SILCHAR-CHURABARI PKG-7 (NHIDCL) (N24002231)	2-2024	2/2027 (N.A.) {2/2027}	791.79 (N.A.) {791.79}	-	1.02

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		194	CONSTRUCTION OF 4 LANE GAURIPUR BYPASS ON NH-17 IN THE STATE OF ASSAM (MoRTH) (N24002237)	3-2024	10/2026 (N.A.) {10/2026}	421.15 (N.A.) {421.15}	-	0
		195	CONSTRUCTION OF 2 LANE BARPETA BYPASS FROM KM 77+900(BARADI) TO KM 86+150(DEURIKUCHI) (LENGTH=8.25K (MoRTH) (N24002238)	3-2023	8/2026 (N.A.) {8/2026}	173.65 (N.A.) {173.65}	-	0
		196	SILCHAR- CHURAIBARI PKG-5 (NHIDCL) (N24002243)	2-2024	10/2027 (N.A.) {10/2027}	1,258.13 (N.A.) {1,258.13}	-	0
		197	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {7/2025}	437.39 (N.A.) {437.39}	586.89	97.43
		198	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	517.62	78.19
		199	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1-1991	6/2019 (01-06-2019) {7/2025}	520.01 (N.A.) {520.01}	306.13	98.42
		200	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH- 37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (01-07-2021) {12/2025}	289.99 (N.A.) {289.99}	233.23	88.03
		201	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {7/2025}	294.17 (N.A.) {294.17}	396.49	98.4
		202	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {7/2025}	252.00 (N.A.) {330.30}	242.97	95.42

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
BIHAR		203	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	217.31	97.76
		204	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (01-06-2025) {8/2025}	216.49 (241.52) {216.49}	114.38	87.02
	CIVIL AVIATION	205	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II (AAI) (N04000082)	5-2018	10/2022 (01-11-2025) {11/2025}	1,216.90 (N.A.) {1,216.90}	1,029.05	93.14
		206	DARBHANGA:DEVELOPMENT OF NEW CIVIL ENCLAVE AT DARBHANGA, BIHAR. SH- CONSTRUCTION OF NEW TERMINAL BUI (AAI) (N04000112)	7-2024	7/2026 (N.A.) {7/2026}	911.66 (N.A.) {911.66}	113.58	20.75
	DEPARTMENT OF HIGHER EDUCATION	207	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA (CPWD EDUCATION) (N28000100)	2-2016	6/2017 (N.A.) {1/2024}	496.18 (496.00) {460.00}	390.15	100
		208	PERMANENT CAMPUS FOR IIM BODH GAYA (CPWD EDUCATION) (N42000009)	9-2018	9/2020 (N.A.) {3/2025}	375.00 (N.A.) {375.00}	342.18	100
	PETROLEUM	209	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA (IOCL) (N16000386)	1-2020	4/2023 (01-08-2026) {8/2026}	14,810.00 (18,113.00) {18,113.00}	11,055.42	89
		210	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA (IOCL) (N16000423)	6-2019	12/2029 (01-03-2030) {3/2030}	163.00 (N.A.) {163.00}	96.08	40.1
		211	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI (IOCL) (N16000453)	1-2022	4/2025 (N.A.) {5/2026}	389.00 (N.A.) {389.00}	38.25	35.4

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		212	CITY GAS DISTRIBUTION PROJECTS AT GOPALGANJ SIWAN WEST CHAMPARAN EAST CHAMPARAN AND DEORIA DISTRICTS (BPCL) (N16000523)	12-2022	6/2030 (N.A.) {6/2030}	3,919.00 (N.A.) {3,919.00}	382.99	13.6
		213	CITY GAS DISTRIBUTION PROJECTS AT DARBHANGA, MADHUBANI, SUPAUL, SITAMARHI AND SHEOHAR DISTRICTS (BPCL) (N16000524)	12-2022	3/2030 (N.A.) {3/2030}	3,638.00 (N.A.) {3,638.00}	390.34	20.8
	POWER	214	BARH STPP(3X660MW) NTPC (NTPC) (180100242)	2-2005	10/2011 (01-07-2023) {3/2025}	8,692.97 (21,312.11) {21,312.11}	22,561.37	95
		215	BUXAR THERMAL POWER PLANT (1320 MW) (SJVN) (N18000194)	3-2019	1/2024 (N.A.) {10/2025}	10,439.09 (N.A.) {14,390.09}	11,845.16	91.56
		216	EASTERN REGION EXPANSION SCHEME: 43 [ERES: 43] (PGCIL) (N18000421)	5-2025	5/2026 (N.A.) {5/2026}	343.00 (N.A.) {343.00}	-	0
		217	EASTERN REGION EXPANSION SCHEME: 44 [ERES: 44] (PGCIL) (N18000422)	5-2025	5/2026 (N.A.) {5/2026}	409.00 (N.A.) {409.00}	-	0
	RAILWAYS	218	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) (ECR) (220100257)	4-1997	12/2024 (N.A.) {3/2027}	614.45 (614.45) {614.45}	483.57	52
		219	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR (ECR) (220100303)	4-2003	12/2014 (N.A.) {12/2026}	2,066.78 (2,087.36) {2,087.36}	2,454.59	73
		220	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR (NEFR) (N22000087)	9-2006	12/2024 (N.A.) {6/2025}	2,650.00 (2,132.03) {4,351.54}	4,074.75	92

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		221	SAKRI-HASANPUR ROAD (NL) (ECR) (N22000171)	4-1999	(N.A.) {3/2027}	325.00 (735.20) {735.20}	604.94	78
		222	ARARIA-SUPAUL (NL) (ECR) (N22000177)	4-2008	3/2024 (N.A.) {5/2025}	1,605.17 (1,605.17) {1,605.17}	1,749.92	65
		223	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC (ECR) (N22000181)	4-2009	3/2022 (N.A.) {3/2026}	819.00 (548.00) {783.83}	566.62	75
		224	SAMASTIPUR-DARBANGHA (ECR) (N22000329)	5-2015	3/2025 (N.A.) {10/2025}	519.33 (519.33) {519.33}	651.94	80
		225	KIUL - GAYA DOUBLING PROJECT (ECR) (N22000349)	12-2015	9/2024 (N.A.) {2/2025}	2,462.11 (1,200.20) {1,771.07}	1,896.91	99
		226	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE (ECR) (N22000350)	12-2015	12/2024 (N.A.) {12/2025}	2,373.64 (1,491.47) {1,600.00}	1,776.70	77
		227	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM (ECR) (N22000472)	4-2016	12/2024 (N.A.) {6/2025}	1,215.54 (1,215.54) {1,215.54}	1,595.74	91
		228	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM (ECR) (N22000473)	4-2016	6/2024 (N.A.) {5/2025}	1,586.22 (1,185.73) {1,300.00}	1,487.54	96
		229	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, (ECR) (N22000476)	4-1991	3/2023 (N.A.) {5/2025}	1,473.30 (803.09) {2,722.16}	2,794.05	90

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		230	DARBHANGA - BYPASS LINE CONNECTING SHISHO HALT AND KAKARGHATI EXCL DARBHANGA YARD (7.64 KM) (ECR) (N22000523)	6-2019	6/2025 (N.A.) {10/2024}	983.62 (253.23) {415.00}	417.57	100
		231	BARAUNI- BACHWARA 3RD AND 4TH LINE (ECR) (N22000524)	7-2022	7/2027 (N.A.) {12/2025}	486.00 (N.A.) {486.00}	135.31	33
		232	JHAJHA - BATIA (UMBRELLA WORK PB#23/2018- 19/NR) (ECR) (N22000526)	2-2019	6/2028 (N.A.) {12/2026}	496.47 (N.A.) {496.47}	22.55	0
		233	SONENAGAR BYE PASS LINE FROM CHIRALAPOTHU TO BAGHA BISHUNPUR (ECR) (N22000528)	10-2022	10/2027 (N.A.) {12/2026}	234.00 (223.69) {223.69}	22.57	0
		234	KATIHAR-KUMEDPUR AND KATIHAR-MUKURIA (64.5 KM) (UMBRELLA WORK PB#57/2019- 20/NR) (NFR) (N22000570)	8-2022	8/2027 (N.A.) {8/2026}	745.00 (N.A.) {1,500.00}	356.14	35
	ROAD TRANSPORT AND HIGHWAYS	235	BALANCE WORK OF 4- LANING OF PATNA- GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT (NHAI) (N24001303)	10-2013	12/2020 (01-12-2024) {12/2024}	649.90 (N.A.) {750.00}	711.53	98.3
		236	BALANCE WORK OF 4- LANING OF PATNA- GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE (NHAI) (N24001304)	10-2013	11/2020 (01-12-2024) {12/2024}	446.97 (598.48) {740.50}	638.80	96.3
		237	BALANCE WORK OF 4- L ANING OF PATNA- GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA (NHAI) (N24001305)	10-2013	11/2020 (01-12-2024) {12/2024}	464.09 (605.53) {765.12}	698.25	97.3
		238	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N (NHAI) (N24001371)	10-2019	8/2023 (01-04-2026) {4/2026}	1,101.99 (N.A.) {1,101.99}	890.20	78.48

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		239	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III) (NHAI) (N24001697)	2-2023	2/2025 (N.A.) {12/2025}	1,358.00 (N.A.) {1,358.00}	228.72	22
		240	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH (NHAI) (N24001698)	8-2022	8/2024 (01-12-2025) {12/2025}	1,198.02 (N.A.) {1,198.02}	43.77	0
		241	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT- GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3 (NHAI) (N24001699)	3-2022	12/2024 (01-12-2025) {12/2025}	312.58 (N.A.) {312.58}	205.99	85.88
		242	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO (NHAI) (N24001700)	12-2021	3/2024 (01-12-2024) {12/2024}	552.55 (553.00) {553.00}	378.25	86.6
		243	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU (NHAI) (N24001701)	4-2022	4/2024 (01-09-2025) {9/2025}	1,769.50 (N.A.) {1,769.50}	69.23	0
		244	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT-GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: (NHAI) (N24001702)	12-2021	9/2024 (N.A.) {6/2025}	184.90 (185.00) {185.00}	166.56	99.78
		245	6 L OF AURANGABAD TO BIHAR-JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N (NHAI) (N24001703)	2-2022	5/2025 (N.A.) {5/2025}	786.81 (787.00) {787.00}	-	8.3
		246	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI (NHAI) (N24001704)	3-2021	3/2024 (01-09-2025) {9/2025}	1,020.84 (N.A.) {1,020.84}	163.19	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		247	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C (NHAI) (N24001705)	3-2022	3/2024 (01-12-2025) {12/2025}	1,485.66 (N.A.) {1,485.66}	35.16	0
		248	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 (NHAI) (N24001708)	9-2020	6/2024 (N.A.) {4/2025}	2,156.22 (N.A.) {2,156.22}	1,397.72	99.14
		249	BAKHTIYARPUR RAJAULI PKG-II FROM KM 54.405 TO KM 101.630 NH20 (NHAI) (N24001709)	9-2020	4/2023 (01-12-2024) {12/2024}	897.45 (N.A.) {1,090.00}	1,037.63	97.85
		250	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G (NHAI) (N24001711)	9-2020	3/2023 (01-12-2024) {12/2024}	939.43 (N.A.) {939.43}	1,030.75	100
		251	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO (NHAI) (N24001712)	8-2020	7/2023 (01-05-2025) {5/2025}	690.00 (N.A.) {690.00}	770.73	98.9
		252	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI?MOTIHARI- RAXAUL SECTION OF NH-28A FRO (NHAI) (N24001715)	12-2018	10/2020 (N.A.) {1/2024}	333.60 (466.59) {461.41}	460.38	100
		253	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER OF NH 122B FROM KM 29.730 TO KM 72.348 IN STATE OF BIH (MoRTH) (N24001870)	2-2022	11/2024 (N.A.) {11/2025}	624.43 (N.A.) {624.43}	292.16	88
		254	WIDENING AND STRENGTHENING FROM KM 70.15 TO KM 121.025 OF NH-80 (MoRTH) (N24001875)	3-2021	1/2025 (N.A.) {7/2025}	477.54 (N.A.) {477.54}	360.27	94.5

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		255	WIDENING and STRENGTHENING FROM KM132.895 TO KM 190.15 NH-80 (MoRTH) (N24001876)	3-2021	3/2024 (N.A.) {9/2025}	566.15 (N.A.) {566.15}	258.29	58.6
		256	CONSTRUCTION OF NEW 4-LANE BRIDGE (PARALLEL TO EXISTING VIKRAMASHILA SETU)FROM KM 8+920 TO KM 13+375 (MoRTH) (N24001877)	7-2020	5/2027 (N.A.) {5/2027}	1,110.23 (N.A.) {1,110.23}	478.96	42.9
		257	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER OF NH-319A FROM KM 0 TO KM 45 IN STATE OF BIHAR UNDER (MoRTH) (N24001878)	2-2022	12/2024 (N.A.) {7/2025}	427.29 (N.A.) {427.29}	210.22	80
		258	CONSTRUCTION OF PROPOSED 4_LANE REVELGUNJ BYPASS NH-19 IN THE STATE OF BIHAR ON EPC MODE CONNECTING (MoRTH) (N24001879)	3-2022	7/2025 (N.A.) {10/2025}	295.24 (N.A.) {295.24}	93.14	63.05
		259	CONSTRUCTION OF 6- LANE BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD (NH- (NHAI) (N24002062)	3-2023	9/2027 (N.A.) {9/2028}	3,012.27 (N.A.) {3,012.27}	303.67	10.83
		260	BALANCE WORK - WB-10 (GANDAK BRIDGE) KM 402.00 TO KM 440.00 (DEVANPUR - KOTWA) (NHAI) (N24002063)	12-2021	1/2024 (N.A.) {3/2026}	210.05 (N.A.) {210.05}	104.35	69
		261	PERMANENT RECTIFICATION OF 3 NOS. OF BLACK SPOTS IN PROJECT HIGHWAY NH-27 OF U.P BORDER - DEWAPUR - (NHAI) (N24002064)	12-2022	12/2025 (N.A.) {12/2025}	381.80 (N.A.) {381.80}	119.56	52
		262	4L GREENFIELD ALIGNMENT OF AMAS TO SHIVRAMPUR FROM 0.000 KM. TO 55.002 KM. OF NH 119 D (PKG-I) (NHAI) (N24002065)	2-2022	3/2025 (N.A.) {3/2025}	1,390.92 (N.A.) {1,390.92}	17.54	22.56

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		263	4L GREENFIELD ALIGNMENT OF SHIVRAMPUR TO RAMNAGAR FROM KM. 55.002 TO KM. 109.300 OF NH 119 D (PKG-I) (NHAI) (N24002066)	2-2022	7/2025 (N.A.) {7/2025}	1,494.31 (N.A.) {1,494.31}	38.28	4.59
		264	IMPROVEMENT OF 2 LANE WITH PAVED SHOULDER OF STRETCH FROM BIKRAMGANJ DAWATH MELAYABAGH NAWANAGR-DUM (MoRTH) (N24002133)	3-2021	3/2025 (N.A.) {8/2025}	178.63 (N.A.) {178.63}	124.52	96
		265	CONSTRUCTION OF 4 LANE ROB AND ITS APPROACHES AT THE LEVEL OF CROSSING (L C NO. 29-B) OF KM 29 (EKAN) (MoRTH) (N24002193)	3-2023	7/2026 (N.A.) {7/2026}	201.08 (N.A.) {201.08}	25.42	28
		266	CONSTRUCTION OF 6-LANE ELEVATED / EXTRA DOSE CABLE BRIDGE ON RIVER GANGA PARALLEL TO AND WESTERN SID (MoRTH) (N24002194)	1-2024	11/2027 (N.A.) {11/2027}	3,064.45 (N.A.) {3,064.45}	142.38	5.19
		267	ESTIMATE FOR IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM RAMNAGAR TO ROSEDA FROM (KM 3.500 TO 4) (MoRTH) (N24002195)	1-2022	4/2026 (N.A.) {4/2026}	495.16 (N.A.) {495.16}	134.57	11.5
		268	CONSTRUCTION OF BHABHUA BYPASS FROM CH. 10+800(DESIGN CH. 10+800) TO CH. 19+860 (DESIGN CH. 18+150) (MoRTH) (N24002196)	2-2022	3/2026 (N.A.) {7/2026}	179.86 (N.A.) {179.86}	26.15	0
		269	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM JUNCTION OF NH-22 NEAR HAJIPUR TO JUNCTION OF NH-12 (MoRTH) (N24002197)	2-2024	2/2026 (N.A.) {2/2026}	226.15 (N.A.) {226.15}	14.44	20
		270	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF BH/WBBORDER-AMDABAD-MANIHARI SECTION FROM DESIGN KM (MoRTH) (N24002198)	1-2022	3/2026 (N.A.) {3/2026}	353.27 (N.A.) {353.27}	29.82	2.5

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		271	PERMANENT RECTIFICATION OF 4 NOS. OF BLACKSPOTS ON NH 27 OF KOTWA MEHSI MUZAFFARPUR SECTION FROM (NHAI) (N24002220)	12-2022	11/2026 (N.A.) {11/2026}	410.75 (N.A.) {410.75}	50.64	26.2
		272	4L OF GREENFIELD ALIGNMENT FROM KM. 47.000 TO KM. 89.210 OF BALBHADARPUR TO BELA NAWDA SECTION OF NH (NHAI) (N24002221)	2-2022	3/2026 (N.A.) {3/2026}	2,185.75 (N.A.) {2,185.75}	595.71	12.84
		273	PATNA-MUZAFFARPUR (NHAI) (N24000165)	8-2010	2/2013 (N.A.) {6/2025}	671.30 (N.A.) {671.30}	1,830.13	98.87
		274	4-LANNING OF CHAPRA-HAJIPUR (NHAI) (N24000187)	1-2011	7/2013 (01-01-2026) {1/2026}	575.00 (N.A.) {575.00}	573.48	89.81
		275	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR (MoRTH) (N24000382)	1-2014	10/2019 (01-08-2025) {8/2025}	675.00 (N.A.) {780.77}	764.76	97.5
		276	FOUR LANING OF PATNA TO KOILWAR (NHAI) (N24000473)	8-2015	(N.A.) {}	556.07 (N.A.) {556.07}	-	0
		277	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 (NHAI) (N24000480)	12-2015	4/2019 (01-03-2025) {11/2025}	1,041.10 (567.00) {639.58}	553.73	97.68
		278	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 (NHAI) (N24000507)	12-2015	12/2019 (N.A.) {8/2025}	1,167.45 (N.A.) {1,182.94}	775.79	99.43
		279	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 (MoRTH) (N24000531)	2-2016	11/2018 (N.A.) {8/2025}	319.68 (N.A.) {503.28}	453.00	98.8

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		280	CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-I- KM 40.00 TO KM 65.400 AND K (MoRTH) (N24000576)	2-2016	5/2016 (N.A.) {8/2025}	178.85 (N.A.) {278.54}	232.61	98.35
		281	PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-III-KM 156.5 (MoRTH) (N24000578)	2-2016	5/2016 (N.A.) {8/2025}	553.30 (N.A.) {706.39}	712.38	98
		282	FOUR LANING OF GAYA-HISUA-RAJGIRI- NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR (MoRTH) (N24000579)	1-2014	10/2016 (N.A.) {8/2025}	1,408.85 (N.A.) {2,138.16}	1,739.19	97
		283	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN (NHAI) (N24000665)	3-2017	3/2020 (01-12-2025) {12/2025}	672.89 (893.92) {893.92}	714.74	86.71
		284	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 (NHAI) (N24000696)	8-2017	2/2022 (01-10-2024) {8/2025}	950.64 (1,161.00) {1,168.33}	1,156.29	99.56
		285	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 (NHAI) (N24000714)	12-2017	10/2024 (01-12-2026) {12/2026}	2,598.00 (N.A.) {1,978.01}	1,427.02	77.9
		286	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I (NHAI) (N24000723)	1-2018	12/2021 (01-08-2025) {12/2025}	573.70 (644.50) {726.99}	509.99	82.51
		287	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION (NHAI) (N24000724)	1-2018	4/2024 (N.A.) {}	895.39 (N.A.) {895.39}	1,632.71	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		288	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER (NHAI) (N24000813)	3-2018	11/2021 (01-12-2024) {8/2025}	496.20 (470.18) {470.18}	399.41	98.5
		289	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND (MoRTH) (N24000943)	9-2018	6/2024 (N.A.) {5/2026}	1,478.40 (N.A.) {1,478.40}	972.42	75.15
		290	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 (MoRTH) (N24001201)	2-2019	9/2024 (N.A.) {9/2026}	2,926.42 (N.A.) {2,926.42}	1,354.63	59.29
	URBAN DEVELOPMENT	291	PATNA METRO RAIL CORPORATION LIMITED (PATNA METRO RAIL) (N28000148)	2-2019	6/2024 (N.A.) {6/2024}	13,365.77 (N.A.) {13,925.50}	3,318.85	45.31
	WATER RESOURCES	292	SEWER NETWORK SPS AND STP BEGUSARAI (BUIDCO) (N30000026)	3-2018	7/2021 (01-12-2019) {4/2025}	230.06 (N.A.) {230.06}	261.47	97
		293	I AND D AND STP WORKS FOR BHAGALPUR (BUIDCO) (N30000027)	10-2017	9/2020 (01-11-2020) {9/2025}	254.13 (413.29) {413.29}	126.67	90
		294	SEWER NETWORKS SPS AND STP HAJIPUR (BUIDCO) (N30000035)	3-2018	8/2021 (01-03-2018) {9/2025}	305.19 (N.A.) {305.19}	346.46	95
		295	SEWER NETWORKS, SPS AND STP, MUNGER (BUIDCO) (N30000036)	3-2018	10/2021 (01-03-2018) {6/2024}	294.02 (350.79) {522.85}	428.70	100
		296	SAIDPUR SEWER NETWORK PATNA (BUIDCO) (N30000039)	4-2015	1/2021 (N.A.) {6/2022}	268.63 (N.A.) {493.85}	491.13	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		297	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK (BUIDCO) (N30000044)	3-2017	5/2021 (01-03-2017) {2/2023}	277.42 (253.98) {277.42}	355.31	100
		298	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA (BUIDCO) (N30000050)	8-2017	6/2022 (N.A.) {12/2025}	578.89 (453.83) {578.89}	165.88	53
		299	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA (BUIDCO) (N30000051)	8-2017	6/2022 (N.A.) {12/2025}	824.00 (734.09) {824.00}	385.33	55
CHHATTISGARH	COAL	300	GEVRA EXPANSION OCP (SECL) (35-70) MTY (SECL) (060100093)	6-2010	3/2023 (01-03-2026) {3/2026}	11,816.40 (N.A.) {11,816.40}	6,617.04	77.2
		301	PELMA OCP(15.00MTY) (SECL) (N06000045)	10-2022	3/2023 (N.A.) {3/2033}	1,624.59 (N.A.) {1,725.04}	15.53	17
		302	CHHAL OC SEAM -III (6.00 MTY) (SECL) (N06000104)	12-2013	3/2022 (01-06-2025) {6/2025}	610.63 (N.A.) {610.63}	576.48	85
		303	AMERA OC RCE (SECL) (N06000123)	2-2015	3/2018 (01-03-2026) {3/2026}	335.97 (N.A.) {335.97}	87.47	42
		304	AMGAON OPENCAST PROJECT RCE (SECL) (N06000135)	7-2015	3/2020 (01-03-2026) {3/2026}	316.10 (N.A.) {316.10}	188.33	71
		305	MAHAMAYA OPENCAST PROJECT (SECL) (N06000164)	5-2018	3/2026 (N.A.) {3/2026}	410.26 (N.A.) {410.26}	180.94	38
		306	JHIRIA WEST OPENCAST PROJECT (SECL) (N06000166)	1-2024	3/2029 (N.A.) {3/2029}	366.94 (N.A.) {366.94}	33.67	41

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		307	BAROUD OC EXPANSION (3-10 MTY) (SECL) (N06000197)	8-2020	3/2029 (N.A.) {3/2029}	2,309.80 (N.A.) {2,309.80}	916.35	47
		308	JAMPALI OCP RCE (SECL) (N06000198)	5-2020	3/2024 (01-03-2025) {6/2025}	278.64 (N.A.) {278.64}	210.90	82
		309	PORDA CHINTAPANI OCP (10 MTY) (SECL) (N06000199)	12-2020	3/2029 (N.A.) {3/2029}	2,310.12 (N.A.) {2,310.12}	83.30	10
		310	DIPKA OC EXPANSION 40 MTY (SECL) (N06000200)	12-2020	3/2029 (N.A.) {3/2029}	5,241.40 (N.A.) {5,241.40}	2,821.87	37.3
		311	JAGANNATHPUR OC RCE (3.0 MTY) (SECL) (N06000232)	7-2016	3/2020 (01-03-2026) {3/2026}	459.49 (N.A.) {459.49}	264.00	92
		312	KATKONA RO UG PROJECT (1.74 MTY) (SECL) (N06000274)	1-2023	3/2029 (N.A.) {3/2029}	329.22 (N.A.) {329.22}	60.38	2
	DEPARTMENT OF HIGHER EDUCATION	313	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. (CPWD EDUCATION) (N28000141)	3-2020	7/2022 (01-02-2024) {3/2024}	808.62 (879.22) {808.62}	640.70	100
	PETROLEUM	314	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT (HPCL) (N16000413)	3-2021	3/2024 (01-03-2025) {3/2025}	456.00 (N.A.) {456.00}	271.44	100
	POWER	315	WESTERN REGION EXPANSION SCHEME XXV (PGCIL) (N18000350)	2-2023	11/2023 (N.A.) {8/2025}	385.84 (N.A.) {385.84}	370.41	95
		316	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII (PGCIL) (N18000354)	3-2023	9/2024 (N.A.) {3/2025}	271.69 (N.A.) {271.69}	192.03	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		317	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME- XXVIII AND XXIX (PGCIL) (N18000355)	3-2023	3/2025 (N.A.) {3/2025}	260.30 (N.A.) {260.30}	197.79	100
		318	LARA SUPER THERMAL POWER PROJECT, STAGE-II (2X800 MW) (NTPC) (N18000381)	8-2023	6/2028 (N.A.) {6/2028}	15,530.00 (N.A.) {15,530.00}	2,124.99	6.5
	RAILWAYS	319	KIRANDUL - JAGDALPUR DOUBLING (ECOR) (N22000318)	12-2012	3/2020 (N.A.) {3/2024}	1,588.70 (N.A.) {1,553.11}	1,534.73	94.9
		320	JHARSUGUDA-BILASPUR 4TH LINE (SECR) (N22000484)	4-2015	10/2024 (01-12-2023) {12/2025}	2,140.34 (2,135.34) {2,135.34}	2,306.80	88
		321	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I (IRCON) (N22000489)	4-2013	9/2018 (N.A.) {3/2026}	3,055.00 (N.A.) {3,438.39}	3,117.24	93
		322	Gauge conversion of Raipur(Kendri)-Dhamtari and Abhanpur-Rajim branch (67.20 km) (SECR) (N22000572)	7-2011	10/2024 (N.A.) {6/2025}	1,171.30 (N.A.) {1,171.30}	617.69	82
		323	NIPANIA-BHATAPRA (14.4 KM) 4TH LINE (PB#72/NR/2022-23) (SECR) (N22000573)	9-2022	12/2026 (N.A.) {12/2026}	170.49 (N.A.) {170.49}	0.13	2
		324	4TH LINE - BHATAPARA-HATHBAND (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000574)	12-2022	12/2026 (N.A.) {12/2026}	177.03 (N.A.) {177.03}	14.52	2
		325	4TH LINE - BHILAI-BHILAI NAGAR (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000575)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {177.34}	1.72	2

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		326	4TH LINE - DADHAPARA-BELHA (9.2 KM) (PB#72/NR/2022-23) (SECR) (N22000576)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {169.06}	17.96	30
		327	4TH LINE - RAJNANDGAON-DONGARHGARH (31.2 KM) (PB#72/NR/2022-23) (SECR) (N22000577)	9-2022	9/2026 (N.A.) {9/2026}	328.34 (N.A.) {328.34}	38.80	20
		328	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (N22000579)	9-2022	9/2026 (N.A.) {9/2026}	167.64 (N.A.) {167.64}	-	0
		329	DOUBLING OF BORIDAND - AMBIKAPUR (SURAJPUR) (SECR) (N22000580)	6-2022	6/2030 (N.A.) {3/2027}	1,376.20 (1,242.94) {1,242.94}	217.79	12
		330	DALLIRAJHARA - ROWGHAT (95 KM) {PART OF DALLIRAJHARA-JAGDALPUR (235 KM)} (RVNL) (N22000602)	3-2008	6/2025 (N.A.) {6/2025}	1,627.56 (N.A.) {1,627.56}	1,349.09	0
		331	CHIRIMIRI-NAGPUR HALT (SECR) (N22000616)	10-2018	6/2030 (N.A.) {6/2030}	241.00 (N.A.) {241.00}	-	0
	ROAD TRANSPORT AND HIGHWAYS	332	DEVELOPMENT OF SIX LANE SARGI- BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA (NHAI) (N24001588)	12-2021	1/2025 (N.A.) {12/2025}	1,470.73 (N.A.) {1,470.73}	700.39	83
		333	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA (NHAI) (N24001593)	11-2021	9/2024 (N.A.) {4/2026}	1,368.19 (N.A.) {1,368.19}	928.78	96.5
		334	4 LANE OF BILASPUR TO URGHA PROJECT (KM 0.00 TO KM 70.2) OF NH-130A (NHAI) (N24001611)	4-2020	3/2024 (N.A.) {12/2025}	1,855.59 (2,523.86) {2,523.86}	730.18	94.27

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		335	UP GRADATION OF NH 930 SHERPAR TO KOHKA FROM KM 67.880 TO KM 114.860 TO TWO LANE WITH PAVED SHOULDER (MoRTH) (N24001917)	3-2020	5/2024 (N.A.) {6/2025}	278.97 (N.A.) {278.97}	206.61	87
		336	UP GRADATION OF NH 130C ABHANPUR TO PAUND FROM NK KM 0.000 TO KM. 40.380 TO TWO LANE WITH PAVED SHOU (MoRTH) (N24001919)	12-2020	9/2023 (01-02-2025) {6/2025}	193.16 (N.A.) {193.16}	103.83	81
		337	UPGRADATION OF NH 130A MUNGELI TO PONDII FROM NH KM. 51.600 TO KM. 77.870 KM. 80.970 TO 96.970 TO 2 (MoRTH) (N24001920)	3-2021	9/2024 (N.A.) {5/2025}	218.57 (N.A.) {218.57}	136.26	89
		338	DEVELOPMENT OF SIX LANE BASANWAHI-MARANGPURI OF NH 130 CD FROM KM.99+500 TO 124+661 UNDER RAIPUR VIS (NHAI) (N24002017)	3-2022	10/2025 (N.A.) {9/2026}	1,307.16 (N.A.) {1,307.16}	252.68	36.23
		339	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 1 SECTION OF NH 53 FROM CH 0.000 TO CH 44.50 (NHAI) (N24002045)	6-2022	7/2025 (N.A.) {7/2025}	1,828.00 (N.A.) {1,828.00}	575.00	47.51
		340	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 2 SECTION OF NH 53 FROM CH 44+500 TO CH.92+230 I (NHAI) (N24002046)	6-2022	5/2025 (N.A.) {5/2025}	1,958.94 (1,959.00) {1,958.94}	725.20	40.88
		341	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 (MoRTH) (N24001217)	1-2016	8/2016 (N.A.) {6/2025}	497.14 (572.66) {572.66}	385.27	60
		342	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION (MoRTH) (N24001221)	1-2016	10/2016 (N.A.) {3/2025}	624.98 (N.A.) {731.50}	620.67	100
		343	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI (MoRTH) (N24001222)	3-2016	7/2016 (N.A.) {12/2025}	452.94 (N.A.) {435.61}	322.59	70

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		344	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION (MoRTH) (N24001226)	12-2014	3/2015 (N.A.) {3/2015}	496.02 (N.A.) {496.02}	240.11	0
		345	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. (MoRTH) (N24001227)	3-2018	1/2019 (N.A.) {5/2025}	349.03 (N.A.) {349.03}	316.52	98
		346	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A (MoRTH) (N24001228)	11-2017	5/2019 (N.A.) {5/2025}	188.80 (N.A.) {188.80}	136.81	97
	STEEL	347	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 (NMDC) (N12000124)	11-2015	6/2023 (01-07-2024) {12/2025}	2,907.00 (5,427.06) {5,427.06}	2,955.56	80.7
		348	SCREENING PLANT-III AT KIRANDUL (NMDC) (N12000127)	3-2021	8/2024 (N.A.) {1/2026}	2,092.97 (2,718.84) {2,718.84}	1,503.52	71.31
		349	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (NMDC) (N12000130)	7-2021	11/2024 (N.A.) {12/2025}	282.44 (349.75) {349.75}	238.99	81.86
		350	REPLACEMENT OF CONVERTER VESSELS, TRUNNION RINGS, SUPPORT SYSTEM AND INSTALLATION OF SECONDARY EMISS (SAIL) (N12000131)	10-2023	6/2026 (N.A.) {6/2026}	471.83 (N.A.) {471.83}	109.38	31.06
		351	REBUILDING OF COKE OVEN BATTERY NO.7 AND 8 OF BHILAI STEEL PLANT (SAIL) (N12000134)	11-2023	10/2025 (N.A.) {10/2025}	884.10 (N.A.) {884.10}	411.94	72.24
		352	REPLACEMENT OF HOT LEVELLER-1 OF PLATE MILL AT BHILAI STEEL PLANT (SAIL) (N12000137)	7-2024	7/2026 (N.A.) {7/2026}	198.62 (N.A.) {198.62}	-	6.76

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>URBAN DEVELOPMENT</u>	353	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI- 5 SHOPS COMMUNI (CPWD) (N28000149)	5-2019	9/2020 (01-10-2024) {10/2024}	299.97 (299.97) {299.97}	272.05	93
<u>DELHI</u>	<u>CIVIL AVIATION</u>	354	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR (AAI) (N04000076)	11-2016	4/2020 (01-04-2024) {4/2024}	303.80 (374.98) {351.21}	344.93	100
	<u>DPIIT</u>	355	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE (IICC FOR DPIIT) (N40000002)	11-2017	12/2019 (N.A.) {4/2024}	4,773.00 (N.A.) {5,401.00}	4,969.89	100
	<u>FINANCE</u>	356	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA (NPCC) (N07000001)	7-2018	4/2022 (N.A.) {4/2022}	228.50 (N.A.) {220.27}	176.28	85
	<u>HOME AFFAIRS</u>	357	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI (CPWD FOR MHA) (N28000071)	10-2013	10/2019 (N.A.) {9/2024}	1,219.21 (2,091.53) {2,091.53}	1,947.12	100
		358	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI (CPWD FOR MHA) (N45000002)	6-2019	7/2022 (N.A.) {9/2025}	277.35 (N.A.) {277.35}	111.00	66
	<u>RAILWAYS</u>	359	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE (NR) (N22000281)	4-2012	3/2023 (N.A.) {12/2027}	586.36 (N.A.) {699.00}	178.54	45
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	360	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR (NHAI) (N24001771)	6-2020	12/2024 (N.A.) {12/2024}	1,479.22 (N.A.) {1,479.22}	1,491.26	99

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		361	6L ACCESS CONTROLLED HIGHWAY FROM DND MAHARANI BAGH JN. WITH JAIPUR PUSHTA ROAD OF NH 148NA FROM (NHAI) (N24001773)	5-2020	7/2024 (N.A.) {9/2025}	1,467.44 (N.A.) {1,942.89}	1,214.36	91.58
		362	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH- 1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (N.A.)0.70 (NHAI) (N24001777)	7-2020	10/2023 (N.A.) {6/2025}	2,171.80 (N.A.) {2,171.80}	958.13	99.99
		363	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) (NHAI) (N24001779)	3-2018	9/2022 (N.A.) {9/2025}	2,507.00 (N.A.) {3,030.73}	1,155.70	95.05
		364	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O (NHAI) (N24001781)	1-2018	10/2021 (N.A.) {8/2025}	2,067.67 (N.A.) {2,160.00}	1,496.49	99.4
		365	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM (NHAI) (N24001825)	7-2020	10/2023 (N.A.) {8/2025}	1,894.96 (N.A.) {1,894.96}	741.88	98.25
	<u>TELECOMMUNIC ATIONS</u>	366	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT (CPWD FOR TELECO) (N28000115)	10-2014	3/2018 (N.A.) {10/2025}	248.20 (N.A.) {248.20}	236.97	98
	<u>URBAN DEVELOPMENT</u>	367	DELHI MRTS PHASE-III (DMRC) (N28000056)	9-2011	3/2016 (01-08-2021) {8/2021}	38,585.00 (43,095.35) {40,180.91}	40,685.45	100
		368	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR (NBCC) (N28000105)	7-2016	(N.A.) {}	2,694.00 (N.A.) {2,694.00}	2,247.61	98

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		369	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I (CPWD) (N28000128)	10-2016	7/2021 (N.A.) {6/2024}	1,180.00 (N.A.) {1,100.80}	36.69	2
		370	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I (CPWD) (N28000129)	10-2016	3/2022 (N.A.) {6/2024}	1,128.00 (N.A.) {1,128.00}	740.35	68
		371	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS (DMRC) (N28000135)	7-2019	3/2025 (N.A.) {3/2026}	24,948.65 (N.A.) {24,948.65}	16,369.75	67.19
		372	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI (CPWD) (N28000153)	1-2022	11/2024 (01-08-2025) {8/2025}	646.52 (N.A.) {646.52}	506.00	94
		373	REDEVELOPMENT OF GPRA AT NETAJI NAGAR NEW DELHI PACKAGE 2 (NBCC) (N28000156)	10-2016	3/2024 (01-08-2025) {3/2025}	1,536.72 (N.A.) {1,536.72}	507.85	91.5
	<u>WATER RESOURCES</u>	374	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD ? 10MG/L (DJB) (N30000014)	3-2017	12/2022 (N.A.) {3/2025}	665.78 (N.A.) {665.78}	782.51	100
<u>GOA</u>	<u>CIVIL AVIATION</u>	375	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. (AAI) (N04000095)	11-2017	9/2021 (01-08-2025) {8/2025}	255.69 (255.69) {255.69}	125.92	86.75
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	376	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. (CPWD EDUCATION) (N42000002)	5-2019	8/2021 (N.A.) {12/2024}	303.90 (N.A.) {390.40}	360.00	99.3

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	377	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM. 508.000 TO KM. 513.150 INCLUDING APPROACHES ON N (MoRTH) (N24002181)	4-2023	4/2026 (N.A.) {4/2026}	641.46 (N.A.) {641.46}	-	0
GUJARAT	CIVIL AVIATION	378	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT (AAI) (N04000088)	1-2018	8/2022 (01-12-2024) {12/2024}	1,405.00 (N.A.) {1,405.00}	1,304.63	100
		379	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. (AAI) (N04000093)	8-2018	2/2021 (01-03-2025) {3/2025}	353.25 (N.A.) {353.25}	348.78	100
		380	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. (AAI) (N04000099)	6-2022	12/2025 (N.A.) {12/2025}	1,305.00 (1,143.95) {1,143.95}	648.65	61
	COAL	381	50 MW WIND POWER PROJECT PART OF 150 MW SECI HYBRID (NLC) (N06000292)	7-2022	6/2025 (01-01-2026) {1/2026}	383.84 (N.A.) {383.84}	303.50	41
	PETROLEUM	382	REDEVELOPMENT OF SANTHAL FIELD (ONGC) (N16000279)	2-2017	3/2026 (N.A.) {3/2026}	1,162.56 (N.A.) {1,162.56}	1,156.90	94.1
		383	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY (IOCL) (N16000382)	11-2019	5/2023 (01-03-2024) {7/2025}	5,251.00 (5,894.00) {5,894.00}	4,689.83	99.7
		384	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY (IOCL) (N16000409)	9-2020	8/2024 (01-12-2025) {12/2025}	18,936.00 (N.A.) {18,936.00}	11,161.74	82.5
		385	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM (IOCL) (N16000411)	10-2020	8/2023 (01-06-2025) {6/2025}	1,614.00 (N.A.) {1,614.00}	1,139.60	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		386	REDEVELOPMENT OF LINCH FIELD (ONGC) (N16000428)	4-2021	3/2025 (N.A.) {7/2025}	631.03 (860.04) {860.04}	435.64	76.6
		387	REDEVELOPMENT OF SOBHASAN COMPLEX (ONGC) (N16000431)	8-2021	2/2026 (N.A.) {2/2026}	885.63 (1,286.67) {1,286.67}	584.23	71.4
		388	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD (ONGC) (N16000444)	1-2022	11/2024 (N.A.) {11/2025}	621.40 (N.A.) {621.40}	137.69	21.4
		389	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT (IOCL) (N16000454)	1-2022	9/2024 (N.A.) {5/2026}	328.00 (N.A.) {328.00}	101.12	51.3
		390	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT (ONGC) (N16000477)	5-2022	2/2025 (N.A.) {9/2025}	249.43 (N.A.) {249.43}	209.42	93.7
		391	KALOL REDEVELOPMENT PROJECT (ONGC) (N16000481)	8-2022	3/2027 (N.A.) {3/2027}	1,487.41 (N.A.) {1,487.41}	952.00	60
		392	OLD PIPE LINE REPLACEMENT (OPRP) GROUP- A (ONGC) (N16000483)	7-2021	7/2025 (N.A.) {7/2025}	173.03 (N.A.) {169.84}	143.32	86.5
		393	REVAMPING OF SV STATIONS, GAS TERMINAL AND KRIHCO TERMINAL (ONGC) (N16000514)	11-2022	8/2026 (N.A.) {8/2026}	837.34 (N.A.) {837.34}	187.10	46.7
	POWER	394	GUJARAT 200 MW (GUVNL TENDER) (NTPC) (N18000295)	1-2021	7/2022 (01-03-2026) {3/2026}	842.27 (1,049.61) {1,049.61}	779.79	66

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		395	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) (NTPC) (N18000296)	5-2021	9/2022 (01-04-2025) {4/2025}	674.92 (726.79) {726.79}	572.53	100
		396	Bagodara Solar Power Project (SJVN) (N18000297)	5-2021	10/2022 (N.A.) {12/2025}	339.35 (N.A.) {339.35}	317.59	51.86
		397	DAYAPAR WIND ENERGY PROJECT 150MW (NTPC) (N18000319)	11-2021	5/2023 (01-08-2025) {8/2025}	937.80 (N.A.) {937.80}	803.82	100
		398	DAYAPAR WIND ENERGY PROJECT 200MW (NTPC) (N18000345)	7-2022	3/2025 (01-01-2026) {1/2026}	1,316.02 (N.A.) {1,316.02}	324.36	28
		399	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) (NTPC) (N18000346)	9-2022	9/2024 (01-02-2026) {2/2026}	7,179.54 (7,235.79) {7,235.79}	5,220.20	89
		400	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) (NTPC) (N18000349)	11-2022	3/2024 (01-03-2026) {3/2026}	1,442.60 (N.A.) {1,442.60}	793.56	2.51
		401	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK (PGCIL) (N18000357)	3-2023	12/2024 (N.A.) {7/2025}	922.30 (N.A.) {922.30}	830.14	90.5
		402	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT (PGCIL) (N18000358)	3-2023	3/2025 (N.A.) {7/2025}	815.12 (N.A.) {815.12}	758.09	100
		403	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK (PGCIL) (N18000359)	3-2023	12/2024 (N.A.) {8/2025}	966.79 (N.A.) {966.79}	870.10	93.6

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		404	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000360)	3-2023	3/2025 (N.A.) {9/2025}	1,167.55 (N.A.) {1,167.55}	957.39	90
		405	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000361)	3-2023	3/2025 (N.A.) {9/2025}	2,820.99 (N.A.) {2,820.99}	2,418.00	82.6
		406	KHAVDA 1200MW (4X300MW) IN KHAVDA RE PARK (NTPC) (N18000365)	6-2023	12/2024 (01-01-2026) {1/2026}	6,283.81 (N.A.) {6,283.81}	1,828.84	42
		407	DAYAPAR WIND- III (HYBRID TRANCHE-V) (NTPC) (N18000366)	5-2023	1/2025 (01-03-2026) {3/2026}	1,095.01 (N.A.) {1,095.01}	382.54	18
		408	TS FOR EVACUATION OF POWER FROM POTENTIAL RE ZONE IN KHAVDA AREA OF GUJARAT UNDER PH-IV PART E3 (PGCIL) (N18000383)	7-2023	7/2025 (N.A.) {9/2025}	334.00 (N.A.) {334.00}	63.46	21
		409	TS FOR EVACUATION OF ADDITIONAL 7GW RE POWER FROM KHAVDA RE PARK UNDER PHASE-III PART B [VATAMAN TRA (PGCIL) (N18000384)	12-2023	12/2025 (N.A.) {6/2026}	3,752.00 (N.A.) {3,752.00}	1,463.23	20
		410	TS FOR EVACUATION OF POWER FROM 7GW REZ IN KHAVDA AREA UNDER PHASE-IV PART E2 (PGCIL) (N18000390)	5-2024	5/2026 (N.A.) {2/2026}	679.00 (N.A.) {679.00}	67.90	16.8
		411	AUGMENTATION OF TRANSFORMATION CAPACITY AT JAM KHAMBHALIYA PS [GIS] [SPV NAME POWERGRID JAM KHAMBHAL (PGCIL) (N18000398)	10-2024	7/2026 (N.A.) {7/2026}	329.00 (N.A.) {329.00}	9.87	1

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		412	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000400)	10-2024	10/2026 (N.A.) {10/2026}	4,766.00 (N.A.) {4,766.00}	333.62	5.1
		413	PROVISION OF DYNAMIC REACTIVE COMPENSATION AT KHAVDA POOLING STATION 1 [KPS1] AND KHAVDA POOLING STA (PGCIL) (N18000402)	11-2024	11/2026 (N.A.) {11/2026}	501.00 (N.A.) {501.00}	5.01	1
		414	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000405)	11-2024	5/2029 (N.A.) {5/2029}	24,819.00 (N.A.) {24,819.00}	1,240.30	1
		415	600 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000406)	4-2022	3/2026 (01-03-2023) {11/2026}	4,100.45 (N.A.) {4,100.45}	11.05	5
		416	AUGMENTATION OF TRANSFORMATION CAPACITY AT KPS2 AND KPS2 (PGCIL) (N18000411)	3-2025	3/2027 (N.A.) {3/2027}	466.00 (N.A.) {466.00}	6.52	0
		417	AUGMENTATION OF BANASKANTHA (RAGHANESDA) PS (GIS) (PGCIL) (N18000412)	3-2025	3/2027 (N.A.) {3/2027}	172.00 (N.A.) {172.00}	1.72	0
	RAILWAYS	418	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) (WR) (N22000142)	4-2011	3/2021 (01-10-2026) {10/2026}	844.10 (844.10) {844.10}	605.51	41
		419	ANAND GODHRA DOUBLING PROJECT 79 KMS (WR) (N22000504)	4-2017	12/2024 (01-06-2025) {6/2025}	692.26 (692.26) {692.26}	688.88	100
		420	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS (WR) (N22000505)	4-2018	3/2024 (01-10-2024) {10/2024}	537.31 (537.31) {688.74}	944.55	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		421	4TH LINE BETWEEN BAREJADI NANDEJ (GERATPUR)- SANAND (38.20 KM) (AHMEDABAD BYPASS). (WR) (N22000532)	2-2023	3/2027 (01-03-2027) {3/2027}	961.67 (961.67) {961.67}	103.15	16
		422	QUADRUPLING BETWEEN GANDHIDHAM - ADIPUR WITH Y CONNECTION AT ADIPUR FOR PROVIDING DIRECT ENTRY TOWAR (WR) (N22000533)	2-2023	12/2025 (01-12-2025) {12/2025}	152.44 (152.44) {152.44}	19.54	63
		423	RAJKOT-KANALUS (111.20 KM) (WR) (N22000535)	10-2021	10/2026 (01-06-2026) {6/2026}	1,080.58 (1,080.58) {1,080.58}	315.70	72
		424	HIMMATNAGAR-KHEDBRAHMA (54.83 KM) (WR) (N22000537)	6-2022	8/2025 (01-07-2025) {7/2025}	354.99 (482.42) {482.42}	322.59	96
		425	PETLAD-BHADRAN (22.5 KM) (WR) (N22000538)	5-2022	5/2030 (01-12-2025) {12/2025}	202.50 (307.12) {307.12}	81.76	8
		426	NADIAD-PETLAD (37.26 KM) (WR) (N22000539)	5-2022	6/2030 (N.A.) {12/2025}	335.34 (461.91) {461.91}	74.35	7
		427	SAMLAYA-TIMBA ROAD (53.53 KM) (WR) (N22000540)	2-2023	3/2030 (01-07-2026) {7/2026}	670.00 (670.17) {670.17}	101.79	12
		428	SAMNI-JAMBUSAR (24.08 KM) (WR) (N22000541)	5-2022	3/2030 (01-12-2025) {12/2025}	216.72 (349.93) {349.93}	86.46	25
		429	VIJAPUR-AMBLIYASAN (41.53 KM) (WR) (N22000547)	5-2022	8/2025 (01-10-2025) {10/2025}	309.81 (415.38) {415.38}	263.13	85
		430	ADRAJ MOTI-VIAJAPUR (39.75 KM) (WR) (N22000548)	5-2022	8/2025 (01-09-2025) {9/2025}	296.54 (N.A.) {296.54}	178.95	80

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		431	NEW BG LINE BETWEEN NALIYA-JAKHAU PORT (WR) (N22000550)	2-2023	1/2028 (01-12-2026) {12/2026}	410.46 (410.46) {410.46}	5.89	2
		432	NEW BG LINE INTERSECTION (5 NOS) BETWEEN GERATPUR-SANAND AND BOTAD- AHMEDABAD (16.51 KM) (PB29/NR/20 (WR) (N22000551)	10-2022	10/2027 (01-10-2027) {10/2027}	437.21 (N.A.) {437.21}	43.26	9
		433	TARANGA HILL ABU ROAD VIA AMBAJI NEW LINE (NWR) (N22000592)	7-2022	7/2030 (N.A.) {12/2026}	2,798.16 (N.A.) {2,798.16}	1,103.16	12.5
		434	JUNAGARH -VISAVADAR (42.28) KM (RVNL) (N22000600)	6-2022	9/2028 (N.A.) {12/2026}	493.00 (N.A.) {492.83}	-	0
		435	MODASA- SHAMLAJI NEW LINE (MM OF AHMEDABAD-HIMMATNAGAR-UDAIPUR (299.2 KM)) (WR) (N22000622)	9-2012	3/2027 (01-03-2026) {3/2026}	261.68 (261.68) {261.68}	202.70	58
	ROAD TRANSPORT AND HIGHWAYS	436	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT (MoRTH) (N24001427)	6-2020	4/2023 (01-09-2024) {9/2024}	166.21 (N.A.) {166.21}	97.12	93
		437	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 (NHAI) (N24001443)	5-2020	3/2024 (01-07-2025) {7/2025}	690.30 (929.95) {929.95}	841.74	94.22
		438	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION (NHAI) (N24001444)	5-2020	1/2024 (01-07-2025) {7/2025}	882.00 (1,229.37) {1,229.37}	1,042.67	91.54

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		439	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB (NHAI) (N24001445)	5-2020	7/2023 (01-06-2025) {6/2025}	691.52 (903.85) {903.85}	893.47	99.45
		440	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG (NHAI) (N24001446)	5-2020	12/2023 (01-06-2025) {6/2025}	894.00 (1,261.58) {1,261.58}	1,166.51	97.28
		441	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 (NHAI) (N24001515)	9-2020	2/2024 (N.A.) {3/2026}	1,542.02 (N.A.) {1,542.02}	989.98	68.5
		442	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 (NHAI) (N24001516)	9-2020	2/2024 (01-08-2025) {8/2025}	1,185.69 (N.A.) {1,185.69}	980.41	93.52
		443	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 (NHAI) (N24001518)	11-2019	9/2023 (N.A.) {8/2025}	1,669.56 (N.A.) {1,669.56}	1,094.58	98.12
		444	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 (NHAI) (N24001519)	9-2020	11/2023 (N.A.) {7/2025}	1,198.55 (N.A.) {1,198.55}	911.23	95.78
		445	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 (NHAI) (N24001520)	11-2019	5/2024 (N.A.) {8/2025}	1,604.06 (N.A.) {1,604.06}	1,245.52	95.73
		446	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT (NHAI) (N24001785)	3-2022	6/2025 (N.A.) {6/2025}	1,373.06 (1,085.00) {1,373.06}	662.04	90.67
		447	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU (NHAI) (N24001786)	3-2021	3/2024 (N.A.) {3/2026}	1,259.00 (2,652.24) {1,910.00}	278.29	34.08

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		448	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU (NHAI) (N24001788)	7-2020	12/2023 (N.A.) {5/2025}	2,271.86 (3,372.97) {3,916.00}	2,655.78	98.9
		449	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA (NHAI) (N24001789)	7-2020	8/2023 (N.A.) {7/2025}	1,710.30 (2,665.08) {1,927.00}	908.08	90.56
		450	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ-RGBS-PACKAGE-3) (NHAI) (N24001790)	2-2020	8/2023 (01-12-2024) {12/2024}	752.30 (N.A.) {766.20}	452.13	98.14
		451	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS-PACKAGE-1) (NHAI) (N24001791)	2-2020	6/2023 (01-03-2024) {5/2024}	606.51 (N.A.) {657.00}	453.89	98.99
		452	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH- 8E (PACKAGE-II) (NHAI) (N24001792)	3-2021	9/2022 (N.A.) {1/2025}	536.03 (N.A.) {536.03}	480.77	100
		453	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) (NHAI) (N24001793)	3-2021	9/2022 (N.A.) {5/2025}	485.75 (N.A.) {485.75}	393.88	99.57
		454	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4) (NHAI) (N24001794)	2-2020	3/2023 (01-12-2024) {12/2024}	778.15 (N.A.) {785.67}	547.22	99.7
		455	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE (NHAI) (N24001827)	3-2022	3/2023 (N.A.) {4/2025}	162.73 (N.A.) {162.73}	131.79	100
		456	UPGRADATION AND STRENGTHENING TO 2 LANE PS FROM KM 95/500 TO KM 129/775 OF NH 168 G IDAR BHILODA SA (MoRTH) (N24002014)	9-2022	12/2023 (01-12-2025) {12/2025}	237.28 (N.A.) {237.28}	0.34	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		457	UPGRADATION TO 4L PS DIVIDED CARRIAGEWAY FROM PATAN (NEAR RAJPUR) TO GOJARIYA FROM KM 52.000 TO KM 1 (NHAI) (N24002034)	12-2021	3/2025 (N.A.) {3/2025}	1,181.34 (1,181.00) {1,181.34}	555.81	79.5
		458	WIDENING TO 6L OF EXISTING 4L JETPUR - GONDAL - RAJKOT SECTION FROM KM. 117.600 TO KM. 185.00 ON NH- (NHAI) (N24002035)	9-2023	9/2025 (N.A.) {9/2025}	2,070.44 (N.A.) {2,070.44}	545.53	37.86
		459	UPGRADATION OF DHORAJI JAMKANDORNA KALAVAD SECTION OF NH 927D FROM DESIGN CHAINAGE KM 00 TO KM 58.11 (MoRTH) (N24002117)	10-2022	2/2024 (01-02-2026) {2/2026}	246.60 (291.00) {291.00}	27.57	15
		460	UPGRADATION TO TWO LANE WITH PAVED SHULDER CONFIGURATION FROM KM 00 TO 47 OF NH 351 MAHUVA TO BADHA (MoRTH) (N24002118)	12-2022	2/2024 (01-08-2025) {8/2025}	173.06 (N.A.) {219.00}	0.15	0
		461	WORK OF DEVELOPMENT AND CONSTRUCTION OF ELEVATED CORRIDOR FROM KM 38/660 TO KM 42/690 (ISCON JUNCTION (MoRTH) (N24002182)	3-2023	3/2026 (N.A.) {3/2026}	530.20 (N.A.) {530.20}	-	0
		462	WIDENING 2 LANE TO 4-LANE FROM KM 92/320 TO KM 115/320 (VAV CHOKDI-SATLASANA TO TO VRUNDAVAN CHOKDI, (MoRTH) (N24002183)	3-2022	3/2026 (N.A.) {3/2026}	151.13 (N.A.) {171.00}	-	0
		463	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. (NHAI) (N24000567)	5-2016	8/2019 (N.A.) {6/2024}	998.18 (N.A.) {998.18}	802.89	100
		464	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST (NHAI) (N24000569)	5-2016	9/2019 (01-05-2024) {6/2025}	723.64 (N.A.) {723.64}	562.31	97

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		465	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU (NHAI) (N24000570)	5-2016	8/2019 (N.A.) {3/2025}	763.08 (N.A.) {763.08}	520.19	99.54
		466	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 (NHAI) (N24000592)	7-2016	7/2020 (N.A.) {5/2025}	829.97 (N.A.) {829.97}	486.93	96.98
		467	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. (NHAI) (N24000649)	1-2017	12/2020 (01-10-2025) {10/2025}	1,251.11 (1,527.75) {1,527.75}	685.73	91.08
		468	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR (NHAI) (N24000834)	3-2018	10/2021 (01-05-2025) {7/2025}	1,161.39 (1,738.03) {1,404.00}	684.22	83
		469	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA (MoRTH) (N24000925)	10-2018	11/2020 (01-09-2024) {9/2024}	400.76 (394.44) {394.44}	287.04	87
	URBAN DEVELOPMENT	470	AHMEDABAD METRO RAIL PROJECT PHASE I (AMR) (N28000122)	11-2014	12/2018 (N.A.) {8/2025}	10,773.00 (N.A.) {12,924.55}	12,486.28	99.9
		471	AHMEDABAD METRO RAIL PROJECT PHASE II (AMR) (N28000137)	3-2019	3/2024 (N.A.) {12/2025}	5,384.17 (N.A.) {5,384.17}	4,135.88	87.68
		472	SURAT METRO RAIL PROJECT (AMR) (N28000138)	3-2019	3/2024 (N.A.) {6/2026}	12,020.32 (N.A.) {12,020.32}	7,043.17	67.49
HARYANA	HEALTH AND FAMILY WELFARE	473	ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT MANETHI, HARYANA. (HITES) (N21000032)	3-2019	3/2023 (01-03-2026) {3/2026}	1,294.34 (1,294.34) {1,294.34}	307.21	26.14

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>HOME AFFAIRS</u>	474	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" (CPWD FOR MHA) (N28000147)	1-2020	10/2023 (01-03-2025) {8/2025}	166.98 (170.23) {170.23}	150.98	97.5
	<u>PETROLEUM</u>	475	R and D CAMPUS II AT FARIDABAD (IOCL) (N16000375)	6-2019	12/2022 (01-07-2025) {3/2026}	2,281.94 (3,219.94) {3,219.94}	1,744.23	63.1
		476	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA (IOCL) (N16000412)	2-2021	9/2024 (01-12-2025) {12/2025}	34,627.00 (38,231.00) {38,231.00}	21,454.90	87.6
		477	POLY BUTADIENE RUBBER PLANT AT PANIPAT (IOCL) (N16000458)	3-2022	3/2025 (01-06-2026) {6/2026}	1,459.00 (2,948.62) {2,948.62}	930.86	68.3
	<u>POWER</u>	478	IMPLEMENTATION OF LILO OF BOTH CIRCUITS OF 400KV VIDHYACHAL PS TO SASAN D/C LINE AT HINDALCO SWITCHY (PGCIL) (N18000420)	2-2025	12/2026 (N.A.) {12/2026}	370.00 (N.A.) {370.00}	-	0
	<u>RAILWAYS</u>	479	DOUBLING BETWEEN BHIWANI-DOBH BAHALI (NWR) (N22000604)	2-2023	2/2028 (01-03-2026) {3/2026}	471.06 (N.A.) {471.06}	121.18	55
		480	DOUBLING BETWEEN REWARI-KATHUWAS (27.73 KM) (NWR) (N22000606)	2-2023	6/2027 (01-05-2026) {5/2026}	352.41 (N.A.) {352.41}	179.38	53
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	481	CONSTRUCTION OF 4-LANE NH-344P-PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA (NHAI) (N24001532)	11-2021	11/2023 (01-01-2024) {8/2024}	694.00 (1,918.00) {1,500.00}	1,466.82	100
		482	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP (NHAI) (N24001533)	11-2020	12/2023 (N.A.) {5/2025}	1,690.23 (N.A.) {2,010.17}	1,462.45	99.91

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		483	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP (NHAI) (N24001534)	12-2020	1/2024 (01-04-2024) {5/2025}	1,334.04 (N.A.) {1,334.00}	1,048.12	99.89
		484	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 (NHAI) (N24001535)	7-2020	7/2022 (01-05-2024) {8/2025}	899.00 (1,882.46) {1,882.46}	1,123.98	97.86
		485	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI (NHAI) (N24001536)	7-2020	7/2022 (N.A.) {6/2025}	817.00 (1,605.00) {1,605.00}	986.08	99.93
		486	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F (NHAI) (N24001633)	12-2020	12/2023 (01-03-2024) {7/2025}	1,430.88 (1,813.91) {1,813.91}	1,190.27	99.9
		487	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO (NHAI) (N24001634)	1-2021	12/2023 (01-03-2024) {7/2025}	1,306.95 (1,564.14) {1,564.14}	949.76	99.97
		488	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O (NHAI) (N24001635)	3-2022	2/2025 (N.A.) {2/2025}	1,269.50 (N.A.) {1,269.50}	176.00	53
		489	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K (NHAI) (N24001673)	3-2020	3/2023 (01-11-2024) {7/2025}	510.97 (N.A.) {510.97}	529.00	97.3
		490	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH-352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU (NHAI) (N24001774)	12-2020	11/2023 (N.A.) {6/2024}	1,524.03 (N.A.) {1,524.03}	1,105.10	67.61

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		491	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH-11 AS A FEEDER ROUTE IN THE STATE (NHAI) (N24001775)	2-2020	1/2023 (01-12-2024) {12/2024}	808.31 (N.A.) {958.00}	930.44	100
		492	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN (NHAI) (N24001783)	11-2018	9/2021 (N.A.) {4/2025}	2,252.75 (N.A.) {2,252.75}	1,223.07	99.95
		493	UPGRADATION OF EXISTING 4 LANE ISMAILABAD-AMBALA SECTION (KM. 0+000 TO KM 42+500) (PART OF AMBALA-KO (NHAI) (N24002037)	1-2023	12/2025 (N.A.) {3/2026}	609.32 (609.00) {609.00}	204.06	52.5
		494	CONSTRUCTION OF 6-LANE GREENFIELD KARNAL RING ROAD STARTING FROM NH-44 NEAR VILLAGE SHAMGARH (DESIGN (NHAI) (N24002038)	11-2022	8/2025 (N.A.) {8/2025}	1,691.45 (1,998.00) {1,998.00}	649.71	58.76
		495	CONSTRUCTION OF 6-LANE GREENFIELD AMBALA RING ROAD STARTING FROM JUNCTION WITH SHAMLI-AMBALA SECTION (NHAI) (N24002039)	2-2023	10/2025 (N.A.) {10/2025}	1,088.64 (1,178.00) {1,178.00}	425.85	53.55
		496	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM RANIPUR BARSII (SAHARANPUR DISTRICT) TO ADHOYA (NHAI) (N24002040)	4-2022	5/2025 (N.A.) {5/2028}	1,554.21 (N.A.) {1,554.21}	522.92	54
		497	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM ADHOYA MUSALMANA (AMBALA DISTRICT) TO SADOPUR (NHAI) (N24002041)	4-2022	5/2025 (N.A.) {5/2025}	1,491.71 (N.A.) {1,491.71}	706.26	49.7
		498	CONSTRUCTION OF 4-LANING OF BHIWANI HANSI ROAD SECTION OF NH 148B (DESIGN LENGTH 42.934 KM) UNDER BH (NHAI) (N24002042)	11-2022	12/2025 (N.A.) {12/2025}	1,322.13 (N.A.) {1,322.13}	393.46	93.01

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		499	CONSTRUCTION OF 4-LANE GREENFIELD JALBEHRA - SHAHBAD SECTION OF NH ? 152G FROM KM 0+000 TO KM 22+850 (NHAI) (N24002043)	3-2022	6/2025 (N.A.) {10/2025}	927.22 (1,173.66) {1,173.66}	504.21	83.5
		500	4L AMBALA - KALAAMB FROM KM. -0.800 TO KM. 33.015 OF OLD NH-72 (NHAI) (N24002044)	6-2023	6/2025 (N.A.) {6/2025}	629.16 (N.A.) {629.16}	154.00	98.9
		501	CONSTRUCTION OF GREENFIELD CONNECTIVITY TO JEWAR INTERNATIONAL AIRPORT FROM DND FARIDABAD BALLABHGAR (NHAI) (N24002048)	7-2022	6/2025 (N.A.) {3/2026}	2,414.67 (2,898.00) {2,898.00}	1,232.13	49.1
<u>HIMACHAL PRADESH</u>	<u>DEPARTMENT OF HIGHER EDUCATION</u>	502	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR (CPWD EDUCATION) (N42000008)	9-2018	6/2022 (01-12-2024) {8/2025}	392.51 (N.A.) {446.43}	316.16	91.5
		503	CONSTRUCTION OF PERMANENT CAMPUSES OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND DHARAMSHAL (CPWD) (N42000011)	3-2021	11/2024 (01-07-2025) {7/2025}	512.37 (300.45) {300.45}	169.63	74
	<u>POWER</u>	504	PARBATI HEP (4X200 MW) (NHPC) II (NHPC) (180100210)	9-2002	9/2009 (01-04-2025) {4/2025}	3,919.59 (N.A.) {13,045.00}	12,832.59	100
		505	LUHRI HYDROELECTRIC PROJECT (STAGE1) (SJVN) (N18000279)	11-2020	1/2026 (N.A.) {12/2028}	1,810.56 (N.A.) {3,584.53}	1,732.67	51.32
		506	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) (SJVN) (N18000291)	10-2020	11/2025 (N.A.) {3/2027}	687.97 (N.A.) {1,511.87}	891.77	67.61
		507	SUNNI DAM HYDRO ELECTRIC PROJECT (SJVN) (N18000344)	1-2023	4/2028 (N.A.) {12/2028}	2,614.51 (N.A.) {4,540.71}	948.35	29.41

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	508	BHANUPALI-BILASPUR BERI NL (RVNL) (N22000273)	4-2008	12/2026 (N.A.) {3/2025}	13,370.29 (N.A.) {6,753.42}	5,369.57	0
	ROAD TRANSPORT AND HIGHWAYS	509	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA (MoRTH) (N24001381)	8-2020	4/2021 (N.A.) {4/2021}	272.98 (N.A.) {272.98}	140.69	100
		510	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. (MoRTH) (N24001382)	8-2020	3/2021 (N.A.) {7/2024}	242.80 (N.A.) {242.80}	100.95	94.76
		511	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 (MoRTH) (N24001383)	8-2020	4/2021 (N.A.) {4/2021}	349.20 (N.A.) {349.20}	239.34	100
		512	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K (MoRTH) (N24001422)	2-2021	9/2021 (N.A.) {7/2024}	345.89 (N.A.) {345.89}	178.19	95.08
		513	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K (MoRTH) (N24001447)	8-2020	12/2024 (N.A.) {12/2024}	371.93 (N.A.) {371.93}	154.04	81
		514	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN-MANDI SECTION (KM 208.950 TO KM 2 (MoRTH) (N24001470)	8-2020	4/2025 (N.A.) {4/2025}	314.32 (N.A.) {314.32}	49.26	51
		515	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF (NHAI) (N24001808)	3-2021	12/2024 (01-12-2024) {12/2024}	1,322.95 (1,442.47) {1,442.47}	888.73	96.61
		516	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU (NHAI) (N24001809)	5-2022	3/2024 (01-12-2024) {12/2024}	469.95 (N.A.) {280.00}	302.91	98.57

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		517	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP (NHAI) (N24001810)	2-2022	6/2024 (N.A.) {6/2024}	190.60 (N.A.) {163.00}	103.48	100
		518	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH-154) (PACKAGE-IB) (NHAI) (N24001811)	4-2021	6/2024 (N.A.) {5/2025}	583.93 (770.00) {770.00}	173.60	100
		519	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) (NHAI) (N24001812)	3-2021	5/2024 (N.A.) {12/2025}	1,002.11 (1,361.79) {1,361.76}	190.30	46.68
		520	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A (NHAI) (N24001813)	7-2021	9/2024 (N.A.) {9/2024}	1,692.05 (N.A.) {1,692.05}	942.14	21.6
		521	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS-5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001915)	3-2021	6/2026 (N.A.) {6/2026}	230.54 (N.A.) {230.54}	20.16	28
		522	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS 5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001916)	3-2021	5/2026 (N.A.) {5/2026}	314.67 (N.A.) {314.67}	76.05	47
		523	PKG NAME: 4L OF KATHLIGHAT TO SHAKRAL VILLAGE FROM KM 128.835 TO KM 146.300 OF NH- 5 (SHIMLA BYPASS) (NHAI) (N24002049)	3-2022	4/2026 (N.A.) {4/2026}	1,703.48 (2,278.00) {2,278.00}	651.98	14.5
		524	REHABILITATION AND UPGRADATION TO 4L CONFIGURATION and STRENGTHENING OF SIHUNI TO RAJOL FROM KM 51.0 (NHAI) (N24002050)	2-2022	9/2025 (N.A.) {9/2025}	696.65 (698.46) {698.46}	391.62	67.73

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		525	CONSTRUCTION OF NEW 2 LANE WITH PAVED SHOULDER OF HAMIRPUR BYPASS (PACKAGE IVA) OF NH-88 (NEW NH-103 (NHAI) (N24002051)	7-2022	10/2025 (N.A.) {10/2025}	739.39 (N.A.) {739.39}	347.45	81.53
		526	REHABILITATION AND UP-GRADATION OF EXISTING ROAD TO 2L PS FROM END OF HAMIRPUR BYPASS (NEAR CHILBAHA (NHAI) (N24002052)	2-2022	4/2025 (N.A.) {4/2025}	1,146.19 (N.A.) {1,146.19}	940.81	71.23
		527	REHABILITATION AND UP-GRADATION TO 4L CONFIGURATION AND STRENGTHENING OF THANPURI TO PAROR SECTION F (NHAI) (N24002192)	6-2022	12/2025 (N.A.) {12/2025}	815.69 (815.69) {815.69}	400.63	33.56
		528	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) (NHAI) (N24000232)	11-2013	11/2016 (N.A.) {}	1,916.79 (N.A.) {1,916.79}	1,660.92	0
		529	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS (NHAI) (N24000606)	8-2016	9/2020 (N.A.) {}	1,583.18 (N.A.) {1,583.18}	-	0
		530	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH (NHAI) (N24000613)	9-2016	7/2020 (N.A.) {3/2025}	1,273.71 (N.A.) {1,478.61}	1,450.53	97.43
		531	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M (NHAI) (N24000852)	3-2018	5/2021 (01-12-2024) {12/2024}	478.74 (N.A.) {1,514.46}	1,349.59	83
		532	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D (CPWD) (N28000154)	4-2022	11/2024 (N.A.) {11/2024}	512.34 (N.A.) {512.34}	-	0
	URBAN DEVELOPMENT							

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
JAMMU AND KASHMIR	CIVIL AVIATION	533	JAMMU - CONSTRUCTION OF NEW CIVIL ENCLAVE (AAI) (N04000107)	7-2022	6/2026 (N.A.) {6/2026}	861.37 (N.A.) {861.37}	154.30	30.25
	DEPARTMENT OF HIGHER EDUCATION	534	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) (CPWD EDUCATION) (N28000130)	3-2019	7/2022 (01-01-2025) {1/2025}	424.93 (N.A.) {500.91}	448.15	96
		535	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) (CPWD EDUCATION) (N28000131)	1-2018	4/2023 (01-04-2025) {4/2025}	676.00 (1,144.68) {1,144.68}	54.75	100
	HEALTH AND FAMILY WELFARE	536	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR (CPWD FOR HEALTH) (N28000150)	3-2019	9/2025 (N.A.) {11/2025}	1,828.00 (N.A.) {1,577.00}	1,302.38	64.5
		537	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR (CPWD FOR HEALTH) (N21000029)	3-2019	9/2023 (01-05-2025) {5/2025}	1,404.00 (1,642.00) {1,642.00}	1,461.68	100
	PETROLEUM	538	SETTING UP A COMMON USER PETROLEUM TERMINAL AT JAMMU FOR RE-SITEMENT OF EXISTING DEPOTS OF PSU OMCS (BPCL) (N16000500)	4-2021	3/2025 (N.A.) {3/2025}	676.89 (N.A.) {676.89}	503.55	76
		539	CGD PROJECT AT JAMMU DISTRICTS (IOCL) (N16000527)	3-2022	3/2032 (01-09-2034) {9/2034}	538.00 (N.A.) {538.00}	4.09	0.6
	POWER	540	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) (CVPPPL) (N18000172)	10-2014	4/2020 (01-07-2025) {12/2026}	8,112.12 (N.A.) {12,727.76}	6,692.58	70
		541	KIRU HYDRO ELECTRIC PROJECT (CVPPPL) (N18000278)	3-2019	8/2024 (N.A.) {12/2026}	4,287.59 (N.A.) {5,409.00}	2,713.25	63.87

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		542	RATLE HE PROJECT (NHPC) (N18000324)	2-2021	2/2026 (N.A.) {8/2028}	5,281.94 (N.A.) {5,281.94}	1,011.56	23.57
		543	KWAR HE PROJECT (CVPPPL) (N18000363)	5-2022	11/2026 (N.A.) {3/2028}	4,526.12 (N.A.) {4,526.12}	1,159.97	22.15
		544	TRANSMISSION SCHEME FOR EVACUATION OF POWER FROM RATLE HEP (850 MW) AND KIRU (624 MW); PART B (PGCIL) (N18000417)	3-2025	3/2027 (N.A.) {3/2027}	219.00 (N.A.) {219.00}	-	0
	RAILWAYS	545	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR (NR) (220100133)	3-1995	8/2024 (01-12-2024) {12/2024}	37,012.00 (37,012.26) {43,780.00}	42,328.83	100
	ROAD TRANSPORT AND HIGHWAYS	546	KHELLANI-KHANABAL PKG-1 (NHIDCL) (N24001323)	3-2021	9/2022 (01-10-2024) {11/2024}	486.45 (N.A.) {486.45}	126.73	96.84
		547	KHELLANI-KHANABAL PKG-3 (NHIDCL) (N24001341)	3-2021	12/2022 (01-10-2024) {5/2025}	398.51 (N.A.) {398.51}	80.64	98.36
		548	KHELLANI-KHANABAL PKG-2 (NHIDCL) (N24001394)	7-2021	2/2023 (01-06-2025) {6/2026}	512.43 (N.A.) {512.43}	71.65	51.75
		549	KHELLANI-KHANABAL PKG-4 (NHIDCL) (N24001395)	7-2021	8/2023 (01-12-2025) {6/2026}	859.67 (N.A.) {859.67}	196.00	44.02
		550	KHELLANI-KHANABAL PKG-5 (NHIDCL) (N24001396)	7-2021	2/2023 (01-03-2025) {8/2025}	497.09 (N.A.) {497.09}	178.73	90.01
		551	GOHA-KHELLANI PKG-3 (NHIDCL) (N24001397)	2-2021	3/2023 (01-02-2025) {3/2025}	431.28 (433.08) {431.28}	372.31	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		552	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA (NHAI) (N24001472)	9-2021	12/2023 (01-06-2024) {6/2024}	811.19 (N.A.) {811.19}	848.72	99
		553	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY (NHAI) (N24001511)	3-2021	2/2024 (01-10-2025) {10/2025}	2,919.96 (N.A.) {2,919.96}	2,334.99	70
		554	FOUR LANING OF JAMMU-AKHNOOR PKG-1 (NHIDCL) (N24001543)	7-2022	1/2025 (N.A.) {10/2025}	245.34 (N.A.) {245.34}	57.20	40.95
		555	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4 (NHAI) (N24001550)	9-2021	9/2024 (01-12-2025) {12/2025}	1,821.72 (1,917.32) {1,917.32}	1,005.37	83.71
		556	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5) (NHAI) (N24001551)	10-2021	9/2024 (01-12-2025) {12/2025}	3,044.02 (3,044.02) {3,044.02}	1,589.44	70.21
		557	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) (JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B (NHAI) (N24001552)	10-2021	9/2024 (01-02-2026) {2/2026}	2,714.95 (2,714.95) {2,714.95}	1,663.19	85.78
		558	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- (NHAI) (N24001619)	8-2022	6/2024 (01-06-2025) {6/2025}	200.05 (200.05) {208.92}	153.30	63.2
		559	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SLIP ZONES AT KM 130.550 TO KM.130.750; KM. (NHAI) (N24001620)	9-2021	10/2023 (01-12-2025) {12/2025}	442.14 (N.A.) {442.14}	352.62	19.88

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		560	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. (NHAI) (N24001621)	7-2021	8/2024 (01-07-2025) {7/2025}	614.48 (N.A.) {614.48}	187.59	7
		561	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX (NHAI) (N24001622)	7-2021	6/2024 (01-07-2025) {7/2025}	1,401.87 (N.A.) {1,401.87}	751.11	0
		562	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350 (NHAI) (N24001623)	1-2020	1/2024 (01-02-2025) {2/2025}	336.01 (N.A.) {336.01}	223.02	34
		563	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI (NHAI) (N24001624)	7-2019	10/2020 (01-04-2023) {9/2024}	157.05 (N.A.) {157.05}	139.54	100
		564	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K (NHAI) (N24001627)	7-2021	2/2025 (01-05-2026) {5/2026}	1,912.17 (N.A.) {1,912.17}	148.88	0
		565	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B (NHIDCL) (N24001833)	7-2022	3/2025 (N.A.) {8/2025}	198.28 (N.A.) {198.28}	85.49	71.09
		566	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 102 TO KM 13 (BRO) (N24001897)	3-2021	7/2024 (01-03-2025) {3/2024}	642.24 (N.A.) {642.24}	345.14	95
		567	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 30.000 TO K (BRO) (N24001898)	7-2020	11/2024 (N.A.) {11/2024}	272.49 (N.A.) {272.49}	133.66	87.24
		568	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 134.95 TO KM (BRO) (N24001899)	2-2021	7/2024 (N.A.) {3/2025}	395.25 (N.A.) {395.25}	140.42	64

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		569	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 49.150 TO KM (BRO) (N24001900)	3-2020	8/2024 (N.A.) {3/2025}	796.97 (N.A.) {796.97}	323.85	79
		570	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 64.535 TO K (BRO) (N24001901)	3-2020	9/2023 (N.A.) {3/2025}	152.93 (N.A.) {152.93}	90.30	78.27
		571	CONSTRUCTION OF TWIN TUBE TUNNELS ON JAMMU KASHMIR RING ROAD (NH-244A) BETWEEN DESIGN CH. 50+600 TO (NHAI) (N24001926)	3-2023	6/2025 (N.A.) {3/2026}	939.86 (N.A.) {939.86}	475.07	69.93
		572	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER FROM (DESIGN CH. 14+200 TO 24+400), (DESIGN CH. 35+300 TO (BRO) (N24001998)	6-2022	8/2025 (N.A.) {8/2025}	832.46 (N.A.) {823.46}	227.50	46
		573	2L NH-1 FROM KM 8.660 TO KM 33.775 (SUMBAL TO WAYUL) TO 4L DUAL CARRIAGEWAY NH STANDARD AS PART OF S (NHAI) (N24002059)	9-2022	6/2026 (01-06-2026) {12/2026}	1,183.60 (N.A.) {1,183.60}	197.13	16.63
		574	DELHI AMRITSAR KATRA EXPRESSWAY (PHASE-II PKG XVIII) DEVELOPMENT AND UPGRADATION OF FOUR LANE ACCESS (NHAI) (N24002060)	3-2023	11/2025 (N.A.) {3/2026}	1,107.00 (N.A.) {975.38}	338.91	38.81
		575	4/6L ACCESS CONTROL EXPRESSWAY FROM DESIGN CHAINAGE KM 515.000 TO 528.300 (KUNJWANI TO SIDHRA SECTIO (NHAI) (N24002061)	8-2022	6/2025 (N.A.) {2/2026}	2,474.47 (N.A.) {2,894.74}	923.64	40.17
		576	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM 162.800 TO KM (BRO) (N24002119)	10-2022	1/2026 (N.A.) {1/2026}	562.45 (N.A.) {562.45}	99.06	25

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		577	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER (PATTAN BYPASS) GREENFIELD BYPASS FROM EXISTING CH. KM 24 (BRO) (N24002179)	3-2023	7/2026 (N.A.) {7/2026}	980.21 (N.A.) {980.21}	300.02	8
		578	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 166.100 TO KM (BRO) (N24002180)	9-2021	7/2026 (N.A.) {7/2026}	734.64 (N.A.) {734.64}	19.60	8
		579	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDERS (BARAMULLA BYPASS) GREENFIELD BYPASS FROM EXISTING CH. K (BRO) (N24002185)	3-2023	9/2026 (N.A.) {9/2026}	992.43 (N.A.) {992.43}	338.33	0
		580	WIDENING AND STRENGTHENING OF RAFIABAD-KUPWARA-CHOWKIBAL-TANGDHAR-CHAMKOT (NH-701) ROAD FROM DESIGN (BRO) (N24002210)	3-2024	5/2027 (N.A.) {5/2027}	1,404.94 (N.A.) {1,404.94}	-	0
		581	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A (NHAI) (N24000471)	12-2015	6/2019 (N.A.) {}	2,168.66 (N.A.) {2,168.66}	-	0
		582	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A (NHAI) (N24000488)	12-2015	12/2018 (01-11-2024) {11/2024}	2,136.97 (2,644.00) {2,644.00}	2,386.51	99.5
		583	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE (NHAI) (N24000717)	12-2017	7/2021 (01-07-2025) {7/2025}	1,471.75 (1,471.75) {1,903.98}	1,731.65	98.94
		584	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA (NHIDCL) (N24000868)	3-2018	7/2021 (01-08-2023) {10/2025}	253.44 (N.A.) {253.44}	191.14	83.23

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		585	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D (NHIDCL) (N24001256)	8-2020	9/2026 (N.A.) {9/2026}	6,808.69 (N.A.) {6,808.69}	3,013.84	49.92
		586	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL (NHIDCL) (N24001264)	7-2020	4/2022 (01-10-2024) {10/2026}	228.39 (N.A.) {228.39}	69.32	88.09
		587	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K (NHIDCL) (N24001266)	7-2020	4/2022 (01-11-2023) {8/2025}	210.79 (N.A.) {210.79}	72.72	93.63
<u>JHARKHAND</u>	<u>COAL</u>	588	RAJRAPPA RCE OCP (3.0 MTY) (CCL) (N06000087)	12-2009	3/2016 (N.A.) {3/2027}	510.85 (N.A.) {510.85}	488.57	75
		589	MURADIH UG TURN-KEY PROJECT (BCCL) (N06000096)	2-2011	4/2014 (N.A.) {12/2026}	339.88 (N.A.) {339.88}	190.48	70
		590	MOONIDIH XV SEAM UG (BCCL) (N06000098)	8-2011	3/2019 (N.A.) {5/2026}	1,230.27 (N.A.) {1,230.27}	620.97	81
		591	CHITRA EAST (RCE) OCP (ECL) (N06000169)	8-2018	3/2026 (01-03-2026) {3/2026}	513.98 (N.A.) {513.98}	228.35	51
		592	TETARIAKHAR EXPANSION OCP (CCL) (N06000186)	11-2019	3/2023 (N.A.) {3/2027}	243.52 (N.A.) {243.52}	44.64	26
		593	PACHWARA SOUTH COAL BLOCK (NLC) (N06000193)	7-2013	9/2028 (N.A.) {9/2028}	2,242.92 (2,242.90) {2,242.90}	1,151.23	54
		594	PATHERDIH 2.5 NLW COAL WASHERY (BCCL) (N06000194)	10-2015	4/2018 (N.A.) {3/2026}	334.27 (N.A.) {334.27}	135.86	47

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		595	REVISED PROJECT REPORT MAGADH EXPANSION OCP (CCL) (N06000216)	8-2020	3/2028 (N.A.) {3/2028}	7,254.37 (N.A.) {7,254.37}	1,527.57	38
		596	EXPANSION PROJECT AMRAPALI OCP (CCL) (N06000217)	8-2020	3/2028 (N.A.) {3/2028}	5,136.15 (N.A.) {5,136.15}	1,092.17	43
		597	UCE OF EPR OF NORTH URIMARI OCP (CCL) (N06000218)	7-2021	3/2029 (N.A.) {3/2029}	778.80 (N.A.) {778.80}	694.11	75
		598	KOTRE BASANTPUR PACHMO OCP (CCL) (N06000237)	8-2020	3/2032 (N.A.) {3/2032}	625.40 (N.A.) {625.40}	441.24	41
		599	CHANDRAGUPT OCP (CCL) (N06000238)	8-2020	3/2032 (N.A.) {3/2032}	973.50 (N.A.) {973.50}	440.56	12.4
		600	SIRKA OCP (CCL) (N06000239)	5-2020	3/2028 (N.A.) {3/2028}	222.82 (N.A.) {222.82}	139.31	51
		601	JHARKHAND LAIYO OCP (CCL) (N06000240)	8-2020	3/2031 (N.A.) {3/2031}	764.57 (N.A.) {764.57}	145.80	28
		602	EPR TAPIN SOUTH OCP (CCL) (N06000241)	11-2020	3/2028 (N.A.) {3/2028}	230.41 (N.A.) {230.41}	21.12	18.3
		603	EPR PUNDI OCP (CCL) (N06000242)	11-2020	3/2027 (N.A.) {3/2027}	713.35 (N.A.) {713.35}	236.57	21
		604	EPR ROHINI KARKATA OCP (CCL) (N06000243)	1-2021	3/2028 (N.A.) {3/2028}	1,020.42 (N.A.) {1,020.42}	83.44	18
		605	EXPANSION OF KONAR OCP (CCL) (N06000245)	1-2022	3/2032 (N.A.) {3/2032}	799.34 (N.A.) {799.34}	416.73	32

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		606	EXPANSION OF KARO OCP (CCL) (N06000246)	1-2022	3/2029 (N.A.) {3/2029}	908.47 (N.A.) {908.47}	217.68	21
		607	EXPANSION OF ASHOK OCP (CCL) (N06000247)	5-2021	3/2028 (N.A.) {3/2028}	2,898.28 (N.A.) {2,898.28}	176.50	20
		608	AMALGAMATED NTST KUJAMA OCP 8.5 MTY (BCCL) (N06000273)	1-2023	3/2030 (N.A.) {3/2030}	4,011.85 (N.A.) {4,011.85}	398.49	25.1
		609	HURA C OC (ECL) (N06000275)	8-2022	3/2029 (N.A.) {3/2029}	859.41 (N.A.) {859.41}	448.72	62
		610	CHUPERBHITA- SIMLONG OCP (ECL) (N06000280)	12-2023	3/2037 (01-03-2037) {3/2037}	979.08 (N.A.) {979.08}	-	0.01
		611	BLOCK-E OCP (15 MTY) (BCCL) (N06000287)	3-2024	3/2029 (N.A.) {3/2029}	5,850.83 (N.A.) {5,850.83}	5.96	2
		612	JARANGDIH OCP (CCL) (N06000295)	2-2020	3/2029 (N.A.) {3/2029}	414.37 (N.A.) {414.37}	85.60	0
	DEPARTMENT OF HIGHER EDUCATION	613	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD (CPWD EDUCATION) (N28000067)	9-2012	3/2016 (N.A.) {3/2016}	171.86 (N.A.) {171.86}	174.48	99
	PETROLEUM	614	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) (ONGC) (N16000445)	11-2019	1/2024 (01-03-2025) {6/2025}	431.00 (N.A.) {431.00}	204.31	58
		615	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI (IOCL) (N16000480)	3-2023	2/2026 (N.A.) {2/2026}	202.07 (N.A.) {202.07}	52.94	42.95

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		616	CGD PROJECT IN BIHAR JHARKHAND (HPCL) (N16000497)	6-2022	6/2030 (N.A.) {6/2030}	1,377.00 (N.A.) {1,377.00}	282.88	24.15
	POWER	617	NORTH KARANPURA STPP (3X660 MW) (NTPC) (N18000177)	2-2014	6/2019 (01-10-2022) {3/2025}	16,242.90 (N.A.) {16,242.90}	17,323.08	98
		618	PATRATU STPP-I (3X800MW) (NTPC) (N18000275)	11-2017	3/2023 (N.A.) {3/2026}	17,112.00 (N.A.) {17,112.00}	17,219.35	81
		619	BADAM COAL MINING PROJECT (NTPC) (N18000367)	2-2019	10/2024 (01-04-2027) {4/2027}	501.79 (784.39) {501.79}	368.94	59.79
		620	KERANDARI COAL MINING PROJECT (NTPC) (N18000370)	9-2015	11/2019 (01-03-2025) {3/2025}	1,553.00 (2,896.64) {2,896.64}	2,095.17	64
	RAILWAYS	621	KODERMA-TILAIYA (NL), ECR (ECR) (220100305)	4-2002	3/2023 (N.A.) {12/2025}	1,625.87 (1,625.87) {1,700.00}	2,039.52	80
		622	BONDAMUNDA RANCHI DOUBLING (SER) (N22000396)	3-2016	6/2024 (N.A.) {6/2026}	3,029.04 (3,029.04) {3,029.04}	2,436.91	84.5
		623	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) (SER) (N22000508)	4-2018	6/2026 (N.A.) {6/2026}	501.52 (N.A.) {472.50}	275.97	4
		624	DOUBLING OF PRADHANKHUNTA JN - PATHERDIH BAZAR-BHOJUDIH (ECR) (N22000529)	11-2022	11/2027 (N.A.) {3/2026}	202.00 (349.22) {349.22}	76.94	2
		625	KHARAGPUR-ADITYAPUR - 3RD LINE (132 KM) (RVNL) (N22000595)	12-2015	3/2025 (N.A.) {3/2025}	3,249.98 (N.A.) {3,270.07}	2,899.45	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		626	3RD LINE BETWEEN DHANBAD SONNAGAR (RVNL) (N22000599)	11-2016	3/2026 (N.A.) {3/2026}	8,975.00 (N.A.) {7,906.38}	4,705.38	0
		627	GARHWA ROAD - RAIL OVER RAIL (ECR) (N22000610)	3-2017	6/2024 (N.A.) {2/2026}	262.71 (N.A.) {262.71}	227.86	70
		628	GOMOH - FLYOVER FOR DOWN TRAINS (ECR) (N22000611)	1-2018	3/2023 (N.A.) {3/2026}	686.03 (N.A.) {487.73}	419.46	45
	ROAD TRANSPORT AND HIGHWAYS	629	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 (NHAI) (N24001589)	9-2020	3/2024 (01-12-2024) {4/2025}	755.26 (N.A.) {1,039.00}	635.78	88.1
		630	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS] (NHAI) (N24001590)	9-2020	10/2023 (01-12-2024) {1/2025}	748.99 (N.A.) {903.00}	831.75	100
		631	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM (NHAI) (N24001594)	2-2022	1/2025 (01-03-2025) {3/2025}	534.73 (N.A.) {534.73}	282.33	99.57
		632	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH (NHAI) (N24001595)	8-2020	3/2024 (01-09-2025) {9/2025}	1,034.00 (1,879.55) {1,879.55}	41.50	97.3
		633	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF (NHAI) (N24001596)	11-2021	7/2023 (01-06-2025) {12/2025}	1,302.72 (1,504.80) {1,504.80}	957.00	75.74
		634	FOUR LANING WITH PAVED SHOULDER OF SECTION FROM KM 53.600 (GOLA ON NH-320) TO KM 81.446 (ORMANJHI ON (NHAI) (N24001854)	6-2023	6/2025 (N.A.) {6/2025}	1,214.93 (1,324.95) {1,462.00}	808.69	75.5

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		635	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM 0.00 TO 44.00 (KURU- GHAGHRA SECTION) OF NH-143A INCLU (MoRTH) (N24001922)	2-2020	8/2023 (N.A.) {12/2024}	153.01 (N.A.) {153.01}	83.63	96.23
		636	WIDENING AND STRENGTHENING OF EXISTING PAVEEMNT TO TWO LANE WITH PAVED SHOULDERS FROM KM 116.00 TO K (MoRTH) (N24001923)	1-2022	7/2024 (N.A.) {12/2024}	315.21 (N.A.) {315.21}	117.26	80
		637	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDER/TWO LANE+ PAVED SHOULDER WITH SERVICE ROA (MoRTH) (N24001924)	3-2022	8/2025 (N.A.) {8/2025}	514.22 (N.A.) {514.22}	15.19	6.1
		638	WIDENING AND STRENGTHENING/RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDER/ TWO LANE WITH PAVED SHOUL (MoRTH) (N24001925)	3-2022	8/2025 (N.A.) {8/2025}	423.18 (N.A.) {423.18}	0.11	0
		639	FOUR LANING OF KHAJURI TO WYNDHAMGANJ FROM KM 219.600 TO KM 260.483 ON NH-75 PKG SEC-V ON HAM (NHAI) (N24002053)	4-2022	9/2025 (N.A.) {9/2025}	1,232.00 (1,343.00) {1,400.00}	606.60	81.76
		640	FOUR LANING OF BHOGU TO SANKHA FROM KM 147.450 TO KM 196.870 ON NH-75 PKG SEC- III (NHAI) (N24002054)	10-2022	11/2025 (N.A.) {11/2025}	1,390.77 (1,391.00) {1,600.00}	319.69	75.01
		641	FOUR LANING OF BASUKINATH-DEOGHAR SECTION OF NH-114A FROM KM 85.081 TO KM 130.240 UNDER NHDP PHASE-I (NHAI) (N24002055)	3-2023	12/2025 (N.A.) {12/2025}	1,444.94 (N.A.) {1,444.94}	-	0
		642	BHARATMALA PARIYOJANA OF BOKARO JAINA MORE - GOLA SECTION OF NH-320 FROM KM. 21.110 TO KM. 53.600 IN (NHAI) (N24002056)	6-2020	6/2025 (N.A.) {6/2025}	964.64 (N.A.) {964.64}	458.58	61.2

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		643	FOUR LANING OF MEHGAMA HANSDIHA SECTION OF NH-33 FROM EXISTING KM 41.900 TO 93.000 IN THE STATE OF J (NHAI) (N24002057)	12-2022	5/2025 (N.A.) {5/2025}	1,443.77 (N.A.) {1,443.77}	-	0
		644	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION (NHAI) (N24000726)	1-2018	11/2021 (01-05-2026) {5/2026}	1,155.16 (N.A.) {950.49}	657.82	73
		645	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I (MoRTH) (N24001216)	12-2016	9/2021 (N.A.) {12/2024}	196.00 (N.A.) {196.00}	164.21	90.1
	STEEL	646	NEW SINTER PLANT AT BOKARO STEEL PLANT (SAIL) (N12000095)	3-2015	10/2017 (01-11-2026) {11/2026}	1,034.01 (1,752.30) {1,752.30}	882.41	51.75
		647	REVAMPING OF OLD SUB SYSTEM OF BLAST FURNACE 3 AT BOKARO STEEL PLANT (SAIL) (N12000129)	9-2023	7/2025 (01-11-2025) {11/2025}	513.82 (N.A.) {513.82}	195.71	67
		648	REBUILDING OF COKE OVEN BATTERY NO.6 OF BOKARO STEEL PLANT (SAIL) (N12000133)	11-2023	11/2026 (N.A.) {11/2026}	627.31 (N.A.) {627.31}	84.56	35
		649	REPLACEMENT OF REMAINING 04 NOS. OF BATTERY CYCLONES WITH 04 NOS. OF ESPS IN SINTER PLANT-1 AT BSL (SAIL) (N12000135)	3-2024	6/2026 (N.A.) {6/2026}	260.37 (N.A.) {260.37}	44.22	18
		650	REPLACEMENT OF EXISTING GRINDERS IN CRM-I & II AT BOKARO STEEL PLANT (SAIL) (N12000142)	1-2025	1/2027 (N.A.) {1/2027}	211.94 (N.A.) {211.94}	-	0
		651	SECONDARY EMISSION CONTROL IN CONVERTERS OF SMS-II AT BOKARO STEEL PLANT (SAIL) (N12000143)	1-2025	10/2026 (N.A.) {10/2026}	207.13 (N.A.) {207.13}	-	5

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
KARNATAKA	CIVIL AVIATION	652	BELAGAVI AIRPORT- EXPANSION OF TERMINAL BUILDING AND ASSOCIATED WORKS (AAI) (N04000105)	6-2023	2/2026 (N.A.) {2/2026}	322.45 (N.A.) {322.45}	104.38	43
		653	HUBBALI AIRPORT - CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS (AAI) (N04000108)	6-2023	2/2026 (N.A.) {2/2026}	320.47 (N.A.) {320.47}	53.87	32.5
	DEPARTMENT OF HIGHER EDUCATION	654	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) (CPWD EDUCATION) (N42000006)	7-2019	3/2022 (N.A.) {11/2025}	851.00 (851.00) {930.36}	918.06	0
		655	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL (CPWD) (N42000010)	8-2021	2/2024 (01-11-2024) {11/2024}	316.25 (N.A.) {316.25}	281.32	91
	PETROLEUM	656	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE (HPCL) (N16000369)	12-2018	12/2022 (01-08-2025) {8/2025}	854.00 (854.00) {854.00}	717.44	99.7
		657	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE (IOCL) (N16000437)	1-2022	7/2025 (01-12-2025) {12/2025}	463.00 (500.62) {500.62}	244.46	71.1
		658	POWER SYSTEM UPGRADATION PROJECT (MANGALORE REFIN) (N16000509)	10-2023	2/2026 (N.A.) {2/2026}	385.00 (N.A.) {385.00}	129.72	59.7
		659	DEMO PLANT FOR PRODUCTION OF BIO-ATF (MANGALORE REFIN) (N16000536)	3-2024	3/2027 (N.A.) {3/2027}	364.00 (N.A.) {364.00}	22.78	10.1
	POWER	660	TS FOR INTRGRATION OF RE ZONE (PHASE II) IN KOPPAL II (PHASE A and B) AND GADAG II (PHASE A) IN KARN (PGCIL) (N18000385)	12-2023	12/2025 (N.A.) {12/2025}	2,889.00 (N.A.) {2,889.00}	1,011.29	36.7

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		661	TS FOR SOLAR ENERGY ZONE IN BIDAR (2500MW), KARNATAKA [BIDAR TRANSMISSION LTD] (PGCIL) (N18000388)	2-2024	2/2026 (N.A.) {2/2026}	2,148.00 (N.A.) {2,148.00}	923.47	52.2
		662	SYSTEM STRENGTHENING AT KOPPAL-II AND GADAG-II FOR INTEGRATION OF RE GENERATION PROJECTS (PGCIL) (N18000409)	1-2025	1/2027 (N.A.) {1/2027}	1,354.00 (N.A.) {1,354.00}	16.25	0
		663	AUGMENTATION OF TRANSFORMATION CAPACITY AT BIDAR PS (PGCIL) (N18000410)	2-2025	2/2027 (N.A.) {2/2027}	288.00 (N.A.) {288.00}	4.03	0
		664	TRANSMISSION SCHEME FOR INTEGRATION OF DAVANAGERE / CHITRADURGA AND BELLARY REZ IN KARNATAKA (PGCIL) (N18000419)	3-2025	3/2027 (N.A.) {3/2027}	3,453.00 (N.A.) {3,453.00}	20.70	0
	RAILWAYS	665	TUMKUR-CHITRADURGA-DAVENGERE NL (SWR) (N22000256)	4-2011	3/2019 (N.A.) {12/2027}	1,876.00 (N.A.) {1,801.01}	503.99	12
		666	BAGALKOT-KUDACHI NL (SWR) (N22000258)	4-2010	3/2027 (N.A.) {12/2028}	1,378.00 (1,378.00) {1,378.00}	646.95	34
		667	HOSPET-HUBLI-LONDA-VASCODAGAMA DL (RVNL) (N22000297)	4-2010	3/2027 (N.A.) {12/2026}	5,060.36 (N.A.) {3,692.60}	3,505.49	0
		668	GADAG-WADI NL (SWR) (N22000299)	4-2013	3/2027 (N.A.) {3/2028}	2,841.84 (N.A.) {2,841.84}	1,352.94	29
		669	MARIKUPPAM - KUPPAM (SWR) (N22000308)	4-2012	3/2016 (N.A.) {12/2027}	279.54 (296.72) {296.72}	121.12	14
		670	KADUR CHIKMAGALUR SAKLIESHPUR NEW LINE (93 KM) (SWR) (N22000486)	3-1996	6/2025 (N.A.) {3/2026}	825.31 (825.31) {825.31}	692.24	83

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		671	BAIYYAPPANAHALLI-HOSUR (48 KM) (NCRTC) (N22000542)	4-2019	3/2026 (N.A.) {3/2026}	375.67 (N.A.) {375.67}	-	0
		672	YESHVANTHPUR-CHANNASANDRA (21.7 KM) (NCRTC) (N22000543)	4-2019	3/2026 (N.A.) {3/2026}	169.65 (N.A.) {169.65}	71.75	0
		673	BELGAUM-DHARWAD VIA KITTUR (73.10 KM) (UMBRELLA WORK PB#22/2019-20/NR) (SWR) (N22000557)	9-2020	12/2027 (N.A.) {3/2029}	1,590.80 (927.42) {927.42}	0.75	0
		674	HASSAN (ALUR) - BELUR (32 KM) (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000558)	6-2019	4/2028 (N.A.) {3/2028}	748.86 (748.85) {748.85}	0.88	1
		675	SHIMOGA-SHIKARIPURA-RANEBENNUR (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000559)	9-2019	12/2027 (N.A.) {12/2028}	1,453.73 (994.47) {994.47}	87.33	7
		676	BANGALORE-WHITEFIELD-BANGALORE CITY- KRISHNARAJAPURAM QUADRUPLING (SWR) (N22000621)	3-2018	6/2025 (N.A.) {2/2026}	492.87 (492.87) {492.87}	254.35	75
	ROAD TRANSPORT AND HIGHWAYS	677	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT (MoRTH) (N24001387)	1-2017	9/2017 (01-05-2023) {5/2023}	264.34 (N.A.) {264.34}	201.07	100
		678	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA (MoRTH) (N24001388)	3-2019	12/2019 (01-11-2024) {11/2024}	423.15 (N.A.) {423.15}	268.97	82
		679	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN (NHAI) (N24001425)	3-2021	11/2021 (01-11-2025) {11/2025}	1,100.88 (1,687.31) {1,687.31}	1,156.26	80.3

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		680	4L OF ADDAHOLE TO BANTWAL CROSS SECTION (NHAI) (N24001426)	3-2021	10/2021 (01-07-2025) {7/2025}	317.90 (572.01) {572.01}	370.84	98
		681	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) (NHAI) (N24001598)	1-2022	4/2025 (01-05-2026) {5/2026}	1,388.70 (1,388.70) {1,388.70}	509.84	71.6
		682	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. (NHAI) (N24001599)	3-2018	12/2022 (01-12-2022) {12/2025}	440.16 (N.A.) {440.16}	355.97	75.27
		683	BANGALORE/TN BORDER TO HOSKOTE (NHAI) (N24001674)	2-2023	2/2025 (01-09-2025) {9/2025}	1,240.60 (1,181.68) {1,181.68}	952.87	83.25
		684	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 (NHAI) (N24001675)	11-2022	5/2025 (N.A.) {5/2025}	1,732.73 (N.A.) {1,732.73}	754.79	97.99
		685	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 (NHAI) (N24001676)	12-2022	6/2025 (01-03-2026) {6/2025}	2,718.46 (N.A.) {2,718.46}	438.90	54.52
		686	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 (NHAI) (N24001677)	11-2022	5/2024 (01-04-2025) {4/2025}	226.76 (226.76) {226.76}	86.76	71.95
		687	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 (NHAI) (N24001679)	10-2022	4/2025 (01-12-2025) {12/2025}	1,479.30 (1,479.30) {1,479.30}	676.61	83.98

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		688	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE (NHAI) (N24001680)	3-2021	10/2024 (01-06-2026) {6/2026}	1,409.68 (1,808.12) {1,808.12}	1,039.17	59
		689	TUMKUR - NELAMANGALA(6L) (NHAI) (N24001681)	8-2022	8/2025 (01-03-2026) {3/2026}	2,032.15 (2,032.15) {2,032.15}	185.64	52.88
		690	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA (NHAI) (N24001682)	11-2021	3/2024 (01-03-2024) {12/2026}	294.62 (309.90) {309.90}	57.86	15.14
		691	AURAD - BIDAR KM 0.00 TO KM 45.878 (NHAI) (N24001683)	9-2021	4/2023 (01-12-2024) {12/2024}	912.37 (N.A.) {424.16}	255.94	100
		692	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION (NHAI) (N24001684)	9-2020	1/2023 (01-09-2020) {5/2025}	688.00 (602.09) {688.00}	514.23	80.07
		693	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 (NHAI) (N24001686)	3-2021	3/2023 (01-12-2025) {12/2025}	1,065.06 (1,444.50) {1,444.50}	736.55	93.5
		694	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 (NHAI) (N24001687)	10-2021	10/2023 (01-12-2025) {12/2025}	1,331.77 (2,082.98) {2,082.98}	483.94	77.06
		695	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN (NHAI) (N24001691)	10-2019	10/2021 (01-12-2025) {12/2025}	1,225.24 (1,505.85) {1,505.85}	1,043.00	96.85

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		696	BALANCE WORK OF CONTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM. 54.370 TO KM. 101.400 (BI (MoRTH) (N24001936)	3-2021	3/2023 (01-07-2024) {7/2024}	344.79 (N.A.) {344.79}	10.00	90
		697	BALANCE WORK OF REHABILITATION AND UPGRADING TO 2LANE/2LANE WITH PAVED SHOULDER CONFIGURATION AND ST (MoRTH) (N24001937)	2-2023	2/2024 (01-02-2025) {2/2025}	398.48 (N.A.) {398.48}	5.00	50
		698	CONSTRUCTION OF ELEVATED CORRIDOR FROM KM. 135.650 TO 136.300 ON 63, FROM KM. 249 TO KM. 250.050 ON (MoRTH) (N24001938)	6-2021	6/2024 (01-06-2025) {6/2025}	298.00 (N.A.) {298.00}	10.70	52
		699	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24001940)	1-2023	1/2026 (01-09-2025) {9/2025}	166.58 (N.A.) {166.58}	3.54	0
		700	WIDENING TO 4 LANE FROM KM. 133.00 TO 158.04 (DESIGN CHAINAGE KM. 130.88 TO 155.145) (SHIRUR CROSS T (MoRTH) (N24001941)	1-2023	1/2025 (01-01-2025) {1/2025}	350.69 (N.A.) {350.69}	10.00	56
		701	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM. 33.13 TO KM. 40.23 AND KM. 52.00 TO KM. 71.00 (EX (MoRTH) (N24001943)	9-2022	3/2024 (01-01-2025) {1/2025}	172.98 (N.A.) {172.98}	6.48	65
		702	WIDENING TO INTERMEDIATE/TWO LANE TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHANAGES KM 112.750 TO (MoRTH) (N24001944)	1-2023	6/2024 (01-07-2024) {7/2024}	255.88 (N.A.) {255.88}	60.99	78.24
		703	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 116.800 TO 149.070(DESIGN CHANGES) ON HOSADURGA HOL (MoRTH) (N24001945)	8-2022	2/2024 (01-12-2024) {12/2024}	170.34 (N.A.) {170.34}	4.25	72

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		704	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM 24.400 TO 27.270, 40.500 TO 41.900, 84.300 TO 88.20 (MoRTH) (N24001946)	11-2022	11/2024 (01-11-2024) {11/2024}	218.93 (N.A.) {218.93}	10.00	95.25
		705	WIDENING TO EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FROM DESIGN KM 153.00 (MoRTH) (N24001947)	2-2023	2/2025 (01-02-2025) {2/2025}	177.94 (N.A.) {177.94}	6.66	47
		706	WIDENING TO 4 LANE FROM KM 51.60 TO 76.20 (HEBRI TO PARKALA) AND FROM KM 85.20 TO 88.90 (KARAVALI JU (MoRTH) (N24001948)	10-2022	10/2024 (01-12-2024) {12/2024}	355.72 (N.A.) {355.72}	11.32	60
		707	FOUR LANING OF LEFT OVER WORKS OF HOSPET BELLARY KARNATAKA/ AP BORDER FROM KM.280.080 TO KM. 375.450 (NHAI) (N24001989)	3-2023	5/2025 (N.A.) {5/2025}	830.28 (N.A.) {830.28}	692.62	77.1
		708	DEVELOPMENT OF 6 LANE ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KM. 97.000 TO KM. 162.500 MARADGI S (NHAI) (N24001993)	12-2022	10/2025 (N.A.) {10/2025}	1,589.00 (N.A.) {1,589.00}	732.47	63.15
		709	4/6L OF BANGALORE - PUNE SECTION OF BYPASS CONNECTING DHARWAD - HUBLI FROM KM. 403.80 TO KM. 433.20 (NHAI) (N24001994)	5-2022	3/2023 (01-09-2025) {9/2025}	1,135.39 (N.A.) {1,135.39}	396.27	70.68
		710	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM 422.000 TO 523.600 (CHITR (MoRTH) (N24002011)	12-2021	6/2024 (01-12-2024) {12/2024}	516.96 (N.A.) {516.96}	19.93	75
		711	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40.00 TO KM 75.00 (EXISTING CHAINAGES) OF MANGALOR (MoRTH) (N24002012)	3-2023	3/2025 (01-03-2025) {3/2025}	718.52 (N.A.) {718.52}	24.81	23

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		712	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM KM.0 TO KM. 80 ON NH 548B (VIJAYAPURA-SANKESWAR SE (MoRTH) (N24002013)	3-2021	2/2022 (01-10-2024) {10/2024}	766.64 (N.A.) {766.64}	13.55	75
		713	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24002186)	3-2024	9/2025 (N.A.) {9/2025}	166.58 (N.A.) {166.58}	3.62	0
		714	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM 55.6 TO KM 90.7 (EXISTING CHAINAGES) OF NH-766C ((MoRTH) (N24002187)	2-2024	2/2026 (N.A.) {2/2026}	313.56 (N.A.) {313.56}	53.65	0
		715	WIDENING TO 2L+PS FROM KM 71.00 TO 104.00 (EXISTING CHAINAGES) (SARJAPUR TO PATTADKALLU) ON BHANAPUR (MoRTH) (N24002188)	3-2024	3/2026 (N.A.) {3/2026}	445.62 (N.A.) {445.62}	33.24	0
		716	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 (DESIGN CHAINAGE 0.00) TO KM 23.338 (DESIGN C (MoRTH) (N24002189)	9-2024	3/2026 (N.A.) {3/2026}	196.05 (N.A.) {196.05}	2.34	0
		717	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP (MoRTH) (N24000334)	3-2015	11/2015 (01-08-2024) {8/2024}	165.67 (N.A.) {165.67}	126.47	98.99
		718	4-LANING OF GOA/KARNATAKA BORDER- KUNDAPUR SECTION (NHAI) (N24000462)	7-2012	8/2016 (01-01-2020) {12/2025}	1,655.01 (1,990.99) {1,990.99}	1,824.10	97.8
		719	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY (NHAI) (N24000552)	3-2016	3/2019 (01-12-2023) {6/2025}	701.40 (591.86) {701.40}	923.99	88

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		720	HOSPET-BELLARY-KARNATAKA AP BORDER (NHAI) (N24000603)	8-2016	3/2019 (01-05-2025) {5/2025}	1,167.42 (N.A.) {1,224.01}	1,028.39	0
		721	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS ? PA (MoRTH) (N24001156)	1-2017	9/2017 (01-05-2023) {5/2023}	166.67 (N.A.) {264.34}	192.08	100
		722	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH (MoRTH) (N24001157)	8-2016	2/2017 (01-07-2024) {7/2024}	175.50 (N.A.) {241.60}	178.73	90.01
		723	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 (MoRTH) (N24001158)	3-2018	6/2019 (01-12-2023) {12/2023}	159.97 (N.A.) {242.61}	113.15	100
		724	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION (MoRTH) (N24001159)	1-2018	7/2018 (N.A.) {3/2022}	159.70 (N.A.) {159.70}	142.88	100
		725	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR (MoRTH) (N24001160)	9-2017	10/2018 (01-04-2022) {4/2022}	191.60 (N.A.) {191.60}	112.01	100
		726	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- (MoRTH) (N24001161)	12-2017	1/2019 (01-04-2022) {4/2022}	297.30 (N.A.) {318.28}	277.27	100
		727	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN (MoRTH) (N24001162)	3-2018	10/2018 (01-11-2022) {11/2022}	325.86 (N.A.) {386.41}	356.76	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		728	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN (MoRTH) (N24001164)	10-2016	3/2017 (01-07-2022) {7/2022}	396.96 (N.A.) {396.96}	329.58	100
		729	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT (MoRTH) (N24001165)	11-2016	3/2017 (01-10-2021) {10/2021}	314.90 (N.A.) {314.90}	233.95	100
		730	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) (MoRTH) (N24001166)	3-2015	1/2016 (N.A.) {7/2024}	159.12 (N.A.) {159.12}	127.72	98
		731	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT (MoRTH) (N24001168)	5-2018	5/2018 (01-12-2023) {12/2023}	171.60 (N.A.) {171.60}	129.72	100
		732	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U (MoRTH) (N24001172)	1-2017	8/2017 (N.A.) {6/2022}	291.49 (N.A.) {291.49}	238.77	100
		733	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI ? JADERCELA SECTION (MoRTH) (N24001173)	2-2017	5/2019 (N.A.) {10/2025}	157.32 (188.00) {187.61}	43.16	60
	STEEL	734	SCREENING PLANT-II, DONIMALAI (NMDC) (N12000136)	9-2023	8/2026 (N.A.) {8/2026}	1,043.63 (N.A.) {1,043.63}	201.25	21.5
	URBAN DEVELOPMENT	735	BANGALORE METRO RAIL PROJECT PHASE-2 (BMRCCL) (N28000058)	2-2014	2/2021 (N.A.) {3/2025}	26,405.14 (N.A.) {26,405.14}	20,936.29	0
		736	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B (BMRCCL) (N28000151)	6-2021	6/2026 (N.A.) {6/2026}	14,788.10 (N.A.) {14,788.10}	2,424.04	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
KERALA	<u>CIVIL AVIATION</u>	737	CALICUT AIRPORT - DEVELOPMENT OF ADDITIONAL RESA ON EITHER END ON RUNWAY 10-28 AT CALICUT AIRPORT (AAI) (N04000111)	6-2023	9/2025 (N.A.) {9/2025}	484.57 (323.98) {323.98}	74.67	18.3
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	738	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA (CPWD EDUCATION) (N28000140)	7-2019	3/2021 (N.A.) {11/2025}	753.63 (N.A.) {753.63}	411.86	67
	<u>HEALTH AND FAMILY WELFARE</u>	739	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST (CPWD FOR HEALTH) (N28000112)	9-2017	3/2020 (01-05-2024) {11/2024}	150.29 (N.A.) {162.00}	162.52	100
	<u>PETROLEUM</u>	740	REPLACEMENT AND EXTENSION OF JETTY PIPELINES AT KOCHI REFINERY (BPCL) (N16000508)	3-2023	3/2026 (N.A.) {3/2026}	621.87 (N.A.) {621.87}	180.09	82.5
		741	SETTING UP POLYPROPYLENE UNIT AT KOCHI REFINERY (BPCL) (N16000530)	12-2023	10/2027 (N.A.) {10/2027}	4,460.00 (N.A.) {4,460.00}	240.70	11.1
	<u>RAILWAYS</u>	742	TRIVANDRUM-KANYAKUMARI DOUBLING (SR) (N22000399)	2-2015	3/2024 (N.A.) {12/2027}	1,431.90 (N.A.) {3,785.45}	3,184.42	42.1
		743	ERNAKULAM-KUMBALAM - PATCH DOUBLING (7.71 KM) (SR) (N22000619)	12-2010	3/2028 (N.A.) {12/2026}	600.82 (N.A.) {595.39}	282.77	8
		744	KUMBALAM-THURAVUR - PATCH DOUBLING (15.59 KM) (SR) (N22000620)	12-2011	3/2027 (N.A.) {12/2026}	812.85 (N.A.) {802.80}	287.48	7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	745	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK (MoRTH) (N24001369)	2-2017	8/2017 (01-03-2022) {8/2024}	294.28 (296.53) {296.53}	286.80	98

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		746	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) (MoRTH) (N24001370)	2-2017	9/2017 (01-01-2023) {8/2024}	380.76 (372.87) {372.87}	347.04	100
		747	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE (NHAI) (N24001648)	8-2022	1/2026 (N.A.) {1/2026}	2,429.52 (N.A.) {2,429.52}	1,185.00	62.02
		748	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 (NHAI) (N24001649)	12-2021	2/2025 (01-02-2025) {1/2026}	3,273.61 (N.A.) {3,273.61}	789.16	61.81
		749	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54 (NHAI) (N24001650)	12-2021	1/2025 (01-04-2026) {4/2026}	3,635.64 (N.A.) {3,635.64}	324.02	39.2
		750	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O (NHAI) (N24001651)	9-2021	9/2024 (01-03-2026) {9/2024}	2,878.97 (N.A.) {2,878.97}	570.80	44.65
		751	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR (NHAI) (N24001652)	3-2020	6/2022 (01-02-2024) {6/2024}	210.37 (216.94) {216.94}	198.10	100
		752	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH 766 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 ((NHAI) (N24001653)	11-2021	4/2025 (N.A.) {4/2025}	3,565.82 (N.A.) {3,064.11}	2,082.00	62.43
		753	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 (NHAI) (N24001654)	6-2021	3/2025 (01-02-2026) {2/2026}	2,641.37 (N.A.) {2,641.37}	607.07	76.9

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		754	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX (NHAI) (N24001655)	6-2021	2/2025 (N.A.) {11/2025}	3,606.00 (3,946.56) {3,946.56}	3,120.31	73.35
		755	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. (NHAI) (N24001656)	6-2021	3/2025 (N.A.) {12/2025}	2,595.00 (N.A.) {4,009.57}	3,071.01	66.73
		756	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC (NHAI) (N24001657)	6-2021	10/2024 (01-12-2025) {12/2025}	2,842.14 (N.A.) {2,842.14}	477.69	71.3
		757	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM (NHAI) (N24001658)	1-2021	7/2024 (01-03-2025) {3/2025}	4,265.42 (N.A.) {4,728.40}	3,474.31	99.1
		758	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66 (OLD NH-17) FROM DESIGN CH (NHAI) (N24001659)	2-2021	7/2024 (01-03-2025) {3/2025}	3,375.31 (3,824.07) {3,824.07}	2,351.62	98.4
		759	SIX LANING OF THALIPARAMBHA- MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH (NHAI) (N24001660)	8-2020	2/2024 (01-08-2025) {3/2026}	2,714.60 (3,557.65) {2,714.60}	1,904.06	72.77
		760	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 (NHAI) (N24001661)	10-2020	4/2024 (01-05-2025) {3/2026}	3,219.47 (3,898.46) {3,896.46}	2,295.34	58.14
		761	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH (NHAI) (N24001662)	5-2020	5/2024 (01-11-2021) {7/2025}	1,981.07 (2,651.79) {1,981.07}	1,543.14	97.38

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		762	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ (NHAI) (N24001663)	6-2020	4/2024 (01-10-2021) {3/2026}	3,041.65 (3,867.66) {3,041.65}	2,406.52	82.75
		763	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ (NHAI) (N24001664)	6-2020	4/2024 (01-10-2021) {3/2026}	1,746.45 (2,538.06) {1,746.45}	1,262.19	79.25
		764	WIDENING/DEVELOPMENT OF EXISTING NH-85 FROM KM 0.000 TO KM 124.636 SECTION TO 2L/2L+PS SECTION IN TH (NHAI) (N24002074)	8-2022	6/2025 (N.A.) {6/2025}	1,231.74 (N.A.) {1,231.74}	486.00	49.7
		765	4-LANNING OF THALSERRY -MAHE BYPASS (NHAI) (N24000704)	9-2017	5/2020 (01-11-2023) {2/2024}	1,124.11 (1,573.18) {1,573.18}	1,527.28	100
		766	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH (NHAI) (N24000784)	2-2018	2/2023 (01-12-2024) {7/2025}	1,424.77 (2,065.95) {2,065.95}	902.09	95.5
		767	KOCHI METRO RAIL PROJECT PHASE II FROM JLN STADIUM TO INFOPARK VIA KAKKANAD (KMRCL) (N28000158)	7-2018	11/2026 (N.A.) {11/2026}	1,957.05 (N.A.) {1,957.05}	250.63	7.4
	URBAN DEVELOPMENT	768	KOCHI METRO RAIL PROJECT PHASE IB SECTION FROM S N JUNCTION TO THRIPIUNITHURA (KMRCL) (N28000159)	6-2019	9/2023 (N.A.) {9/2023}	355.70 (448.00) {448.33}	448.39	100
LADAKH	CIVIL AVIATION	769	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT (AAI) (N04000078)	7-2018	9/2021 (01-10-2025) {10/2025}	480.33 (640.00) {640.00}	416.49	65.92
	ROAD TRANSPORT AND HIGHWAYS	770	KARGIL-ZANSKR PACKAGE-1 (NHIDCL) (N24001343)	3-2021	1/2023 (01-12-2024) {11/2025}	384.23 (N.A.) {384.23}	162.54	60.4

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		771	KARGIL-ZANSKR PACKAGE-2 (NHIDCL) (N24001344)	3-2021	1/2023 (01-02-2025) {11/2025}	404.89 (N.A.) {404.89}	244.21	67.27
		772	KARGIL-ZANSKR PACKAGE-3 (NHIDCL) (N24001345)	8-2020	1/2023 (01-08-2025) {8/2025}	381.01 (N.A.) {381.01}	230.28	76.11
		773	KARGIL-ZANSKR PACKAGE-8 (NHIDCL) (N24001348)	3-2021	1/2023 (01-08-2025) {8/2025}	398.37 (N.A.) {398.37}	279.84	84.05
		774	CONSTRUCTION OF REALIGNMENT BETWEEN PANDRASS- PASHKYUN (TOTAL LENGTH 27.10 KM) ON ROAD ZOZILA-KARGIL (BRO) (N24001999)	11-2021	6/2025 (N.A.) {6/2025}	426.14 (N.A.) {426.14}	16.27	37
MADHYA PRADESH	CIVIL AVIATION	775	UPGRADATION OF JABALPUR AIRPORT (AAI) (N04000087)	6-2016	6/2021 (01-07-2024) {7/2024}	412.24 (N.A.) {412.24}	403.17	100
		776	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 (AAI) (N04000098)	10-2021	8/2023 (01-08-2024) {8/2024}	446.12 (455.00) {455.00}	451.55	100
	COAL	777	KANCHAN OC EXPANSION (SECL) (N06000125)	12-2014	3/2021 (01-03-2026) {3/2026}	371.04 (N.A.) {371.04}	137.63	47
		778	AMADAND OPENCAST EXPANSION PROJECT (SECL) (N06000148)	3-2016	3/2021 (01-03-2027) {3/2027}	869.44 (N.A.) {869.44}	272.09	75
		779	GANDHIGRAM UG MINE (WCL) (N06000183)	8-2019	3/2026 (N.A.) {3/2026}	414.16 (N.A.) {414.16}	11.75	28
		780	BLOCK-B EXPANSION OPENCAST PROJECT (NCL) (N06000184)	7-2019	3/2023 (N.A.) {3/2027}	998.71 (N.A.) {998.71}	453.75	46.24

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		781	NIGAH EXPANSION OCP (15 TO 25 MTPA) (NCL) (N06000196)	11-2020	3/2025 (N.A.) {3/2028}	1,729.68 (N.A.) {1,729.68}	772.95	44.93
		782	RAMPUR BATURA OC (4.0 MTY) (SECL) (N06000233)	7-2019	3/2026 (N.A.) {3/2026}	1,248.93 (N.A.) {1,248.93}	490.58	44
		783	TAWA III UG MINE (WCL) (N06000250)	12-2021	3/2027 (N.A.) {3/2027}	314.09 (N.A.) {324.25}	0.56	9
		784	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) (WCL) (N06000257)	9-2022	3/2027 (N.A.) {3/2027}	399.20 (N.A.) {497.01}	64.13	42
		785	VISHNUPURI UG TO OC (WCL) (N06000260)	11-2022	3/2029 (N.A.) {3/2029}	220.62 (N.A.) {227.65}	-	7
		786	URDHAN OC (WCL) (N06000265)	1-2023	3/2031 (N.A.) {3/2031}	206.88 (N.A.) {228.42}	22.12	9
		787	SHARDA UG (WCL) (N06000266)	9-2023	3/2028 (N.A.) {3/2028}	166.25 (N.A.) {200.16}	1.69	11
	PETROLEUM	788	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF (BPCL) (N16000518)	5-2023	5/2028 (N.A.) {5/2028}	43,367.00 (N.A.) {43,367.00}	1,687.00	13
	POWER	789	SHAJAPUR 325MW SOLAR PV PROJECT (NTPC) (N18000348)	6-2022	3/2024 (01-06-2025) {6/2025}	1,530.49 (N.A.) {1,578.34}	1,219.41	100
		790	TS FOR EVACUATION POWER RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX): PART-C (PGCIL) (N18000392)	8-2024	8/2026 (N.A.) {8/2026}	2,708.00 (N.A.) {2,708.00}	622.84	25.7

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		791	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-2 5.5GW] [JAISALMER/BARME (PGCIL) (N18000399)	10-2024	10/2026 (N.A.) {10/2026}	3,674.00 (N.A.) {3,674.00}	345.36	12.7
	RAILWAYS	792	RAMGANJMUNDI-BHOPAL (NL),WCR (WCR) (220100314)	4-2001	12/2025 (01-12-2025) {6/2026}	3,032.00 (3,032.46) {5,125.16}	3,513.09	69
		793	RATLAM-MHOW-KHANDWA-AKOLA (GC) (WR) (N22000120)	4-2008	2/2027 (01-02-2027) {2/2027}	5,677.88 (5,677.80) {6,203.51}	4,314.25	80
		794	KATNI - SINGRAULI DOUBLING PROJECT (WCR) (N22000351)	12-2015	12/2026 (01-12-2027) {12/2027}	2,445.29 (2,445.30) {4,353.50}	3,122.03	92
		795	KATNI GRADE SEPARATOR/BYE PASS (WCR) (N22000416)	8-2016	9/2024 (01-06-2025) {9/2024}	1,247.64 (1,247.64) {2,300.00}	1,453.81	89
		796	ANUPPUR-KATNI (SECR) (N22000485)	4-2015	12/2021 (01-12-2023) {3/2025}	1,860.94 (1,680.00) {2,311.02}	1,955.51	100
		797	NIMACH BADI SADRI NEW LINE PROJECT (WR) (N22000503)	4-2017	3/2022 (01-12-2026) {12/2026}	495.18 (N.A.) {495.18}	306.32	46
		798	NIMACH-RATLAM (133 KM) (WR) (N22000536)	10-2021	10/2027 (01-12-2025) {12/2025}	1,095.88 (1,095.88) {1,095.88}	1,197.14	72
		799	SATNA - REWA (50 KM) (WCR) (N22000554)	11-2015	3/2026 (N.A.) {3/2026}	500.00 (40.00) {500.00}	1.41	80
		800	INDORE BUDNI (INDORE JABALPUR) (RVNL) (N22000601)	9-2018	9/2030 (N.A.) {9/2030}	7,474.01 (N.A.) {7,393.75}	1,004.86	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	801	4LBERKHEDI TO GODPEHRA NH-44 (NHAI) (N24001614)	2-2022	11/2024 (N.A.) {12/2025}	524.84 (N.A.) {524.84}	2,455.45	60
		802	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) (NHAI) (N24001615)	3-2021	4/2024 (01-06-2025) {6/2025}	790.78 (N.A.) {790.78}	2,141.21	77.02
		803	2L PS OF SATNA - MAIHAR SECTION OF NH- 135BG FROM KM 80.800 TO KM 120.125 (NHAI) (N24001616)	1-2021	10/2023 (N.A.) {2/2025}	428.04 (N.A.) {428.04}	351.97	100
		804	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50 (NHAI) (N24001618)	9-2019	9/2022 (N.A.) {2/2025}	194.40 (235.00) {235.00}	208.32	98.84
		805	4L OF CHANDESARA TO KHEDAKHAJURIYA FROM KM. 0.000 TO (N.A.) 750 AND KM 0.000 TO KM 41.400 OF NH-752D (NHAI) (N24001759)	1-2020	6/2024 (01-12-2025) {12/2025}	909.84 (N.A.) {909.84}	503.76	99
		806	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] (NHAI) (N24001762)	10-2021	1/2024 (01-12-2025) {12/2025}	1,146.22 (N.A.) {1,146.22}	663.10	91.4
		807	ADDITIONAL WORKS (2VUPS, MR-10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE-DEWAS SECTION OF N (NHAI) (N24001765)	8-2022	7/2024 (N.A.) {12/2025}	207.77 (N.A.) {207.77}	147.24	100
		808	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] (NHAI) (N24001766)	1-2022	10/2024 (N.A.) {12/2025}	1,011.29 (N.A.) {1,011.29}	318.76	70.68
		809	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND (NHAI) (N24001767)	1-2021	4/2024 (N.A.) {12/2025}	1,001.69 (N.A.) {1,001.69}	520.29	83

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		810	BALANCE WORK OF 4L OF INDORE- GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF (NHAI) (N24001768)	8-2019	4/2023 (N.A.) {11/2023}	323.51 (N.A.) {323.51}	246.27	100
		811	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 (NHAI) (N24001770)	2-2022	3/2024 (01-03-2025) {7/2025}	417.51 (N.A.) {417.51}	312.94	100
		812	2- LANE WITH PAVED SHOULDERS OF HINOTIYA TO MEHULWA FROM DESIGN KM 27+000 9OF EXISTING SH-19 KM 26+5 (NHAI) (N24001921)	8-2021	9/2025 (N.A.) {9/2025}	581.65 (592.03) {581.65}	135.75	45.78
		813	CONSTRUCTION OF MIHONA BYPASS, LAHAR BYPASS, DABOH BYPASS and BHANDER BYPASS (TOTAL LENGTH 20.60 KM) (MoRTH) (N24001962)	3-2022	12/2024 (N.A.) {3/2025}	179.19 (N.A.) {179.19}	47.91	96
		814	UPGRADATION OF NASRULLAGANI-REHTI- BUDHNI SCCTION TO 2-LANE WITH PAVED SHOULDER FROM KM 0+150 TO KM (MoRTH) (N24001963)	12-2021	10/2024 (N.A.) {9/2025}	305.12 (N.A.) {305.12}	71.47	34.46
		815	UPGRADATION and WIDENING OF JHARKHEDA- BERASIA - DHOLKHEDI FROM DESIGN KM 0+000 TO KM 87+900 (DESIGN (MoRTH) (N24001964)	3-2022	5/2025 (N.A.) {5/2025}	365.21 (N.A.) {365.21}	112.27	64
		816	REHABILITATION AND UPGRADATION OF KURWAI?MUNGAOLI?CHANDERI ROAD SECTION OF NH-346, FROM DESIGN CHAIN (MoRTH) (N24001965)	3-2022	2/2025 (N.A.) {12/2025}	386.49 (N.A.) {386.49}	77.42	48.77
		817	BALANCE WORK FOR REHABILITATION AND UP-GRADATION OF SIDHI-SINGRAULI FROM KM 82.400 TO KM 187.993 SEC (MoRTH) (N24001966)	12-2020	4/2023 (N.A.) {6/2025}	529.44 (N.A.) {529.44}	378.40	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		818	4L GREENFIELD RUDHI TO DESHGAON (PKG V OF BETUL-KHANDWA/DESHGAON) - N/04015/06003/MP (NHAI) (N24001967)	11-2018	10/2025 (N.A.) {10/2025}	521.21 (N.A.) {521.21}	110.63	49.57
		819	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF JIRAPUR-SUSNER-MP-RJ B (MoRTH) (N24002018)	1-2022	3/2025 (N.A.) {3/2025}	239.72 (232.22) {232.22}	73.40	100
		820	UPGRADATION OF DINDORI-SAGARTOLA-KABICHABUTRA (MP-CG BORDER) SECTION OF NH -45 FROM KM 0+00(DESIGN) (MoRTH) (N24002019)	1-2022	9/2025 (N.A.) {9/2025}	329.14 (319.09) {319.09}	52.70	50.12
		821	CONSTRUCTION OF KAITHI-PADARIA KALA BYPASS, PATNA-TAMOLI BYPASS, JASO BYPASS , NAGOD BYPASS (TOTAL L (MoRTH) (N24002020)	3-2022	10/2025 (N.A.) {10/2025}	158.36 (158.00) {158.36}	22.68	30
		822	BALANCE WORK OF 4L OF NAURADEHI SANCTUARY DE-SCOPED STRETCH OF HIRAN RIVER TO SINDOOR RIVER FROM KM. (NHAI) (N24002067)	1-2021	7/2023 (N.A.) {4/2025}	178.18 (N.A.) {178.18}	161.64	94.65
		823	CONSTRUCTION OF 4-LANE FROM BARELA TO MANEGAON SECTION OF NH-30 FROM DESIGN CH. 2.900 TO DESIGN CH. (NHAI) (N24002068)	12-2022	3/2025 (N.A.) {12/2025}	652.33 (N.A.) {652.33}	334.34	73.16
		824	CONSTRUCTION OF ADDITIONAL 3 LANE WITH PAVED SHOULDER (DESIGN LENGTH 8.87 KM) AS REALIGNMENT OF BAKA (NHAI) (N24002069)	7-2022	12/2024 (N.A.) {12/2024}	209.29 (N.A.) {209.29}	140.22	100
		825	INDORE - EDLABAD (PKG-II) [TEJAJINAGAR TO BALWARA] (NHAI) (N24002070)	1-2022	1/2025 (N.A.) {1/2026}	1,162.80 (N.A.) {1,162.80}	537.71	80.5

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		826	CONSTRUCTION OF (I) 4-LANE HIGHWAY FROM VIDISHA TO HINOTIYA FROM KM. 0.000 TO KM. 27.000 (LENGTH=27 (NHAI) (N24002077)	9-2022	12/2025 (N.A.) {12/2025}	1,000.63 (N.A.) {1,000.63}	210.15	53.86
		827	FOUR LANING OF RAGHOGARH (DESIGN CH.29.300/EXISTING CH. 29.555) TO NANASA (DESIGN CH.92.971/EXISTING (NHAI) (N24002166)	3-2024	3/2026 (01-03-2026) {3/2026}	799.20 (N.A.) {799.20}	306.28	35.1
		828	BALANCE WORKS OF 4 LANE DIVIDED CARRIAGEWAY OF MISSING LINK SECTION OF NH-39 (REWA BYPASS) FROM JUNC (NHAI) (N24002200)	4-2024	4/2026 (N.A.) {4/2026}	355.36 (N.A.) {355.36}	66.14	34.4
		829	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 (MoRTH) (N24000513)	3-2015	8/2017 (01-12-2023) {6/2025}	511.83 (N.A.) {511.83}	478.84	93.06
		830	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN (NHAI) (N24000709)	12-2017	2/2020 (01-12-2024) {12/2024}	950.27 (N.A.) {786.43}	643.90	99.5
	<u>SOCIAL JUSTICE</u>	831	CENTRE FOR DISABILITY SPORTS (CPWD) (N38000001)	2-2019	3/2024 (N.A.) {3/2024}	170.99 (N.A.) {170.99}	162.63	100
	<u>URBAN DEVELOPMENT</u>	832	BHOPAL METRO RAIL (MPMRCL) (N28000124)	11-2018	2/2023 (01-06-2028) {6/2028}	6,941.40 (N.A.) {6,941.40}	3,043.74	42.16
		833	INDORE METRO RAIL (MPMRCL) (N28000125)	11-2018	2/2023 (01-12-2028) {12/2028}	7,500.80 (N.A.) {7,500.80}	3,798.28	53.54
<u>MAHARASHTRA</u>	<u>CIVIL AVIATION</u>	834	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT (AAI) (N04000079)	3-2017	4/2021 (01-12-2023) {12/2023}	475.39 (N.A.) {533.56}	533.14	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		835	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM (AAI) (N04000096)	6-2017	12/2020 (01-04-2024) {4/2024}	255.68 (270.00) {270.00}	267.86	100
	COAL	836	AMALGAMATED YEKONA-I YEKONA-II (WCL) (N06000132)	8-2015	3/2025 (N.A.) {3/2025}	727.28 (N.A.) {727.28}	530.02	86
		837	UKNI DEEP OC (WCL) (N06000179)	1-2019	3/2021 (01-03-2025) {3/2025}	237.06 (N.A.) {318.14}	163.86	91
		838	GHONSA EXPANSION DEEP OC (WCL) (N06000205)	3-2021	3/2028 (N.A.) {3/2029}	184.71 (N.A.) {241.72}	9.25	6
		839	SASTI EXPANSION OC (WCL) (N06000206)	8-2020	3/2026 (N.A.) {3/2026}	319.04 (N.A.) {371.59}	68.64	24
		840	DHUPTALA OC(SASTI UG TO OC) (WCL) (N06000209)	10-2021	3/2028 (N.A.) {3/2028}	711.00 (N.A.) {720.87}	159.15	33
		841	ADASA UG TO OC (1.50 MTY) (WCL) (N06000219)	11-2018	3/2024 (01-03-2025) {3/2025}	316.00 (N.A.) {333.43}	208.20	78
		842	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) (WCL) (N06000222)	2-2020	3/2027 (N.A.) {3/2027}	822.88 (N.A.) {1,184.33}	578.89	48
		843	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) (WCL) (N06000226)	9-2018	3/2024 (01-03-2025) {3/2025}	235.90 (N.A.) {313.34}	116.46	87
		844	SAONER UG MINE I EXPANSION (WCL) (N06000251)	1-2022	3/2028 (N.A.) {3/2028}	228.64 (N.A.) {253.51}	118.34	27

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		845	SINGHORI DEEP OC (WCL) (N06000252)	5-2022	3/2029 (N.A.) {3/2029}	335.75 (N.A.) {421.84}	22.01	16
		846	MAKARDHOKDA I EXPANSION OC (WCL) (N06000253)	6-2022	3/2026 (N.A.) {3/2026}	361.87 (N.A.) {497.06}	33.90	12
		847	BHATADI EXPANSION OC (WCL) (N06000254)	5-2022	3/2028 (N.A.) {3/2028}	580.60 (N.A.) {729.86}	61.33	17
		848	NEW MAJARI UG TO OC (3.0 MTY) (WCL) (N06000255)	9-2022	3/2027 (N.A.) {3/2027}	402.27 (N.A.) {496.38}	47.99	27
		849	BHANEKAON OC (1.15MTY) (WCL) (N06000256)	9-2022	3/2028 (N.A.) {3/2028}	405.20 (N.A.) {494.60}	10.21	7
		850	GOKUL EXPANSION OC (WCL) (N06000264)	4-2021	3/2026 (N.A.) {3/2026}	309.58 (N.A.) {456.95}	3.65	7
		851	KOLGAON EXPANSION (DEEP) OC (WCL) (N06000267)	9-2023	3/2027 (N.A.) {3/2027}	198.71 (N.A.) {206.19}	0.55	5
		852	AMALGAMATED GAURI PAUNI EXPANSION OC (WCL) (N06000271)	3-2024	3/2030 (N.A.) {3/2030}	1,225.21 (N.A.) {1,428.25}	52.83	17
		853	GAURI CENTRAL OCM (WCL) (N06000278)	6-2024	3/2030 (N.A.) {3/2030}	973.07 (N.A.) {1,015.07}	-	0
		854	BALLARPUR NORTHWEST OC MINE (WCL) (N06000282)	12-2022	3/2029 (N.A.) {3/2029}	360.18 (N.A.) {360.18}	-	0
		855	NORTHERN EXTENSION OF MUNGOLI NIRGUDA DEEP OC (WCL) (N06000283)	6-2024	3/2029 (N.A.) {3/2029}	1,024.91 (N.A.) {1,184.44}	-	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		856	AMALGAMATED GONDEGAON - GHATROHAN EXPANSION OCM (WCL) (N06000284)	9-2024	3/2029 (N.A.) {3/2029}	668.54 (N.A.) {871.59}	-	0
		857	WAGHODA UG (WCL) (N06000293)	1-2025	3/2030 (N.A.) {3/2030}	379.30 (N.A.) {379.30}	-	0
		858	KOLARPIMPRI EXPANSION OCM (2.50 MTY) (WCL) (N06000294)	2-2025	3/2030 (N.A.) {3/2030}	630.37 (N.A.) {630.37}	-	0
	DEPARTMENT OF HIGHER EDUCATION	859	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI (CPWD EDUCATION) (N28000117)	1-2018	7/2020 (01-11-2023) {2/2024}	223.37 (275.00) {230.00}	141.16	100
	HEALTH AND FAMILY WELFARE	860	500 BEDDED HOSPITAL INCLUDING 50 SUPERSPECIALITY BEDS FOR ESIC AT PUNE (CPWD) (N21000033)	7-2022	9/2025 (N.A.) {9/2025}	429.25 (N.A.) {429.25}	99.08	0
	PETROLEUM	861	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS (ONGC) (N16000213)	12-2015	4/2018 (01-12-2023) {6/2025}	3,190.69 (3,375.90) {3,375.90}	3,051.26	89.5
		862	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV (ONGC) (N16000358)	4-2019	3/2022 (01-06-2024) {6/2025}	3,228.80 (3,976.67) {3,976.67}	3,867.19	100
		863	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND (GAIL) (N16000430)	5-2019	4/2025 (01-10-2025) {10/2025}	8,797.00 (11,256.00) {11,256.00}	6,694.98	84.5
		864	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL (BPCL) (N16000442)	4-2021	6/2024 (N.A.) {4/2025}	1,164.69 (N.A.) {1,164.69}	893.78	84.1

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		865	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY (IOCL) (N16000446)	9-2021	10/2023 (01-06-2025) {6/2025}	378.00 (N.A.) {378.00}	142.31	90.6
		866	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI (BPCL) (N16000452)	5-2022	3/2024 (N.A.) {9/2024}	423.39 (N.A.) {423.39}	268.34	76
		867	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) (IOCL) (N16000456)	9-2022	8/2025 (N.A.) {3/2026}	165.00 (N.A.) {165.00}	79.17	69.8
		868	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK (ONGC) (N16000470)	6-2022	10/2025 (N.A.) {2/2026}	4,144.41 (6,406.90) {6,406.90}	3,203.26	80.5
		869	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS (IOCL) (N16000487)	3-2022	3/2030 (N.A.) {9/2031}	865.00 (N.A.) {865.00}	66.06	2.8
		870	ANDHERI RESIDENTIAL TOWERS MUMBAI (IOCL) (N16000503)	6-2017	5/2025 (01-06-2026) {6/2026}	281.35 (389.67) {389.67}	218.84	50.8
		871	CONSTRUCTION OF ADDITIONAL TANKAGES AND ALLIED FACILITIES AT JNPT TERMINAL (IOCL) (N16000504)	4-2022	10/2024 (01-08-2026) {8/2026}	341.43 (436.14) {436.14}	244.76	49.5
		872	INSTALLATION OF INDEPENDENT DE- AROMATIZED SOLVENTS PRODUCTION FACILITIES AT MUMBAI REFINERY (BPCL) (N16000507)	3-2023	7/2025 (N.A.) {7/2025}	405.00 (N.A.) {405.00}	189.80	81.5
		873	PART REPLACEMENT PIPELINE PROJECT (PRPP) (ONGC) (N16000515)	11-2022	5/2024 (01-12-2024) {11/2025}	1,219.48 (N.A.) {1,145.10}	1,145.10	87

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		874	POL AND LOBS INSTALLATIONS WITH RECEIPT PIPELINES AT RASAYANI (BPCL) (N16000519)	5-2023	5/2026 (N.A.) {5/2026}	2,585.00 (N.A.) {2,585.00}	525.74	56.5
		875	MHN TCPP PGC BGC PROJECT (MTPBP) (ONGC) (N16000526)	2-2024	5/2026 (N.A.) {5/2026}	2,329.45 (N.A.) {2,354.23}	672.00	45.9
		876	PRP-VIII GROUP B (NH AND BS ASSET) (ONGC) (N16000533)	6-2024	5/2026 (N.A.) {2/2026}	2,379.84 (N.A.) {2,379.84}	1,646.11	57.8
		877	HP TDAE UNIT IN MUMBAI REFINERY (HPCL) (N16000534)	6-2024	4/2026 (N.A.) {4/2026}	240.00 (N.A.) {240.00}	27.90	33.6
		878	INTEGRATED DEVELOPMENT OF 4 CONTRACT AREAS UNDER DSF2 (ONGC) (N16000537)	5-2023	4/2027 (N.A.) {4/2027}	6,183.79 (N.A.) {6,183.79}	-	12.6
		879	LUBE MODERNIZATION AND BOTTOM UPGRADATION PROJECT (HPCL) (N16000540)	12-2024	3/2028 (N.A.) {3/2028}	4,679.00 (N.A.) {4,679.00}	177.41	4.2
	POWER	880	BIKANER SOLAR POWER PROJECT (SJVN) (N18000335)	4-2022	5/2024 (N.A.) {9/2025}	5,491.89 (532.00) {5,491.89}	4,374.00	80.35
		881	TS FOR EVACUATION OF 7GW RE INJECTION AT KHAVDA PS UNDER PHASE-IV PART E4 (PGCIL) (N18000377)	11-2023	7/2025 (N.A.) {11/2025}	224.00 (N.A.) {224.00}	15.68	7
	RAILWAYS	882	AHMEDNAGAR-PARLI VAIJNATH(NL) CR (CR) (220100181)	2-1997	3/2026 (N.A.) {1/2026}	2,539.00 (N.A.) {4,957.27}	4,909.30	97

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		883	MUMBAI URBAN TRANSPORT PROJECT PHASE-II (MRTPT) (N22000092)	4-2008	3/2014 (N.A.) {3/2014}	8,087.11 (N.A.) {918.53}	7,349.29	0
		884	WARDHA-NANDED MAHARASHTRA (CR) (N22000231)	4-2008	3/2027 (N.A.) {1/2026}	3,445.48 (N.A.) {3,445.34}	3,156.47	47
		885	KALYAN-KASARA 3RD LINE (CR) (N22000233)	4-2011	12/2025 (N.A.) {12/2026}	792.89 (N.A.) {1,395.79}	882.04	50
		886	WARDHA-SEWAGRAM NGP 3RD LINE (CR) (N22000250)	4-2012	12/2025 (N.A.) {2/2026}	540.02 (N.A.) {540.02}	737.54	80
		887	WARDHA-BALHARSHAH - 3RD LINE (132 KM) (CR) (N22000356)	2-2015	12/2025 (N.A.) {3/2026}	1,384.72 (N.A.) {1,384.72}	1,590.45	67
		888	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) (CR) (N22000358)	2-2015	3/2027 (N.A.) {3/2027}	2,449.91 (N.A.) {2,449.91}	1,761.99	50
		889	PUNE-MIRAJ-LONDA (467 KM) (CR) (N22000359)	2-2015	2/2025 (N.A.) {5/2025}	3,627.47 (3,627.00) {7,037.24}	4,742.07	84
		890	DAUND - MANMAD (236 KM) (CR) (N22000360)	2-2016	12/2025 (N.A.) {1/2026}	2,081.27 (N.A.) {2,081.27}	2,768.50	88
		891	MANMAD - JALGAON - 3RD LINE (160 KM) (CR) (N22000361)	2-2016	12/2024 (N.A.) {3/2026}	1,035.16 (N.A.) {1,558.75}	1,692.15	97
		892	WARDHA - NAGPUR - 4TH LINE (76 KM) (CR) (N22000362)	2-2016	12/2025 (N.A.) {2/2026}	638.00 (N.A.) {637.95}	968.65	80

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		893	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) (SECR) (N22000420)	9-2016	12/2024 (N.A.) {12/2026}	3,544.92 (N.A.) {3,544.25}	3,081.12	95
		894	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM (WR) (N22000434)	3-2010	10/2024 (N.A.) {3/2024}	311.00 (N.A.) {311.36}	-	0
		895	WADSA-GADHCHIROLI NEW LINE (52.36 KM) (SECR) (N22000480)	6-2018	3/2027 (N.A.) {12/2026}	1,886.05 (N.A.) {1,880.61}	807.87	25
		896	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (N22000511)	8-2022	8/2027 (N.A.) {3/2029}	955.00 (N.A.) {2,089.25}	117.54	0
		897	SOLAPUR-TULJAPUR-OSMANABAD (UMBRELLA WORK) (CR) (N22000513)	1-2019	3/2028 (N.A.) {12/2027}	904.92 (N.A.) {2,933.01}	1,150.11	10
		898	DHULE (BORVIHAR)-NARDANA (UMBRELLA WORK) (CR) (N22000514)	1-2019	12/2026 (N.A.) {3/2028}	492.76 (N.A.) {1,158.99}	234.48	5
		899	KALYAN-MURBAD VIA ULHASNAGAR (UMBRELLA WORK) (CR) (N22000515)	2-2023	3/2027 (N.A.) {3/2027}	836.12 (N.A.) {836.12}	9.29	0
		900	BARAMATI - LONAND (CR) (N22000615)	2-1999	3/2027 (N.A.) {3/2027}	736.44 (N.A.) {1,843.90}	712.06	50
		901	MUMBAI URBAN TRANSPORT PROJECT IIIA (MRVC) (N22000627)	4-2019	12/2027 (N.A.) {12/2027}	33,690.00 (N.A.) {33,690.00}	2,156.62	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		902	NAGPUR- NAGBHIR RAILWAY LINE GAUGE CONVERSION PROJECT (MRIDC) (N22000629)	10-2019	6/2024 (N.A.) {10/2025}	1,400.00 (N.A.) {2,383.00}	1,791.72	87
	ROAD TRANSPORT AND HIGHWAYS	903	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH (MoRTH) (N24001448)	11-2021	2/2022 (N.A.) {2/2022}	223.35 (N.A.) {223.35}	209.36	87.88
		904	REPANPALLI TO SIRONCHA (MoRTH) (N24001468)	3-2022	6/2022 (N.A.) {6/2024}	282.07 (N.A.) {282.07}	34.65	0
		905	TUNNEL AT KHAMBATAKI GHAT SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 (NHAI) (N24001486)	2-2019	2/2022 (01-12-2024) {8/2025}	493.00 (N.A.) {493.00}	409.36	77.64
		906	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL-ALANDI SECTION (NHAI) (N24001488)	9-2021	9/2023 (01-12-2024) {8/2025}	618.45 (N.A.) {618.45}	672.67	96.9
		907	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) (NHAI) (N24001493)	12-2022	12/2024 (N.A.) {11/2025}	1,749.86 (N.A.) {1,749.86}	1,858.98	69.14
		908	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 () (NHAI) (N24001495)	11-2022	11/2024 (N.A.) {9/2025}	930.00 (N.A.) {930.00}	675.62	77.15
		909	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001502)	9-2021	9/2023 (01-07-2025) {8/2025}	624.45 (580.15) {580.15}	420.42	0.5
		910	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001503)	9-2021	9/2023 (01-01-2025) {3/2025}	667.66 (666.21) {666.21}	610.63	3

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		911	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) (NHAI) (N24001504)	5-2022	5/2024 (01-06-2025) {6/2025}	1,260.00 (N.A.) {1,260.00}	665.73	99
		912	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) (NHAI) (N24001505)	3-2022	3/2024 (01-06-2025) {6/2025}	1,549.02 (N.A.) {1,549.02}	699.00	87.24
		913	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) (NHAI) (N24001506)	2-2022	2/2024 (01-06-2025) {6/2025}	2,747.00 (N.A.) {2,747.00}	1,130.30	84.22
		914	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) (NHAI) (N24001507)	11-2022	5/2024 (01-06-2025) {6/2025}	1,124.00 (N.A.) {1,124.00}	483.84	75.15
		915	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) (NHAI) (N24001508)	11-2022	10/2024 (01-06-2025) {6/2025}	1,450.00 (N.A.) {1,450.00}	718.65	86.02
		916	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE) (NHAI) (N24001521)	11-2022	10/2024 (01-07-2025) {7/2025}	990.00 (N.A.) {990.00}	406.91	77.38
		917	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) (NHAI) (N24001546)	1-2023	1/2025 (N.A.) {1/2025}	1,025.20 (N.A.) {1,025.20}	457.33	44.61
		918	BALANCE WORKS OF 4L PANVEL-INDAPUR SECTION OF NH-66 (OLD NH-17) FROM KM 42.300 (KASU) TO KM 84.600 () (NHAI) (N24001607)	10-2022	5/2024 (01-12-2025) {12/2025}	332.00 (N.A.) {332.00}	283.14	74.75
		919	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) (NHAI) (N24001608)	9-2021	7/2025 (N.A.) {7/2025}	2,208.68 (N.A.) {2,208.68}	565.20	76.26

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		920	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH-66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO (NHAI) (N24001609)	1-2023	12/2023 (01-06-2025) {9/2025}	151.26 (N.A.) {151.26}	153.77	89.8
		921	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL ? ALANDI S (NHAI) (N24001610)	1-2022	5/2024 (01-03-2025) {8/2025}	1,833.73 (N.A.) {1,833.73}	554.81	96.94
		922	FOUR LANING OF AURANGABAD-PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA . (NHAI) (N24001795)	10-2022	7/2024 (01-06-2025) {12/2024}	490.40 (N.A.) {289.00}	275.78	96
		923	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B (NHAI) (N24001796)	3-2022	10/2024 (01-04-2025) {4/2025}	1,013.33 (1,013.33) {1,111.33}	355.07	62.01
		924	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 (NHAI) (N24001797)	10-2021	1/2024 (N.A.) {5/2025}	815.77 (N.A.) {815.77}	732.70	100
		925	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH-53 (NHAI) (N24001798)	2-2021	11/2023 (N.A.) {5/2025}	540.21 (N.A.) {540.21}	457.12	100
		926	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J (NHAI) (N24001799)	2-2021	10/2023 (N.A.) {12/2025}	1,166.96 (N.A.) {1,251.00}	1,098.21	81.17
		927	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) (NHAI) (N24001804)	12-2019	9/2022 (01-06-2024) {12/2025}	1,654.07 (N.A.) {980.00}	887.38	97.66
		928	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG ? II) (NHAI) (N24001834)	5-2023	5/2025 (N.A.) {5/2025}	839.00 (N.A.) {839.00}	478.38	58.8

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		929	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG?III) (NHAI) (N24001835)	5-2023	5/2025 (N.A.) {5/2025}	986.00 (N.A.) {986.00}	580.10	56.4
		930	REHABILITATION AND UP-GRADATION TO 4 LANE ROAD WITH PAVED SHOULDER CONFIGURATION OF SECTION FROM UND (MoRTH) (N24001880)	3-2022	7/2025 (N.A.) {7/2025}	778.18 (N.A.) {778.18}	135.78	0
		931	CONSTRUCTION OF NEW FOUR LANE BYPASS TO PARBHANI CITY (PARWA TO ASOLA) KM 463/265 TO KM 481/180 (DES (MoRTH) (N24001882)	3-2022	10/2024 (N.A.) {10/2024}	496.64 (N.A.) {496.64}	-	8
		932	CONSTRUCTION OF 4 LANE FLYOVER AT NAGPUR RTO CHOWK TO NAGPUR UNIVERSITY CAMPUS FROM CH 2/250 TO 5/10 (MoRTH) (N24001883)	3-2021	3/2024 (N.A.) {4/2024}	478.83 (N.A.) {478.83}	233.48	65
		933	REHABILITATION AND UPGRADATION OF SATANA TO MANGRUL (CHANDWAD) SECTION OF NH752 G DESIGN CH: KM 64.0 (MoRTH) (N24001884)	3-2023	5/2025 (N.A.) {5/2025}	428.80 (N.A.) {428.80}	54.11	30.69
		934	REHABILITATION AND UP-GRADATION OF JINTUR- SHIRAD SHAHAPUR SECTION KM 258.300 TO KM 306.300 [DESIGN (MoRTH) (N24001885)	2-2023	12/2024 (N.A.) {12/2024}	414.81 (N.A.) {414.81}	-	0
		935	DEVELOPMENT/WIDENING OF TALEGAON ? CHAKAN ? SHIKRAPUR ? NHAVARA SECTION OF NH 548DG (NHAVARA TO CHOU (MoRTH) (N24001886)	10-2022	8/2024 (N.A.) {8/2024}	304.68 (N.A.) {304.68}	97.09	59
		936	REHABILITATION AND UPGRADATION OF BHOKARDAN TO KUMBHARI FATA DESIGN CH. (KM 13+500 TO 17+00) AND RAJ (MoRTH) (N24001887)	8-2022	6/2024 (N.A.) {6/2024}	291.37 (N.A.) {291.37}	157.59	97.95

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		937	UP-GRADATION OF TIRORA-GONDIA, STATE HIGHWAY FROM EXISTING KM 163+213 (ON SH-335, TIRORA) TO KM 191+ (MoRTH) (N24001888)	8-2021	4/2023 (N.A.) {5/2024}	288.14 (N.A.) {288.14}	72.78	40.45
		938	2 LANE + PS PIMPLNER TO SATANA -[DESIGN CHAINAGE KM 21.427 TO 64.00] OF NH-752G] (MoRTH) (N24001889)	9-2019	7/2021 (N.A.) {12/2023}	277.81 (N.A.) {277.81}	155.01	80.26
		939	REHABILITATION AND UPGRADATION OF PARLI TO SIRSALA SECTION OF NH-361F (KM 136+700 TO 115+000) (LENGT (MoRTH) (N24001890)	2-2023	12/2024 (N.A.) {12/2024}	261.82 (N.A.) {261.82}	70.59	46
		940	BALANCE WORK OF REHABILITATION AND UP-GRADATION TO NH-166F FROM MAHAD JUNCTION (AT KM 123/400 ON NH- (MoRTH) (N24001891)	7-2021	11/2023 (N.A.) {3/2024}	256.54 (N.A.) {256.54}	80.10	60
		941	REHABILITATION AND UPGRADATION OF SHIRAPUR JUNCTION TO SHIVAJI CHOWK (DESIGN CHAINAGE KM. 130+00 TO (MoRTH) (N24001892)	2-2023	12/2024 (N.A.) {12/2024}	245.61 (N.A.) {245.61}	43.39	33
		942	2 LANE + PS ASTHAMODE - TIVATYAL [DESIGN CH. KM 24.300 - 62.00] [KM 134.98-172.95 OF NH-63] (MoRTH) (N24001894)	9-2019	7/2021 (N.A.) {12/2023}	228.82 (N.A.) {228.82}	145.50	93.27
		943	REHABILITATION AND UPGRADATION TO TWO LANES WITH PAVED SHOULDER CONFIGURATION FROM WATUR TO CHARTHANA (MoRTH) (N24001895)	11-2021	9/2023 (N.A.) {12/2023}	228.01 (N.A.) {228.01}	106.11	99.5
		944	UPGRADATIOBN AND REHABILITATION OF SECTION OF NH 361 F FROM PARLI (00/000) TO GANGAKHED (30/400) TO (MoRTH) (N24001896)	11-2021	9/2023 (N.A.) {4/2024}	224.44 (N.A.) {224.44}	75.34	45.63

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		945	REHABILITATION AND UP-GRADATION OF SABALKHED TO ASHTI SECTION FROM KM 37+900 TO KM 55+100 AND CHINCH (MoRTH) (N24001902)	12-2022	9/2024 (N.A.) {9/2024}	213.32 (N.A.) {213.32}	20.00	34
		946	REHABILITATION AND UP-GRADATION OF MUDKHED TO NANDED SECTION FROM KM. 372+000 TO KM 388+400 OF NH 16 (MoRTH) (N24001903)	8-2022	4/2025 (N.A.) {4/2025}	206.54 (N.A.) {206.54}	21.36	10
		947	KOPARGAON TO SAVALI VIHIR SECTION (MoRTH) (N24001904)	9-2022	7/2024 (N.A.) {7/2024}	195.38 (N.A.) {195.38}	29.59	19.76
		948	CONSTRUCTION OF MAJOR BRIDGE ACROSS MANJRA RIVER NEAR YESGI VILLAGE @ KM, 166/500 ON NH 63 TQ BILOLI (MoRTH) (N24001905)	10-2021	8/2023 (N.A.) {12/2023}	188.69 (N.A.) {188.69}	111.25	100
		949	UP-GRADATION TO 4 LANING OF DAULTABAD T-POINT TO MALIWADA [FROM DESIGN KM.0.000 TO KM 4.000] AND UPG (MoRTH) (N24001906)	8-2022	3/2024 (N.A.) {3/2024}	185.59 (N.A.) {185.59}	63.56	48
		950	CONSTRUCTION OF SIX LANE FLYOVER AT KATRAJ JUNCTION AT KM, 3/880 OF NH 548-DD (VADGAON - KATRAJ - KO (MoRTH) (N24001907)	6-2021	2/2024 (N.A.) {3/2024}	169.15 (N.A.) {169.15}	36.94	35.96
		951	UPGRADATION OF EXHISTING 2 LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDERS RIGID PAVEMENT FROM DESI (MoRTH) (N24001908)	12-2021	5/2024 (N.A.) {5/2024}	167.97 (N.A.) {167.97}	35.28	36.76
		952	STRENGTHING AND WIDINING OF EXISTING CARRIAGEWAY TO 10 M IN KM, 156/160 TO 229/160 (TEMBHURNI - KUSL (MoRTH) (N24001909)	11-2021	6/2024 (N.A.) {6/2024}	157.72 (N.A.) {157.72}	80.37	65.94

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		953	REHABILITATION AND UPGRADATION OF JAMKHEDE TO SAUTADA SECTION OF NH548 D (FROM KM 195.375 TO KM 208.7 (MoRTH) (N24001910)	9-2022	7/2024 (N.A.) {7/2024}	157.62 (N.A.) {157.62}	13.86	17.03
		954	PANGAON TO DHARMAPURI AND PARALI TO INJEGAON 2L+PS (MoRTH) (N24001911)	3-2018	7/2024 (N.A.) {12/2023}	152.03 (N.A.) {152.03}	81.35	97.57
		955	4L OF INDORA CHOWK TO PACHPAOLI AND AGRASEN CHOWK - ASHOKA CHOWK (NHAI) (N24002071)	3-2023	6/2026 (N.A.) {6/2026}	998.27 (N.A.) {998.27}	348.48	48.34
		956	IMPROVEMENT OF EXISTING ALIGNMENT OF PANDHARPUR TOWN PART BYPASSED SECTION FROM WAKHARI TO LORD VITT (NHAI) (N24002072)	7-2022	10/2025 (N.A.) {10/2025}	150.21 (150.21) {150.21}	33.70	6
		957	STRENGTHENING OF 6-LANE PIMPALGAON- NASHIK-GONDE (KM. 380 - KM. 440) SECTION OF NH-3 IN MAHARASHTRA U (NHAI) (N24002137)	2-2024	3/2025 (N.A.) {3/2025}	175.00 (206.49) {206.49}	201.00	100
		958	REHABILITATION/UPGRADATION OF EXISTING HIGHWAY TO 2L+PS/4 LANE OF DHAWALI TO RAJOLI FROM DESIGN KM.1 (MoRTH) (N24002169)	3-2022	9/2025 (N.A.) {9/2025}	316.44 (N.A.) {316.44}	-	0
		959	REHABILITATION/ UPGRADATION OF EXISTING HIGHWAY TO FOUR LANE STANDARDS IN KURKHEDA TOWN FROM (KM.413 (MoRTH) (N24002170)	3-2022	5/2025 (N.A.) {5/2025}	163.86 (N.A.) {163.86}	-	0
		960	REHABILITATION AND UP-GRADATION FOR TALERE A?? GAGANBAWDAA?? KOLHAPUR ROAD (NH-166G) STRETCHES START (MoRTH) (N24002171)	2-2023	4/2025 (N.A.) {4/2025}	249.13 (N.A.) {249.13}	-	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		961	UP-GRADATION TO 4 LANE CONFIGURATION FOR THE WORK OF PETH NAKA TO SANGLI ROAD, NH-166H, FROM KM 0+00 (MoRTH) (N24002172)	2-2023	12/2025 (N.A.) {12/2025}	856.82 (N.A.) {856.82}	-	0
		962	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF MAHUD SANGOLA ROAD NH (MoRTH) (N24002173)	2-2023	4/2025 (N.A.) {4/2025}	253.78 (N.A.) {253.78}	-	0
		963	UP-GRADATION TO FOUR LANE/ TWO LANE WITH PAVED SHOULDERS CONFIGURATION OF KALYAN - MURBAD - MALSHEJ (MoRTH) (N24002174)	2-2023	8/2026 (N.A.) {8/2026}	984.07 (N.A.) {984.07}	-	0
		964	CONSTRUCTION OF FOUR-LANE CONCRETE ROAD FROM POLICE HEADQUARTER GONDIA CITY TO RAWANWADI VILLAGE (BI (MoRTH) (N24002175)	2-2023	8/2025 (N.A.) {8/2025}	328.11 (N.A.) {328.11}	-	0
		965	REHABILITATION/UP GRADATION OF KARANJA ? KHERDA - MURTIZAPUR SECTION TO 4LANE+PAVED SHOULDER STAND A (MoRTH) (N24002176)	3-2023	2/2026 (N.A.) {2/2026}	594.44 (N.A.) {594.44}	-	0
		966	REHABILITATION / UPGRADATION TO 4 LANE WITH PAVED SHOULDER OF EXISTING SECTION IN SILLOD TOWN WITH D (MoRTH) (N24002177)	3-2023	7/2025 (N.A.) {7/2025}	153.79 (N.A.) {153.79}	-	0
		967	REHABILITATION, UPGRADATION AND WIDENING OF EXISTING HIGHWAY TO RIGID PAVEMENT 2 LANE WITH PAVED SHO (MoRTH) (N24002178)	2-2023	7/2026 (N.A.) {7/2026}	723.13 (N.A.) {723.13}	-	0
		968	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM (MoRTH) (N24000332)	1-2015	(N.A.) {}	225.81 (N.A.) {225.81}	118.84	94.27

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		969	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN (NHAI) (N24000442)	12-2015	3/2019 (01-11-2023) {7/2025}	649.50 (N.A.) {649.50}	623.82	94.1
		970	NAGPUR RING ROAD PACKAGE-2 (NHAI) (N24000560)	3-2016	7/2019 (01-03-2024) {6/2025}	591.66 (N.A.) {591.66}	632.92	100
		971	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000584)	3-2016	(N.A.) {12/2023}	1,142.62 (1,907.03) {1,142.62}	1,056.08	95.17
		972	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000585)	3-2016	(N.A.) {}	1,101.58 (N.A.) {1,101.58}	608.53	0
		973	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) (NHAI) (N24000656)	3-2017	3/2020 (01-07-2022) {12/2025}	744.64 (N.A.) {1,007.00}	467.65	97.69
		974	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) (NHAI) (N24000659)	3-2017	3/2017 (01-05-2021) {5/2025}	1,059.73 (1,071.00) {1,071.00}	928.19	97.25
		975	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF (NHAI) (N24000851)	3-2018	7/2021 (N.A.) {12/2025}	1,162.92 (1,182.87) {1,182.87}	412.38	64
		976	SARSAM TO KOTHARI (MoRTH) (N24001002)	2-2016	7/2019 (N.A.) {12/2023}	545.64 (N.A.) {545.64}	232.64	93.68
		977	AKOLA TO AKOT (MoRTH) (N24001003)	1-2017	6/2019 (N.A.) {12/2023}	313.95 (N.A.) {313.95}	270.02	98.03
		978	DIGRAS DARWAH KARANJA (MoRTH) (N24001013)	1-2017	6/2019 (N.A.) {12/2023}	391.06 (391.00) {391.06}	287.60	92.76

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		979	DAHEGAON TO KUHI (MoRTH) (N24001017)	1-2017	6/2019 (N.A.) {12/2023}	228.89 (229.00) {228.89}	154.82	99
		980	BHANDARA TO GHOTITOK (MoRTH) (N24001018)	1-2017	6/2019 (N.A.) {6/2019}	392.83 (393.00) {392.83}	264.35	97.5
		981	AMD1 TO SAONER (MoRTH) (N24001021)	1-2017	6/2019 (N.A.) {12/2023}	396.91 (397.00) {396.91}	253.59	98.23
		982	WADI TO ASOLA (MoRTH) (N24001022)	1-2017	9/2019 (N.A.) {12/2023}	363.82 (364.00) {363.82}	154.65	93.15
		983	SHAHPUR PATGAON SECTION I (MoRTH) (N24001027)	1-2018	12/2019 (N.A.) {3/2024}	150.79 (N.A.) {150.79}	81.14	100
		984	JINTUR TO PARBHANI (MoRTH) (N24001039)	1-2017	(N.A.) {12/2023}	356.66 (N.A.) {356.66}	209.48	100
		985	RALEGAON TO RAMTIRTH (MoRTH) (N24001046)	1-2017	7/2019 (N.A.) {8/2023}	210.81 (N.A.) {210.81}	132.00	95.99
		986	VITA TO NAGAJ (MoRTH) (N24001050)	3-2018	12/2019 (N.A.) {12/2023}	304.58 (305.00) {304.58}	154.68	68.39
		987	KARAD PATAN CHIPLUN GUHAGAR (MoRTH) (N24001057)	2-2017	6/2019 (N.A.) {6/2019}	407.19 (407.00) {407.19}	323.02	0
		988	KARWANDI TO RAJURI (MoRTH) (N24001058)	3-2018	12/2019 (N.A.) {3/2024}	276.95 (277.00) {276.95}	160.94	92.06
		989	PALPHATA TO PHULAMBARI (MoRTH) (N24001060)	3-2018	12/2019 (N.A.) {12/2023}	227.19 (227.00) {227.19}	141.92	95

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		990	NANDED TO JALKOT (MoRTH) (N24001069)	12-2017	9/2019 (N.A.) {9/2019}	456.93 (457.00) {456.93}	278.22	95
		991	PUNE TO MALE VILLAGE (MoRTH) (N24001078)	3-2018	12/2019 (N.A.) {12/2023}	228.31 (N.A.) {228.31}	113.29	84.32
		992	ARDHAPUR TO HIMAYATNAGAR (MoRTH) (N24001079)	12-2017	6/2020 (N.A.) {12/2023}	426.06 (426.00) {426.06}	268.96	96.46
		993	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER (MoRTH) (N24001080)	3-2018	12/2019 (N.A.) {10/2023}	256.15 (N.A.) {256.15}	115.53	82
		994	HIMAYATNAGAR TO PHULSAWANGI (MoRTH) (N24001081)	3-2018	12/2019 (N.A.) {12/2023}	294.87 (295.00) {294.87}	183.17	100
		995	PUNE RAIGARH DISTRICT BORDER TO MANGAON (MoRTH) (N24001082)	3-2018	12/2019 (N.A.) {12/2023}	223.46 (N.A.) {223.46}	123.46	100
		996	KOLDE TO KHETIYA (MoRTH) (N24001090)	1-2017	7/2019 (N.A.) {12/2023}	509.18 (N.A.) {509.18}	246.83	92.38
		997	SATARA TO MHASWAD (MoRTH) (N24001092)	1-2017	7/2019 (N.A.) {12/2023}	653.46 (N.A.) {653.46}	369.62	0
		998	SATARA MURVAD PILLOV PANDHARPUR (MoRTH) (N24001095)	1-2017	(N.A.) {6/2024}	388.44 (N.A.) {388.44}	240.05	100
		999	SELDOH TO PANVAR (MoRTH) (N24001097)	7-2018	5/2020 (N.A.) {5/2020}	404.33 (404.00) {404.33}	140.65	100
		1000	MHASWAD TO TEMBHURNI (MoRTH) (N24001099)	1-2017	7/2019 (N.A.) {12/2023}	488.60 (N.A.) {488.60}	279.42	76.5

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1001	KURUDWADI TO PANDHARPUR (MoRTH) (N24001101)	1-2017	7/2019 (N.A.) {11/2023}	307.63 (N.A.) {307.63}	208.22	95.29
		1002	PANDHARPUR TO SANGOLA (MoRTH) (N24001102)	7-2017	7/2019 (N.A.) {12/2023}	218.38 (N.A.) {218.38}	176.99	99.86
		1003	PEN TO KHOPOLI (MoRTH) (N24001106)	3-2018	3/2018 (N.A.) {1/2024}	301.39 (302.00) {301.39}	170.12	82.07
		1004	PANCHARAL TO MANDANGHAR (MoRTH) (N24001107)	7-2018	5/2020 (N.A.) {5/2020}	381.08 (302.00) {381.08}	45.66	0
		1005	KOLHA TO NASRATPUR (MoRTH) (N24001111)	4-2016	4/2019 (N.A.) {8/2024}	281.78 (282.00) {281.78}	77.83	100
		1006	NASRATPUR TO BARASGAON (MoRTH) (N24001112)	7-2016	9/2019 (N.A.) {9/2019}	406.54 (407.00) {406.54}	274.30	0
		1007	INDAPUR TO VADPALE (MoRTH) (N24001114)	1-2017	12/2019 (N.A.) {3/2024}	1,202.52 (1,656.94) {1,202.52}	1,450.82	61.42
		1008	PAITHAN TO SHIRUR (MoRTH) (N24001122)	3-2017	6/2019 (N.A.) {3/2024}	341.80 (N.A.) {341.80}	226.19	79
		1009	SHIRUR TO KHARDA (MoRTH) (N24001123)	2-2017	6/2019 (N.A.) {12/2023}	381.77 (N.A.) {381.77}	199.48	83.93
		1010	AURANGABAD TO SILLIOD (MoRTH) (N24001124)	2-2017	6/2019 (N.A.) {12/2023}	456.32 (541.93) {456.32}	355.54	94.07
		1011	SILLIOD TO FARDAPUR (MoRTH) (N24001125)	2-2017	6/2019 (N.A.) {12/2023}	337.46 (432.98) {337.46}	335.30	91.56

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1012	KUMBHARI PHTA TO DEULGAON RAJA (MoRTH) (N24001127)	2-2017	6/2019 (N.A.) {2/2024}	406.51 (N.A.) {406.51}	340.26	100
		1013	BHOGAN KHURD TO KASHEDI (MoRTH) (N24001132)	9-2017	6/2021 (N.A.) {12/2023}	743.21 (743.00) {743.21}	911.64	88.69
		1014	KANTE TO WAKED (MoRTH) (N24001134)	3-2016	11/2019 (N.A.) {12/2024}	1,230.02 (1,230.00) {1,230.02}	791.80	0
		1015	PARLI PIMPLA DAHIGUDA (MoRTH) (N24001138)	2-2017	6/2019 (N.A.) {8/2023}	205.72 (206.00) {205.72}	813.50	94.1
	URBAN DEVELOPMENT	1016	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) (MMRCL) (N28000086)	7-2013	3/2020 (01-07-2025) {7/2025}	23,136.00 (N.A.) {37,276.00}	28,615.78	94.77
		1017	PUNE METRO RAIL PROJECT (PHASE 1) (MMRC) (N28000121)	12-2016	11/2021 (01-09-2024) {9/2024}	11,420.00 (13,656.22) {13,656.22}	13,088.19	100
		1018	NAGPUR METRO RAIL PROJECT PHASE II (NMRCL) (N28000155)	12-2022	12/2027 (N.A.) {12/2027}	6,708.00 (N.A.) {6,708.00}	895.38	23.82
		1019	PCMC NIGDI PROJECT EXTENSION OF CORRIDOR 1 OF PUNE METRO PHASE 1 (MMRC) (N28000157)	10-2023	1/2027 (N.A.) {1/2027}	910.18 (N.A.) {910.18}	103.13	19.08
		1020	PUNE METRO PHASE-1 EXTENSION FROM SWARGATE TO KATRAJ (MMRC) (N28000160)	9-2024	3/2029 (N.A.) {3/2029}	2,954.53 (N.A.) {2,954.53}	17.35	2.91
MANIPUR	CIVIL AVIATION	1021	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (01-12-2025) {12/2025}	499.00 (N.A.) {499.00}	154.47	40.82

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	1022	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	12/2026 (01-03-2028) {3/2028}	14,322.79 (12,274.06) {22,234.60}	15,485.02	69.2
	ROAD TRANSPORT AND HIGHWAYS	1023	IMPROVEMENT/UPGRADATION OF EXISTING 2- LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (01-06-2025) {12/2025}	379.39 (N.A.) {379.39}	218.03	70.94
		1024	IMPROVEMENT/UPGRADATION OF EXISTING 2- LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8-2020	4/2022 (N.A.) {8/2026}	228.97 (N.A.) {228.97}	-	4.6
		1025	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (01-03-2025) {12/2025}	226.32 (N.A.) {226.32}	105.78	74.48
		1026	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (01-01-2025) {9/2025}	188.36 (N.A.) {188.36}	126.71	99.02
		1027	IMPAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3-2021	12/2022 (01-03-2025) {3/2026}	195.14 (N.A.) {195.14}	61.81	0
		1028	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (01-09-2024) {11/2025}	234.08 (N.A.) {234.08}	139.45	92.82
		1029	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (01-05-2025) {10/2025}	211.70 (N.A.) {211.70}	83.79	71.06
		1030	IMPAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (01-03-2025) {10/2025}	467.00 (N.A.) {467.00}	193.81	79.81
		1031	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (01-01-2025) {1/2025}	185.80 (N.A.) {185.80}	117.78	100
		1032	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (01-01-2025) {12/2025}	483.87 (N.A.) {483.87}	278.89	92.94

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1033	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (01-02-2025) {3/2025}	198.77 (N.A.) {198.77}	127.86	100
		1034	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (01-03-2025) {12/2025}	673.27 (N.A.) {673.27}	382.37	80.28
		1035	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (01-01-2025) {1/2026}	477.86 (N.A.) {477.86}	246.09	84.87
		1036	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (01-11-2024) {12/2025}	311.18 (N.A.) {311.18}	190.96	83.78
		1037	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (01-10-2024) {2/2025}	467.41 (N.A.) {467.41}	264.83	100
		1038	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (01-07-2025) {12/2025}	579.63 (N.A.) {579.63}	180.72	72.5
		1039	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (01-03-2025) {7/2025}	310.76 (N.A.) {310.76}	129.15	96.77
		1040	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (01-01-2026) {3/2026}	410.68 (N.A.) {410.68}	152.34	70.11
		1041	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (01-09-2025) {12/2025}	504.76 (N.A.) {504.76}	190.26	78.25
		1042	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (01-02-2025) {3/2025}	152.11 (N.A.) {152.11}	73.48	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1043	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (01-08-2025) {8/2025}	315.56 (N.A.) {315.56}	137.81	88.74
		1044	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (01-12-2025) {3/2026}	760.16 (N.A.) {760.16}	157.48	62.92
		1045	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (01-03-2026) {3/2026}	578.98 (N.A.) {578.98}	153.92	71.25
		1046	MARREM KHULLEN TO JESSAMI SECTION IMPHAL - UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	17.79	15
		1047	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	13.14	18.04
		1048	JESSAMI TO LAYNEN BRIDGE UKHRUL - JESSAMI PKG-7 (NHIDCL) (N24002227)	3-2023	6/2026 (N.A.) {6/2026}	164.89 (N.A.) {164.89}	3.83	9.78
		1049	IMPHAL-KOHIMA ROAD PKG-5A (NHIDCL) (N24002232)	9-2020	8/2026 (N.A.) {8/2026}	228.97 (N.A.) {228.97}	-	10.13
		1050	CHOITHAR TO MARREM KHULLEN SECTION IMPHAL - UKHRUL - JESSAMI PKG-5 (NHIDCL) (N24002242)	3-2023	3/2027 (N.A.) {3/2027}	564.05 (N.A.) {564.05}	-	0
		1051	IMPHAL - KHONGSANG - JIRIBAM PKG-2 (NHIDCL) (N24002244)	3-2021	3/2026 (N.A.) {3/2026}	195.14 (N.A.) {195.14}	4.42	11.53
		1052	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (01-06-2025) {9/2025}	292.24 (N.A.) {292.24}	130.66	90.69

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA		1053	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (01-06-2025) {10/2025}	365.53 (N.A.) {365.53}	156.31	77.69
		1054	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (01-01-2025) {12/2025}	167.95 (204.12) {167.95}	88.05	69.89
		1055	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (01-02-2025) {12/2025}	177.76 (N.A.) {177.76}	89.67	80.53
	DEPARTMENT OF HIGHER EDUCATION	1056	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (01-07-2025) {7/2025}	484.32 (429.70) {494.52}	270.55	84
	ROAD TRANSPORT AND HIGHWAYS	1057	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM () (NHIDCL) (N24001313)	11-2020	12/2023 (01-10-2025) {10/2025}	351.12 (N.A.) {351.12}	299.22	63
		1058	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	434.50	32
		1059	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	214.34	30.3
		1060	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	107.86	24
		1061	RANIKOR-MAHESKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (01-06-2024) {2/2025}	157.86 (146.92) {157.86}	152.95	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1062	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3-2021	12/2022 (01-06-2024) {2/2025}	260.21 (N.A.) {260.21}	239.35	100
		1063	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (N.A.) {7/2025}	302.88 (N.A.) {302.88}	228.68	96
		1064	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (01-05-2026) {5/2026}	359.86 (N.A.) {359.86}	233.26	60.81
		1065	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11-2021	6/2024 (01-12-2024) {5/2025}	283.50 (N.A.) {283.50}	257.26	100
		1066	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	222.26	30
		1067	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	293.36	25.52
		1068	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	297.91	25.27
		1069	DAINADUBI-DARUGIRI PKG-1B (NHIDCL) (N24002233)	3-2023	3/2027 (N.A.) {3/2027}	705.83 (N.A.) {705.83}	0.32	2.13
		1070	IMPROVEMENT AND WIDENING TWO LANNIG WITH PAVED SHOULDER OF NATIONAL HIGHWAY 127B FROM KM 31.500 (GOE (MoRTH) (N24002239)	12-2023	5/2027 (N.A.) {5/2027}	504.00 (N.A.) {504.00}	-	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1071	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (01-06-2025) {6/2025}	553.51 (610.09) {553.51}	438.16	88.07
MIZORAM	RAILWAYS	1072	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2025 (N.A.) {6/2025}	6,527.45 (5,021.45) {8,071.30}	8,066.76	97
	ROAD TRANSPORT AND HIGHWAYS	1073	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9-2020	10/2022 (N.A.) {4/2025}	275.02 (N.A.) {247.25}	237.68	100
		1074	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	265.38	100
		1075	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {10/2024}	292.24 (N.A.) {331.17}	294.78	94.4
		1076	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (01-04-2024) {4/2024}	233.25 (N.A.) {233.25}	172.09	100
		1077	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	502.24	63.7
		1078	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	373.89	61
		1079	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (N.A.) {5/2024}	492.94 (N.A.) {492.94}	365.86	100
		1080	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWL RANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	379.40	95.31

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1081	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	279.44	75.4
		1082	ZORINPUI- HMAWNGBU-LONGMASU (NH-502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	33.77	3
		1083	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {4/2025}	519.09 (N.A.) {785.65}	670.91	97.51
		1084	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {5/2024}	640.07 (N.A.) {1,286.35}	1,195.84	98.9
		1085	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4-2017	6/2023 (N.A.) {3/2024}	642.96 (N.A.) {988.23}	686.42	100
		1086	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {4/2025}	473.18 (N.A.) {688.25}	541.04	95
		1087	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {4/2025}	537.82 (N.A.) {789.05}	779.37	99.88
		1088	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {5/2025}	518.53 (N.A.) {906.76}	849.68	97.9

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1089	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {5/2025}	404.29 (N.A.) {750.32}	666.58	100
		1090	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {5/2025}	428.11 (N.A.) {746.39}	613.69	99.82
MULTI STATE	COAL	1091	NILJAI EXPANSION (DEEP) OC (3.5 MTY) (WCL) (N06000154)	8-2016	3/2022 (01-03-2025) {3/2025}	319.76 (319.76) {319.76}	183.67	98
		1092	BINA KAKRI AMALGAMATION OCP 14 MTPA (NCL) (N06000192)	8-2020	3/2024 (N.A.) {3/2027}	836.42 (N.A.) {836.42}	778.71	89.08
	DPIIT	1093	NATIONAL INDUSTRIAL CORRIDOR PROJECT (DMIC FOR DPIIT) (N40000001)	9-2011	3/2027 (01-03-2032) {3/2032}	20,084.00 (26,684.00) {26,684.00}	11,262.06	50.99
	PETROLEUM	1094	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II (GAIL) (N16000285)	6-2009	12/2012 (01-12-2025) {12/2025}	2,915.00 (5,909.00) {5,909.00}	4,381.20	94.2
		1095	SRIKAKULAM ANGUL PIPELINE PROJECT (GAIL) (N16000388)	9-2019	7/2022 (01-12-2025) {12/2025}	2,658.34 (N.A.) {2,658.34}	2,179.10	94.6
		1096	DHAMRA HALDIA PIPELINE PROJECT (GAIL) (N16000391)	3-2020	11/2022 (01-12-2025) {12/2025}	1,030.65 (N.A.) {1,030.65}	841.90	86.8
		1097	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT (GAIL) (N16000398)	6-2020	5/2023 (01-09-2025) {9/2025}	7,844.25 (N.A.) {7,844.25}	6,412.20	95.1

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1098	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS (IOCL) (N16000426)	6-2019	12/2029 (01-03-2030) {3/2030}	169.00 (N.A.) {169.00}	71.00	100
		1099	NORTH EAST GAS GRID (IGGL) (N16000439)	11-2020	3/2024 (01-07-2025) {3/2027}	9,265.00 (9,265.00) {9,265.00}	6,270.19	84.51
		1100	GURDASPUR JAMMU PIPELINE (GAIL) (N16000531)	7-2023	7/2026 (01-07-2026) {7/2026}	521.92 (521.92) {521.92}	153.20	35.5
	POWER	1101	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P (PGCIL) (N18000249)	12-2014	12/2018 (01-03-2025) {3/2027}	4,754.42 (9,129.32) {9,129.32}	7,602.44	81.7
		1102	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES (PGCIL) (N18000250)	12-2014	12/2018 (01-03-2025) {9/2025}	5,111.33 (6,700.00) {6,700.00}	5,230.02	96
		1103	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM (PGCIL) (N18000328)	2-2022	4/2025 (N.A.) {8/2025}	318.12 (N.A.) {318.12}	254.50	98
		1104	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM (PGCIL) (N18000330)	3-2022	12/2024 (N.A.) {9/2025}	288.71 (N.A.) {288.71}	199.53	48
		1105	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000331)	2-2022	9/2023 (N.A.) {8/2025}	359.47 (N.A.) {359.47}	327.28	90
		1106	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000332)	5-2022	11/2023 (N.A.) {9/2025}	1,666.00 (2,218.00) {2,218.00}	2,029.28	94.1

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1107	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B (PGCIL) (N18000337)	7-2022	6/2023 (N.A.) {9/2025}	4,546.26 (N.A.) {4,546.26}	4,091.67	93
		1108	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C (PGCIL) (N18000338)	7-2022	3/2025 (N.A.) {3/2025}	186.19 (N.A.) {186.19}	91.53	100
		1109	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION (PGCIL) (N18000343)	10-2022	10/2025 (N.A.) {6/2025}	307.87 (N.A.) {307.87}	298.87	100
		1110	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B (PGCIL) (N18000352)	3-2023	11/2024 (N.A.) {9/2025}	3,546.94 (N.A.) {3,546.94}	2,837.55	94
		1111	ER WR TRANSMISSION LIMITED (PGCIL) (N18000353)	3-2023	3/2025 (N.A.) {6/2025}	281.16 (N.A.) {281.16}	281.15	100
		1112	NANGALDAM-TALWARA(NL),NR (NR) (220100188)	3-1981	12/2025 (01-01-2027) {6/2027}	2,018.00 (603.00) {2,017.96}	1,629.74	75
	RAILWAYS	1113	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) (WCR) (220100232)	9-1998	3/2027 (N.A.) {3/2025}	8,913.94 (63.57) {8,248.50}	2,500.34	43
		1114	CHHAPRA-BALLIA UP (NER) (N22000134)	3-2013	2/2025 (N.A.) {12/2025}	941.05 (954.00) {1,045.82}	1,004.59	95.5
		1115	CHOTTAUDEPUR-DHAR(NL) (WR) (N22000138)	4-2007	12/2026 (01-12-2027) {12/2027}	1,793.65 (1,793.63) {1,793.63}	1,641.84	59
		1116	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) (WR) (N22000139)	4-2007	2/2027 (01-02-2027) {2/2027}	1,942.00 (1,873.10) {2,873.11}	3,119.79	59

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1117	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) (NCR) (N22000148)	4-2011	3/2025 (N.A.) {12/2024}	2,912.96 (N.A.) {3,845.60}	1,024.32	0
		1118	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR (NCR) (N22000158)	4-2010	2/2019 (N.A.) {12/2026}	746.83 (N.A.) {746.83}	391.89	39
		1119	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING (NFR) (N22000183)	4-2013	8/2024 (N.A.) {10/2024}	2,047.51 (N.A.) {2,832.35}	3,709.47	100
		1120	NEW BG LINE FROM BALURGHAT TO HILLY NFR (NFR) (N22000206)	4-2010	3/2027 (N.A.) {3/2027}	1,208.67 (N.A.) {1,181.57}	425.12	8
		1121	NEW BG LINE FROM JAGBANI TO BIRATNAGAR (NFR) (N22000207)	4-2010	3/2022 (01-12-2026) {12/2026}	401.65 (485.96) {485.96}	361.33	86
		1122	MURKONGSELEK-PASIGHAT NL (NFR) (N22000208)	4-2011	3/2025 (N.A.) {11/2025}	435.06 (N.A.) {1,249.35}	803.88	54
		1123	PIRPAINTI-JASIDIH (ER) (N22000219)	4-2013	3/2028 (01-03-2028) {3/2028}	2,555.03 (N.A.) {2,610.84}	1,140.05	45
		1124	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION (SCR) (N22000261)	4-2012	2/2025 (N.A.) {3/2025}	1,953.00 (N.A.) {1,952.68}	1,936.28	0
		1125	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL (NR) (N22000274)	4-2007	3/2024 (N.A.) {3/2025}	1,053.23 (N.A.) {1,053.00}	592.53	99
		1126	RAYADURGA-TUMKUR NL (SWR) (N22000279)	4-2007	9/2015 (N.A.) {2/2028}	2,495.59 (2,495.86) {2,495.86}	1,675.34	65

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1127	HOTGI-KUDGI-GADAG (SWR) (N22000333)	3-2015	12/2024 (N.A.) {2/2026}	1,877.81 (1,877.81) {2,458.87}	2,574.88	89
		1128	KAZIPET-BALHRSHA (SCR) (N22000367)	4-2015	1/2025 (N.A.) {1/2025}	2,594.59 (N.A.) {2,909.00}	2,862.60	0
		1129	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT (NHSRCL) (N22000463)	12-2015	8/2027 (N.A.) {8/2027}	108,000.00 (N.A.) {108,000.00}	78,839.00	52.89
		1130	WESTERN DEDICATED FREIGHT CORRIDOR (DFCC) (N22000464)	11-2007	3/2022 (N.A.) {3/2020}	51,101.00 (N.A.) {51,101.00}	47,476.00	83
		1131	CHANDIGARH-BADDI (NR) (N22000467)	4-2007	6/2025 (01-12-2026) {12/2026}	1,540.13 (1,540.14) {1,540.14}	956.13	30
		1132	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) (SER) (N22000506)	3-2019	12/2024 (N.A.) {6/2026}	2,400.00 (N.A.) {1,866.31}	2,112.20	61
	ROAD TRANSPORT AND HIGHWAYS	1133	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 (NHAI) (N24001628)	11-2021	2/2025 (01-08-2025) {8/2025}	2,155.95 (N.A.) {2,155.95}	1,360.04	71.01
		1134	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O (NHAI) (N24001629)	4-2022	11/2024 (01-07-2025) {7/2025}	796.65 (N.A.) {796.65}	452.41	91.71
		1135	VARANASI-AURANGABAD KM.786 TO KM.978.40 (NHAI) (N24000182)	9-2011	3/2014 (N.A.) {6/2025}	2,848.00 (N.A.) {3,241.56}	3,901.66	90.42
	SHIPPING AND PORTS	1136	JAL MARG VIKAS PROJECT (IWAI) (N25000072)	1-2018	3/2023 (01-12-2025) {12/2025}	5,369.18 (5,061.15) {5,061.15}	3,472.54	69.48

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	TELECOMMUNICATIONS	1137	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (N26000114)	3-2020	6/2021 (01-11-2021) {12/2025}	461.42 (461.42) {461.42}	166.02	81
		1138	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (IPMPLS) NETWORK and (BSNL) (N26000115)	3-2023	3/2024 (01-07-2024) {3/2025}	239.60 (N.A.) {239.60}	179.63	100
		1139	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (N26000116)	5-2023	8/2024 (01-11-2024) {6/2025}	645.13 (N.A.) {645.13}	348.03	89.15
		1140	PLANNING ENGINEERING SUPPLY INSTALLATION TESTING COMMISSIONING INTEGRATION and ANNUAL MAINTENANCE OF (BSNL) (N26000117)	6-2023	6/2025 (N.A.) {6/2025}	24,556.35 (24,544.55) {24,544.55}	8,211.15	95.54
		1141	OPTICAL TRANSPORT NETWORK (OTN) PH-4 IN BSNL (BSNL) (N26000118)	2-2024	8/2025 (N.A.) {8/2025}	810.99 (N.A.) {810.99}	635.37	100
	URBAN DEVELOPMENT	1142	DELHI GHAZIABAD MEERUT RRTS CORRIDOR (NCRTC) (N28000134)	3-2019	6/2025 (N.A.) {6/2025}	30,274.00 (N.A.) {30,274.00}	25,812.28	86.8
NAGALAND	PETROLEUM	1143	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	6.62	19
	RAILWAYS	1144	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2026 (N.A.) {12/2029}	6,663.20 (6,663.20) {6,663.20}	4,942.71	74

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	1145	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	119.20	65.06
		1146	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (01-10-2022) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		1147	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (01-11-2025) {11/2025}	330.80 (N.A.) {330.80}	171.89	92.44
		1148	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (01-11-2026) {11/2026}	232.29 (350.88) {232.29}	79.69	17.31
		1149	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3-2020	6/2022 (01-09-2022) {1/2025}	206.53 (N.A.) {206.53}	119.25	100
		1150	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (01-09-2025) {9/2025}	258.52 (N.A.) {258.52}	89.46	81.4
		1151	PEREN-DIMAPUR PKG-5 (NHIDCL) (N24001407)	2-2021	3/2023 (N.A.) {3/2023}	207.33 (N.A.) {207.33}	-	0
		1152	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	65.19	73.34
		1153	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (01-06-2026) {6/2026}	252.19 (N.A.) {252.19}	14.33	20.27

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1154	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (01-12-2025) {12/2025}	297.24 (N.A.) {297.24}	150.10	80.31
		1155	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (01-03-2025) {3/2025}	226.44 (N.A.) {226.44}	140.24	100
		1156	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3-2022	12/2024 (N.A.) {1/2025}	605.36 (N.A.) {605.36}	273.21	100
		1157	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (01-09-2025) {9/2025}	192.93 (N.A.) {192.93}	112.09	93.38
		1158	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {12/2025}	177.77 (N.A.) {199.02} {199.02}	46.94	63.33
		1159	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	100.51	58.57
		1160	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	50.60	28.05
		1161	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	168.20	66.03

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1162	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (01-11-2022) {5/2025}	373.07 (534.41) {534.41}	382.50	99.81
		1163	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (01-09-2025) {9/2025}	429.52 (794.74) {794.74}	321.40	92.46
		1164	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (01-02-2023) {4/2025}	387.00 (688.12) {688.12}	392.01	100
		1165	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (01-08-2024) {4/2025}	500.09 (698.81) {698.81}	393.53	100
		1166	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (01-08-2022) {8/2025}	215.79 (N.A.) {215.79}	132.93	80.38
		1167	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (01-06-2023) {9/2025}	323.98 (N.A.) {323.98}	119.94	60.11
		1168	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3-2017	11/2020 (01-02-2023) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
		1169	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3-2019	12/2022 (01-01-2023) {1/2023}	237.51 (N.A.) {237.51}	215.47	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1170	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (01-09-2024) {6/2026}	277.44 (N.A.) {277.44}	169.46	67.91
		1171	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (01-06-2025) {12/2025}	159.85 (342.29) {159.85}	108.15	33.55
		1172	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (01-04-2023) {8/2025}	202.36 (N.A.) {202.36}	75.39	32.67
		1173	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9-2020	4/2022 (01-05-2024) {12/2025}	315.63 (N.A.) {315.63}	116.70	0
		1174	BASUNDHARA (WEST) OC EXTN(7.00 MTY) (MCL) (N06000112)	5-2014	3/2019 (N.A.) {3/2028}	479.15 (N.A.) {479.15}	271.99	63.04
ODISHA	COAL	1175	SIARMAL OCP (40.00MTY) (MCL) (N06000113)	2-2021	3/2029 (N.A.) {3/2029}	5,194.96 (N.A.) {5,194.96}	3,454.71	53.63
		1176	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP (MCL) (N06000167)	5-2018	3/2027 (N.A.) {3/2027}	2,434.75 (N.A.) {2,434.75}	1,765.96	61.49
		1177	REORGANISATION OF BHARATPUR OCP EXPANSION (MCL) (N06000171)	11-2018	3/2029 (N.A.) {3/2029}	2,838.87 (N.A.) {2,838.87}	1,837.17	47.35
		1178	TALABIRA II AND III OCP (NLC) (N06000189)	7-2017	1/2027 (N.A.) {1/2027}	2,401.07 (N.A.) {2,401.07}	1,626.71	86

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1179	NAINI COAL MINE (SCCL) (N06000203)	3-2020	3/2024 (N.A.) {3/2027}	494.30 (N.A.) {494.30}	491.33	80
		1180	GOPALJI-KANIHA OCP (MCL) (N06000229)	4-2022	3/2028 (N.A.) {3/2028}	6,107.87 (N.A.) {6,107.87}	1,703.67	17.73
		1181	BALARAM EXPANSION OCP (MCL) (N06000230)	8-2020	3/2029 (N.A.) {3/2029}	3,504.21 (N.A.) {3,504.21}	1,026.96	52.44
		1182	SUBHADRA OCP (MCL) (N06000249)	5-2021	3/2029 (01-03-2029) {3/2029}	1,693.81 (N.A.) {1,693.81}	1,277.82	40.05
		1183	NLC TALABIRA THERMAL POWER PROJECT (PHASE-1: 3 X 800 MW) (NLC) (N06000270)	1-2024	5/2029 (01-03-2030) {3/2030}	27,213.00 (N.A.) {27,213.00}	1,928.60	1.55
		1184	RPR OF HINGULA EXPANSION OCP (MCL) (N06000285)	11-2022	3/2029 (N.A.) {3/2029}	1,561.85 (N.A.) {1,561.85}	49.85	23.57
		1185	BHUBANESWARI EXPANSION OCP (MCL) (N06000286)	3-2024	3/2031 (N.A.) {3/2031}	5,366.28 (N.A.) {5,366.28}	9.08	9.59
		1186	BALABHADRA OCP (MCL) (N06000288)	4-2023	3/2030 (N.A.) {3/2030}	978.44 (N.A.) {978.44}	209.50	7.68
		1187	INTEGRATED KULDA GARJANBAHAL OCP (MCL) (N06000289)	4-2023	3/2030 (N.A.) {3/2030}	3,563.50 (N.A.) {3,563.50}	505.09	4
	DEPARTMENT OF HIGHER EDUCATION	1188	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR (CPWD EDUCATION) (N28000126)	1-2019	3/2022 (N.A.) {10/2025}	790.79 (N.A.) {790.79}	708.50	97

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>MINES</u>	1189	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT (NALCO) (N10000010)	12-2014	4/2021 (01-06-2026) {6/2026}	4,103.00 (5,677.40) {5,677.40}	3,831.39	74.52
		1190	UTKAL D AND E COAL BLOCK (NALCO) (N10000011)	5-2016	1/2020 (01-11-2023) {3/2024}	534.00 (N.A.) {1,021.97}	829.39	88.5
		1191	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (NALCO) (N10000012)	12-2015	11/2020 (01-09-2025) {8/2027}	355.00 (581.00) {581.00}	163.55	12.6
		1192	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN (NALCO) (N10000013)	11-2017	4/2021 (01-05-2026) {5/2026}	483.00 (483.00) {495.00}	387.75	89.43
		1193	POTTANGI BAUXITE MINES (NALCO) (N10000016)	5-2018	12/2024 (N.A.) {5/2025}	1,437.00 (N.A.) {1,381.00}	650.05	51.1
		1194	CONSTRUCTION OF RED MUD POND - II AT NALCO DAMANJODI ODISHA (NALCO) (N10000017)	9-2019	3/2023 (01-05-2024) {5/2024}	225.79 (N.A.) {270.66}	5.00	100
	<u>PETROLEUM</u>	1195	ADDITIONAL STORAGE TANKS AT PARADIP (IOCL) (N16000361)	11-2018	9/2021 (01-12-2024) {3/2025}	462.30 (552.44) {552.44}	493.72	100
		1196	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY (IOCL) (N16000396)	7-2020	1/2024 (01-04-2025) {4/2026}	13,805.00 (N.A.) {13,805.00}	7,704.73	90
	<u>POWER</u>	1197	EASTERN REGION EXPANSION SCHEME XXIX (PGCIL) (N18000351)	3-2023	11/2025 (N.A.) {7/2025}	524.04 (N.A.) {524.04}	482.12	99.8

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1198	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) (NTPC) (N18000364)	8-2022	5/2027 (N.A.) {12/2027}	11,844.00 (N.A.) {12,539.00}	3,703.12	21.4
	RAILWAYS	1199	KHURDA ROAD-BOLANGIR(NL)ECOR (ECOR) (220100284)	4-1994	12/2026 (01-12-2026) {12/2026}	3,550.00 (3,791.66) {5,089.37}	4,910.22	86
		1200	TALCHER-BIMALAGARH(NL)(ECOR) (ECOR) (220100328)	4-2005	3/2025 (N.A.) {3/2026}	1,928.10 (N.A.) {1,928.07}	1,757.75	40
		1201	BHADRAK - NERGUNDI 3RD LINE (ECOR) (N22000316)	3-2013	11/2024 (01-01-2026) {6/2026}	1,284.39 (1,284.39) {1,284.39}	1,297.80	80
		1202	JAGADALPUR-KORAPUT DOUBLING (ECOR) (N22000376)	4-2015	3/2024 (N.A.) {3/2022}	1,547.38 (N.A.) {1,547.38}	1,304.60	93.7
		1203	KORAPUT - SINGAPUR ROAD DOUBLING (ECOR) (N22000379)	4-2015	12/2027 (01-03-2026) {3/2026}	2,362.00 (2,361.74) {2,361.74}	1,816.25	80
		1204	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE (ECOR) (N22000380)	4-2015	3/2027 (N.A.) {8/2026}	820.61 (N.A.) {810.02}	580.59	0
		1205	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. (ECOR) (N22000381)	4-2015	3/2026 (01-11-2025) {11/2025}	1,172.92 (N.A.) {2,022.75}	1,971.33	80
		1206	VIZIANAGARAM -SAMABALPUR 3RD LINE (RVNL) (N22000409)	1-1991	12/2026 (N.A.) {12/2026}	4,803.16 (N.A.) {4,803.16}	4,691.52	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1207	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL (IRCON) (N22000418)	4-2016	3/2020 (N.A.) {12/2025}	5,200.00 (N.A.) {5,200.00}	389.00	100
		1208	JEYPORE MALKANGIRI NEW LINE (ECOR) (N22000516)	2-2018	7/2033 (N.A.) {7/2033}	2,344.00 (N.A.) {642.69}	220.78	90.1
		1209	JEYPORE NABARANGPUR NEWLINE (ECOR) (N22000517)	7-2017	7/2028 (01-12-2029) {12/2029}	748.00 (N.A.) {747.91}	-	0
		1210	TALCHER - ANGUL NEW LINE WITH Y CONNECTION AT TALCHER (ECOR) (N22000518)	7-2018	12/2026 (N.A.) {12/2026}	278.96 (495.00) {494.62}	29.50	0
		1211	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (ECOR) (N22000519)	8-2022	8/2027 (N.A.) {8/2027}	190.90 (N.A.) {190.90}	10.00	0
		1212	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION (ECOR) (N22000520)	9-2022	9/2027 (N.A.) {3/2028}	189.93 (N.A.) {189.93}	14.04	0
		1213	BRUNDAMAL-JHARSUGUDA- FLYOVER CONNECTION FOR JOINING DN LINE (ECOR) (N22000521)	12-2009	12/2026 (N.A.) {12/2026}	296.51 (N.A.) {297.00}	162.44	10
		1214	BAGHUAPAL FLY OVER (20 KM) (ECOR) (N22000522)	8-2019	8/2027 (01-08-2027) {8/2027}	183.00 (257.97) {257.97}	0.83	0
		1215	ROURKELA-BONDAMUNDA A-CABIN 5TH LINE (10 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SER) (N22000571)	9-2022	9/2026 (N.A.) {2/2026}	209.75 (N.A.) {244.99}	82.27	30

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	1216	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 (NHAI) (N24001647)	8-2020	3/2022 (N.A.) {7/2025}	200.00 (154.73) {154.73}	150.38	100
		1217	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 (NHAI) (N24001665)	12-2021	10/2024 (N.A.) {12/2025}	1,592.00 (1,592.00) {1,592.00}	1,127.76	78.13
		1218	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE-OD (NHAI) (N24001666)	12-2021	9/2024 (N.A.) {8/2025}	714.00 (714.00) {714.00}	589.97	95.45
		1219	6L GREENFIELD KALIAGURA ? BAUNSAGUAR SECTION OF NH-130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG (NHAI) (N24001667)	9-2021	5/2024 (N.A.) {12/2025}	1,734.00 (1,734.00) {1,734.00}	1,238.62	86.47
		1220	6L OF BADAUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130-CD (PACKAGE ? OD-3) (NHAI) (N24001668)	3-2021	4/2024 (N.A.) {11/2025}	1,249.00 (N.A.) {1,249.00}	522.17	87.16
		1221	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH-130-CD (PACKAGE ? OD-1) (NHAI) (N24001669)	2-2021	3/2024 (N.A.) {7/2025}	586.00 (N.A.) {586.00}	241.77	92.98
		1222	6L OF KARKI ? KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH-130-CD (PACKAGE ? OD-4) (NHAI) (N24001670)	2-2021	3/2024 (N.A.) {7/2025}	593.00 (N.A.) {593.00}	282.15	94.55
		1223	6L OF HATIBENA - BADAUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE ? OD-2) (NHAI) (N24001671)	2-2021	3/2024 (N.A.) {7/2025}	925.00 (N.A.) {925.00}	460.47	97

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1224	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE ? (NHAI) (N24001678)	8-2021	6/2024 (N.A.) {12/2025}	1,460.00 (1,460.00) {1,460.00}	986.76	91.52
		1225	CONSTRUCTION OF ROAD FROM KM 0/0 TO 72/0 OF NH-26 SUCH AS 4 LANE FROM KM 0/0 TO 21/0 (BARGARH TO BAR (MoRTH) (N24001857)	6-2020	12/2023 (01-08-2025) {8/2025}	414.24 (N.A.) {414.24}	307.52	98
		1226	WIDENING AND STRENGTHENING TO 2L+PS INCLUDING LA OF KANDARPUR-BALIKUDA FROM KM 277/500 TO 318/970 OF (MoRTH) (N24001858)	3-2022	6/2025 (N.A.) {12/2025}	499.79 (N.A.) {499.79}	285.58	48.2
		1227	CONSTRUCTION OF BYPASS ON NH-59 FROM KM 336/350 TO 349/910 (13.56 KM) NEAR BERHAMPUR TOWN INCLUDING (MoRTH) (N24001859)	3-2021	3/2024 (N.A.) {8/2025}	196.94 (N.A.) {196.94}	71.55	93
		1228	CONSTRUCTION OF BYPASS TO NAYAGARH TOWN FROM KM 235.469 TO 252.482 OF NH-57 INCLUDING LAND ACQUISITI (MoRTH) (N24001860)	1-2022	4/2025 (N.A.) {8/2025}	300.33 (N.A.) {300.33}	203.81	70
		1229	CONSTRUCTION OF BYPASS TO KHORDHA TOWN FROM KM 294/000 TO 300/300 ON NH-57 INCLUDING LA IN THE STATE (MoRTH) (N24001861)	2-2022	11/2024 (01-08-2025) {8/2025}	157.49 (N.A.) {157.49}	72.57	54
		1230	CONSTRUCTION OF BYPASS ROAD TO BALANGIR TOWN FROM KM 72/400 (DESING KM 0/0) TO KM 79/800 (DESIGN KM (MoRTH) (N24001862)	2-2022	10/2025 (01-11-2025) {11/2025}	238.78 (N.A.) {238.78}	50.64	40
		1231	CONSTRUCTION OF 5 HL BRIDGES AT KM 379/000 (PANGAM), KM 439/400 (POTTERU), KM 444/237 (KONGURUKONDA) (MoRTH) (N24001863)	3-2021	6/2024 (01-10-2025) {5/2025}	154.05 (N.A.) {154.05}	47.47	30

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1232	CONSTRUCTION OF FOUR LANE ROB AND ITS APPROACHES IN LIEU OF EXISTING LEVEL CROSSING NO. RV-71 AT KM (MoRTH) (N24001864)	11-2021	6/2025 (N.A.) {10/2025}	154.49 (N.A.) {154.49}	60.48	45
		1233	CONSTRUCTION OF 4 LANE ROB WITH APPROACHES IN LIEU OF LC NO. RV-172 AT KM 176.00 OF NH-201 (PRESENT (MoRTH) (N24001865)	12-2021	5/2025 (01-10-2025) {10/2025}	324.09 (N.A.) {324.09}	111.45	35
		1234	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM. (NHAI) (N24002078)	12-2023	12/2025 (N.A.) {3/2026}	711.00 (N.A.) {711.00}	217.96	60.8
		1235	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002079)	12-2023	12/2025 (N.A.) {3/2026}	742.25 (N.A.) {742.25}	223.47	55.1
		1236	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002080)	12-2023	12/2025 (N.A.) {3/2026}	762.75 (N.A.) {762.75}	266.33	60.7
		1237	3L MAJOR BRIDGE OVER RIVER BRAHMANI AT KM. 401.250 (DUBURI CHANDIKHOLE SECTION) OF NH 200 (NEW NH 5 (NHAI) (N24002081)	8-2022	1/2025 (N.A.) {12/2026}	153.61 (N.A.) {153.61}	22.77	34.49
		1238	WIDENING AND STRENGTHENING TO 2L+PS FROM KM 0.000 TO 40.000 (DHAUGAON-PODAMARI SECTION) OF NH 326 I (MoRTH) (N24002135)	3-2022	2/2026 (N.A.) {2/2026}	186.52 (N.A.) {186.52}	48.30	35
		1239	WIDENING AND STRENGTHENING TO 4L+PS/2L+PS FROM KM 0.000 TO 35.800 (KUAKHIA - MANGALPUR SECTION) OF N (MoRTH) (N24002136)	3-2022	2/2026 (N.A.) {2/2026}	636.10 (N.A.) {636.10}	264.98	36.53
		1240	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE ? PARADIP SECTION OF NH-53 (OLD NH (NHAI) (N24002219)	3-2024	10/2026 (N.A.) {10/2026}	882.45 (N.A.) {882.45}	82.62	14.1

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1241	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S (NHAI) (N24000619)	9-2016	8/2019 (N.A.) {7/2025}	2,510.04 (N.A.) {2,510.04}	1,181.34	99.98
		1242	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO (NHAI) (N24000715)	12-2017	7/2020 (N.A.) {7/2025}	686.65 (565.00) {686.65}	574.26	98
		1243	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE ((NHAI) (N24000733)	1-2018	8/2022 (N.A.) {12/2025}	633.68 (492.83) {633.68}	560.38	86
		1244	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG (NHAI) (N24000734)	1-2018	8/2021 (N.A.) {7/2025}	614.48 (503.30) {757.12}	664.48	99
		1245	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON (NHAI) (N24000736)	1-2018	9/2020 (N.A.) {7/2025}	686.65 (504.09) {1,015.16}	488.98	98.35
		1246	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 (NHAI) (N24000738)	1-2018	9/2021 (N.A.) {12/2025}	999.00 (1,152.70) {1,152.70}	540.10	82.01
		1247	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) ((NHAI) (N24000739)	1-2018	6/2021 (01-07-2025) {7/2025}	503.88 (609.03) {609.03}	536.89	98.5
		1248	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. (MoRTH) (N24000912)	8-2016	2/2017 (N.A.) {12/2025}	287.70 (N.A.) {293.66}	275.42	98.66
		1249	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA (MoRTH) (N24000914)	12-2016	8/2018 (N.A.) {9/2025}	223.50 (N.A.) {223.50}	220.50	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1250	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA (MoRTH) (N24000917)	3-2018	8/2018 (N.A.) {4/2025}	199.16 (N.A.) {199.16}	158.73	100
	<u>STEEL</u>	1251	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY (SAIL) (N12000122)	11-2020	5/2023 (01-03-2025) {3/2025}	377.18 (N.A.) {377.18}	434.90	
		1252	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP (SAIL) (N12000125)	1-2022	5/2025 (01-08-2025) {8/2025}	970.18 (N.A.) {970.18}	720.07	94.31
<u>PUNJAB</u>	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1253	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. (CPWD EDUCATION) (N28000142)	10-2019	5/2022 (N.A.) {8/2025}	348.24 (N.A.) {348.24}	245.37	91.2
	<u>PETROLEUM</u>	1254	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB (HPCL) (N16000402)	5-2020	2/2023 (01-09-2024) {3/2026}	1,421.46 (N.A.) {1,421.46}	1,163.10	95.63
		1255	BHATINDA SANGRUR PIPELINE (HPCL) (N16000440)	11-2021	5/2024 (01-02-2025) {8/2025}	367.00 (397.00) {397.00}	334.26	91.9
		1256	CGD PROJECT AT PATHANKOT DISTRICT (IOCL) (N16000488)	3-2022	3/2030 (01-09-2033) {9/2033}	151.00 (N.A.) {151.00}	8.73	2
	<u>RAILWAYS</u>	1257	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI (NR) (N22000502)	6-2009	8/2016 (N.A.) {8/2025}	404.00 (N.A.) {404.00}	190.00	100
		1258	LUDHIANA MULLANPUR DOUBLING (NR) (N22000589)	9-2020	3/2025 (N.A.) {7/2025}	235.00 (N.A.) {235.00}	7.99	98

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1259	FEROZPUR - PATTI (25.72 KM) (NR) (N22000614)	4-2017	3/2027 (N.A.) {3/2027}	299.74 (N.A.) {781.00}	-	0
	ROAD TRANSPORT AND HIGHWAYS	1260	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO (NHAI) (N24001415)	12-2020	4/2024 (01-07-2024) {7/2024}	881.00 (N.A.) {881.00}	960.36	92.34
		1261	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI (NHAI) (N24001416)	12-2020	1/2024 (01-03-2025) {3/2025}	989.66 (N.A.) {989.66}	338.21	31.08
		1262	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH- 5) NEAR MULLANPUR DAKHA TO (NHAI) (N24001417)	12-2020	4/2024 (01-09-2025) {9/2025}	1,234.40 (N.A.) {1,234.40}	853.68	61.88
		1263	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO (NHAI) (N24001418)	12-2020	4/2024 (01-09-2025) {9/2025}	1,094.46 (N.A.) {1,094.46}	802.93	62.99
		1264	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- (NHAI) (N24001419)	2-2021	4/2024 (01-11-2024) {11/2024}	1,269.96 (N.A.) {1,269.96}	585.86	43.45
		1265	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR- (NHAI) (N24001420)	2-2021	4/2024 (01-12-2025) {12/2025}	853.66 (N.A.) {853.66}	177.27	20.65
		1266	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA (NHAI) (N24001630)	7-2021	2/2025 (N.A.) {2/2025}	1,501.02 (N.A.) {1,501.02}	282.00	75
		1267	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD (NHAI) (N24001631)	3-2021	10/2024 (N.A.) {10/2024}	1,525.31 (N.A.) {1,525.31}	290.00	95

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1268	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM (NHAI) (N24001632)	1-2021	5/2024 (01-06-2025) {8/2025}	1,741.86 (2,281.02) {2,281.02}	1,294.40	96.5
		1269	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA ? RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR (NHAI) (N24001636)	5-2021	12/2024 (01-10-2026) {10/2026}	1,368.91 (1,368.91) {1,368.91}	163.58	15.31
		1270	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K (NHAI) (N24001637)	3-2021	1/2025 (N.A.) {1/2025}	1,754.84 (N.A.) {1,754.84}	1,145.02	40.01
		1271	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 (NHAI) (N24001638)	11-2021	7/2024 (01-08-2025) {8/2025}	646.42 (646.42) {646.42}	481.67	96
		1272	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE (NHAI) (N24001639)	5-2020	12/2024 (01-08-2025) {8/2025}	864.23 (864.23) {864.23}	434.88	65
		1273	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N (NHAI) (N24001640)	3-2021	11/2024 (N.A.) {11/2024}	1,229.38 (N.A.) {1,229.38}	762.83	48.58
		1274	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR (NHAI) (N24001641)	3-2021	10/2024 (01-12-2025) {12/2025}	1,641.75 (N.A.) {1,641.75}	188.55	26.01
		1275	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI (NHAI) (N24001642)	2-2021	8/2024 (01-12-2025) {12/2025}	1,474.77 (N.A.) {1,474.77}	475.88	75.25

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1276	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I (NHAI) (N24001643)	12-2020	6/2024 (01-06-2025) {6/2025}	857.91 (N.A.) {857.91}	164.88	41.02
		1277	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV (NHAI) (N24001644)	12-2020	9/2023 (01-09-2025) {9/2025}	524.88 (416.58) {416.58}	157.14	73
		1278	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION OF NH-354 SECTION ARIFKES-FEROZEPUR-MUKTS (MoRTH) (N24001960)	3-2021	10/2023 (N.A.) {10/2025}	263.19 (N.A.) {220.00}	119.50	61
		1279	WORK OF WIDENING/UPGRADATION OF 2- LANE WITH PAVED SHOULDER OF SRI MUKTSAR SAHIB TO MALOUT ROAD FROM (MoRTH) (N24001961)	3-2022	10/2023 (N.A.) {7/2025}	152.58 (N.A.) {152.58}	97.00	85
		1280	6L OF JODHPUR ROMANA (BATHINDA) - MANDI DABWALI (PUNJAB HARYANA BORDER) SECTION OF NH-54 FROM KM. 0. (NHAI) (N24002075)	12-2020	8/2025 (01-08-2025) {8/2025}	757.13 (757.00) {757.00}	246.51	98.75
		1281	6L AMRITSAR-BATHINDA GREENFIELD SECTION FROM JN. WITH BHAGTA BHAI KA- BHADAUR ROAD NEAR DYALPURA BHAI (NHAI) (N24002076)	3-2021	10/2025 (01-06-2026) {6/2026}	2,029.17 (2,029.00) {2,029.00}	84.23	47
		1282	6L ACCESS CONTROLLED LUDHIANA- BATHINDA GREENFIELD HIGHWAY FROM JN. WITH AMRITSAR-BATHANDA GREENFIELD (NHAI) (N24002091)	6-2021	9/2025 (01-03-2026) {3/2026}	906.51 (906.51) {906.51}	170.39	54
		1283	6-LANE AMRITSAR-BATHINDA GREENFIELD SECTION OF NH-754A FROM JUNCTION WITH MOGA JALANDHAR ROAD (NH-70 (NHAI) (N24002092)	3-2021	10/2025 (N.A.) {10/2025}	1,801.37 (N.A.) {1,801.37}	1,075.64	51.2

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1284	6L OF AMBALA-CHANDIGARH GREENFIELD SECTION FROM KM. 0.000 TO KM. 25.000 WITH 4L SPUR TO LALRU FROM K (NHAI) (N24002098)	3-2022	10/2025 (N.A.) {10/2025}	1,641.66 (N.A.) {1,641.66}	100.00	55
		1285	4L OF EXISTING BEAS ? BABA BAKALA - DERA BABA NANAK SECTION FROM START OF BATALA BYPASS TILL INTERSE (NHAI) (N24002100)	10-2021	6/2025 (N.A.) {12/2025}	1,003.38 (N.A.) {1,003.38}	281.62	72.58
		1286	4L OF BEAS-MEHTA-BATALA-DERA BABA NANAK FROM INTERSECTION WITH JALANDHAR-AMRITSAR HIGHWAY (NH-3) NEA (NHAI) (N24002101)	8-2021	6/2025 (01-12-2025) {12/2025}	809.51 (N.A.) {809.51}	220.73	53.54
		1287	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I SPUR-I) FROM JN. WITH KAPURTHALA - SULTANPUR LODHI ROAD (NH (NHAI) (N24002102)	1-2020	4/2026 (N.A.) {4/2027}	2,165.23 (N.A.) {2,165.23}	180.85	20.5
		1288	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA (MoRTH) (N24000907)	3-2018	8/2020 (N.A.) {6/2025}	293.10 (N.A.) {315.00}	318.24	100
		1289	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 (MoRTH) (N24000909)	10-2017	10/2019 (N.A.) {12/2025}	1,069.59 (N.A.) {1,069.59}	739.08	44
		1290	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 (MoRTH) (N24000910)	3-2018	11/2020 (N.A.) {6/2026}	170.57 (N.A.) {150.00}	135.00	79
		1291	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES (MoRTH) (N24000941)	3-2018	8/2020 (N.A.) {8/2020}	293.64 (N.A.) {293.64}	295.46	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
RAJASTHAN	CIVIL AVIATION	1292	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT (AAI) (N04000101)	5-2022	11/2024 (01-10-2025) {10/2025}	480.00 (N.A.) {480.00}	254.71	77.75
		1293	UDAIPUR AIRPORT- CONSTRUCTION OF NEW INTEGRATED PASSENGER TERMINAL BUILDING (AAI) (N04000104)	6-2023	3/2026 (N.A.) {3/2026}	887.00 (N.A.) {887.00}	312.40	44.61
	COAL	1294	NLCIL 300 MW SOLAR POWER PROJECT (PART OF 510 MW CPSU SCHEME) (NLC) (N06000269)	3-2023	9/2024 (N.A.) {11/2025}	1,813.00 (N.A.) {1,813.00}	746.26	66
	PETROLEUM	1295	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE (IOCL) (N16000435)	12-2021	10/2024 (01-12-2025) {12/2025}	9,028.00 (N.A.) {9,028.00}	6,734.76	82.3
		1296	CGD PROJECT IN TONK, SAWAI MADHOPUR, DAUSA, KARALI (HPCL) (N16000496)	3-2022	3/2030 (N.A.) {3/2030}	1,751.00 (N.A.) {1,751.00}	301.39	25.5
		1297	SETTING UP OF PETROCHEMICAL EVACUATION MARKETING TERMINAL (PEMT) AT BARMER (HPCL) (N16000512)	12-2023	12/2026 (N.A.) {12/2026}	461.05 (N.A.) {461.05}	98.70	47.5
		1298	RAJASTHAN REFINERY PROJECT (HPCLRRL(JV)) (N16000513)	10-2017	10/2022 (01-03-2025) {12/2025}	43,129.00 (72,937.00) {72,937.00}	58,305.57	87.4
		1299	CGD PROJECTS AT FAZILKA (EXCEPT AREA ALREADY AUTHORIZED) GANGANAGAR AND HANUMANGARH DISTRICTS (BPCL) (N16000520)	12-2022	6/2030 (N.A.) {6/2030}	3,207.00 (N.A.) {3,207.00}	324.65	21.9
	POWER	1300	SAMBHU KI BHURJ-II SOLAR 300MW (NTPC) (N18000286)	3-2020	9/2021 (01-03-2025) {3/2025}	1,782.00 (N.A.) {1,782.00}	1,369.88	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1301	BHENSARA 320 MW (NTPC) (N18000293)	1-2021	7/2022 (01-03-2025) {3/2025}	1,221.73 (1,533.38) {1,533.38}	1,139.42	100
		1302	NOKH PLOT-1 SOLAR PV PROJECT 245MW (NTPC) (N18000320)	3-2022	8/2023 (N.A.) {6/2025}	1,352.71 (N.A.) {1,352.71}	1,057.36	0
		1303	NOKH PLOT-2 SOLAR PV PROJECT 245MW (NTPC) (N18000321)	3-2022	8/2023 (N.A.) {3/2025}	1,409.52 (N.A.) {1,409.52}	1,403.89	0
		1304	NOKH PLOT-3 SOLAR PV PROJECT 245MW (NTPC) (N18000322)	3-2022	8/2023 (N.A.) {5/2025}	1,426.94 (N.A.) {1,426.94}	1,170.29	0
		1305	BHADLA-II 500MW SOLAR PV PROJECT (NTPC) (N18000347)	6-2022	3/2024 (01-09-2025) {9/2025}	2,598.92 (N.A.) {2,598.92}	1,815.27	60
		1306	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART (PGCIL) (N18000356)	3-2023	9/2024 (N.A.) {9/2025}	1,433.28 (N.A.) {1,433.28}	1,290.22	91.9
		1307	300 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000368)	5-2022	11/2023 (N.A.) {9/2025}	1,677.12 (N.A.) {1,677.12}	1,295.80	92
		1308	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III, PART E1 (PGCIL) (N18000373)	8-2023	2/2025 (N.A.) {9/2025}	688.74 (N.A.) {688.74}	564.77	93
		1309	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART H (PGCIL) (N18000374)	10-2023	4/2025 (N.A.) {8/2025}	2,211.00 (N.A.) {2,211.00}	1,702.27	69.4

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1310	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART C1 (PGCIL) (N18000375)	10-2023	4/2025 (01-10-2025) {10/2025}	1,796.00 (N.A.) {1,796.00}	1,149.44	77.3
		1311	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART B1 (PGCIL) (N18000376)	9-2023	4/2025 (N.A.) {9/2025}	2,191.00 (N.A.) {2,191.00}	1,511.45	75.7
		1312	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART J (PGCIL) (N18000378)	12-2022	3/2025 (01-04-2026) {4/2026}	331.00 (N.A.) {331.00}	18.23	27
		1313	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART E2 (PGCIL) (N18000379)	11-2023	6/2025 (N.A.) {9/2025}	428.00 (N.A.) {428.00}	85.60	45
		1314	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART A [BIKANER III N (PGCIL) (N18000386)	12-2023	12/2025 (N.A.) {12/2025}	2,998.00 (N.A.) {2,998.00}	1,439.18	47.1
		1315	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART D [NEEMRANA II B (PGCIL) (N18000387)	12-2023	12/2025 (N.A.) {12/2025}	2,056.00 (N.A.) {2,056.00}	1,318.23	53.3
		1316	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PH-III PART D [SIKAR KHETRI TRANSMISSION] (PGCIL) (N18000389)	2-2024	8/2025 (N.A.) {9/2025}	2,000.00 (N.A.) {2,000.00}	1,200.00	58
		1317	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) PART- B (JAISALMER/BARMER COMPLEX) (PGCIL) (N18000391)	8-2024	8/2026 (N.A.) {8/2026}	3,279.00 (N.A.) {3,279.00}	491.85	18.6

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1318	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-C (PGCIL) (N18000393)	8-2024	8/2026 (N.A.) {8/2026}	2,227.00 (N.A.) {2,227.00}	489.94	18.6
		1319	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-E (PGCIL) (N18000394)	8-2024	8/2026 (N.A.) {8/2026}	3,251.00 (N.A.) {3,251.00}	650.20	16.2
		1320	ADDITIONAL TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM BHADLA-III PS AS PART OF RAJASTHAN REZ P (PGCIL) (N18000396)	8-2024	2/2026 (N.A.) {2/2026}	369.00 (N.A.) {369.00}	10.30	3.8
		1321	TRANSMISSION SYSTEM STRENGTHENING FOR INTERCONNECTIONS OF BHADLA-III AND BIKANER III COMPLEX [SPV NA (PGCIL) (N18000397)	8-2024	8/2026 (N.A.) {8/2026}	1,382.00 (N.A.) {1,382.00}	27.60	1
		1322	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-2 5.5 GW] [JAISALMER/BAR (PGCIL) (N18000401)	11-2024	11/2026 (N.A.) {11/2026}	2,735.00 (N.A.) {2,735.00}	27.35	3.8
		1323	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6GW)] [BIKANER COMPLEX (PGCIL) (N18000403)	11-2024	11/2026 (N.A.) {11/2026}	5,969.00 (N.A.) {5,969.00}	101.47	0
		1324	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6 GW)] [BIKANER COMPLE (PGCIL) (N18000404)	11-2024	11/2026 (N.A.) {11/2026}	5,357.00 (N.A.) {5,357.00}	107.14	3.8
		1325	RAJASTHAN REZ PH-V (PART-1: 4 GW) [SIROHI/NAGAUR] COMPLEX (PGCIL) (N18000414)	3-2025	3/2027 (N.A.) {3/2027}	5,028.00 (N.A.) {5,028.00}	20.12	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1326	AUGMENTATION AT FATEHGARH-II PS, FATEHGARH-IV PS (SECTION-II) AND BARMER-I (PGCIL) (N18000415)	3-2025	12/2026 (N.A.) {12/2026}	404.00 (N.A.) {428.00}	4.04	0
		1327	NOKH SOLAR PV PROJECT 735 MW (NTPC) (N18000418)	3-2022	4/2024 (01-07-2025) {7/2025}	4,189.17 (4,378.17) {4,378.17}	213.45	97
	RAILWAYS	1328	AGRA FORT-BANDIKUI (NCR) (N22000553)	6-2022	6/2027 (01-05-2026) {5/2026}	1,389.81 (N.A.) {987.83}	42.46	12
		1329	GUDHA THATHANA MITHRI TEST TRACK FOR RDSO (NWR) (N22000593)	4-2019	3/2025 (01-06-2025) {6/2025}	528.48 (N.A.) {500.85}	357.48	98
		1330	DEDICATED TEST TRACK FOR RDSO (PHASE II) (NWR) (N22000594)	11-2021	11/2026 (N.A.) {12/2025}	466.42 (N.A.) {466.22}	743.91	83
		1331	DOUBLING BETWEEN CHURU-RATANGARH (42.81 KM) (NWR) (N22000605)	2-2023	2/2028 (N.A.) {6/2025}	422.60 (N.A.) {422.60}	216.78	95
		1332	SAWAIMADHOPUR - BYPASS LINE (6.98 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NWR) (N22000607)	12-2022	6/2026 (01-05-2027) {5/2027}	304.00 (239.54) {239.54}	133.73	35
		1333	GC OF NATHDWARA - DEVGARH MADARIYA (82.5KM) (NWR) (N22000608)	1-2023	6/2028 (01-12-2026) {12/2026}	968.92 (N.A.) {968.92}	410.60	42
	ROAD TRANSPORT AND HIGHWAYS	1334	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. (MoRTH) (N24001411)	12-2020	10/2023 (N.A.) {12/2025}	379.23 (N.A.) {379.23}	268.62	96.1

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1335	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR (MoRTH) (N24001527)	12-2021	5/2024 (01-12-2025) {12/2025}	411.40 (N.A.) {411.40}	219.61	72
		1336	WIDENING OF PACHPADRA-BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE (MoRTH) (N24001528)	1-2022	12/2024 (01-08-2025) {8/2025}	194.88 (N.A.) {194.88}	105.69	83
		1337	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH-68) IN THE STATE OF RAJASTHAN ON EPC M (MoRTH) (N24001529)	12-2021	8/2024 (01-05-2025) {5/2025}	451.66 (N.A.) {451.66}	401.78	99
		1338	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN-LALSOT-KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH (MoRTH) (N24001530)	12-2021	9/2024 (N.A.) {8/2025}	150.11 (N.A.) {150.11}	82.83	88
		1339	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR (NHAI) (N24001557)	3-2022	11/2024 (01-08-2025) {8/2025}	1,636.15 (N.A.) {1,636.15}	553.96	99.8
		1340	4L OF KARWAR (KM. 281.980 OF NH-62 NAGPUR ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) (NHAI) (N24001558)	11-2021	8/2024 (01-07-2025) {7/2025}	736.75 (N.A.) {736.75}	260.95	97.8
		1341	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE -0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK (NHAI) (N24001559)	9-2021	6/2024 (01-04-2025) {4/2025}	672.35 (N.A.) {672.35}	328.24	99.5
		1342	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) (NHAI) (N24001563)	10-2019	8/2023 (01-07-2025) {7/2025}	846.59 (N.A.) {846.59}	167.92	99.25

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1343	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7) (NHAI) (N24001564)	10-2019	7/2023 (01-07-2025) {7/2025}	662.08 (N.A.) {662.08}	128.28	96.5
		1344	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA (NHAI) (N24001567)	11-2019	10/2022 (01-08-2025) {8/2025}	1,272.97 (N.A.) {1,272.97}	527.31	89.63
		1345	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N (NHAI) (N24001568)	11-2019	5/2023 (01-07-2025) {7/2025}	1,119.35 (N.A.) {1,119.35}	1,447.44	99.8
		1346	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M (NHAI) (N24001573)	11-2019	12/2022 (01-07-2025) {7/2025}	1,658.06 (N.A.) {1,658.06}	157.42	99.9
		1347	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH (NHAI) (N24001612)	7-2020	1/2024 (01-12-2025) {12/2025}	1,788.69 (N.A.) {1,788.69}	965.50	78.5
		1348	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FOR FATEHPUR BYPASS, MANDAWA BYPASS AND JHUNJHUNU BYPAS (MoRTH) (N24001866)	3-2022	8/2024 (N.A.) {6/2025}	186.29 (N.A.) {186.29}	142.69	90
		1349	UPGRADATION OF TWO LANE PAVED SHOULDER FROM SHAHPURA TO THANAGAZI OF NH-248A ON EPC MODE IN THE STAT (MoRTH) (N24001867)	3-2022	7/2024 (N.A.) {8/2025}	174.34 (N.A.) {174.34}	118.08	90
		1350	Sagwara Bypass and Garhi- Partapur Bypass of NH-927A in the State of Rajasthan. (MoRTH) (N24001868)	3-2022	8/2025 (N.A.) {8/2025}	187.65 (N.A.) {187.65}	117.57	90

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1351	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF GHAGARIYA-MUNABAO SECTION FROM KM (MoRTH) (N24001869)	12-2022	8/2025 (N.A.) {8/2025}	235.15 (N.A.) {235.15}	159.69	100
		1352	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FROM CHARBHUJA AT DESIGN KM 0.00 (EXISTING KM 150.00) TO (MoRTH) (N24001927)	2-2022	9/2025 (N.A.) {9/2025}	838.43 (N.A.) {838.43}	455.87	99
		1353	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER NORTHERN BYPASS PHASE-II OF KOTA CITY FROM DESIGN CHAINAG (MoRTH) (N24001928)	3-2022	4/2025 (N.A.) {12/2025}	317.74 (N.A.) {317.74}	136.23	13
		1354	ADDITIONAL STRUCTURES ON 6LGURGAON-JAIPUR SECTION OF NH-48 BETWEEN KM 42.700 TO KM 273.00 (NHAI) (N24002058)	8-2022	6/2024 (01-07-2025) {7/2025}	409.64 (N.A.) {409.64}	240.90	81.65
		1355	UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF HANUMANGARH TO KENCHIYAN OF NH 54 ON EPC MODE IN THE ST (MoRTH) (N24002167)	3-2024	10/2026 (N.A.) {10/2026}	334.64 (N.A.) {334.64}	128.00	50
		1356	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM NEECHLI ODEN (NATHDWARA) AT DESIGN KM 88.800 TO BHATE (MoRTH) (N24002168)	3-2023	10/2026 (N.A.) {10/2026}	606.61 (N.A.) {606.61}	118.00	20
		1357	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA (NHAI) (N24000795)	2-2018	4/2021 (01-06-2025) {6/2025}	741.86 (649.00) {649.00}	663.37	99.99
SIKKIM	CIVIL AVIATION	1358	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	29.68	12.5

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	DEPARTMENT OF HIGHER EDUCATION	1359	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8-2020	1/2025 (N.A.) {1/2025}	314.06 (N.A.) {303.55}	157.24	80
	POWER	1360	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,424.21	68.17
		1361	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,524.17	89.45
	RAILWAYS	1362	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	5/2015 (01-12-2027) {12/2027}	7,876.92 (11,963.43) {11,963.43}	8,743.57	79.5
	ROAD TRANSPORT AND HIGHWAYS	1363	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (01-10-2023) {12/2025}	183.31 (439.56) {439.56}	355.31	51.85
		1364	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (01-08-2024) {12/2025}	262.84 (414.20) {414.20}	221.86	49.2
		1365	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (01-10-2023) {12/2025}	292.80 (N.A.) {292.80}	202.92	61.41
		1366	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (01-10-2024) {3/2026}	230.45 (244.91) {244.91}	206.95	82.8
		1367	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (01-07-2025) {3/2026}	493.42 (478.79) {478.79}	308.18	59.49

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1368	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (01-06-2025) {12/2026}	816.79 (786.60) {786.60}	332.24	45.9
		1369	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1-2021	9/2023 (01-04-2025) {12/2025}	332.20 (348.92) {348.92}	149.38	0
		1370	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (01-12-2025) {12/2025}	410.60 (379.30) {379.30}	238.13	74.82
		1371	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (01-03-2026) {3/2026}	385.15 (N.A.) {385.15}	175.16	83.3
		1372	SPECIAL PROTECTION WORK ON REHABILITATION AND RESTORATION OF SLIDING AND SINKING ZONE FROM RANGPO TO (NHIDCL) (N24001913)	3-2017	6/2022 (N.A.) {6/2022}	165.56 (N.A.) {165.56}	-	71.74
		1373	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (01-05-2022) {12/2023}	375.80 (N.A.) {375.80}	288.56	96.55
		1374	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11-2017	10/2020 (01-08-2023) {4/2024}	290.05 (N.A.) {290.05}	218.36	100
		1375	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {10/2025}	402.94 (N.A.) {402.94}	247.12	76.54

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1376	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (01-11-2024) {10/2025}	295.97 (N.A.) {295.97}	249.97	95.71
		1377	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100
		1378	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {10/2025}	311.00 (N.A.) {273.78}	257.86	95.12
		1379	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (01-08-2024) {10/2025}	345.38 (395.59) {395.59}	362.61	89.81
TAMIL NADU	CIVIL AVIATION	1380	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI (AAI) (N04000074)	6-2018	2/2022 (01-06-2026) {6/2026}	2,467.00 (N.A.) {2,467.00}	1,620.03	71.65
		1381	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI (AAI) (N04000075)	8-2018	10/2021 (01-12-2023) {12/2023}	951.28 (1,112.49) {1,112.49}	1,084.94	100
		1382	DEVELOPMENT OF TUTICORIN AIRPORT (AAI) (N04000090)	6-2019	3/2022 (01-04-2025) {4/2025}	380.87 (451.74) {451.74}	362.06	100
	COAL	1383	JAWAHAR KHANI OPENCAST (JK OC) MINE (SCCL) (N06000259)	12-2021	3/2025 (N.A.) {3/2026}	297.88 (N.A.) {297.88}	46.37	20

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1384	50 MW SOLAR POWER PROJECT -NEYVELI MINED OUT AREA (NLC) (N06000279)	5-2023	6/2025 (01-11-2025) {11/2025}	218.03 (N.A.) {218.03}	148.89	40
	FINANCE	1385	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI (CPWD FOR FINANC) (N28000109)	11-2017	11/2021 (N.A.) {11/2022}	348.77 (N.A.) {348.77}	223.39	100
	MINES	1386	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (NALCO) (N10000014)	9-2017	6/2019 (01-12-2025) {12/2025}	166.62 (163.17) {163.17}	135.63	65
	PETROLEUM	1387	IRUGUR-DEVANGONTHI POL PIPELINE (BPCL) (N16000234)	11-2012	2/2017 (01-10-2025) {10/2025}	678.00 (1,732.00) {1,732.00}	642.76	64.1
		1388	CBR 9 MMTA PROJECT (CPCL) (N16000434)	1-2021	6/2025 (N.A.) {6/2025}	31,580.00 (31,580.00) {36,354.00}	1,326.17	10.2
		1389	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI (IOCL) (N16000438)	1-2022	7/2024 (01-06-2025) {12/2025}	827.00 (887.71) {887.71}	580.94	85.9
		1390	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) (IOCL) (N16000455)	1-2022	7/2024 (01-05-2026) {5/2026}	829.00 (N.A.) {829.00}	259.48	60.16
		1391	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS (IOCL) (N16000486)	3-2022	3/2030 (N.A.) {12/2030}	501.00 (N.A.) {501.00}	112.66	5.3
		1392	CGD PROJECTS AT THE NILGIRIS AND ERODE DISTRICTS (BPCL) (N16000521)	12-2022	3/2030 (N.A.) {3/2030}	3,685.00 (N.A.) {3,685.00}	213.89	11.2

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	1393	TRANSMISSION SYSTEM UNDER ISTS FOR EVACUATION OF POWER FROM KUDANKULAM UNIT - 3 AND 4 (2X1000 MW) (PGCIL) (N18000408)	1-2025	7/2028 (N.A.) {7/2028}	548.00 (N.A.) {548.00}	9.32	2.5
	RAILWAYS	1394	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP (M RTP) (N22000028)	4-2006	7/2024 (01-08-2025) {8/2025}	734.01 (981.83) {981.83}	640.43	98
		1395	TIDIVANAM-NAGARI (NL) (SR) (N22000085)	9-2006	9/2016 (01-03-2028) {3/2028}	3,631.34 (3,631.34) {3,631.34}	873.31	15
		1396	CHENNAI BEACH-CHENNAI EGMORE (4.3 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SR) (N22000568)	3-2022	3/2026 (01-02-2025) {3/2025}	359.60 (274.20) {310.00}	305.93	95
		1397	MORAPPUR-DHARMAPURI (SR) (N22000618)	2-2019	3/2028 (01-03-2028) {3/2028}	358.95 (N.A.) {358.95}	40.09	0
		1398	KARAIKAL PERALAM(23KM)-NEW LINE PROJECT (SR) (N22000625)	1-2019	3/2026 (01-03-2025) {6/2025}	304.22 (N.A.) {373.42}	292.65	97
		1399	NAGAPATTINAM THIRUTURAIPUNDI (38KM)- NEW LINE PROJECT (SR) (N22000626)	7-2008	3/2026 (01-03-2027) {3/2027}	677.12 (N.A.) {668.44}	146.95	20
	ROAD TRANSPORT AND HIGHWAYS	1400	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON (NHAI) (N24001428)	3-2018	11/2021 (01-06-2025) {6/2025}	998.70 (1,358.32) {1,358.32}	975.74	98.32
		1401	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER (NHAI) (N24001429)	3-2018	11/2021 (01-07-2025) {7/2025}	1,294.47 (1,588.40) {1,588.40}	867.34	98.72

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1402	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM (NHAI) (N24001430)	3-2018	1/2022 (01-06-2025) {6/2025}	2,120.40 (2,565.63) {2,565.63}	1,588.35	99.8
		1403	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN (NHAI) (N24001431)	3-2018	10/2020 (01-01-2026) {1/2026}	1,872.68 (2,899.77) {2,899.77}	1,341.26	65
		1404	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 (MoRTH) (N24001455)	2-2022	8/2022 (N.A.) {3/2025}	191.33 (207.97) {207.97}	100.42	100
		1405	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) (NHAI) (N24001600)	10-2020	5/2023 (01-06-2025) {6/2025}	434.12 (N.A.) {434.12}	268.92	100
		1406	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 (NHAI) (N24001601)	1-2019	1/2023 (01-11-2025) {11/2025}	1,051.69 (N.A.) {1,051.69}	589.46	81.87
		1407	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001602)	1-2019	12/2022 (01-11-2025) {11/2025}	1,409.38 (N.A.) {1,409.38}	660.29	91.2
		1408	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001603)	1-2019	10/2022 (01-06-2025) {6/2025}	1,518.53 (N.A.) {1,607.54}	915.40	100
		1409	4-LANING OF MELUR - PILLAYARPATTI - KARAIKUDI SECTION OF NH-338, NH-36, NH- 383 (NHAI) (N24001605)	6-2018	3/2022 (N.A.) {8/2025}	1,103.86 (N.A.) {1,103.86}	568.15	87

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1410	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH-744A (MADURAI RING ROAD) (NHAI) (N24001606)	12-2018	3/2022 (01-09-2025) {9/2025}	854.94 (N.A.) {854.94}	400.13	80.3
		1411	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS (NHAI) (N24001692)	1-2022	9/2024 (01-02-2025) {8/2025}	467.99 (N.A.) {468.00}	113.05	84.34
		1412	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 (NHAI) (N24001693)	9-2021	10/2024 (N.A.) {10/2024}	1,751.18 (N.A.) {1,757.27}	49.69	0
		1413	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG- II) FROM KM.23+350 TO KM (NHAI) (N24001694)	2-2019	12/2023 (01-12-2024) {12/2024}	1,243.57 (N.A.) {1,243.57}	171.63	0
		1414	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460 (NHAI) (N24001696)	2-2019	8/2023 (01-12-2024) {12/2024}	1,291.37 (N.A.) {1,291.37}	215.02	0
		1415	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM (NHAI) (N24001716)	7-2022	8/2023 (01-12-2024) {12/2024}	186.50 (242.40) {242.40}	34.33	100
		1416	BANGALORE CHENNAI EXPRESSWAY PHASE- III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K (NHAI) (N24001717)	11-2020	8/2024 (N.A.) {3/2026}	1,155.49 (1,525.10) {1,525.10}	489.94	53.56
		1417	BANGALORE CHENNAI EXPRESSWAY PHASE- III PACKAGE II (WALAJAHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 (NHAI) (N24001718)	12-2020	7/2024 (N.A.) {10/2025}	843.48 (1,077.40) {1,068.60}	434.49	91.26

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1418	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT (NHAI) (N24001719)	2-2021	7/2024 (N.A.) {12/2025}	2,948.31 (3,605.73) {3,605.73}	820.23	78.11
		1419	BANGALORE CHENNAI EXPRESSWAY PHASE- III ? PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1 (NHAI) (N24001720)	10-2020	5/2024 (N.A.) {10/2025}	1,023.91 (1,438.62) {1,438.62}	635.04	86.22
		1420	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 (NHAI) (N24001721)	2-2019	5/2024 (01-08-2025) {3/2026}	1,008.99 (1,360.53) {1,360.53}	324.81	50.33
		1421	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH (NHAI) (N24001722)	11-2021	2/2023 (N.A.) {12/2024}	463.44 (463.07) {463.44}	334.80	99
		1422	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 (NHAI) (N24001723)	10-2018	2/2021 (N.A.) {8/2025}	707.90 (766.51) {766.51}	542.69	91
		1423	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 (NHAI) (N24001725)	1-2019	5/2021 (N.A.) {1/2025}	819.89 (1,314.82) {922.85}	419.84	57.32
		1424	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 ? 29/250 INCLUDING LA AND SHIFTING OF NH-234 (MoRTH) (N24001828)	1-2022	11/2024 (N.A.) {5/2025}	221.03 (243.95) {243.95}	176.50	100
		1425	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU (MoRTH) (N24001829)	10-2022	11/2024 (N.A.) {5/2025}	172.15 (N.A.) {172.15}	163.82	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1426	CONSTRUCTION OF STRR (WEST SIDE)- NH948A-BALAGONDAPALLI (TAMIL NADU) TO KARNATAKA/TAMIL NADU BORDER F (NHAI) (N24001968)	4-2022	5/2025 (N.A.) {5/2025}	1,260.74 (N.A.) {1,260.74}	487.46	44.95
		1427	4L OF THIRUMANGALAM TO VADUGAPATTI SECTION FROM KM 0.000 TO KM 36.000 OF NH- 744 (NHAI) (N24002084)	3-2022	2/2025 (N.A.) {9/2025}	1,076.97 (N.A.) {1,076.97}	540.46	87.42
		1428	CONSTRUCTION OF NEW DOUBLE TIER 4 LANE ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI (NHAI) (N24002107)	3-2023	5/2026 (N.A.) {5/2026}	1,382.00 (N.A.) {1,382.00}	-	0
		1429	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002108)	3-2023	5/2026 (N.A.) {5/2026}	1,618.96 (N.A.) {1,618.96}	-	0
		1430	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002109)	3-2023	5/2026 (N.A.) {5/2026}	1,301.37 (N.A.) {1,301.37}	-	0
		1431	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002110)	3-2023	5/2026 (N.A.) {5/2026}	1,207.40 (N.A.) {1,207.40}	-	0
		1432	FOUR LANING OF MUGAIYUR TO MARAKKANAM SECTION OF NH-332A FROM KM 31.000 TO KM 62.000 (NHAI) (N24002111)	2-2019	12/2025 (01-05-2026) {5/2026}	825.94 (1,116.13) {1,116.13}	344.92	40.55
		1433	SIX LANING OF TUTICORIN PORT ROAD SECTION OF NH-7A (NEW NH-138) FROM KM 0.000 TO KM 6.140 [EFFECTIVE (NHAI) (N24002112)	3-2023	7/2024 (N.A.) {7/2025}	200.30 (N.A.) {200.30}	113.71	93.11

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1434	4L OF LEFT-OVER WORKS INCLUDING ADDITIONAL STRUCTURES FROM KERALA/TAMIL NADU BORDER TO KANYAKUMARI S (NHAI) (N24002113)	3-2023	8/2025 (N.A.) {8/2025}	1,141.78 (N.A.) {1,141.78}	466.20	47.86
		1435	4L OF VADUGAPATTI TO THERKUVENGANALLUR (RAJAPALYAM) SECTION FROM KM 36.000 TO KM 71.600 OF NH744 UND (NHAI) (N24002114)	2-2022	4/2025 (N.A.) {10/2025}	1,097.59 (N.A.) {1,317.06}	705.17	97.8
		1436	WIDENING TO 4L/4L+PS AND STRENGTHENING IN SELECTED STRETCHES FROM KM 0/8 TO 50/570 OF NH 532 INCLUD (MoRTH) (N24002151)	3-2022	1/2024 (N.A.) {7/2025}	257.14 (294.70) {294.70}	277.57	90
		1437	WIDENING FROM 2L+PS TO 4L/4L+PS AND IMPROVEMENTS THE SELECTED STRETHCES FROM KM 26/5 - 81/2 INCLU (MoRTH) (N24002152)	3-2023	11/2023 (N.A.) {11/2025}	274.84 (N.A.) {274.84}	265.83	100
		1438	STRENGTHENING OF 2L+PS FROM KM 17/8 ? 18/2, CONSTRUCTION OF 2L+PS FROM KM 18/2 TO KM 20/0 AND CONSTR (MoRTH) (N24002153)	3-2023	2/2024 (N.A.) {8/2025}	169.68 (N.A.) {169.68}	145.29	100
		1439	CONSTRUCTION OF BYPASS TO MADURAI - ACHAMBATHU - VIRATIPATHU IN KM 6/850 - 10/382 OF NH 49 EXTN. (NE (MoRTH) (N24002165)	3-2022	8/2026 (N.A.) {8/2026}	238.97 (260.07) {260.07}	118.00	50
		1440	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TIRUVALLUR (DESIGN CHAINAGE KM 17+56) (NHAI) (N24002216)	12-2024	12/2026 (N.A.) {12/2026}	1,376.10 (N.A.) {1,376.10}	39.00	8.74
		1441	FOUR LANNING OF CHOLOPURAM- THANJAVUR (NHAI) (N24000697)	8-2017	9/2020 (N.A.) {7/2025}	1,176.37 (N.A.) {1,176.37}	1,325.06	99.5

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
TELANGANA		1442	4-LANNING OF STHIYATHOPU-CHOLOPURAM (NHAI) (N24000708)	9-2017	8/2020 (01-07-2025) {7/2025}	1,227.87 (N.A.) {1,227.87}	1,436.16	99.5
		1443	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 (NHAI) (N24000826)	3-2018	10/2022 (01-07-2025) {7/2025}	505.35 (N.A.) {837.69}	376.61	99.75
	CIVIL AVIATION	1444	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD (AAI) (N04000086)	5-2020	5/2022 (01-06-2023) {6/2023}	353.61 (N.A.) {353.61}	303.22	100
	COAL	1445	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 (SCCL) (N06000161)	3-2017	3/2022 (N.A.) {3/2026}	413.84 (N.A.) {413.84}	397.54	85
		1446	GODAVARIKHANI COAL MINE (SCCL) (N06000202)	7-2019	3/2023 (N.A.) {3/2026}	438.98 (N.A.) {438.98}	178.21	70
		1447	VENKATESH KHANI COAL MINE (SCCL) (N06000204)	10-2020	3/2023 (N.A.) {3/2027}	484.51 (N.A.) {484.51}	318.12	55
		1448	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT (SCCL) (N06000210)	11-2015	3/2023 (N.A.) {3/2026}	489.62 (N.A.) {489.62}	405.54	70
		1449	RCE OF INDARAM OPENCAST PROJECT (SCCL) (N06000211)	8-2017	3/2021 (N.A.) {3/2025}	349.28 (N.A.) {424.81}	402.64	80
		1450	RCE OF KALYANIKHANI OPENCAST PROJECT (SCCL) (N06000213)	3-2016	3/2020 (N.A.) {3/2026}	384.32 (N.A.) {384.32}	265.53	75

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1451	RCE OF KAKATHIYAKHANI OC - 2 PROJECT (SCCL) (N06000214)	8-2017	3/2020 (N.A.) {3/2026}	442.42 (N.A.) {442.42}	203.14	63
		1452	GOLETI OPENCAST MINE (SCCL) (N06000258)	7-2021	3/2026 (N.A.) {3/2026}	345.60 (N.A.) {345.60}	72.09	20
	HEALTH AND FAMILY WELFARE	1453	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD (CPWD FOR HEALTH) (N28000098)	10-2016	3/2020 (01-01-2025) {1/2025}	209.84 (281.05) {281.05}	253.64	98.5
		1454	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR (HITES) (N21000031)	12-2018	7/2024 (N.A.) {12/2025}	1,110.55 (N.A.) {1,110.55}	753.76	83.07
	RAILWAYS	1455	MANOHARABAD-KOTHPALL NEW LINE(SCR) (SCR) (N22000032)	4-2006	3/2027 (N.A.) {3/2025}	1,160.00 (N.A.) {3,014.00}	1,568.57	0
	ROAD TRANSPORT AND HIGHWAYS	1456	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM (NHAI) (N24001482)	8-2022	10/2024 (01-08-2022) {12/2025}	772.11 (N.A.) {772.11}	558.24	80.51
		1457	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUDEM V (NHAI) (N24001483)	2-2022	9/2024 (01-02-2022) {9/2025}	637.11 (N.A.) {637.11}	415.98	85.4
		1458	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUDEM VILLAGE TO RECHERLA (NHAI) (N24001484)	9-2022	2/2024 (01-09-2022) {9/2025}	804.69 (N.A.) {804.69}	514.29	91.2
		1459	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 (NHAI) (N24001522)	1-2021	1/2024 (01-01-2021) {7/2025}	1,307.95 (N.A.) {1,307.95}	727.42	99.98

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1460	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, (NHAI) (N24001555)	3-2022	1/2025 (N.A.) {1/2025}	955.49 (N.A.) {955.49}	233.46	35.96
		1461	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 (NHAI) (N24001556)	12-2021	7/2024 (N.A.) {7/2024}	521.53 (N.A.) {521.53}	250.70	49.63
		1462	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 (NHAI) (N24001625)	1-2022	1/2025 (N.A.) {7/2025}	1,227.57 (N.A.) {1,227.57}	288.58	45.65
		1463	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM (NHAI) (N24001626)	2-2022	1/2025 (N.A.) {1/2025}	972.06 (N.A.) {972.06}	408.48	70.26
		1464	WIDENING AND STRENGTHENING OF EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FRO (MoRTH) (N24002000)	3-2021	7/2024 (N.A.) {7/2024}	317.19 (N.A.) {317.19}	178.64	72
		1465	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF MEDAK - SIDDIPET SECTION FROM KM 0/0 TO KM 69/978 OF NH- (MoRTH) (N24002001)	1-2022	1/2025 (N.A.) {1/2025}	882.18 (N.A.) {882.18}	376.66	73.14
		1466	WIDENING AND IMPROVEMENT OF EXISTING CARRIAGE WAY TO 2 LANE WITH PAVED SHOULDERS FROM KM. 86/160 TO (MoRTH) (N24002002)	1-2022	12/2024 (N.A.) {12/2024}	423.48 (N.A.) {423.48}	166.39	71.65
		1467	REHABILITATION AND UP-GRADATION OF VALIGONDA TO THORRUR SECTION TO TWO LANE WITH PAVED SHOULDERS FRO (MoRTH) (N24002003)	1-2022	12/2024 (N.A.) {12/2024}	549.28 (N.A.) {549.28}	257.89	74.75

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1468	REHABILITATION AND UPGRADATION OF LB-NAGAR TO MALKAPUR SECTION TO 6-LANE MAIN CARRIAGEWAY WITH SERVI (MoRTH) (N24002004)	3-2021	7/2024 (N.A.) {7/2024}	545.11 (N.A.) {545.11}	198.03	76.64
		1469	WIDENING TO TWO LANE WITH PAVED SHOULDERS OF 'BODHAN BASAR BHAINSA ' SECTION FROM KM 38/900 TO 95/3 (MoRTH) (N24002005)	3-2022	3/2025 (N.A.) {3/2025}	644.45 (N.A.) {644.45}	221.65	93.6
		1470	ONSTRUCTION OF 4-LANE FLYOVER AT AMBERPET-X ROAD, HYDERABAD ON NH-202 IN THE STATE OF TELANGANA (MoRTH) (N24002006)	10-2017	6/2023 (N.A.) {6/2023}	186.71 (N.A.) {186.71}	149.64	92.1
		1471	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/000 TO KM 79/300 OF KALWAKURTHY - KOLLAPUR SECTI (MoRTH) (N24002007)	3-2022	7/2025 (N.A.) {7/2025}	886.69 (N.A.) {886.69}	252.22	67.94
		1472	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF SIDDIPET-ELKATHURTHY SECTION FROM KM 69/978 TO KM 133/6 (MoRTH) (N24002008)	1-2022	12/2024 (N.A.) {12/2024}	578.85 (N.A.) {578.85}	292.69	82.05
		1473	WIDENING AND STRENGTHENING TO 2/4 LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR ? CHINCHOLI SECTION FROM (MoRTH) (N24002009)	1-2022	1/2025 (N.A.) {7/2025}	703.68 (N.A.) {703.68}	210.72	76.45
		1474	WIDENING AND STRENGTHENING TO 4 LANE / 2-LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR-CHINCHOLI SECTION (MoRTH) (N24002010)	3-2022	3/2024 (N.A.) {10/2025}	631.49 (N.A.) {631.49}	75.33	28.98
		1475	IMPROVEMENT OF GEOMETRICS OF THONDUPALLY TO KOTHUR FROM KM 22.300 TO KM 34.14 OF NH-44-RCW (NHAI) (N24002082)	2-2022	9/2024 (N.A.) {1/2026}	541.58 (N.A.) {541.58}	34.98	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1476	FOUR LANING OF KARIMNAGAR-WARANGAL SECTION OF NH-563 FROM DESIGN CH.48.860 KM NEAR SH-1 CH.170.400 K (NHAI) (N24002083)	3-2022	7/2025 (N.A.) {7/2025}	2,146.86 (2,413.00) {2,414.46}	999.54	72.35
		1477	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM- VIJAYAWADA) (NHAI) (N24002190)	3-2023	8/2026 (N.A.) {8/2026}	983.00 (N.A.) {983.00}	-	8.5
		1478	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM - VIJAYAWADA) (NHAI) (N24002236)	3-2023	3/2025 (N.A.) {3/2027}	832.62 (N.A.) {832.62}	-	0
		1479	REHABILITATION AND UPGRADATION OF NH - 565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT (MoRTH) (N24000245)	1-2014	3/2016 (01-09-2019) {9/2019}	270.00 (N.A.) {270.00}	-	72.15
		1480	REHABILITATION AND UPGRADATION OF NH- 221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR (MoRTH) (N24000247)	10-2014	2/2017 (N.A.) {2/2017}	295.47 (N.A.) {295.47}	224.42	82.76
		1481	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM (MoRTH) (N24000248)	3-2015	1/2017 (N.A.) {1/2017}	153.21 (N.A.) {153.21}	100.96	93.2
		1482	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON (MoRTH) (N24000980)	10-2016	2/2019 (N.A.) {2/2019}	298.32 (N.A.) {298.32}	178.47	0
		1483	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ (MoRTH) (N24000981)	10-2016	3/2019 (N.A.) {3/2019}	248.83 (N.A.) {248.83}	173.79	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1484	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE (MoRTH) (N24000982)	1-2017	5/2019 (N.A.) {5/2019}	244.54 (N.A.) {244.54}	174.35	99.96
		1485	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH (MoRTH) (N24000983)	1-2017	10/2019 (N.A.) {10/2019}	196.52 (N.A.) {196.52}	125.53	92.74
		1486	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI (MoRTH) (N24000984)	1-2017	12/2019 (N.A.) {12/2019}	283.00 (N.A.) {283.00}	259.15	99.32
		1487	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION (MoRTH) (N24000986)	1-2017	5/2019 (N.A.) {5/2019}	300.00 (N.A.) {300.00}	239.93	99.09
		1488	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH (MoRTH) (N24000987)	1-2018	5/2020 (N.A.) {5/2020}	283.15 (N.A.) {283.15}	270.01	92.62
		1489	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 (MoRTH) (N24000988)	1-2018	12/2019 (N.A.) {12/2019}	230.03 (N.A.) {230.03}	231.31	100
		1490	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 (MoRTH) (N24000989)	2-2018	6/2020 (N.A.) {6/2020}	206.13 (N.A.) {206.13}	190.94	98.56
		1491	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT (MoRTH) (N24000990)	2-2018	11/2019 (N.A.) {11/2019}	294.13 (N.A.) {294.13}	198.75	90.1

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1492	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC) (MoRTH) (N24000993)	3-2018	9/2020 (N.A.) {9/2020}	322.81 (N.A.) {322.81}	315.23	98.14
		1493	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES (MoRTH) (N24000994)	3-2018	7/2020 (N.A.) {2/2026}	626.76 (N.A.) {626.76}	272.64	46
		1494	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR) (MoRTH) (N24000996)	1-2017	10/2019 (N.A.) {10/2019}	605.08 (N.A.) {605.08}	413.37	99.9
		1495	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL ? MALLAMPALLY SECTION OF NH-365 (MoRTH) (N24000997)	3-2018	7/2019 (N.A.) {7/2019}	192.67 (N.A.) {192.67}	176.37	96
		1496	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR (MoRTH) (N24000998)	1-2019	(N.A.) {}	193.19 (N.A.) {249.72}	222.58	100
		1497	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (01-09-2025) {9/2025}	656.00 (N.A.) {656.00}	427.77	83.17
TRIPURA	PETROLEUM							
	ROAD TRANSPORT AND HIGHWAYS	1498	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (01-10-2023) {11/2024}	159.13 (171.50) {171.50}	84.33	100
		1499	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {4/2025}	201.99 (N.A.) {287.47}	148.22	100
		1500	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (N.A.) {12/2025}	354.79 (N.A.) {354.79}	34.08	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1501	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (01-05-2025) {5/2025}	456.88 (N.A.) {456.88}	122.67	50.18
		1502	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {12/2025}	195.95 (N.A.) {195.95}	46.46	45.42
		1503	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	26.34	8.82
		1504	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	9.54	16.61
		1505	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	52.82	34.61
		1506	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	95.71	32.85
		1507	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	3.81	3.05
		1508	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	81.54	24.56
		1509	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM SECTION PKG-4 (NHIDCL) (N24002228)	1-2024	12/2026 (N.A.) {12/2026}	726.90 (N.A.) {726.90}	7.36	3.85

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1510	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (01-02-2024) {12/2024}	277.50 (302.02) {302.02}	262.91	99.94
UTTAR PRADESH	CIVIL AVIATION	1511	CCS INTERNATIONAL AIRPORT , LUCKNOW (AAI) (N04000077)	6-2018	9/2021 (01-10-2026) {10/2026}	1,383.00 (1,938.00) {3,291.81}	2,652.63	80.58
		1512	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 (AAI) (N04000094)	3-2021	12/2022 (01-07-2025) {7/2025}	242.14 (328.00) {358.00}	344.58	99.9
		1513	PRAYAGRAJ AIRPORT - CONSTRUCTION OF NEW TERMINAL BUILDING, SECOND LINK TAXI TRACK, APRON EXPANSION, (AAI) (N04000102)	5-2023	11/2024 (01-07-2025) {7/2025}	185.75 (274.38) {274.38}	206.39	97.25
		1514	AGRA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT AGRA AIRPORT. (AAI) (N04000113)	6-2024	7/2026 (N.A.) {7/2026}	579.00 (N.A.) {579.00}	72.23	13
		1515	VARANASI: DEVELOPMENT OF LAL BAHADUR SHASTRI INTERNATIONAL AIRPORT, VARANASI. (AAI) (N04000114)	7-2024	7/2027 (N.A.) {7/2027}	2,869.65 (N.A.) {2,869.65}	283.00	14.51
	COAL	1516	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW (NLC) (N06000152)	7-2016	11/2021 (01-10-2025) {10/2025}	17,237.00 (21,780.94) {21,780.94}	19,949.00	91.39
		1517	KHADIA EXPANSION OCP (NCL) (N06000208)	6-2021	3/2025 (N.A.) {3/2027}	491.67 (N.A.) {491.67}	202.24	40.86
	HOME AFFAIRS	1518	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI (CPWD FOR MHA) (N45000003)	5-2019	1/2022 (01-03-2023) {3/2023}	199.31 (N.A.) {199.31}	86.49	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	1519	60 KTA POLYPROPYLENE PROJECT (GAIL) (N16000429)	3-2019	4/2024 (01-04-2024) {7/2025}	910.56 (1,299.02) {1,299.02}	974.00	96.9
		1520	AUGMENTATION OF FACILITIES AT MATHURA BITUMEN PLANT (IOCL) (N16000505)	4-2022	4/2025 (01-12-2026) {12/2026}	260.12 (N.A.) {260.12}	1.07	25
		1521	GRASS-ROOT TERMINAL AT MIRZAPUR UTTAR PRADESH (IOCL) (N16000506)	9-2022	6/2026 (N.A.) {11/2026}	980.45 (N.A.) {980.45}	206.85	50.75
		1522	CITY GAS DISTRIBUTION PROJECTS AT LAKHIMPUR KHERI , SITAPUR, BAHAIRCH, SHRAVASTI,BALRAMPUR, (BPCL) (N16000525)	12-2022	6/2030 (N.A.) {6/2030}	16,654.00 (N.A.) {16,654.00}	550.36	9.7
	POWER	1523	KHURJA SUPER THERMAL POWER PROJECT (THDCIL) (N18000272)	3-2019	9/2023 (N.A.) {8/2025}	11,089.42 (13,276.16) {13,276.16}	12,580.53	96
		1524	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III (2X800 MW) (NTPC) (N18000382)	3-2024	2/2030 (N.A.) {2/2030}	17,195.31 (N.A.) {17,195.31}	1,569.79	0.5
		1525	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART- 4: 3.5 GW): PART A (PGCIL) (N18000407)	12-2024	12/2026 (N.A.) {12/2026}	5,846.00 (N.A.) {5,846.00}	198.76	2.1
		1526	TRANSMISSION SYSTEM FOR STRENGTHENING TO FACILITATE EVACUATION OF POWER FROM BHADLA/BIKANER COMPLEX (PGCIL) (N18000423)	12-2024	6/2026 (N.A.) {6/2026}	213.00 (N.A.) {213.00}	-	0
	RAILWAYS	1527	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING (RVNL) (N22000401)	4-2015	12/2024 (N.A.) {12/2024}	2,018.23 (N.A.) {2,018.23}	1,780.22	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1528	2880.4 (ECR) (N22000417)	8-2015	8/2024 (N.A.) {1/2025}	2,880.40 (2,880.40) {2,880.40}	3,074.78	100
		1529	KARAILA ROAD - SHAKTINAGAR DOUBLING (ECR) (N22000419)	8-2015	8/2024 (N.A.) {12/2024}	762.97 (762.97) {762.97}	808.96	100
		1530	BURHWAL - GONDA - 3RD RUNNING LINE. (NER) (N22000468)	4-2016	3/2025 (N.A.) {9/2025}	1,015.59 (N.A.) {1,450.00}	1,277.57	52
		1531	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU- SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. (NER) (N22000470)	4-2016	12/2024 (N.A.) {8/2025}	1,177.96 (N.A.) {2,145.00}	2,050.16	85
		1532	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING (NCR) (N22000495)	3-2018	3/2026 (N.A.) {3/2027}	4,329.53 (N.A.) {4,329.53}	2,125.66	50
		1533	JHANSI BINA DOUBLING (NCR) (N22000496)	9-2016	3/2022 (N.A.) {4/2026}	2,002.00 (N.A.) {2,001.00}	1,745.48	90
		1534	MATHURA-JHANSI-3RD LINE (273.80 KM) (RVNL) (N22000501)	6-2016	12/2024 (N.A.) {12/2024}	5,323.39 (N.A.) {5,190.26}	5,046.07	0
		1535	SURFACE TRIANGLE LINE BETWEEN BHADURA STATION AND NEW CROSSING STN KARMA DOUBLING (ECR) (N22000525)	10-2022	10/2027 (N.A.) {10/2027}	199.96 (N.A.) {199.96}	55.09	0
		1536	MUGHALSARAI - ALLAHABAD - 3RD LINE (NCR) (N22000544)	8-2019	12/2026 (N.A.) {12/2026}	2,649.44 (N.A.) {2,390.00}	83.10	55

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1537	ALIGARH-HARDUAGANJ FLYOVER (22 KM) (NCR) (N22000545)	4-2020	6/2026 (N.A.) {6/2026}	1,456.89 (1,244.13) {1,456.89}	10.14	8.2
		1538	LALITPUR - BIRARI WITH FLYOVER AT LALITPUR (NCR) (N22000546)	3-2017	12/2024 (N.A.) {11/2025}	356.09 (N.A.) {356.00}	213.97	65
		1539	ALIGARH-DAUD KHAN - 3RD LINE 6.9 KM AND CONSTRUCTION OF FLYOVER AT DAUD KHAN (NCR) (N22000562)	4-2019	12/2025 (N.A.) {12/2025}	451.99 (779.49) {779.49}	122.08	44
		1540	ALLAHABAD-BAMHRAULI - 4TH LINE (10 KM) WITH FLY-OVER AT SUBEDARGANJ (NCR) (N22000563)	4-2019	3/2026 (N.A.) {3/2026}	494.11 (N.A.) {494.11}	42.61	42
		1541	BHANDAI - FLYOVER FOR ETAWAH BOUND DOWN TRAINS (NCR) (N22000564)	4-2019	12/2025 (N.A.) {3/2026}	187.21 (N.A.) {250.17}	1.29	8
		1542	SAHJANWA - DOHRIGHAT (NER) (N22000565)	8-2019	3/2029 (N.A.) {12/2027}	371.77 (N.A.) {1,319.75}	577.85	5
		1543	BAHRAICH - NANPARA -NEPALGANJ (56.15 KM) (NER) (N22000566)	7-2020	12/2024 (N.A.) {8/2025}	950.00 (N.A.) {500.00}	424.74	25
		1544	BAHRAICH SRAVASTI BALRAMPUR (TULSIPUR) (NER) (N22000569)	10-2018	10/2030 (N.A.) {3/2028}	4,939.78 (N.A.) {4,939.78}	1,334.98	7.5
		1545	JANGHAI PRATAPGARH AMETHI DOUBLING (NR) (N22000583)	11-2017	3/2025 (N.A.) {12/2025}	721.72 (N.A.) {1,100.00}	58.98	70

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1546	BARABANKI MALHAUR 3RD AND 4TH LINE (32.84 KM) (NR) (N22000590)	1-2019	3/2025 (01-01-2026) {1/2026}	323.85 (N.A.) {407.00}	18.91	59
		1547	DOUBLING BETWEEN JAUNPUR JN- ZAFFARABAD (6.28 KM) (NR) (N22000591)	3-2023	12/2026 (N.A.) {12/2026}	177.33 (N.A.) {177.33}	0.89	10
		1548	JANGHAI-PHAPHAMAU - DOUBLING WITH ELECTRIFICATION (46.79 KM) (RVNL) (N22000596)	11-2018	3/2025 (N.A.) {3/2025}	357.48 (N.A.) {409.38}	362.09	0
		1549	BHATNI - AUNRIHAR WITH ELECTRIFICATION (125 KM) (EXCL INDARA - MAU (116.95 KM)) (RVNL) (N22000598)	5-2018	12/2024 (N.A.) {2/2025}	2,529.46 (N.A.) {2,529.46}	1,636.33	0
		1550	MATHURA - VRINDAVAN (11 KM) (NCR) (N22000612)	8-2022	6/2025 (N.A.) {6/2025}	402.88 (N.A.) {402.88}	-	0
		1551	DOMINGARH - GORAKHPUR - GORAKHPUR CANTT - KUSUMHI - 3RD RUNNING LINE (21.15 KM) (NER) (N22000613)	11-2016	2/2025 (N.A.) {7/2025}	351.03 (N.A.) {500.37}	494.01	86.5
	ROAD TRANSPORT AND HIGHWAYS	1552	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN (NHAI) (N24001306)	10-2020	3/2023 (N.A.) {8/2025}	724.60 (N.A.) {724.60}	569.96	96
		1553	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD (MoRTH) (N24001421)	7-2018	2/2024 (N.A.) {8/2025}	1,948.25 (N.A.) {1,948.25}	1,146.61	79
		1554	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH- 24A INCLUDING RETAINING W (MoRTH) (N24001424)	3-2021	9/2023 (N.A.) {1/2025}	185.09 (269.81) {269.81}	266.35	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1555	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM (MoRTH) (N24001456)	4-2020	2/2024 (N.A.) {1/2025}	199.39 (212.96) {199.39}	200.01	100
		1556	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH-730C F (MoRTH) (N24001457)	4-2020	7/2024 (N.A.) {9/2025}	172.50 (169.56) {172.50}	106.06	76
		1557	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP (MoRTH) (N24001461)	4-2020	3/2024 (N.A.) {8/2025}	236.47 (N.A.) {236.47}	145.95	88
		1558	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP (MoRTH) (N24001462)	4-2020	7/2024 (N.A.) {8/2025}	211.09 (N.A.) {211.09}	147.58	96
		1559	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 (MoRTH) (N24001464)	3-2021	8/2023 (N.A.) {8/2025}	264.86 (N.A.) {264.86}	129.12	84
		1560	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO (MoRTH) (N24001469)	11-2021	5/2024 (N.A.) {7/2025}	307.11 (N.A.) {307.11}	199.38	91
		1561	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH-730C FROM KM.0.00 TO 52.770 UNDER GNHCP (MoRTH) (N24001471)	4-2020	11/2024 (N.A.) {7/2025}	325.24 (340.16) {325.24}	284.35	98
		1562	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) (MoRTH) (N24001479)	3-2021	5/2024 (N.A.) {8/2025}	395.62 (392.03) {395.62}	281.93	76

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1563	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH-334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW (MoRTH) (N24001480)	10-2021	4/2024 (N.A.) {3/2025}	227.06 (N.A.) {227.06}	141.89	100
		1564	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO (NEAR MOHAND) OF GANESHPUR ? DEHRADUN SECTION FROM K (NHAI) (N24001523)	3-2021	10/2023 (01-07-2025) {7/2025}	836.24 (N.A.) {836.24}	792.55	98.85
		1565	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR ? DEHRADUN SECTION FROM (NHAI) (N24001524)	3-2021	10/2023 (01-07-2025) {7/2025}	990.28 (N.A.) {990.28}	997.62	98.89
		1566	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF (MoRTH) (N24001587)	3-2020	9/2024 (N.A.) {8/2025}	262.37 (343.77) {343.77}	278.92	85
		1567	4L SPUR OF SHAMLI-MUZZAFARNAGAR CONNECTING NH-709AD (PANIPAT-SHAMLI-MUZZAFARNAGAR) AND NH-58 (MEERUT) (NHAI) (N24001726)	1-2023	8/2024 (N.A.) {8/2024}	391.26 (N.A.) {391.26}	14.12	80.3
		1568	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B (NHAI) (N24001727)	3-2022	2/2025 (N.A.) {9/2025}	762.62 (N.A.) {838.68}	571.23	95.5
		1569	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO (NHAI) (N24001728)	12-2021	7/2025 (N.A.) {1/2025}	1,138.81 (N.A.) {1,138.81}	528.10	99.82
		1570	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT ? SHAMLI ? MUZZAFARNAGAR) AND NH-709A (KARN) (NHAI) (N24001729)	8-2022	4/2024 (N.A.) {7/2025}	326.79 (N.A.) {329.79}	113.42	98.5

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1571	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) (NHAI) (N24001730)	12-2021	1/2025 (N.A.) {3/2025}	1,384.79 (N.A.) {1,384.79}	657.94	97.98
		1572	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 (NHAI) (N24001731)	12-2021	5/2025 (01-05-2025) {9/2025}	2,470.64 (N.A.) {2,335.00}	691.28	94.68
		1573	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS (NHAI) (N24001732)	12-2021	10/2024 (N.A.) {9/2025}	540.97 (N.A.) {540.97}	314.76	94.76
		1574	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.-MAVIKALAN) TO VILL.-LOHADDA FROM K (NHAI) (N24001733)	3-2022	8/2024 (N.A.) {7/2025}	1,602.48 (N.A.) {1,602.48}	454.77	94
		1575	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-LOHADDA TO VILL.-KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. (NHAI) (N24001734)	3-2022	8/2024 (N.A.) {7/2025}	1,335.45 (N.A.) {1,335.45}	480.89	85.02
		1576	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-KHYAWARI TO VILL.-LATIFPUR AT SAHARANPUR BYPASS FROM KM (NHAI) (N24001735)	3-2022	8/2024 (N.A.) {7/2025}	1,428.19 (N.A.) {1,428.19}	544.15	89.5
		1577	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-KARAUNDA MAHAJAN TO VILL.-KHYAWARI FROM KM. 56.500 TO K (NHAI) (N24001736)	1-2022	8/2024 (N.A.) {7/2025}	1,159.96 (N.A.) {1,159.96}	515.80	98.69
		1578	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III (NHAI) (N24001737)	11-2021	4/2024 (N.A.) {4/2024}	923.15 (N.A.) {923.15}	455.61	100
		1579	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV (NHAI) (N24001738)	9-2021	10/2023 (01-12-2024) {12/2024}	300.79 (N.A.) {300.79}	122.56	80.61

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1580	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U (NHAI) (N24001739)	10-2019	11/2023 (01-12-2024) {12/2024}	1,779.83 (N.A.) {2,200.00}	1,066.00	100
		1581	4L OF SHAMLI BYAPSS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II (NHAI) (N24001744)	5-2019	11/2022 (N.A.) {7/2025}	779.17 (N.A.) {779.17}	71.39	98.5
		1582	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N (NHAI) (N24001745)	12-2021	7/2025 (01-07-2025) {7/2025}	1,972.10 (N.A.) {1,936.00}	504.87	67
		1583	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR (NHAI) (N24001746)	3-2021	4/2024 (01-07-2025) {7/2025}	364.47 (N.A.) {364.47}	209.19	92.98
		1584	4 LANING OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74 (NHAI) (N24001753)	2-2022	6/2024 (01-06-2025) {6/2025}	570.98 (570.98) {570.98}	424.98	97.49
		1585	SPUR OF MEERUT-GARH-MUKTESHVAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN (NHAI) (N24001754)	1-2022	10/2024 (N.A.) {10/2024}	953.79 (N.A.) {953.79}	384.66	71.02
		1586	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH (NHAI) (N24001755)	10-2019	3/2023 (01-12-2024) {12/2024}	1,936.68 (N.A.) {2,458.03}	1,380.90	100
		1587	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR (NHAI) (N24001772)	8-2021	3/2024 (01-12-2024) {12/2024}	1,147.26 (N.A.) {1,147.26}	172.34	60

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1588	4L BYPASSES FOR JAGATPUR, B4BUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA (NHAI) (N24001815)	12-2022	11/2024 (N.A.) {11/2024}	1,699.00 (1,078.00) {1,699.00}	1,033.72	100
		1589	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81) (NHAI) (N24001826)	2-2019	2/2022 (01-06-2025) {12/2025}	927.77 (N.A.) {1,603.00}	1,202.77	91.25
		1590	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 (NHAI) (N24001830)	6-2020	11/2023 (01-12-2024) {12/2024}	2,002.79 (N.A.) {2,002.79}	1,989.85	99
		1591	4L FROM MATHURA BYPASS (START) AT EXISTING KM. 154.20 OF NH-44 TO GAJU VILLAGE AT KM 32.982 OF NH-53 (NHAI) (N24001851)	1-2022	3/2025 (N.A.) {3/2025}	1,738.20 (N.A.) {1,738.20}	742.13	65
		1592	6L OF AGRA BYPASS (NORTHERN) CONNECTING KM. 174.500 OF NH-2 (NEW NH-19) TO KM. 141.000 OF YAMUNA EXP (NHAI) (N24001852)	10-2021	2/2025 (N.A.) {2/2025}	957.62 (N.A.) {957.62}	832.80	86
		1593	CONSTRUCTION OF LEFT OUT PORTION OF AGRA INNER RING ROAD CONNECTING VILLAGE DEORI TO NH-44 VILLAGE B (NHAI) (N24001853)	10-2021	9/2024 (01-03-2025) {3/2025}	772.05 (N.A.) {772.05}	593.39	67.5
		1594	CONSTRUCTION OF 4-LANE GREEN FIELD HIGHWAY FROM KM. 35.000 TO KM. 49.155 OF NH-731A WITH PAVED SHOUL (MoRTH) (N24001929)	1-2022	10/2025 (N.A.) {10/2025}	697.66 (N.A.) {697.66}	318.82	98
		1595	BALANCE WORKS OF 4-LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 (NEW NH NO. 09) FROM KM. 0.000 (KM 1 (NHAI) (N24001992)	8-2022	2/2024 (01-07-2025) {7/2025}	199.31 (244.26) {244.26}	190.10	97.62

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1596	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER HIGHWAY FROM DESIGN CH.0.000 TO CH.49.200 OF NH-731B ON (MoRTH) (N24001996)	3-2022	11/2025 (N.A.) {11/2025}	640.18 (602.76) {602.76}	487.39	81
		1597	CONSTRUCTION OF SHOHRATGARH BYPASS ON NH-730 UNDER EPC MODE IN THE STATE OF UTTAR PRADESH (MoRTH) (N24001997)	10-2022	5/2025 (N.A.) {2/2026}	189.31 (N.A.) {189.31}	59.91	22
		1598	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 90.00 TO (MoRTH) (N24002015)	11-2021	6/2025 (N.A.) {8/2025}	403.36 (328.49) {403.36}	150.57	73
		1599	CONSTRUCTION OF PRATAPGARH BYPASS (EXTENSION) CONNECTING NH-31 TO NH-330 (MoRTH) (N24002016)	10-2022	6/2025 (N.A.) {8/2025}	225.17 (N.A.) {225.17}	96.56	55
		1600	WIDENING TO FOUR LANE WITH PAVED SHOULDER FROM DESIGN KM.49.200 TO KM.89.285 OF NH-731B ON EPC MODE (MoRTH) (N24002029)	3-2022	1/2026 (N.A.) {1/2026}	917.91 (956.30) {917.91}	615.53	47
		1601	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM EXISTING KM.0.000 TO KM.55.610 (DESIGN KM. 0.000 T (MoRTH) (N24002031)	12-2021	2/2026 (N.A.) {2/2026}	840.93 (773.58) {840.93}	524.04	44
		1602	CONSTRUCTION OF 4-LANE HIGHWAY WITH PAVED SHOULDERS FROM KM 49.155 TO KM 74.700 OF NH-731A ON HYBRID (MoRTH) (N24002032)	1-2022	1/2026 (N.A.) {1/2026}	1,156.72 (N.A.) {1,156.72}	407.20	70
		1603	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM GOGWAN JALALPUR (SHAMLI DISTRICT) TO RANIPUR (NHAI) (N24002036)	4-2022	5/2025 (N.A.) {5/2025}	1,843.59 (N.A.) {1,843.59}	843.87	50.2

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1604	GARHMUKTESHWAR (KM. 83.200 OF NH-24) TO MEERUT (KM. 9.860 OF NH-235) INCLUDING CONNECTOR TO NH-119 (NHAI) (N24002073)	10-2019	10/2023 (N.A.) {6/2025}	2,068.99 (2,171.00) {2,171.00}	209.60	53.08
		1605	WIDENING OF RAEBARELI TO PRAYAGRAJ SECTION FROM KM. 82.650 TO KM. 161.450 OF NH-30 AND LINK ROAD FRO (NHAI) (N24002085)	11-2023	3/2025 (N.A.) {3/2025}	1,470.93 (N.A.) {1,470.93}	1,088.30	100
		1606	CONSTRUCTION OF FOUR LANE HIGHWAY FORM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002086)	10-2022	7/2025 (N.A.) {7/2025}	1,706.47 (N.A.) {1,706.47}	719.13	77.25
		1607	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002087)	10-2022	10/2025 (N.A.) {10/2025}	1,493.14 (N.A.) {1,493.14}	93.30	66
		1608	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002088)	10-2022	8/2025 (N.A.) {8/2025}	1,493.50 (N.A.) {1,493.50}	492.86	58
		1609	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER GREENFIELD SECTION OF N (NHAI) (N24002089)	10-2022	6/2025 (N.A.) {6/2025}	617.87 (N.A.) {617.88}	106.20	72
		1610	CONSTRUCTION OF FOUR-LANE ?WESTERN SIDE SPUR OF RAMPUR-RUDRAPUR SECTION CONNECTING NH-24 TO NH-87 BY (NHAI) (N24002090)	3-2021	11/2024 (01-12-2025) {12/2025}	646.27 (N.A.) {646.27}	110.65	52.09
		1611	IMPROVEMENT , UP-GRADATION OF NH-734 SECTION OF MORADABAD - THAKURDWARA - KASHIPUR: ?PACKAGE-I: MORA (NHAI) (N24002093)	10-2022	9/2025 (N.A.) {2/2026}	1,841.92 (N.A.) {1,841.92}	449.98	54.4

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1612	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 123.650 TO 175.080, FROM START OF SHA (NHAI) (N24002094)	9-2022	11/2025 (N.A.) {11/2025}	1,212.26 (N.A.) {1,212.26}	361.81	34.19
		1613	FOUR LANING OF SONAULI GORAKHPUR SECTION OF NH 29E (NEW NH 24) FROM DESIGN CH. 0.000 TO DESIGN CH. 7 (NHAI) (N24002095)	12-2021	3/2025 (N.A.) {3/2025}	2,555.50 (N.A.) {2,555.50}	966.89	63.57
		1614	CONSTRUCTION OF 4 LANE GREEN FIELD NORTHERN EAST SIDE GORAKHPUR BYPASS (26.616 KMS) STARTING FROM NH (NHAI) (N24002096)	2-2023	1/2026 (N.A.) {1/2026}	1,973.98 (N.A.) {1,973.98}	736.14	48.5
		1615	STRENGTHENING OF EXISTING 4L AYODHYA BYPASS SECTION FROM DESIGN KM.121.600 TO KM. 144.020 OF NH 28 ((NHAI) (N24002097)	2-2023	9/2025 (N.A.) {8/2025}	526.45 (N.A.) {526.45}	228.37	83
		1616	CONSTRUCTION OF RING ROAD AROUND KANPUR FROM KM.000 TO KM. 23.325 (CHACHENDI SACHENDI I TO MAHARAJPU (NHAI) (N24002104)	1-2023	6/2026 (N.A.) {6/2026}	1,754.00 (N.A.) {1,754.00}	350.78	35.2
		1617	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS (PHASE-I) FROM DESIGN KM 43+200 (AT MAHUWARI VI (NHAI) (N24002105)	8-2023	6/2026 (N.A.) {6/2026}	1,378.36 (N.A.) {739.00}	213.86	30.89
		1618	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS FROM DESIGN KM 50.860 (NABABA URF NIBI KALA UPA (NHAI) (N24002106)	8-2023	3/2025 (N.A.) {10/2025}	993.77 (N.A.) {349.48}	372.98	92.98
		1619	CONSTRUCTION OF MARIAHU BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION (KM.53.540 TO KM.59.200) (MoRTH) (N24002115)	3-2023	8/2025 (N.A.) {2/2026}	438.24 (362.39) {438.24}	211.72	39

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1620	REHABILITATION AND UPGRADATION FROM KM 51.600 TO KM 75.700 OF NH-321G (NUHKHAS TO ETAH SECTION) TO T (MoRTH) (N24002116)	1-2022	8/2025 (N.A.) {8/2025}	343.54 (N.A.) {343.54}	75.96	42
		1621	CONSTRUCTION OF JASRA BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION FROM KM. 379.670 ON NH-76 ((MoRTH) (N24002120)	2-2023	9/2025 (N.A.) {9/2025}	274.06 (N.A.) {274.06}	135.53	88
		1622	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM. 420.00 (MoRTH) (N24002121)	1-2022	9/2025 (N.A.) {2/2026}	509.65 (N.A.) {509.65}	188.84	34
		1623	REHABILITATION AND UP-GRADATION FROM KM. 0.000 TO KM. 40.390 OF NH-730S (MAHARAJGANJ ? NICHLOUL ? TH (MoRTH) (N24002134)	3-2023	12/2025 (N.A.) {12/2025}	809.25 (N.A.) {809.25}	279.77	35
		1624	CONSTRUCTION OF FOUR LANE HIGHWAY WITH PAVED SHOULDER FROM KM.74.700 TO KM.112.950 OF NH-731A (I/C Y (MoRTH) (N24002138)	3-2022	6/2026 (N.A.) {6/2026}	1,141.67 (N.A.) {1,141.67}	423.37	50
		1625	CONSTRUCTION OF BALRAMPUR BYPASS WITH 2L FLEXIBLE PAVEMENT CONFIGURATION FROM KM.223.000 OF NH-330 T (MoRTH) (N24002150)	12-2022	2/2026 (N.A.) {2/2026}	515.69 (N.A.) {515.69}	187.80	37
		1626	WIDENING TO 4L RIGID PAVEMENT CONFIGURATION FROM KM 90.00 TO KM 100.800 OF NH-96 (KM 42.0 TO KM 53.3 (MoRTH) (N24002199)	12-2022	11/2026 (N.A.) {11/2026}	309.63 (N.A.) {309.63}	13.52	15
		1627	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER/FOUR LANE CONFIGURATION FROM EXISTING K (MoRTH) (N24002201)	1-2022	5/2027 (N.A.) {5/2027}	974.19 (N.A.) {974.19}	616.12	14

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1628	REHABILITATION AND UPGRADATION TO FOUR LANE ROAD FROM KM 70.500 TO KM 78.600 OF NH-92 UNDER EPC MODE (MoRTH) (N24002211)	1-2022	1/2027 (N.A.) {1/2027}	296.02 (N.A.) {296.02}	27.96	0
		1629	WIDENING AND STRENGTHENING FROM DESIGN KM. 67.280 TO KM. 88.622 OF NH-727A (SALEMPUR-MAIRWA ROAD) TO (MoRTH) (N24002212)	3-2023	7/2026 (N.A.) {7/2026}	371.89 (N.A.) {371.89}	151.99	45
		1630	REHABILITATION and UP-GRADATION TO 2L+PS FROM KM. 0.0 TO KM. 7.80 AND KM. 35.400 TO KM. 52.345 (DESI (MoRTH) (N24002213)	3-2023	7/2026 (N.A.) {7/2026}	701.02 (N.A.) {701.02}	270.54	22
		1631	CONSTRUCTION OF AMETHI BYPASS (PART-II) AT KM.30.050 OF NH-931 UNDER EPC MODE IN THE STATE OF UTTAR (MoRTH) (N24002214)	12-2022	2/2027 (N.A.) {2/2027}	283.86 (N.A.) {283.86}	58.92	7
		1632	WIDENING TO 4L FROM KM.108.50 TO 139.00 OF NH-135A PKG-II (JAUNPUR TO AKBARPUR SECTION) ON HAM IN TH (MoRTH) (N24002234)	3-2023	3/2027 (N.A.) {3/2027}	1,511.57 (N.A.) {1,511.57}	154.69	12
		1633	CONSTRUCTION OF RAEBARELI RING ROAD (PHASE-2) WITH FOUR LANE CONFIGURATION FOR RAEBARELI CITY IN THE (MoRTH) (N24002235)	3-2022	5/2027 (N.A.) {5/2027}	1,273.72 (N.A.) {1,273.72}	330.15	0
		1634	IMPROVEMENT AND UP-GRADATION OF NH-227B (84 KOSI PARIKRAMA MARG) PACKAGE ?I, FROM KM 228.920 (JAGARN (MoRTH) (N24002240)	3-2022	11/2026 (N.A.) {11/2026}	912.50 (N.A.) {912.50}	388.50	1
		1635	IMPROVEMENT AND UP-GRADATION OF NH-227B (84 KOSI PARIKRAMA MARG) PACKAGE ?III, FROM KM.47.800 (GOSAI (MoRTH) (N24002241)	3-2022	11/2026 (N.A.) {11/2026}	587.97 (N.A.) {587.97}	107.68	3
		1636	CONSTRUCTION OF BASTI RING ROAD (PHASE-I) WITH 4L CONFIGURATION FOR BASTI CITY IN THE STATE OF UTTAR (MoRTH) (N24002245)	12-2022	6/2027 (N.A.) {6/2027}	1,138.72 (N.A.) {1,138.72}	263.70	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1637	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B (MoRTH) (N24000331)	12-2019	4/2022 (N.A.) {7/2025}	282.41 (N.A.) {319.96}	276.35	88
		1638	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 (NHAI) (N24000564)	3-2016	7/2020 (01-07-2025) {7/2025}	1,408.00 (1,659.12) {1,659.12}	1,336.33	91.39
		1639	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO (NHAI) (N24000796)	3-2018	12/2021 (01-12-2023) {7/2024}	1,117.84 (N.A.) {1,203.92}	1,960.91	99.99
		1640	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA (NHAI) (N24000798)	3-2018	11/2021 (N.A.) {6/2025}	2,140.93 (N.A.) {2,140.93}	2,081.52	100
	<u>URBAN DEVELOPMENT</u>	1641	KANPUR METRO RAIL PROJECT (LMRCL) (N28000144)	5-2019	3/2024 (N.A.) {3/2027}	11,076.48 (N.A.) {11,076.48}	8,839.21	72.6
		1642	AGRA METRO RAIL PROJECT (LMRCL) (N28000145)	5-2019	3/2024 (N.A.) {6/2027}	8,379.62 (N.A.) {8,379.62}	5,116.00	54.7
	<u>WATER RESOURCES</u>	1643	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH (UPJalNigam) (N30000021)	1-2019	12/2021 (01-01-2020) {3/2025}	231.79 (234.03) {234.03}	141.79	100
		1644	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH (UPJalNigam) (N30000024)	2-2019	6/2022 (N.A.) {12/2025}	681.78 (N.A.) {690.71}	13.34	27
<u>UTTARAKHAND</u>	<u>CIVIL AVIATION</u>	1645	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN (AAI) (N04000085)	7-2018	9/2020 (01-09-2024) {9/2024}	456.86 (500.00) {500.00}	483.96	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	1646	TEHRI PUMPED STORAGE PLANT(1000MW) (THDCIL) (N18000010)	7-2006	7/2010 (01-06-2022) {9/2025}	1,657.00 (4,825.60) {8,182.00}	8,046.19	98.3
		1647	TAPOVAN-VISHNUGAD HEP (4X130MW) (NTPC) (N18000014)	11-2006	3/2013 (01-12-2021) {4/2029}	2,978.48 (N.A.) {10,907.00}	7,007.93	72.4
		1648	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT (THDCIL) (N18000042)	8-2008	6/2013 (N.A.) {3/2027}	2,491.58 (3,860.35) {6,823.72}	4,918.46	71
		1649	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW (NTPC) (N18000142)	7-2012	8/2017 (N.A.) {8/2017}	1,527.00 (N.A.) {1,527.00}	149.93	0
	RAILWAYS	1650	RISHIKESH - KARNAPRAYAG NEW LINE (RVNL) (N22000406)	4-2011	12/2025 (N.A.) {3/2025}	38,953.15 (N.A.) {24,659.00}	18,820.04	0
	ROAD TRANSPORT AND HIGHWAYS	1651	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR ? DEHRADUN SECTION FROM KM. (NHAI) (N24001525)	3-2021	3/2024 (01-05-2025) {5/2025}	169.08 (N.A.) {169.08}	105.77	99.99
		1652	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF (NHAI) (N24001526)	8-2021	10/2024 (01-08-2025) {8/2025}	1,377.79 (1,384.11) {1,377.79}	684.93	58.41
		1653	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) (NHAI) (N24001553)	3-2022	2/2025 (01-11-2025) {11/2025}	1,092.90 (1,092.90) {1,092.90}	463.92	89.25
		1654	4L POANTA SAHEB?MEDNIPUR FROM KM. 435.65 TO KM. 458.65 OF NH-07(PKG-1) (NHAI) (N24001990)	6-2022	5/2025 (01-10-2025) {10/2025}	524.54 (683.26) {683.26}	91.94	74.78

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1655	ACCESS ROAD/BRIDGE CONNECTIVITY FROM NH-09 AT KM.40 NEAR JAGBUDA BRIDGE (INDIA) TO BOUNDARY PILLAR (NHAI) (N24001991)	5-2022	9/2024 (01-11-2026) {11/2026}	314.31 (N.A.) {314.31}	178.52	71.79
		1656	CONSTRUCTION FOR MITIGATION MEASURES KM 368.00-UTTARAKHAND-TO KM 433.00 ON NH-07-PKG-1 (NHIDCL) (N24002163)	12-2023	12/2025 (N.A.) {12/2025}	216.88 (N.A.) {216.88}	82.19	75.8
		1657	CONSTRUCTION FOR MITIGATION MEASURES KM 450.00-UTTARAKHAND-TO KM 468.00 ON NH-07-PKG-3 (NHIDCL) (N24002164)	12-2023	12/2025 (N.A.) {12/2025}	250.33 (N.A.) {250.33}	46.63	48.5
		1658	CONSTRUCTION FOR MITIGATION MEASURES PKG-2 (NHIDCL) (N24002206)	12-2023	6/2026 (N.A.) {6/2026}	259.64 (N.A.) {259.64}	18.62	20.23
		1659	4-LANING OF KASHIPUR-SITARGANJ SECTION (AMR) (N24000465)	11-2012	8/2016 (N.A.) {8/2016}	605.84 (N.A.) {605.84}	-	0
		1660	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 (NHIDCL) (N24000741)	3-2018	11/2020 (01-03-2024) {3/2024}	274.31 (N.A.) {274.31}	253.61	100
		1661	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI (NHIDCL) (N24000742)	3-2018	11/2020 (N.A.) {3/2024}	403.36 (N.A.) {403.36}	340.32	100
		1662	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA (NHIDCL) (N24000743)	3-2018	11/2020 (N.A.) {3/2024}	417.24 (N.A.) {417.24}	344.20	100

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1663	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000772)	12-2017	12/2019 (N.A.) {12/2019}	257.34 (N.A.) {257.34}	232.69	100
		1664	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000773)	12-2017	12/2019 (N.A.) {12/2019}	200.34 (N.A.) {200.34}	227.98	100
		1665	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 (MoRTH) (N24000774)	12-2017	12/2019 (N.A.) {12/2019}	248.22 (N.A.) {248.22}	236.80	100
		1666	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000775)	6-2017	6/2019 (N.A.) {6/2019}	282.08 (N.A.) {282.08}	234.97	100
		1667	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG (MoRTH) (N24000776)	11-2017	11/2019 (N.A.) {11/2019}	232.81 (N.A.) {232.81}	201.58	100
		1668	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION (MoRTH) (N24000777)	11-2017	11/2019 (N.A.) {11/2019}	283.51 (N.A.) {283.51}	278.51	100
		1669	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000778)	11-2017	11/2019 (N.A.) {11/2019}	266.52 (N.A.) {266.52}	250.34	100
		1670	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR (MoRTH) (N24000779)	2-2018	2/2020 (N.A.) {2/2020}	418.88 (N.A.) {418.88}	339.71	94

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1671	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K (MoRTH) (N24000780)	2-2018	(N.A.) {}	293.68 (N.A.) {293.68}	244.25	100
		1672	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN (MoRTH) (N24000781)	5-2018	5/2020 (N.A.) {5/2020}	248.00 (N.A.) {248.00}	120.50	67
		1673	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 (MoRTH) (N24000782)	3-2018	(N.A.) {}	460.73 (N.A.) {461.00}	-	0
		1674	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) (NHIDCL) (N24000855)	3-2018	7/2022 (N.A.) {9/2026}	1,383.78 (N.A.) {1,383.78}	714.33	64.27
		1675	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER (MoRTH) (N24001130)	8-2016	12/2017 (N.A.) {12/2017}	234.88 (N.A.) {234.88}	237.19	100
WEST BENGAL	CIVIL AVIATION	1676	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA (AAI) (N04000080)	1-2016	3/2020 (01-12-2023) {12/2023}	458.00 (N.A.) {458.00}	251.64	100
		1677	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA (AAI) (N04000081)	1-2019	11/2021 (01-05-2023) {5/2023}	389.71 (397.00) {397.00}	396.61	100
		1678	NSCBI AIRPORT KOLKATA: RE-CONSTRUCTION OF RIGID POSITIONS OF SECONDARY RUNWAY, 'K' AND 'A' TAXIWAY (AAI) (N04000109)	4-2023	10/2025 (N.A.) {10/2025}	328.30 (N.A.) {328.30}	91.70	42.5

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1679	BAGDOGRA AIRPORT: DEVELOPMENT OF NEW CIVIL ENCLAVE AT BAGDOGRA AIRPORT. SUB-HEAD : CONSTRUCTION OF N (AAI) (N04000115)	8-2024	3/2027 (N.A.) {3/2027}	1,549.00 (N.A.) {1,549.00}	239.75	9.62
	COAL	1680	RANIGANJ MASTER PLAN (ECL) (N06000163)	8-2009	8/2019 (N.A.) {8/2019}	2,661.73 (N.A.) {5,146.48}	787.60	42
		1681	SIDULI MINE (OC AND UG) (ECL) (N06000165)	5-2018	3/2027 (N.A.) {3/2027}	535.18 (N.A.) {535.17}	5.00	14
		1682	NAKRAKONDA KUMARDIH B OCP (ECL) (N06000170)	8-2018	3/2029 (N.A.) {3/2029}	502.68 (N.A.) {502.67}	71.07	25.51
		1683	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT (ECL) (N06000191)	4-2020	3/2026 (01-03-2026) {3/2026}	483.65 (N.A.) {483.65}	55.53	12.09
		1684	2.0 MTPA BHOJUDIH NLW WASHERY (BCCL) (N06000195)	12-2015	9/2020 (N.A.) {7/2025}	384.57 (N.A.) {384.57}	351.16	97
		1685	SONEPUR BAZARI EXPANSION OC (ECL) (N06000220)	7-2021	3/2029 (N.A.) {3/2029}	5,365.88 (5,366.00) {5,365.88}	562.41	17.38
		1686	EXPANSION PR OF JHANJRA UG (5.00 MTY) (ECL) (N06000223)	4-2020	3/2029 (N.A.) {3/2029}	1,210.12 (N.A.) {1,210.12}	495.37	40
		1687	MOHANPUR EXPANSION OC PHASE II (ECL) (N06000236)	11-2020	3/2026 (N.A.) {3/2026}	888.99 (N.A.) {888.99}	89.54	30.25
		1688	BONJEMEhari EXPANSION OCP (ECL) (N06000244)	8-2021	3/2026 (01-03-2026) {3/2026}	570.12 (N.A.) {570.11}	81.58	16

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1689	ITAPARA OC (ECL) (N06000272)	12-2023	3/2030 (N.A.) {3/2030}	929.10 (N.A.) {929.10}	65.03	6.8
		1690	UCE OF TILABONI UG (ECL) (N06000276)	1-2023	3/2029 (N.A.) {3/2029}	749.07 (N.A.) {749.07}	52.09	10.3
		1691	UCE OF PARASEA BELBAID REORGANISATION UG (ECL) (N06000277)	1-2023	3/2029 (01-03-2028) {3/2028}	389.10 (N.A.) {389.10}	131.42	16.41
		1692	PARASCOLE JAMBAD OCP (ECL) (N06000281)	11-2024	3/2037 (N.A.) {3/2037}	1,193.55 (N.A.) {1,193.55}	6.04	0.01
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1693	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED (CPWD EDUCATION) (N28000146)	3-2020	6/2020 (N.A.) {3/2024}	193.83 (N.A.) {193.83}	187.65	99
	<u>HOME AFFAIRS</u>	1694	NSG AT KOLKATA (CPWD FOR MHA) (N28000104)	10-2014	4/2018 (N.A.) {8/2025}	162.88 (210.83) {210.83}	193.91	100
	<u>MINES</u>	1695	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA (CPWD) (N10000015)	4-2019	4/2022 (N.A.) {8/2026}	255.37 (N.A.) {255.37}	74.13	40
	<u>PETROLEUM</u>	1696	DURGAPUR-HALDIA PIPELINE PROJECT (GAIL) (N16000275)	3-2017	12/2020 (01-12-2025) {12/2025}	1,740.00 (2,433.15) {2,433.15}	2,193.80	90
		1697	CITY GAS DISTRIBUTION IN WEST BENGAL (HPCL) (N16000392)	3-2019	3/2031 (01-03-2031) {3/2031}	5,830.20 (N.A.) {5,830.20}	875.27	100
		1698	HALDIA PANAGARH PIPELINE PROJECT (HPCL) (N16000478)	11-2022	11/2025 (N.A.) {11/2025}	1,010.00 (N.A.) {1,010.00}	573.18	80.09

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1699	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS (IOCL) (N16000491)	3-2022	3/2030 (N.A.) {6/2031}	609.00 (N.A.) {609.00}	56.00	2.1
		1700	CGD PROJECT IN WEST BENGAL 11TH ROUND (HPCL) (N16000498)	6-2022	6/2030 (N.A.) {6/2030}	2,628.00 (N.A.) {2,628.00}	320.83	24.1
		1701	CITY GAS DISTRIBUTION PROJECTS AT ALIPURDUAR AND COOCH BEHAR (BPCL) (N16000522)	12-2022	3/2030 (N.A.) {3/2030}	1,017.00 (N.A.) {1,017.00}	168.34	31.9
	POWER	1702	RAMMAM-III HEPP (3X40 MW) (NTPC) (N18000178)	9-2014	9/2019 (01-12-2024) {3/2029}	1,381.84 (N.A.) {1,803.00}	1,302.76	43.68
	RAILWAYS	1703	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER (ER) (220100272)	4-2000	3/2019 (01-02-2026) {2/2026}	1,188.91 (N.A.) {2,582.49}	1,283.98	75
		1704	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) (KOMRCL) (N22000108)	4-2010	8/2026 (N.A.) {3/2016}	4,829.60 (N.A.) {2,397.72}	197.20	17
		1705	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) (RVNL) (N22000109)	4-2010	12/2026 (N.A.) {12/2025}	2,298.42 (N.A.) {2,733.86}	392.98	0
		1706	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) (RVNL) (N22000110)	4-2010	12/2025 (N.A.) {3/2026}	8,964.35 (N.A.) {8,964.35}	7,387.40	0
		1707	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. (RVNL) (N22000111)	4-2010	12/2026 (N.A.) {12/2026}	4,834.54 (N.A.) {4,834.54}	3,918.86	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1708	PURULIA TO KOTSHILA DOUBLING (39.1 KM) (SER) (N22000510)	4-2018	12/2024 (N.A.) {3/2025}	393.83 (N.A.) {393.83}	319.21	100
		1709	AZIMGANJ-MURSHIDABAD (JIYAGANJ) INCL. RLY. BRIDGE OVER RIVER BHAGIRATHI (ER) (N22000609)	10-2001	2/2024 (N.A.) {2/2024}	164.33 (N.A.) {187.05}	160.82	100
		1710	NAHATI - RANAGHAT 3RD LINE (MM OF KALINARAYANPUR - KRISHNANAGAR) (ER) (N22000624)	7-2015	3/2025 (N.A.) {3/2026}	1,000.00 (N.A.) {283.54}	171.63	44
		1711	EAST WEST METRO CORRIDOR KOLKATA (KOMRCL) (N22000628)	2-2009	9/2016 (N.A.) {9/2016}	4,874.58 (8,575.00) {10,442.41}	-	0
		1712	KALIPAHARI - BAKHTARNAGAR 5TH LINE (17.61 KM) (ER) (N22000630)	4-2024	6/2027 (N.A.) {6/2027}	350.46 (N.A.) {350.46}	-	0
		1713	SITARAMPUR BYE - PASS LINE (6.59 KM) (ER) (N22000631)	2-2023	3/2027 (N.A.) {3/2027}	461.64 (N.A.) {461.64}	26.87	0
		1714	MURARAI - BARHARWA 3RD LINE (48.90 KM) (ER) (N22000632)	5-2025	5/2028 (N.A.) {5/2028}	935.19 (N.A.) {935.19}	-	0
	ROAD TRANSPORT AND HIGHWAYS	1715	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 (NHAI) (N24001747)	3-2020	9/2024 (N.A.) {9/2024}	2,193.23 (2,314.00) {2,314.00}	2,085.00	97.04
		1716	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA (NHAI) (N24001748)	3-2021	9/2024 (N.A.) {12/2025}	2,200.93 (N.A.) {2,622.05}	2,622.05	97.6

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1717	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE (NHAI) (N24001749)	8-2021	8/2023 (N.A.) {9/2025}	557.55 (N.A.) {567.31}	473.26	91.41
		1718	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA (NHAI) (N24001750)	8-2018	12/2021 (N.A.) {8/2025}	622.04 (N.A.) {622.04}	579.31	91.64
		1719	DEVELOPMENT TO 4/6-LANNING OF NH-31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 (MoRTH) (N24001850)	3-2022	9/2025 (01-09-2025) {9/2025}	995.04 (995.04) {995.04}	422.06	51.21
		1720	CONSTRUCTION OR 4 LANE RANIGANJ BYPASS OF LENGTH 5 261 KM ON NH 60 NEW NH 14 FROM KM 273 00 OF NH (MoRTH) (N24002184)	3-2023	3/2026 (01-03-2026) {3/2026}	410.83 (N.A.) {410.83}	164.34	37.5
		1721	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF LEVEL CROSSING NO 10 B T AT KM 307 050 OF NH 60 B (MoRTH) (N24002191)	3-2016	8/2025 (N.A.) {8/2025}	155.87 (N.A.) {155.87}	21.68	10.61
		1722	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) (NHAI) (N24000463)	12-2015	6/2018 (01-05-2024) {8/2023}	1,083.00 (1,414.01) {1,414.01}	1,080.05	100
		1723	SIX-LANING OF BARWA ADDA-PANAGARH (NHAI) (N24000515)	4-2014	9/2016 (N.A.) {5/2025}	1,665.00 (N.A.) {4,980.13}	4,980.13	100
		1724	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU (NHAI) (N24000788)	3-2018	9/2022 (01-12-2022) {12/2025}	841.57 (708.30) {708.30}	12,485.63	96.49

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1725	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H (MoRTH) (N24000874)	3-2016	11/2018 (01-12-2023) {9/2025}	271.17 (291.20) {291.20}	199.72	82.56
		1726	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. (MoRTH) (N24000880)	2-2018	9/2020 (01-01-2024) {2/2025}	426.18 (426.18) {426.18}	364.92	100
	STEEL	1727	REBUILDING OF COKE OVEN BATTERY NO.4 OF DURGAPUR STEEL PLANT (SAIL) (N12000132)	11-2023	12/2026 (N.A.) {12/2026}	916.78 (N.A.) {916.78}	110.08	10.98
		1728	INSTALLATION OF NEW BAR MILL AT DURGAPUR STEEL PLANT (SAIL) (N12000138)	9-2024	6/2027 (N.A.) {6/2027}	2,115.44 (N.A.) {2,115.44}	100.12	19.97
		1729	UP-GRADATION OF BLAST FURNACE NO. 3 AT DURGAPUR STEEL PLANT (SAIL) (N12000139)	9-2024	6/2026 (N.A.) {6/2026}	758.09 (N.A.) {758.09}	35.34	2.5
		1730	REVAMPING OF AIR POLLUTION CONTROL SYSTEMS OF SP-1 AT DURGAPUR STEEL PLANT (SAIL) (N12000140)	11-2024	5/2026 (N.A.) {5/2026}	196.40 (N.A.) {196.40}	0.19	1
		1731	THIRD LADLE FURNACE IN SECONDARY REFINERY UNIT AT IISCO STEEL PLANT (SAIL) (N12000141)	11-2024	7/2026 (N.A.) {7/2026}	227.96 (N.A.) {227.96}	2.61	29
	WATER RESOURCES	1732	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA (KMDA) (N30000032)	5-2018	2/2022 (N.A.) {8/2025}	198.43 (224.69) {286.97}	77.79	98
		1733	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA (KMDA) (N30000034)	8-2017	9/2022 (01-01-2023) {12/2026}	307.12 (N.A.) {653.67}	-	0

Table:-7. Project List: Ongoing Projects 1st Quarter (April-June),2025-26

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1734	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH (KMDA) (N30000042)	5-2018	2/2022 (01-09-2020) {3/2025}	160.00 (154.73) {154.73}	93.32	92
			Total			2842540.23 (-) {3158147.58}	1774657.7	

Abbreviations used in the Report

AGENCY_NAME	AGENCY_NAME_SHORT
AIRPORT AUTHORITY OF INDIA LIMITED	AAI
ARTIFICIAL LIMBS MANUFACTURING CORPM. OF INDIA	ALIMCO
BHARAT ALUMINUM CORPORATION	BALCO
BHABHA ATOMIC RESEARCH CENTRE	BARC
BHARAT COKING COAL LIMITED	BCCL
BRAHMAPUTRA CRECKER & POLYMER LTD.	BCPL
BHAVINI LIMITED	BHAVNI
BHARAT HEAVY ELECTRICALS LIMITED	BHEL
BANGALORE METRO RAIL CORPORATION LIMITED	BMRCL
BOKARO STEEL PLANT	BOKARO STEEL PL
BRAHMAPUTRA BOARD	BPB
BHARAT PETROLEUM CORPORATION LIMITED	BPCL
BORDER ROAD ORGANISATION	BRO
BONGAIGAON REFINERY PETROLEUM LIMITED	BRPL
BHARAT SANCHAR NIGAM LIMITED	BSNL
Bihar Urban Infrastructure Development Corporation Ltd	BUIDCO
BRAHMAPUTRA VALLY FERTILISER CORPORATION	BVFC
CENTRE FOR DEVELOPMENT OF TELEMATICS, TELECOM, TECHNOLOGY	C-DOT
CENTRAL COAL FIELDS LIMITED	CCL
CONTAINER CORPORATION OF INDIA	CCOI
CHENAB VALLEY POWER CORPORATION LIMITED	CHENAB VALLEY P
CHENNAI METRO RAIL LTD	CMRL
CHENNAI PETROLEUM CORPORATION LIMITED	CPCL
CENTRAL PUBLIC WORKS DEPARTMENT	CPWD
CPWD OF HIGHER EDUCATION	CPWD EDUCATION
CPWD FOR DEFENCE	CPWD FOR DEFENC
CPWD FOR FINANCE	CPWD FOR FINANC
CPWD FOR HEALTH	CPWD FOR HEALTH
CPWD FOR MHA	CPWD FOR MHA
CPWD FOR POWER	CPWD FOR POWER
CPWD FOR RURAL	CPWD FOR RURAL
CPWD FOR TELECOM	CPWD FOR TELECO
CPWD FOR RENEWABLE ENERGY	CPWD R ENERGY
CENTRAL RAILWAYS	CR
COCHIN REFINERY LIMITED	CRL
COCHIN SHIPYARD LTD	CSL
CHENAB VELLEY POWER PROJECTS [P] LIMITED	CVPPPL
DUMMY AGENCY	DA
DEDICATED FREIGHT CORRIDOR CORPORATION OF INDIA LTD	DFCC
DIRECTORATE GENERAL OF CIVIL AVIATION	DGCA
Delhi Jal Board	DJB
Delhi Mumbai Industrial Corridor	DMIC
DMIC FOR DPIIT	DMIC FOR DPIIT
DELHI METRO RAIL CORPORATION	DMRC
DEPARTMENT OF TELECOMMUNICATION	DOT
Department for Promotion of Industry and Internal Trade	DPIIT
DAMODAR VALLEY CORPORATION	DVC
EASTERN COAL FIELDS LIMITED	ECL
EAST COAST RAILWAY	ECOR
EAST CENTRAL RAILWAYS	ECR

AGENCY_NAME	AGENCY_NAME_SHORT
EDCIL(India) Limited	EDCIL
ENNORE PORT LTD.	ENNORE PORT LTD
ENNORE TANK TERMINAL PVT.LTD.	ENNORE TANK
EASTERN RAILWAYS	ER
FERTILISER AND CHEMICAL TRIVANCORE	FACT
FREIGHT OPERATION INFORMATION SYSTEM	FOIS
SETTING UP FILM AND TELEVISION INSTITUTE	FTI
GAS AUTHORITY OF INDIA LIMITED	GAIL
GOA SHIPYARD LIMITED	GSL
HEALTH & FAMILY WELFARE	H&FW
HINDUSTAN AERONAUTICS LTD	HAL
HINDUSTAN COPPER LIMITED	HCL
HALDIA FERTILISER CORPORATION	HFC
HLL Infra Tech Services Limited	HITES
HYDERABAD METRO RAIL LTD	HMRL
HINDUSTAN PETROLEUM CORPORATION LIMITED	HPCL
HPCL Rajasthan Refinery Limited(JV)	HPCLRRL(JV)
HPOIL Gas Pvt. Ltd	HPOIL(JV)
HOSPITAL SERVICES CONSULTANCY CORPORATION LTD	HSCC
HINDUSTAN STEELWORK CONSTRUCTION LIMITED	HSCL
HINDUSTHAN STEELWORKS CONSTRUCTION LIMITED	HSCL
HSCL FOR DONER	HSCL FOR DONER
HSCL FOR RURAL	HSCL FOR RURAL
HSCL FOR WATER	HSCL FOR WATER
INDIAN FARMERS FERTILISER CORPORATION	IFFCO
INDIRA GANDHI CENTRE FOR ATOMIC RESEARCH	IGCAR
INDRADHANUSH GAS GRID LTD	IGGL
India International Convention and Expo Centre	IICC
IICC FOR DPIIT	IICC FOR DPIIT
INDIAN IRON STEEL COMPANY	IISCO
Indian Institute of Technology, Kharagpur	IITKGP
INDIAN OIL CORPORATION LIMITED	IOCL
INDIAN PETRO-CHEMICAL CORPORATION LIMITED	IPCL
Indian Railway Construction Company Limited	IRCON
INDIAN STRATEGIC PETROLEUM RESERVES LTD	ISPRL
INDIAN TELEPHONE INDUSTRY	ITI
Inland Waterways Authority of India	IWAI
INLAND WATER TRANSPORT	IWT
JAWAHAR LAL NEHRU NATIONAL URBAN RENEWAL MISSION	JNNURM
JWAAHARLAL NEHRU PORT TRUST	JNPT
Jharkhand Urban Infrastructure Development Company Ltd	JUIDCO
Kolkata Metropolitan Development Authority	KMDA
KOCHI METRO RAIL CORPORATION LTD	KMRCL
KOLKATA METRO RAIL CORPORATION LIMITED	KOMRCL
KAMARAJAR PORT LIMITED	KPL
KONKAN RAILWAY	KR
Rail Infrastructure Development Company	KRIDE
KOCHI REFINERIES LIMITED	KRL
Kochi Salem Pipeline Private Limited(JV)	KSPPL(JV)
LINE DOUBLING	LD
LUCKNOW METRO RAIL CORPORATION LIMITED	LMRCL
MANGALORE REFINERY AND PETROCHEMICALS LIMITED	MANGALORE REFIN

AGENCY_NAME	AGENCY_NAME_SHORT
MAHANADI COAL FIELDS LIMITED	MCL
MECON LIMITED	MECON LIMITED
AHMEDABAD METRO RAIL	MEGA
MADRAS FERTILISER LIMITED	MFL
Munitions India Limited	MIL
MAHARASTRA METRO RAIL CORPORATION LTD.	MMRC
MUMBAI METRO RAIL CORPORATION LTD	MMRCL
MINISTRY OF WATER RESOURCES	MOWR
Madhya Pradesh Metro Rail Co Limited	MPMRCL
Maharashtra Rail Infrastructure Development Corporation Limited	MRIDC
MANGALORE REFINARY LIMITED	MRL
METROPOLITAN RAPID TRANSPORT PROJECTS	MRTP
Mumbai Railway Vikas Corporation	MRVC
MAHANAGAR TELEPHONE NIGAM LIMITED	MTNL
MUMBAI PORT TRUST	MUMBAI PORT TRU
Armoured Vehicles Nigam Limited	MVNL
MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)	MoRTH
NATIONAL ALUMINUM COMPANY LIMITED (NALCO)	NALCO
NATRIIP IMPLEMENTATION SOCIETY	NATIS
NATIONAL BUILDING CONSTRUCTION CORPORATION LTD	NBCC
NBCC FOR COMMERCE	NBCC FOR COMMER
NBCC FOR HEALTH	NBCC FOR HEALTH
NORTHERN COAL FIELDS LIMITED	NCL
NORTH CENTRAL RAILWAY	NCR
NATIONAL CAPITAL REGION TRANSPORT CORP	NCRTC
NATIONAL CENTRE OF EXCELLENCE	NCoE
NORTH EAST ELECTRIC POWER CORPORATION	NEEPCO
NORTH EAST GAS GRID	NEGG
NORTH EASTERN RAILWAY	NER
National Film Archive of India	NFAI
NUCLEAR FUEL CORPORATION	NFC
NATIONAL FERTILISER LIMITED	NFL
NORTH EAST FRONTIER RAILWAY	NFR
NATIONAL HIGHWAYS AUTHORITY OF INDIA	NHAI
NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.	NHIDCL
NATIONAL HYDRO-ELECTRIC POWER CORPORATION	NHPC
National High Speed Rail Corporation Limited	NHSRCL
NEW LINE	NL
NEYVELI LIGNITE CORPORATION	NLC
NATIONAL MISSION FOR CLEAN GANGA	NMCG
NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)	NMDC
NAGPUR METRO RAIL CORPORATION LTD	NMRCL
NATIONAL PROJECTS CONSTRUCTION CORPORATION LIMITED	NPCC
NUCLEAR POWER CORPORATION OF INDIA LIMITED	NPCIL
NORTHERN RAILWAY	NR
NUMALIGARH REFINERY LIMITED	NRL
SETTING UP OF NEW RAILWAY ZONES	NRZ
NATIONAL THERMAL POWER CORPORATION	NTPC
NORTH WESTERN RAILWAY	NWR
OIL INDIA LIMITED	OIL
OIL & NATURAL GAS CORPORATION LIMITED	ONGC
PATNA METRO RAIL CORPORATION	PATNA METRO RAI

AGENCY_NAME	AGENCY_NAME_SHORT
PAWAN HANS HELICOPTERTERS LTD.	PAWAN HANS HELI
POWER GRID CORPORATION OF INDIA LIMITED	PGCIL
PORT TRUST	PORT TRUST
Polavaram Project Authority	PPA
RASHTRIYA CHEMICAL & FERTILISER LIMITED	RCF
RAILWAY ELECTRIFICATION	RE
RASTRIYA ISPAT NIGAM LIMITED	RINL
RAIL INDIA TECHNICAL AND ECONOMIC SERVICE	MITES
MITES OF HIGHER EDUCATION	MITES OF HIGHER
RAIL VIKAS NIGAM LTD.	RVNL
SIGNALLING & TELECOMMUNICATIONS	S&T
STEEL AUTHORITY OF INDIA LIMITED (SAIL)	SAIL
SINGARENI COLLIERS COMPANY LIMITED	SCCL
SOUTH CENTRAL RAILWAY	SCR
SOUTH-EASTERN COAL FIELDS LIMITED	SECL
SOUTH EAST CENTRAL RAILWAY	SECR
SOUTH EASTERN RAILWAY	SER
SER(GC) GAUGE CONVERSION	SER(GC
SHIPPING CRP. OF INDIA	SHIPP.
SATLUJ JAL VIDYUT NIGAM LIMITED	SJVN
SOUTHERN RAILWAY	SR
SOUTH WESTERN RAILWAY	SWR
Sikkim University	Sikkim Universi
THDC INDIA LIMITED	THDCIL
TUTICORIN PORT TRUST	TUTICORIN
URANIUM CORPORATION OF INDIA LIMITED	UCIL
URBAN DEVELOPMENT	UD
Uttarakhand Pey Jal Nigam	UKJalNigam
Uttar Pradesh Jal Nigam	UPJalNigam
VISAKHAPATNAM PORT TRUST	VPT
Varanasi Smart City	Varanasi Smart
WAPCOS	WAPCOS
WESTERN COAL FIELDS LIMITED	WCL
WEST CENTRAL RAILWAY	WCR
WESTERN RAILWAY	WR
WORKSHOPS & PRODUCTION UNIT	WS&PU



Government of India

Ministry of Statistics and Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
