



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation

481th — Flash Report on Central Sector Infrastructure Projects —



(Rs. 150 crore
& above)

NOVEMBER 2025



Scan the QR code to access
the PAIMANA Portal.

www.mospi.gov.in [@GoIStats](#) [/GoIStats](#) [GoIStats](#) [Ministry of Statistics & PI](#)



CONTENTS

I. Overview*	2-4
II. North Eastern Region	5-6
III. As per Harmonized Master List (HML) 2022	7-13
IV. Major Infrastructure Central Ministries & Departments	14-19
V. Appendix : <i>List of Tables</i>	20 onwards
Table 1: Ministry-wise Ongoing Projects	
Table 2: State-wise Ongoing Projects	
Table 3: Completed Projects	
Table 4: Newly Added Projects	
Table 5: Ongoing Projects of North Eastern Region	
Table 6: All Ongoing Projects	

**Note: This report is web-generated from the PAIMANA portal (ipm.mospi.gov.in) as of November 2025, based on the projects worth Rs. 150 crores and above reported by Central Line Ministries/ Departments/ Implementing Agencies (excluding Ministry of Road Transport & Highways, may reflect from next month onwards) on the IPM portal (indiainvestmentgrid.gov.in) latest by 24th December 2025.*





Overview





Flash Report

Central Sector Infrastructure Projects Costing Rs. 150 crore & above

NOVEMBER 2025

823 | 16

Ongoing Projects |
Line Ministries & Departments

₹ 24,18,198

Original Cost
(crores)

₹ 29,54,787

Revised Cost
(crores)

₹ 15,74,942

(53.3% of Revised Cost)
Expenditure
(crores)

13


Commissioned during month

21

Newly Added during month


Sectoral Comparison : Major Sectors*

[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

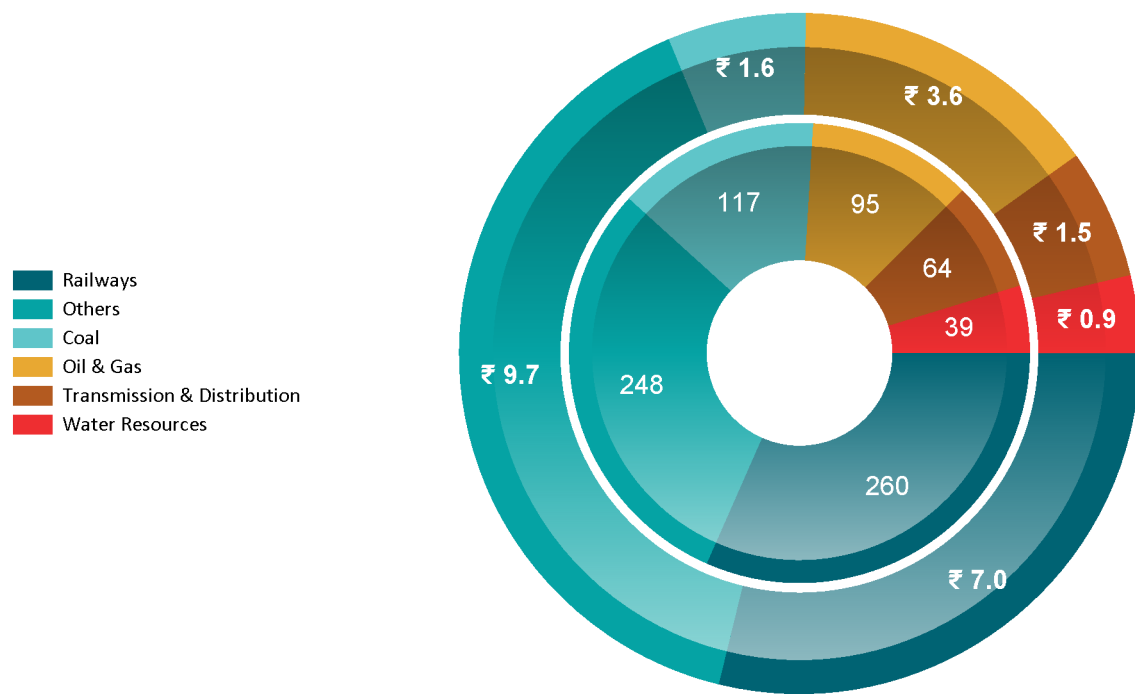


Ministry Comparison : Major Ministries*


[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

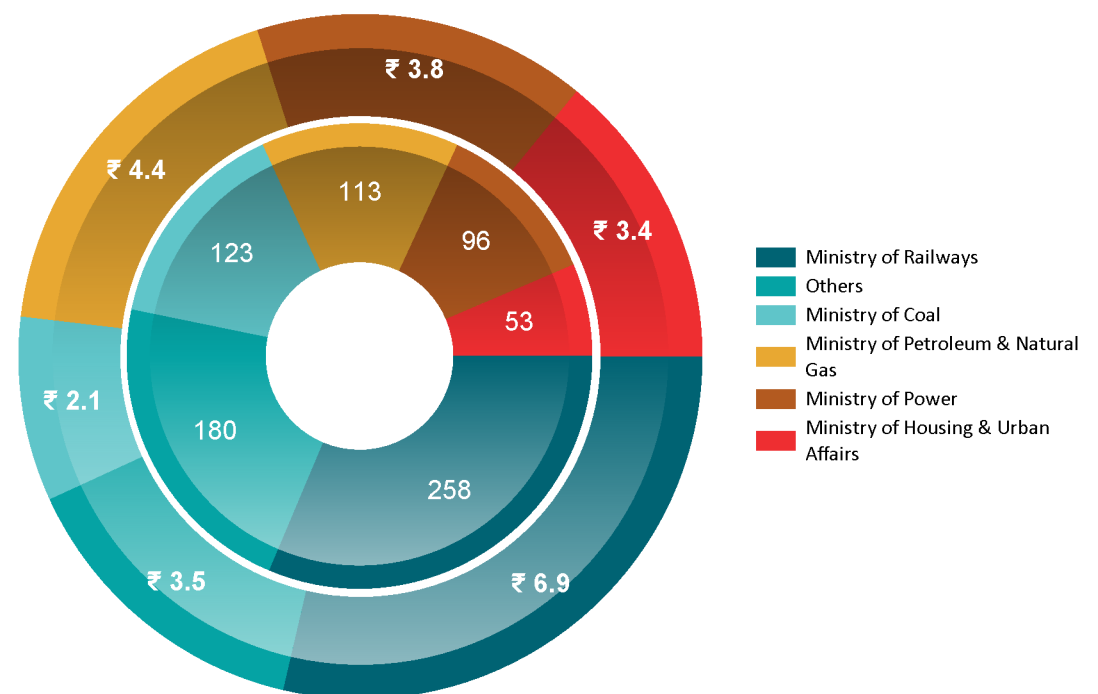

Cost Analytics : Major Sectors*

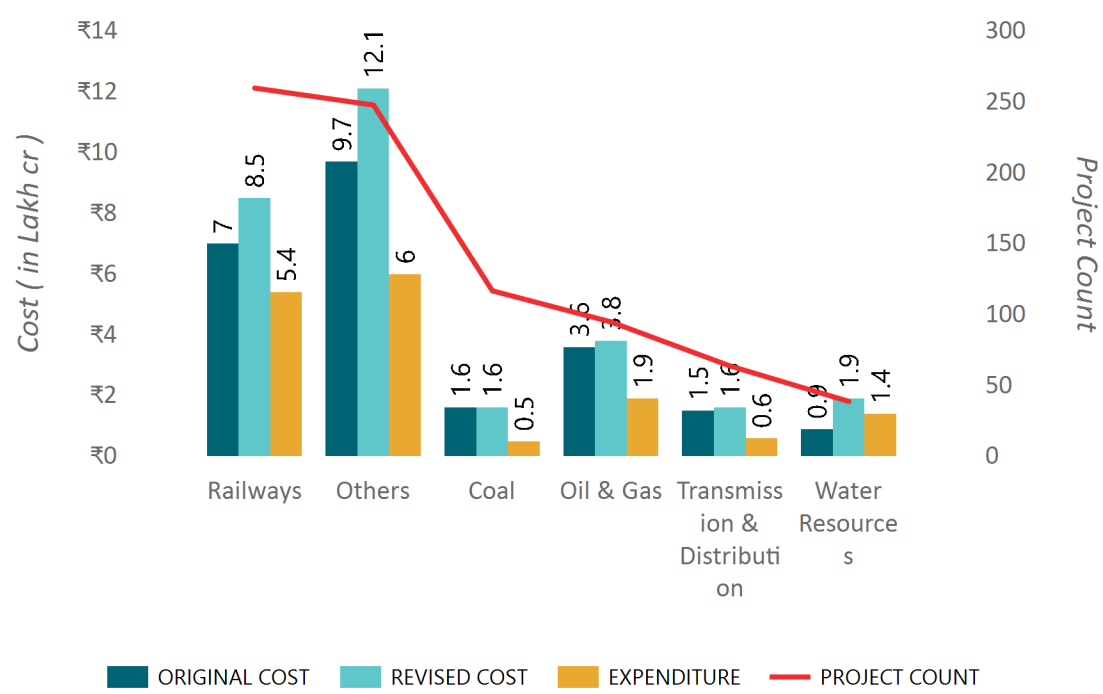


Cost Analytics : Major Ministries*

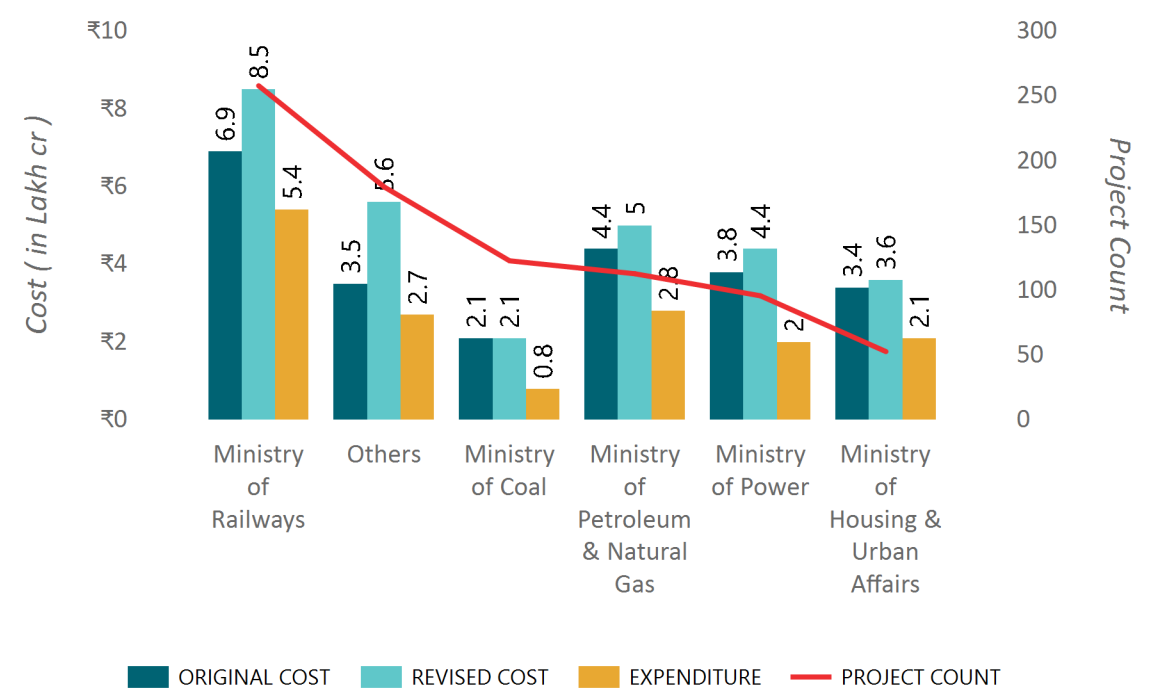


Note: * as per Project Count

Analytics: as per HML

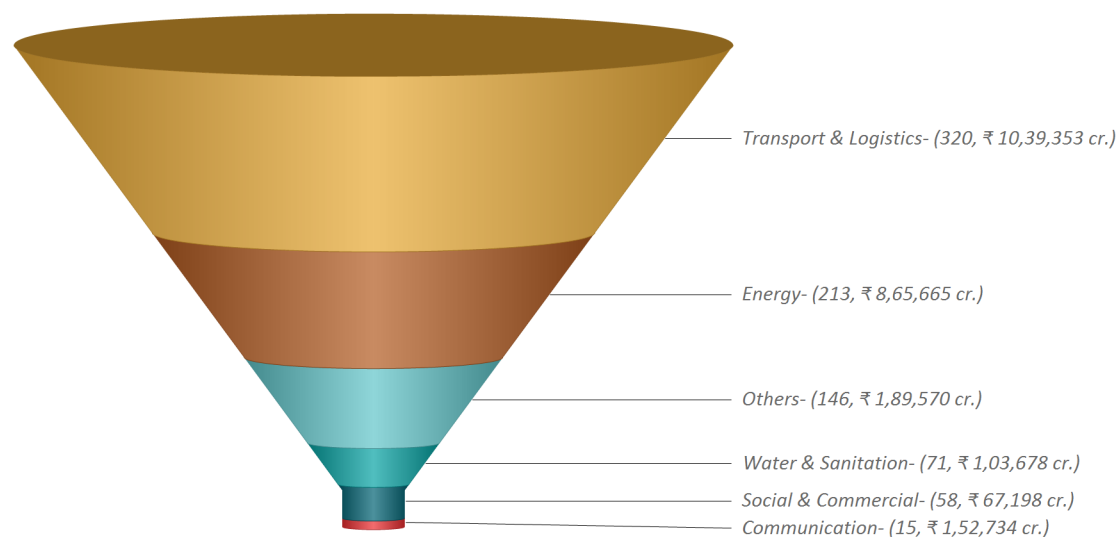


Note: all indicated legends are in format (Project count, Original Cost in crores)

Physical & Financial progress (%) : Project count

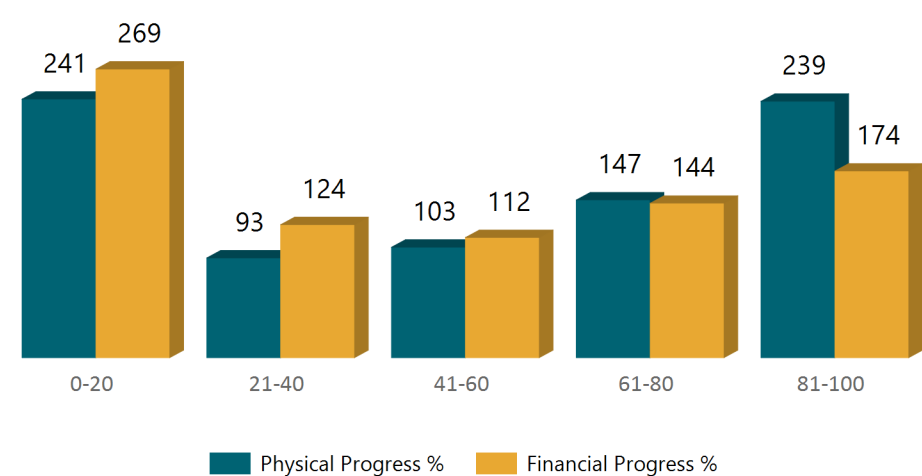




State Comparison : Major States*

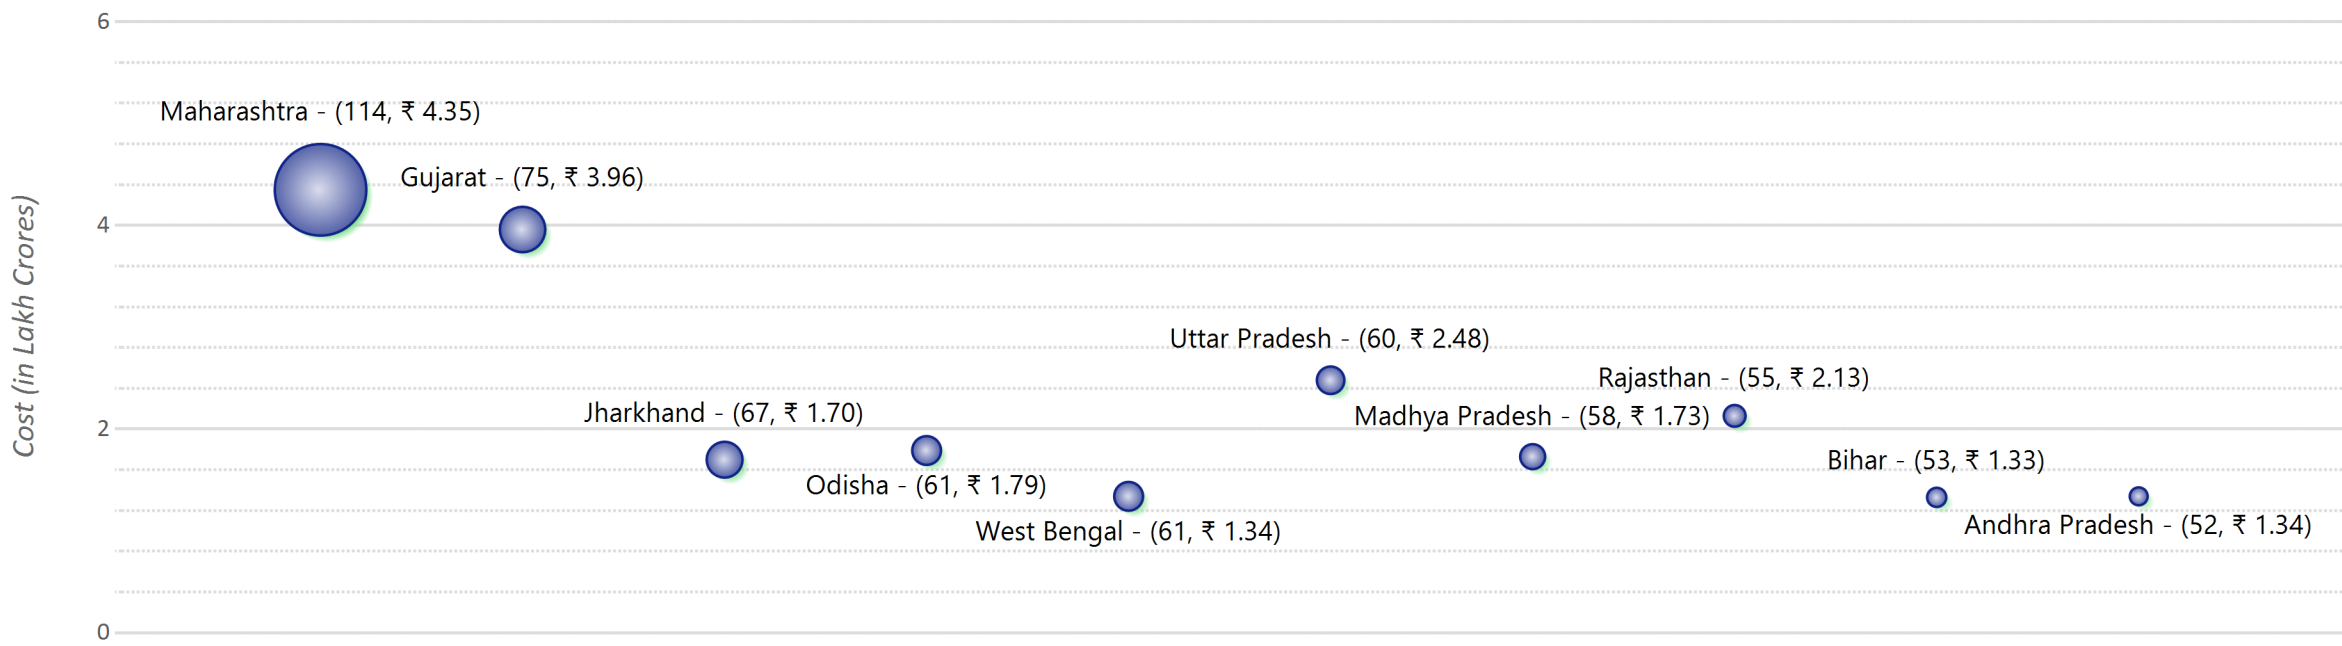


Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
* as per project count

Ministry-wise Distribution of total 239 projects
with reported Physical Progress between 81-100%

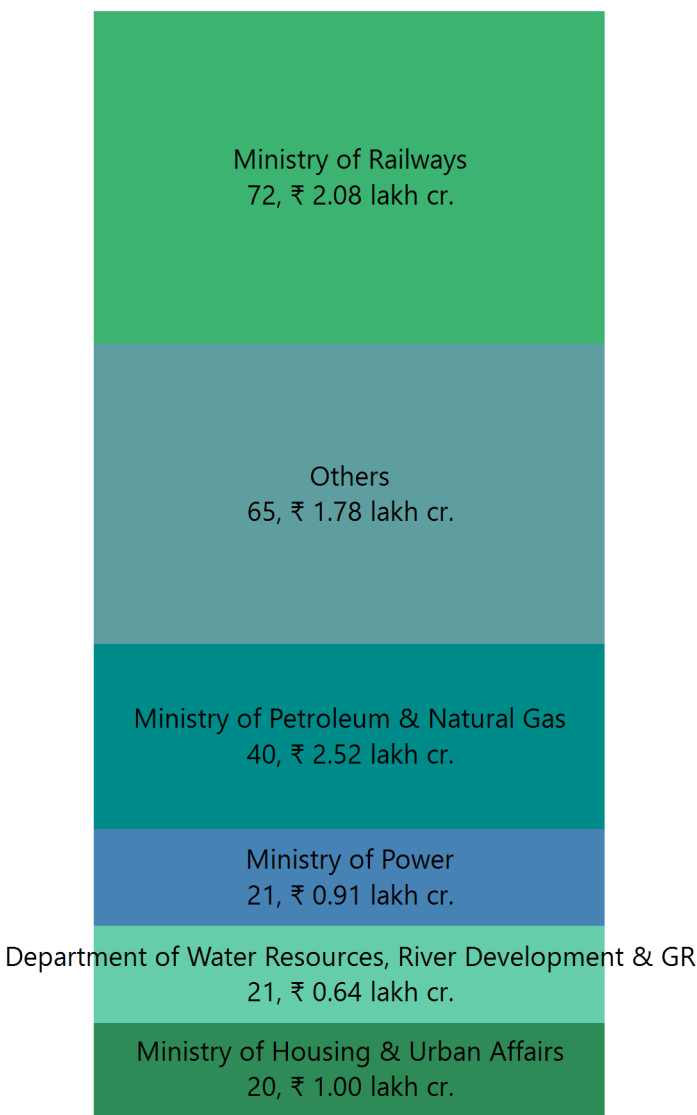

Total Ongoing Projects: Mega & Major




Total North East Region Ongoing Projects: Mega & Major




Note: all indicated legends are in format (Project count, Original Cost)
* Mega project if having original cost ≥ 1000 crore
* Major project if having original cost < 1000 crore

Project volume (nos.)

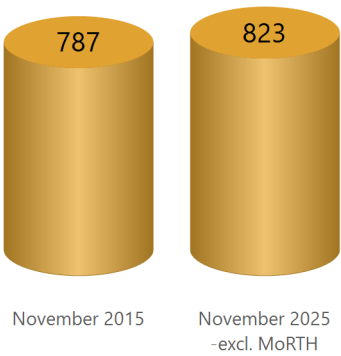


Change in Project Count : +5%

Total Project value (in lakh crore)

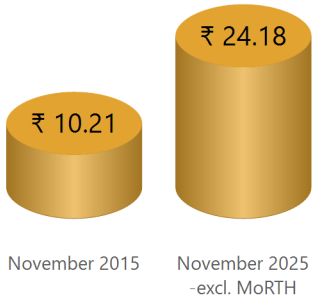

Change in Total Value : +140%

Cumulative Expenditure (in lakh crore)

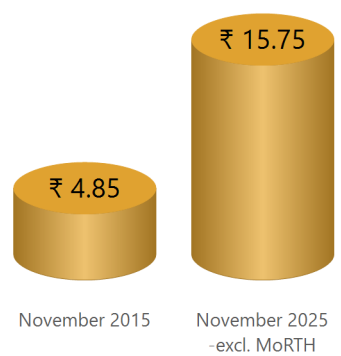

Change in Expenditure : +218%



North Eastern Region





Special Focus : North Eastern Region

NOVEMBER 2025

58 | 10

Ongoing Projects |
Line Ministries & Departments

₹ 1,89,163

Original Cost
(crores)

₹ 2,76,783

Revised Cost
(crores)

₹ 1,92,785

(69.65% of Revised Cost)
Expenditure
(crores)

1


Commissioned during month

3


Newly Added during month

Ministry Comparison : Major Ministries*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

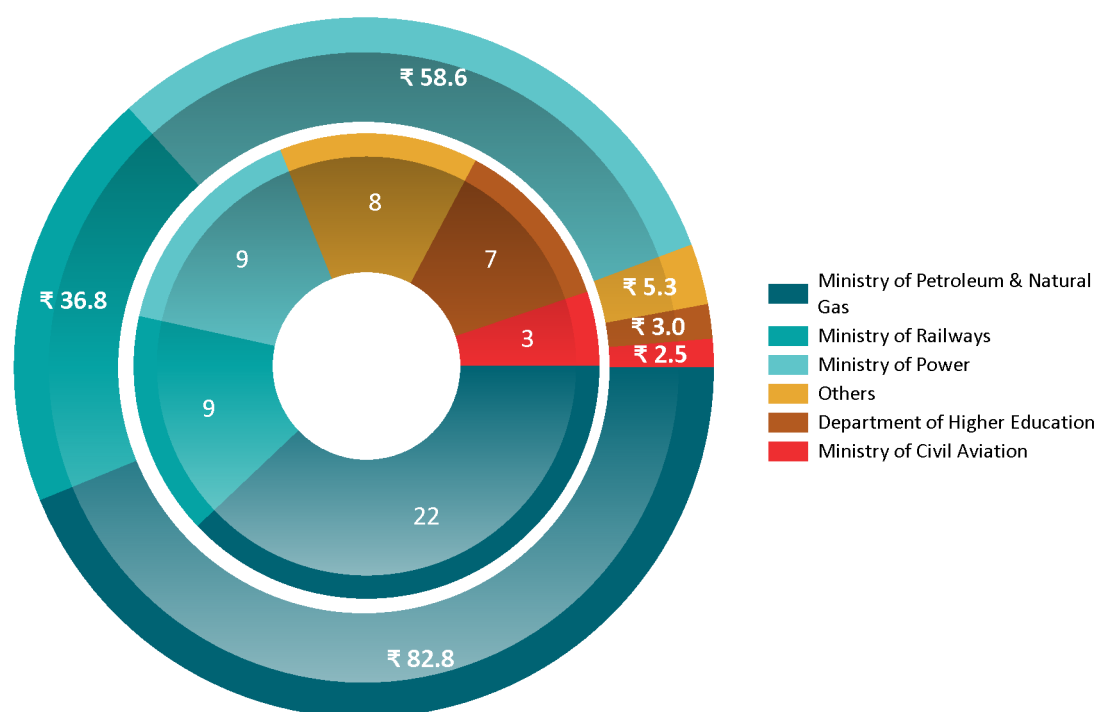


Cost Analytics : Major Ministries*

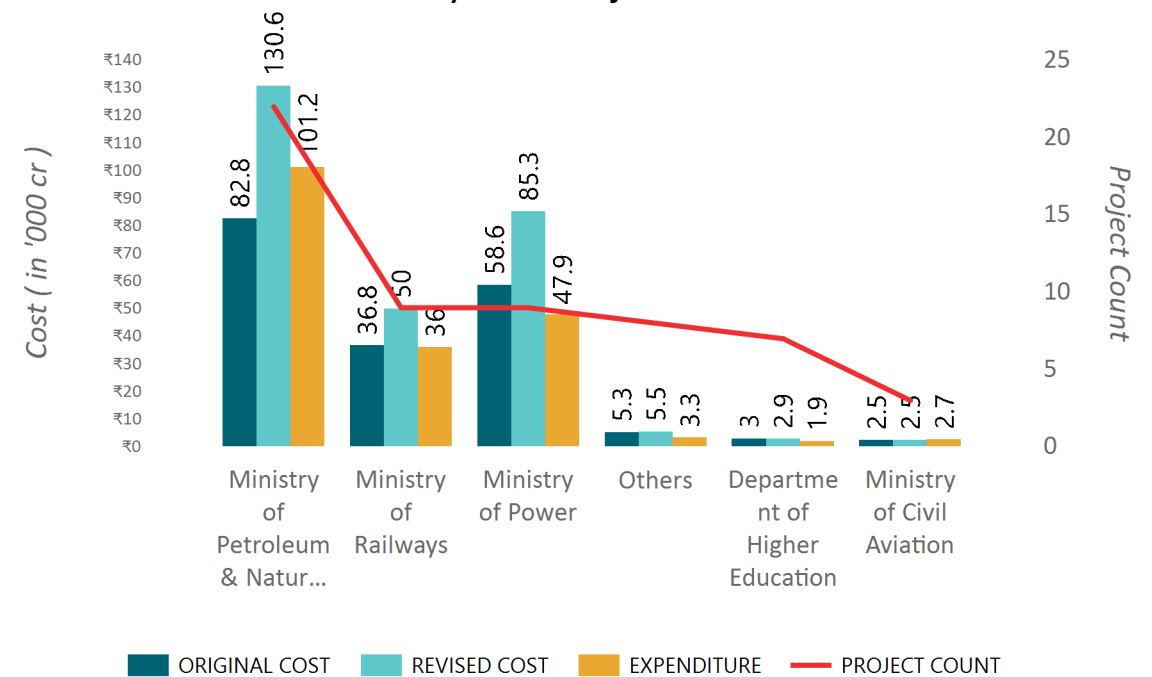


Note: * as per Project Count

Analytics: as per HML

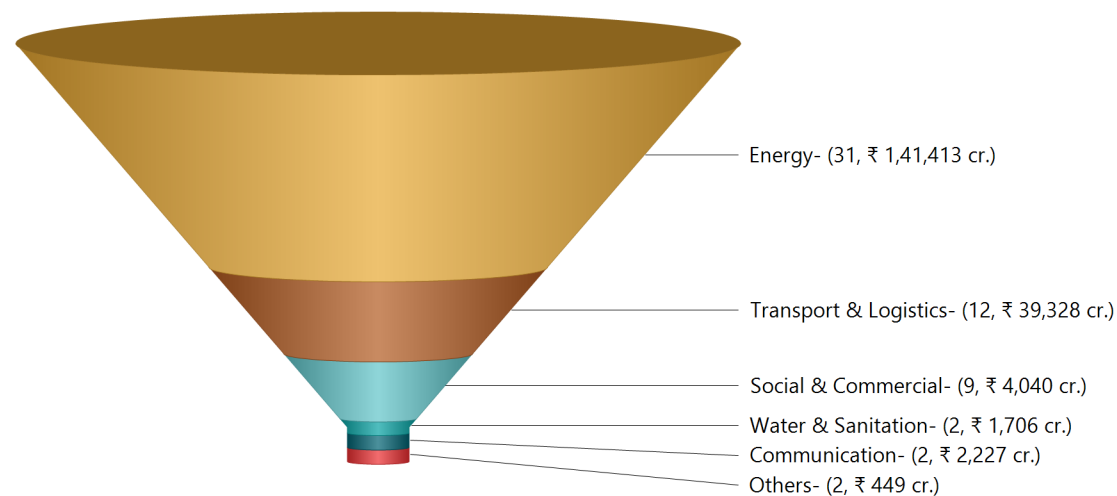


Physical & Financial progress (%) : Project count

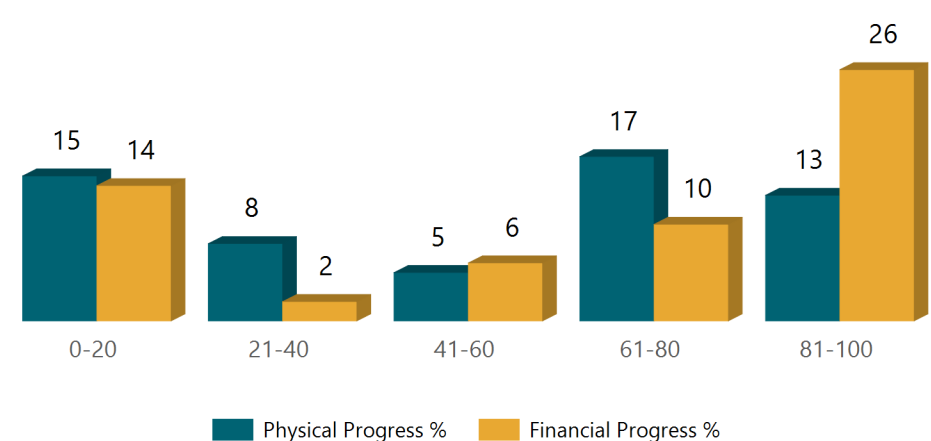

Note: all indicated legends are in format (Project count, Original Cost in crores)

State Comparison : All States

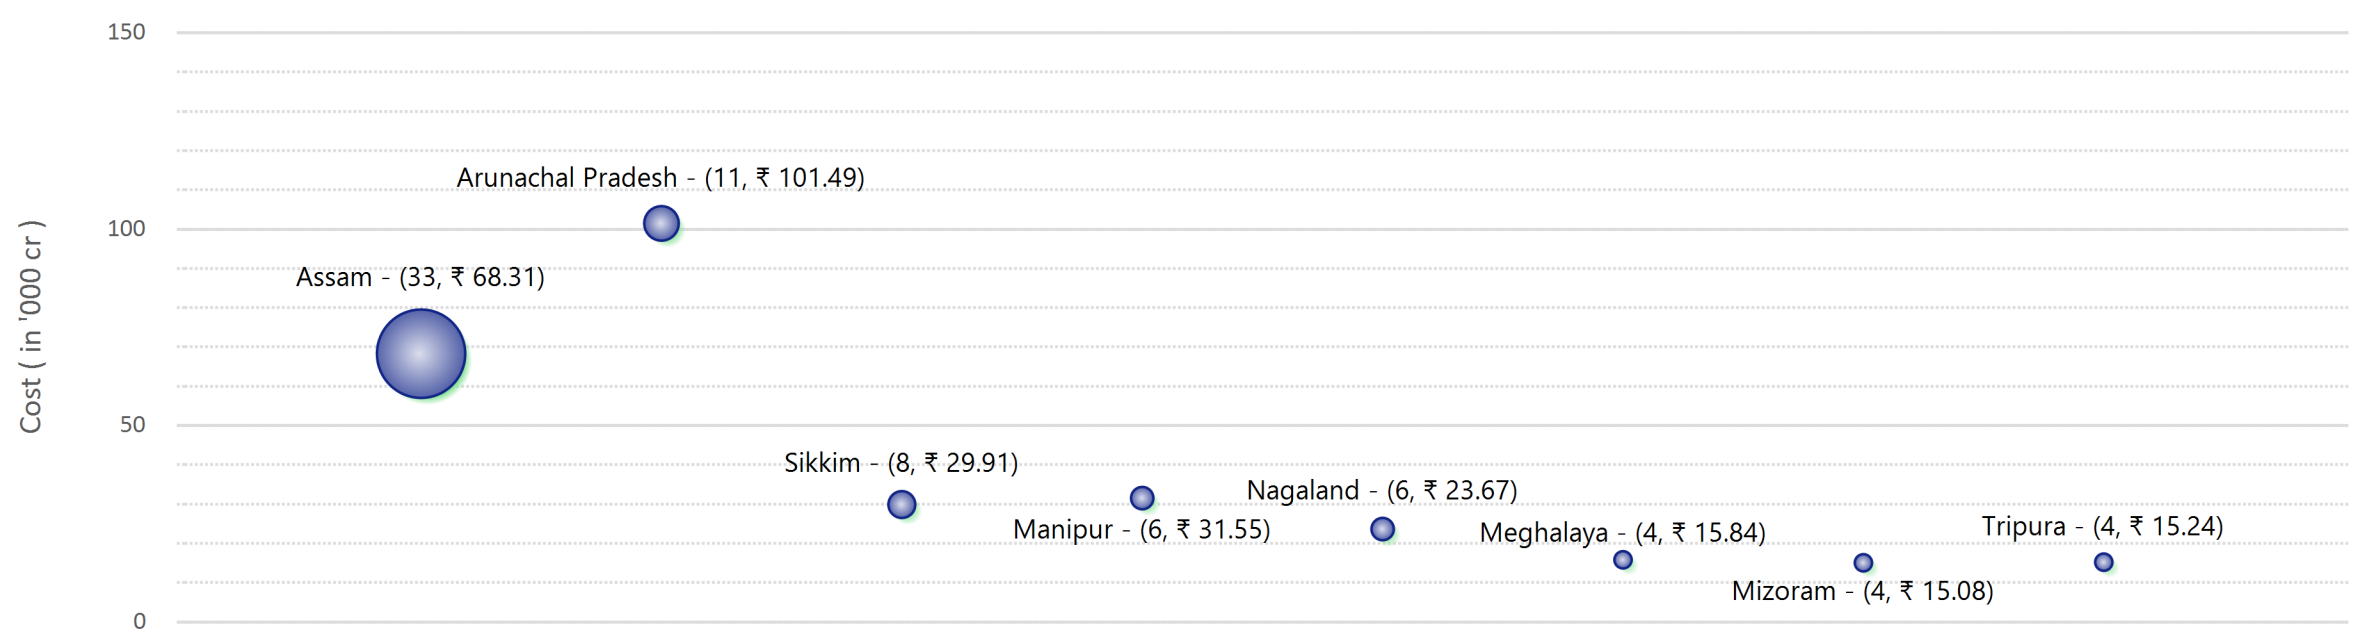

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in Thousand crores)



As per Harmonized Master List (HML)2022



HML Category 1 : Transport & Logistics

NOVEMBER 2025

320
Ongoing Projects

₹ 10,39,353
Original Cost
(crores)


₹ 12,14,067
Revised Cost
(crores)

₹ 7,67,211
(63.19% of Revised Cost)
Expenditure
(crores)


2
Commissioned during month

3
Newly Added during month

Cost Analytics : All Sectors

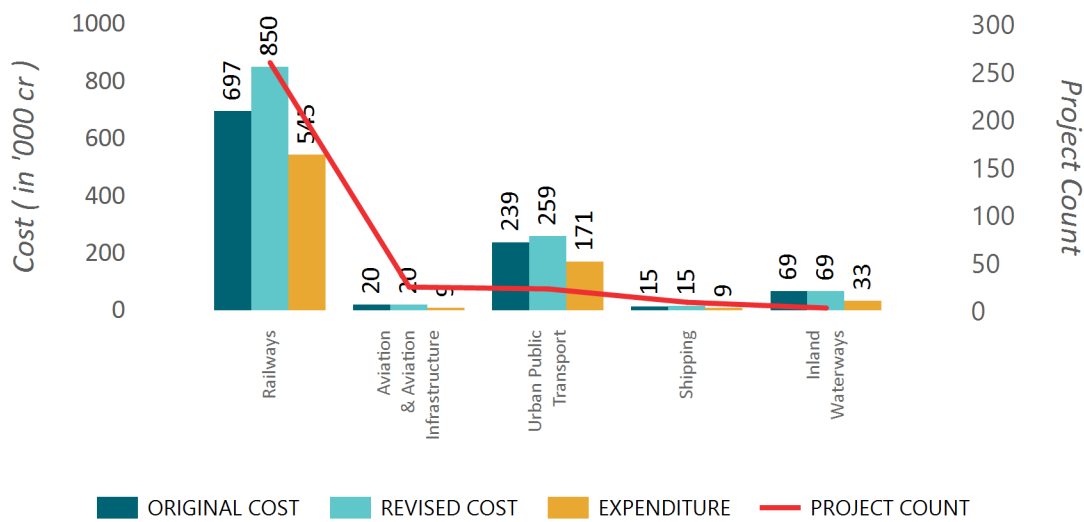

Physical & Financial progress (%) : Project count

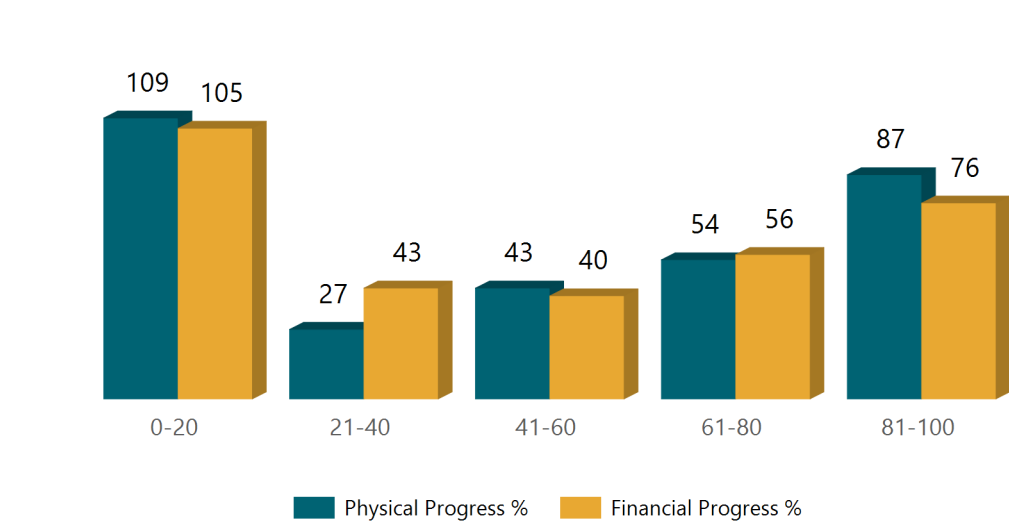

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Railways	260	696,643	850,437	544,630
2	Aviation & Aviation Infrastructure	25	19,950	20,411	9,093
3	Urban Public Transport	23	238,843	259,425	171,216
4	Shipping	9	15,124	15,291	8,976
5	Inland Waterways	3	68,792	68,504	33,297

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	84,200	55
2	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246		29,336	47
3	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
4	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65
5	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	2,805	16

HML Category 2 : Energy

NOVEMBER 2025

213
Ongoing Projects



₹ 8,65,665
Original Cost
(crores)

₹ 10,00,693
Revised Cost
(crores)

₹ 5,05,744
(50.54% of Revised Cost)
Expenditure
(crores)

7
Commissioned during month

14
Newly Added during month

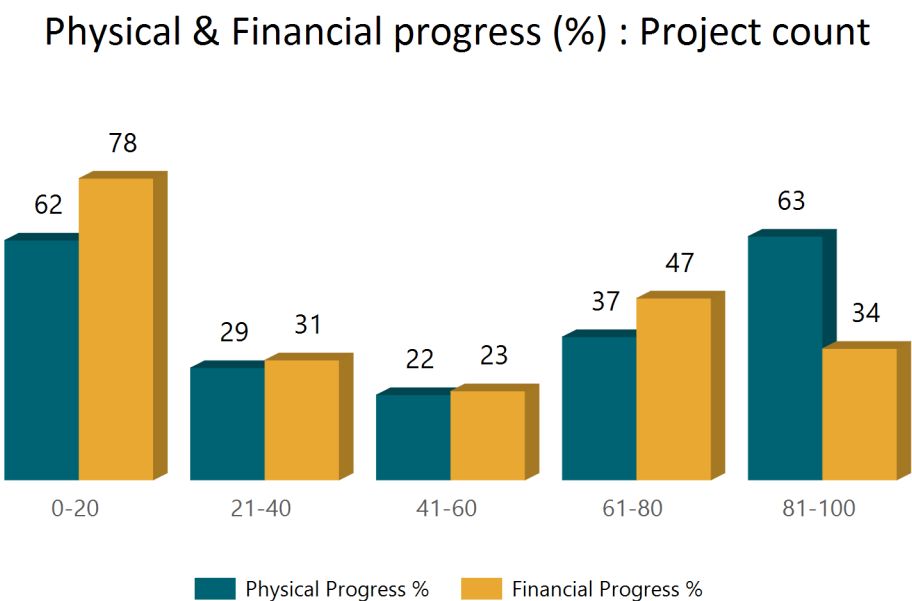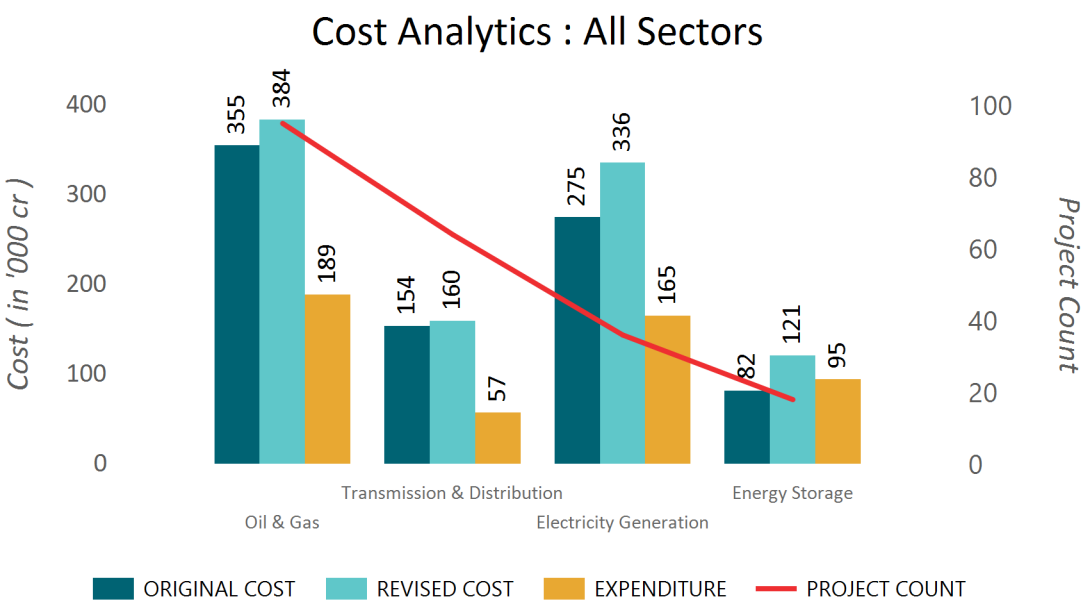

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Oil & Gas	95	355,051	384,190	188,847
2	Transmission & Distribution	64	153,555	159,518	57,184
3	Electricity Generation	36	275,176	336,179	165,130
4	Energy Storage	18	81,884	120,807	94,582

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	2,033	17
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	62,888	89
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA	34,627	36,225	27,366	91
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	32,250	96
5	602182	DIBANG MULTIPURPOSE PROJECT	31,876		3,777	16



HML Category 3 : Water & Sanitation

NOVEMBER 2025

71

Ongoing Projects

₹ 1,03,678

Original Cost
(crores)

₹ 2,03,556

Revised Cost
(crores)

₹ 1,45,548

(71.5% of Revised Cost)
Expenditure
(crores)


1

Commissioned during month


0

Newly Added during month

Cost Analytics : All Sectors

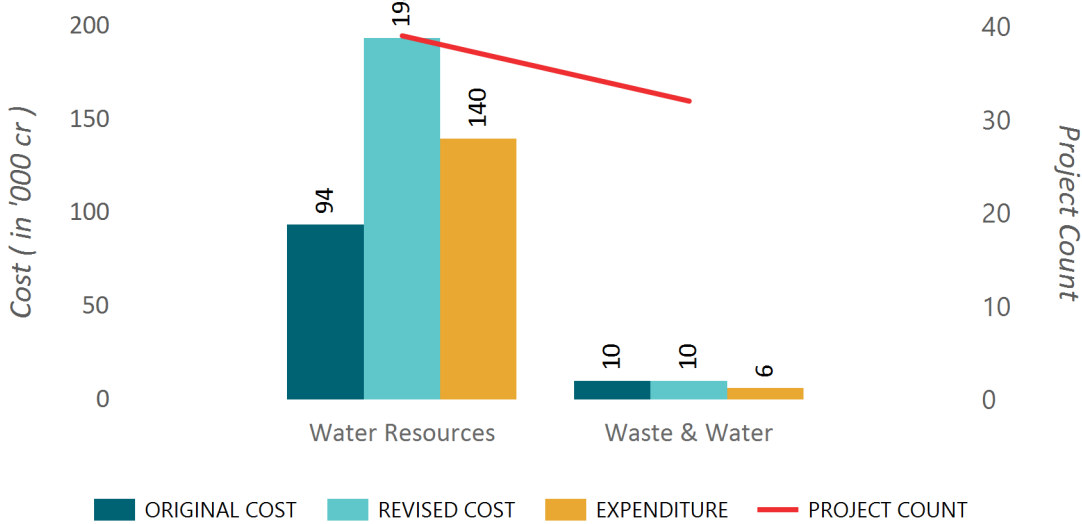

Physical & Financial progress (%) : Project count

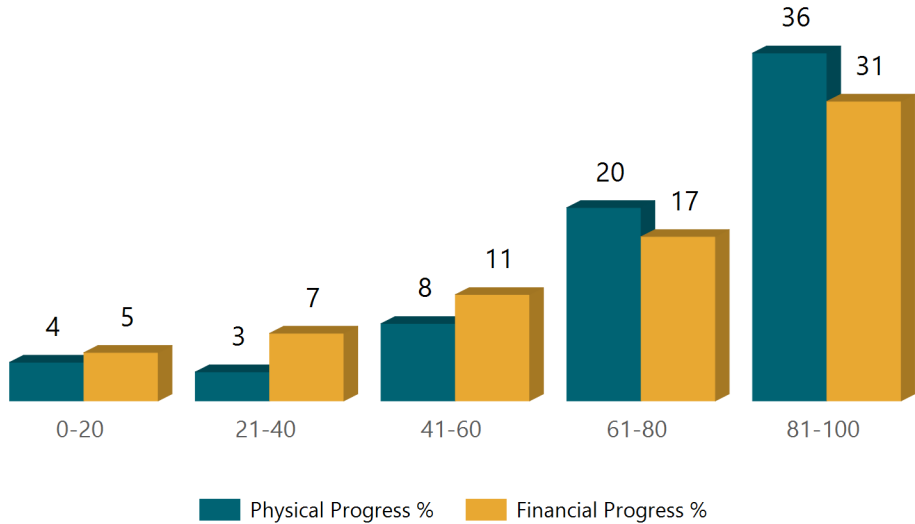

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Water Resources	39	93,740	193,594	139,573
2	Waste & Water	32	9,938	9,962	5,975

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701372	SARDAR SAROVAR PROJECT	20,718	33,413	31,861	93
2	701415	POLAVARAM IRRIGATION PROJECT	10,151	55,549	25,292	84
3	701405	J. CHOKKA RAO DEVADULA LIFT IRRIGATION SCHEME	8,201	14,730	4,665	87
4	400112	JIGAON IRRIGATION PROJECT	7,223		9,035	90
5	701386	GOSIKHURD PROJECT	7,196	12,770	13,838	72

HML Category 4 : Communication

NOVEMBER 2025

15
Ongoing Projects

₹ 1,52,734
Original Cost
(crores)


₹ 2,74,827
Revised Cost
(crores)

₹ 77,536
(28.21% of Revised Cost)
Expenditure
(crores)


0
Commissioned during month

0
Newly Added during month

Cost Analytics : All Sectors

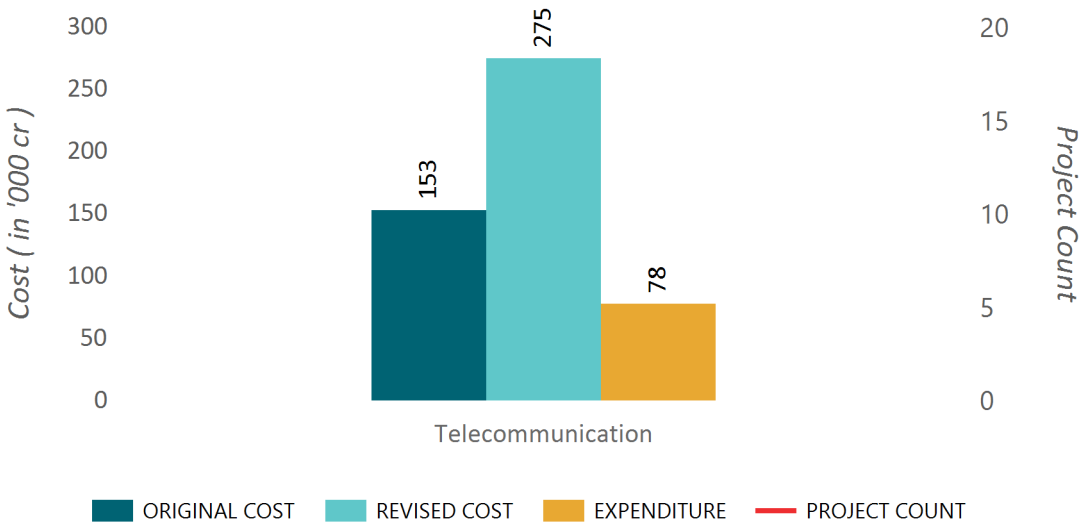

Physical & Financial progress (%) : Project count

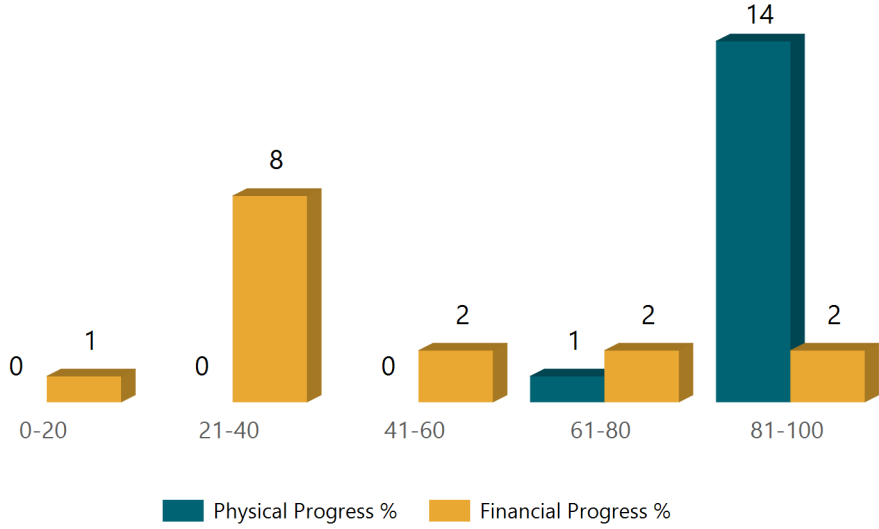

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Telecommunication	15	152,734	274,827	77,536

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	706775	BHARATNET	61,109	188,000	46,432	81
2	701593	4G SERVICES BY BSNL	28,466	19,592	8,471	97
3	400013	SATURATION 4G MOBILE COVERAGE OF UNCOVERED VILLAGES THROUGH USOF	26,316	30,620	9,792	78
4	709857	PLANNING, ENGINEERING, SUPPLY, INSTALLATION, TESTING, COMMISSIONING, INTEGRATION & ANNUAL MAINTENANCE OF 4G MOBILE NETWORK AT 1 LAKH SITES ON PAN INDIA BASIS INCLUDING MUMBAI & DELHI LSA ON TURNKEY BASIS UNDER PHASE IX.2 PROJECT.	24,545		8,472	97
5	701602	PROVISION OF 4G BASED MOBILE SERVICES IN 7,287 UNCOVERED VILLAGES OF 44 ASPIRATIONAL DISTRICT ACROSS 5 STATES OF ANDHRA PRADESH, CHHATTISGARH, JHARKHAND, MAHARASHTRA & ODISHA	3,685		1,203	82

HML Category 5 : Social & Commercial

NOVEMBER 2025

58
Ongoing Projects



₹ 67,198
Original Cost
(crores)

₹ 68,660
Revised Cost
(crores)

₹ 14,069
(20.49% of Revised Cost)
Expenditure
(crores)

1
Commissioned during month

4
Newly Added during month

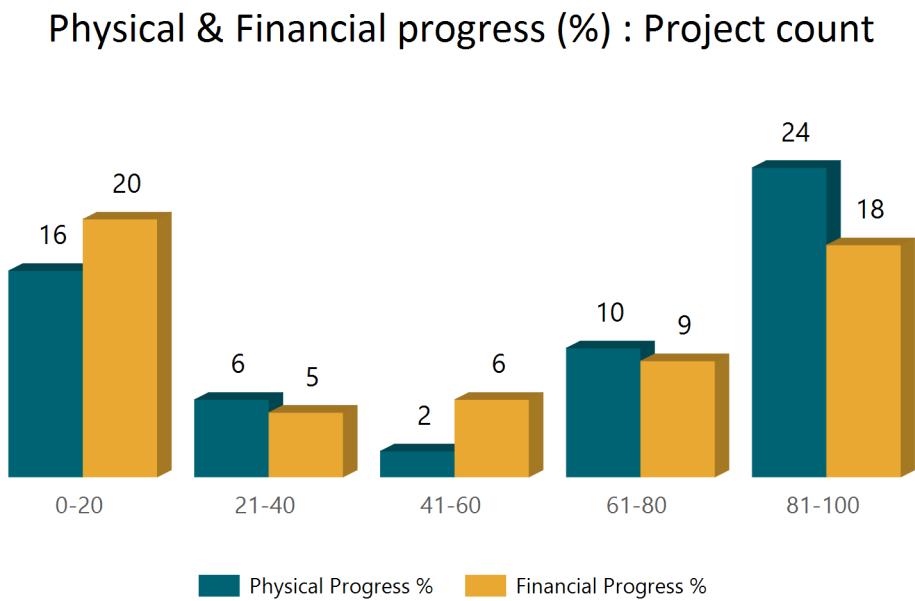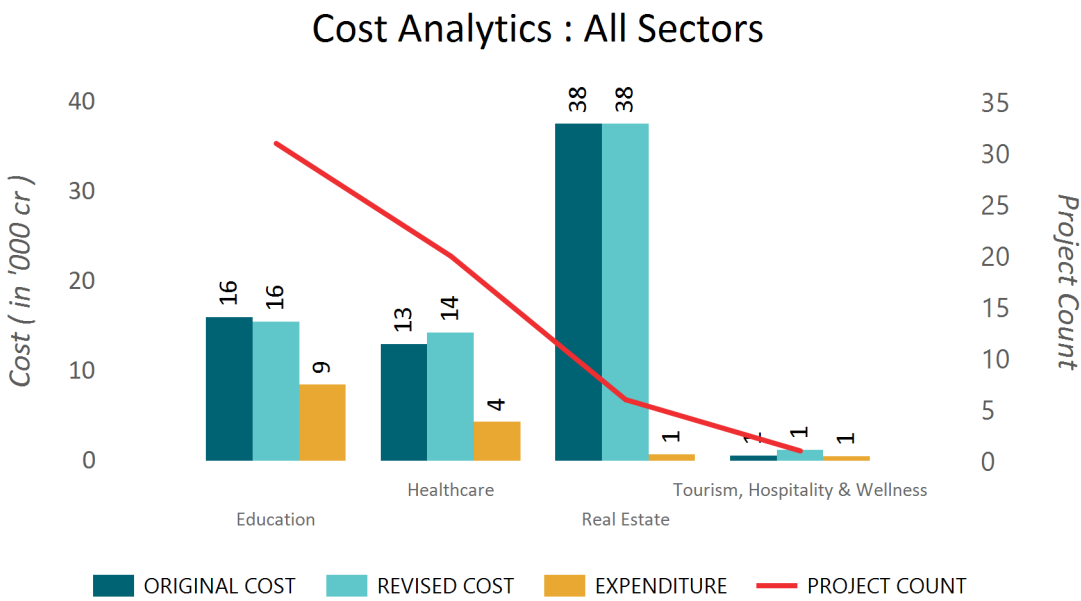

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Education	31	16,022	15,534	8,505
2	Healthcare	20	13,012	14,297	4,333
3	Real Estate	6	37,591	37,591	715
4	Tourism, Hospitality & Wellness	1	573	1,238	516

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850		0	0
2	617883	REDEVELOPMENT OF RESIDENTIAL COLONIES AT AYUR VIGYAN NAGAR AND WEST ANSARI NAGAR CAMPUSES OF AIIMS, NEW DELHI	4,441		25	61
3	701658	KRISHNAPATNAM NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	2,139		503	24
4	701167	AIIMS KASHMIR AT AWANTIPORA JAMMU & KASHMIR	1,828	2,161	1,355	2
5	701657	TUMAKURU NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	1,702		153	14

Other Sectors

NOVEMBER 2025

146
Ongoing Projects

₹ 1,89,570
Original Cost
(crores)


₹ 1,92,982
Revised Cost
(crores)

₹ 64,834
(33.6% of Revised Cost)
Expenditure
(crores)

2
Commissioned during month

0
Newly Added during month

Physical & Financial progress (%) : Project count

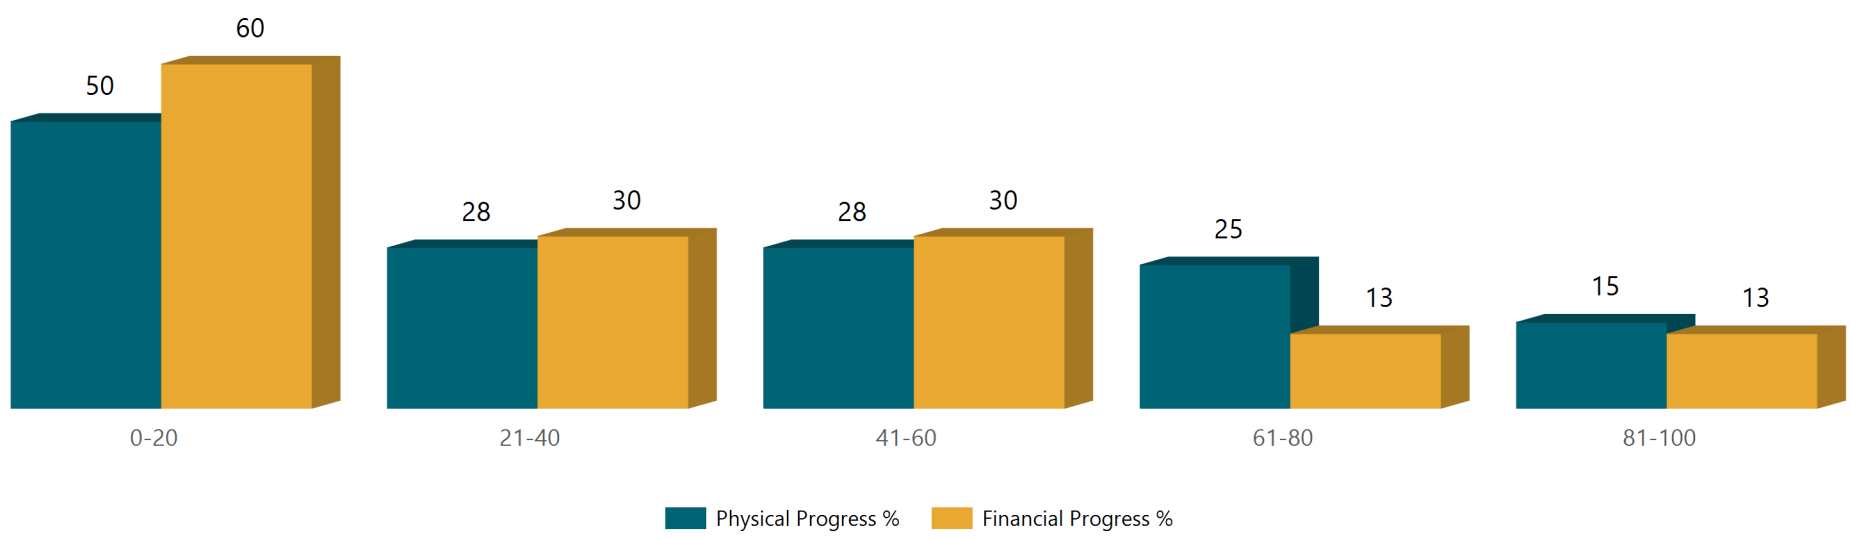

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Coal	117	159,359	157,097	48,897
2	Steel	20	19,267	22,505	8,979
3	Metals & Mining	7	10,044	12,481	6,763
4	Construction	2	899	899	194

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400424	GEVRA OC [70 MTY]	11,816		6,711	78
2	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,742	17
3	400150	RPR MAGADH EXP OCP	7,254		1,601	38
4	617416	REVISED JHARIA MASTER PLAN FOR DEALING WITH FIRE, SUBSIDENCE & REHABILITATION OF AFFECTED FAMILIES IN JHARIA COALFIELD- REG.	5,940		1	12
5	616253	BLOCK E OCP	5,851		20	3



Major Infrastructure Central Ministries & Departments





Ministry of Railways

NOVEMBER 2025

258

Ongoing Projects

₹ 6,93,157

Original Cost
(crores)

₹ 8,46,186

Revised Cost
(crores)

₹ 5,42,700

(64.13% of Revised Cost)

Expenditure
(crores)

131 | ₹ 632,889

Mega Projects
Count | Original Cost (crores)

127 | ₹ 60,269

Major Projects
Count | Original Cost

0


Commissioned during month

2

Newly Added during month

Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

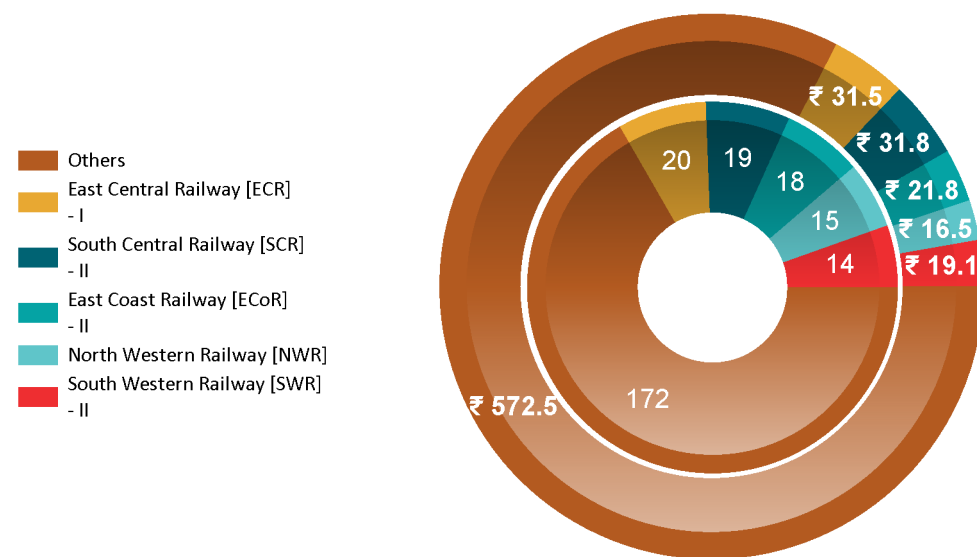


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Physical & Financial progress (%) : Project count

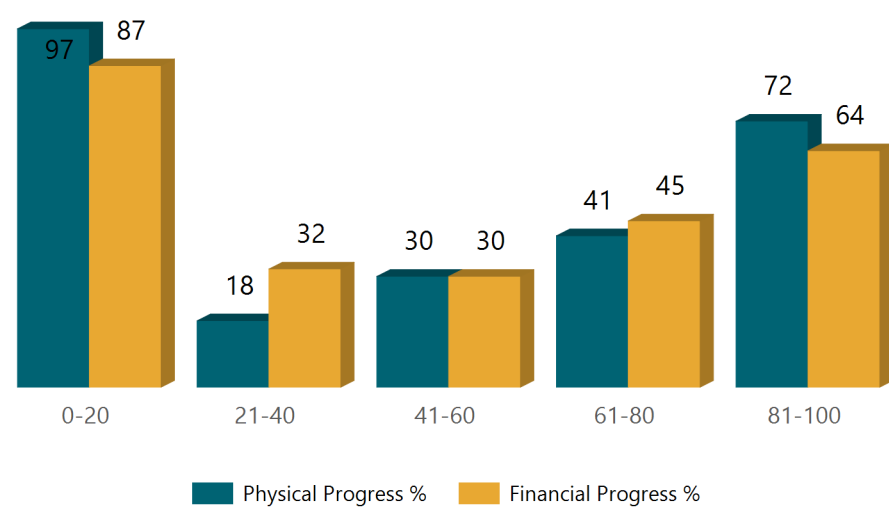

Cost Analytics : Major Sectors*

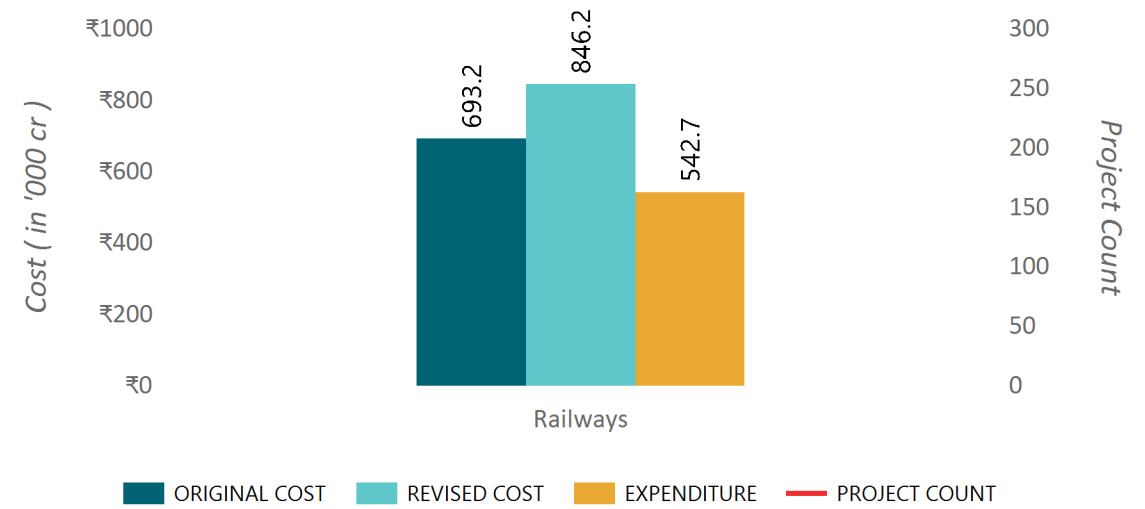

State Comparison : Major States*

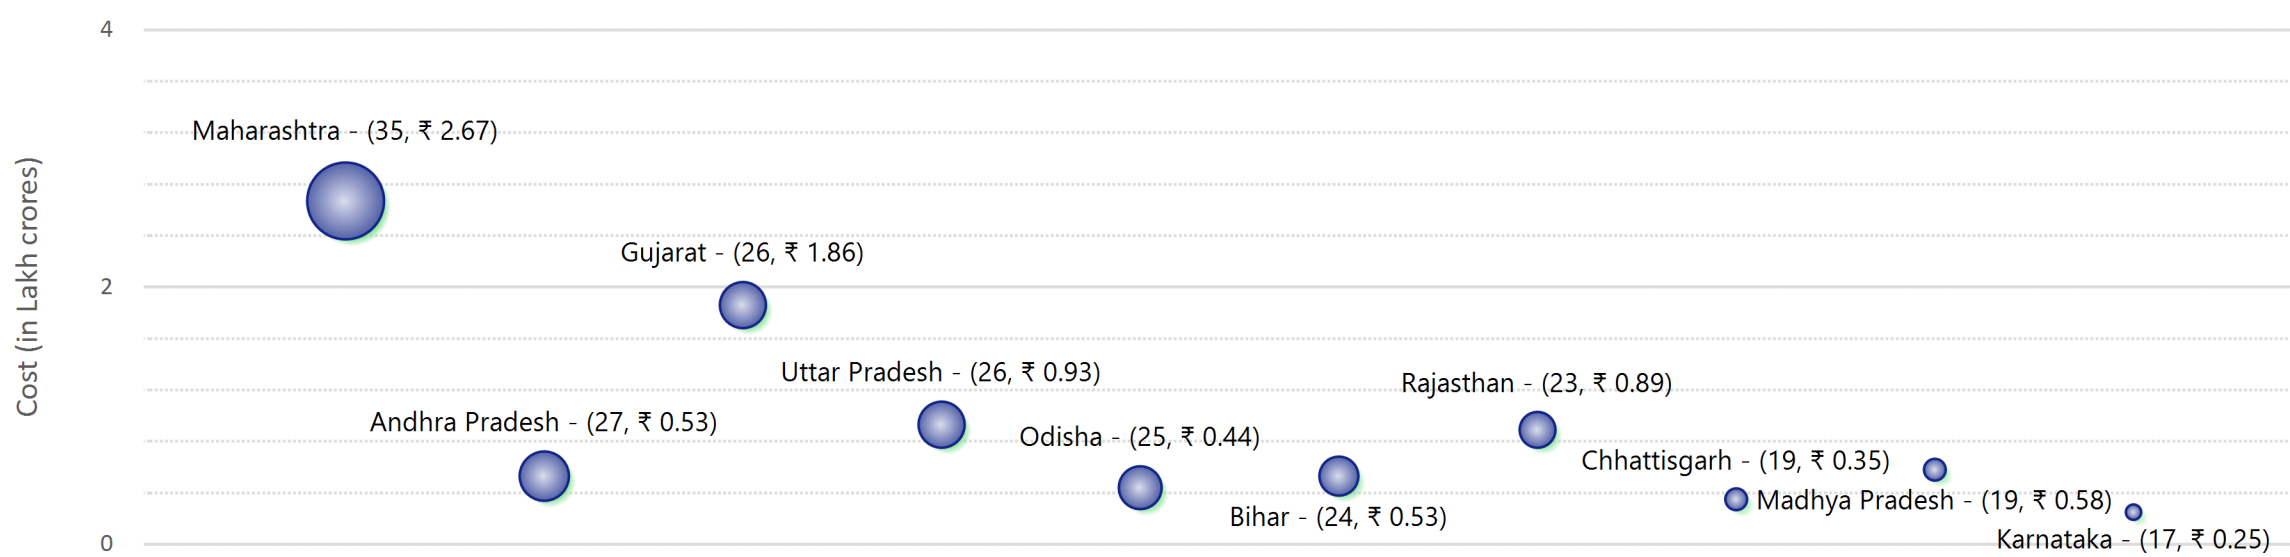

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	84,200	55
2	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
3	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65
4	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	2,805	16
5	705391	JIRIBAM-IMPHAL NEW LINE PROJECT	14,323	21,886	15,782	72



Ministry of Coal

NOVEMBER 2025

123

Ongoing Projects

₹ 2,10,964

Original Cost
(crores)

₹ 2,13,727

Revised Cost
(crores)

₹ 75,718

(35.43% of Revised Cost)
Expenditure
(crores)

39 | ₹ 169,485

Mega Projects
Count | Original Cost (crores)

84 | ₹ 41,479

Major Projects
Count | Original Cost

1


Commissioned during month

0

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

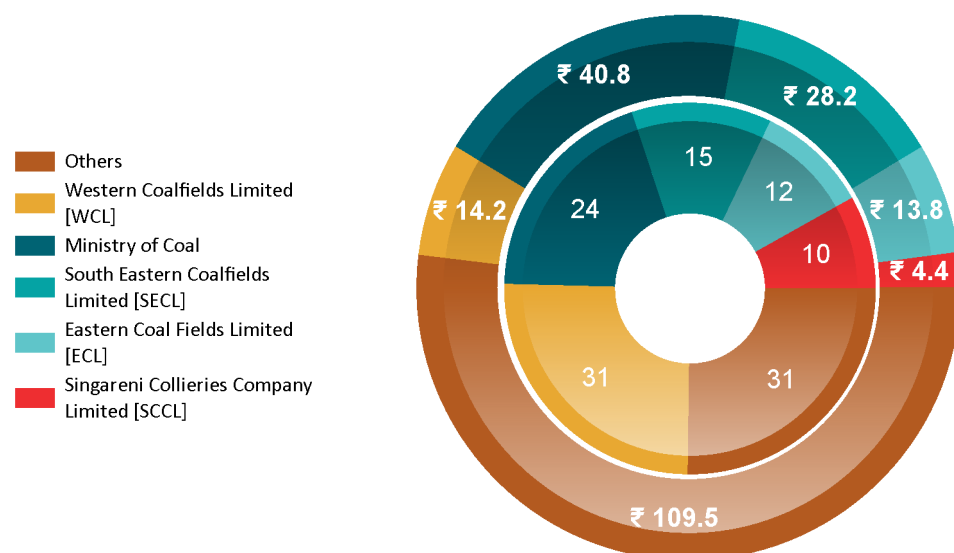


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

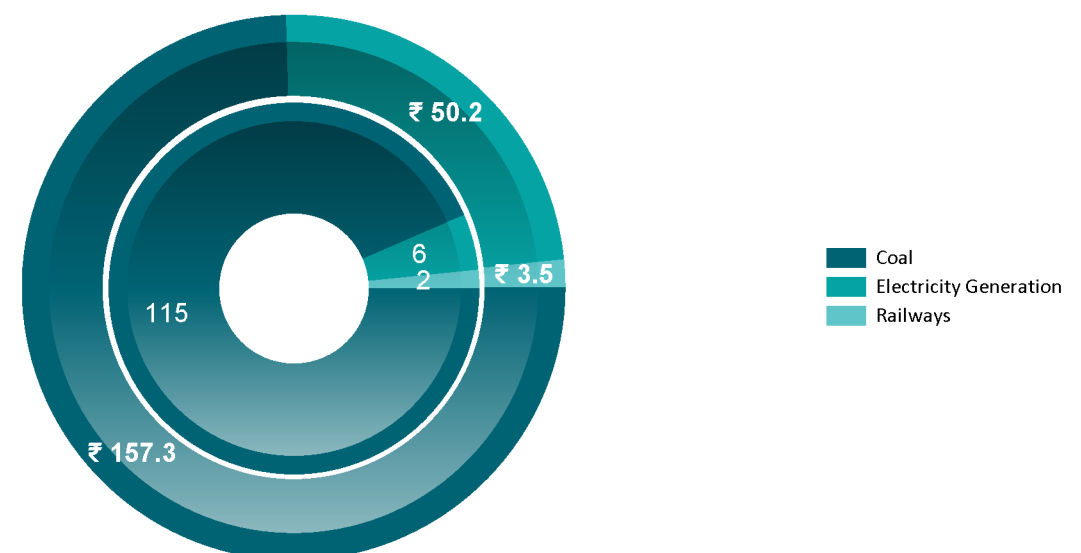


Physical & Financial progress (%) : Project count

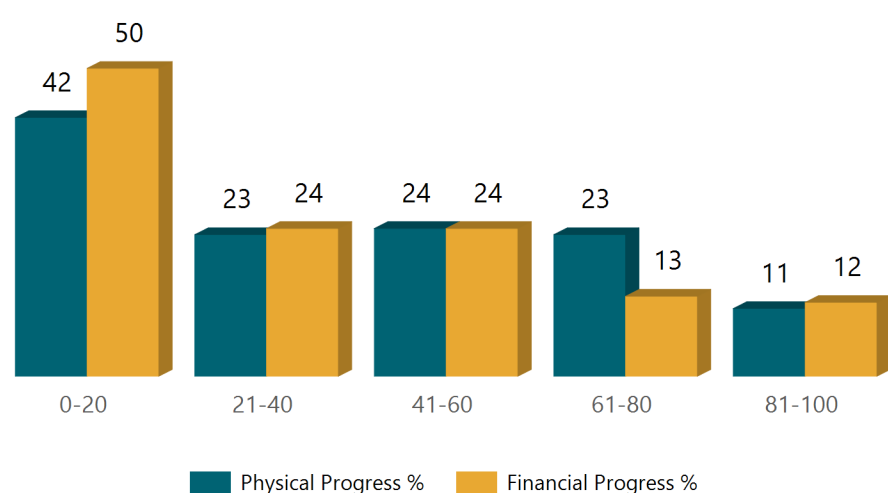

Cost Analytics : Major Sectors*

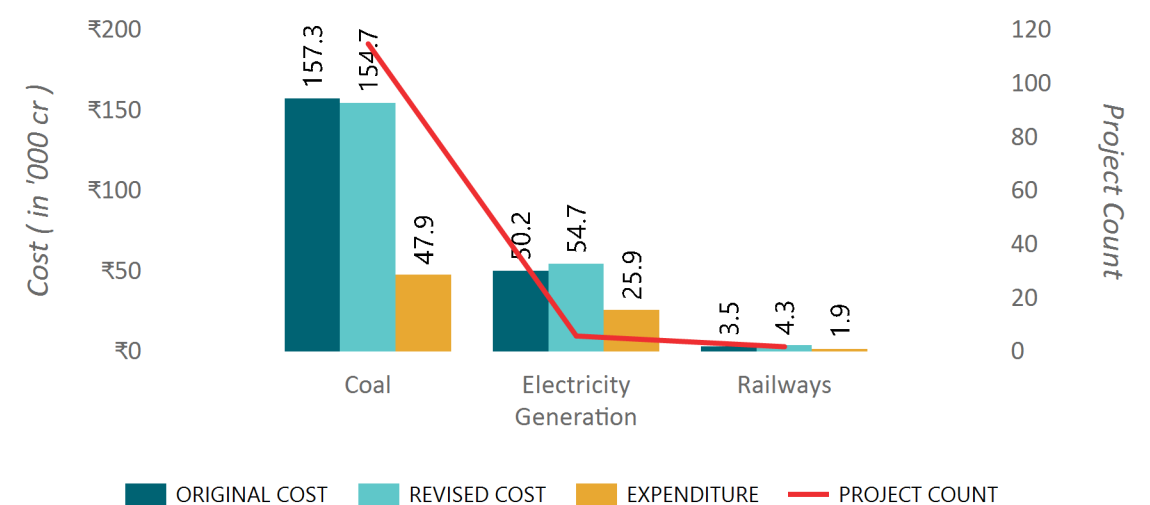

State Comparison : Major States*

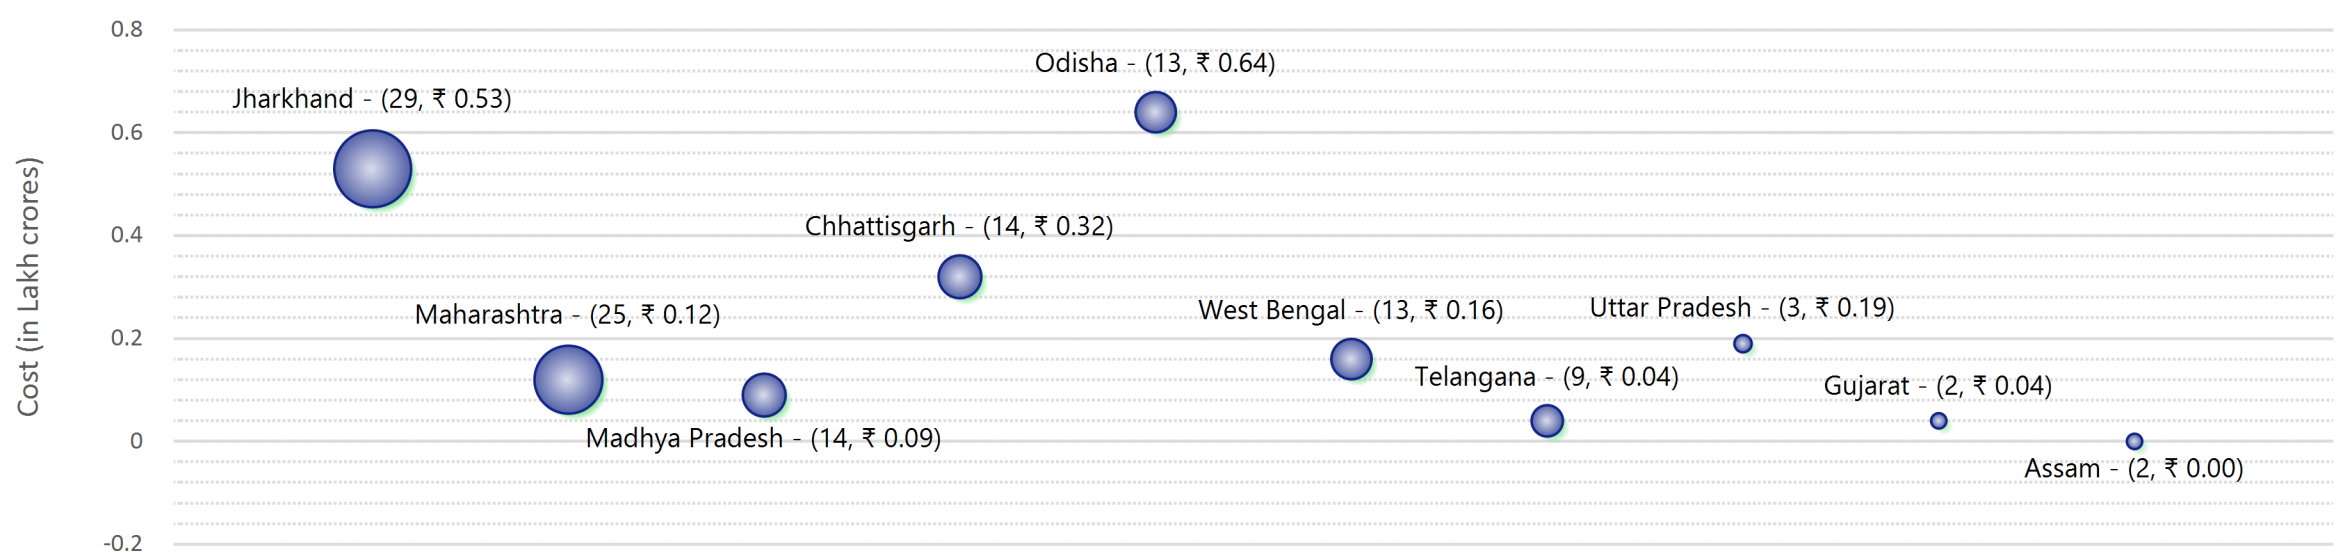

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400231	NLC TALABIRA THERMAL POWER PROJECT	27,213	27,213	2,551	1
2	400259	GHATAMPUR THERMAL POWER PLANT 3 X 660 MW	17,238	21,781	20,711	93
3	400424	GEVRA OC [70 MTY]	11,816	11,816	6,711	78
4	400185	GOPALJI KANIHA OCP [10 TO 30 M]	8,416	6,108	1,742	17
5	400150	RPR MAGADH EXP OCP	7,254	7,254	1,601	38

Ministry of Petroleum & Natural Gas

NOVEMBER 2025

113
Ongoing Projects

₹ 4,36,935
Original Cost
(crores)

₹ 5,04,997
Revised Cost
(crores)

₹ 2,83,429
(56.13% of Revised Cost)
Expenditure
(crores)


50 | ₹ 408,477
Mega Projects
Count | Original Cost (crores)

63 | ₹ 28,458
Major Projects
Count | Original Cost


0
Commissioned during month

11
Newly Added during month


Agency Comparison : Major Agencies*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

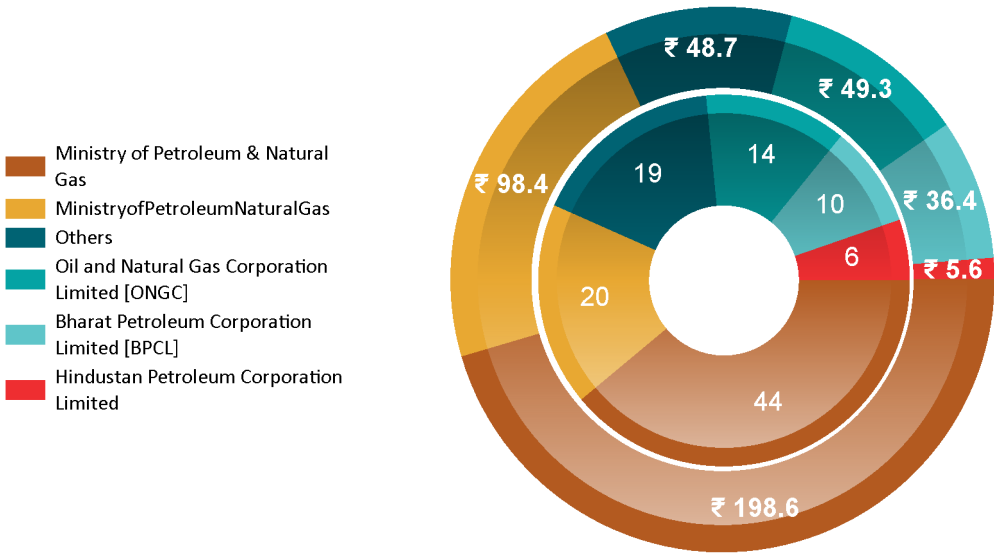


Sectoral Comparison : Major Sectors*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

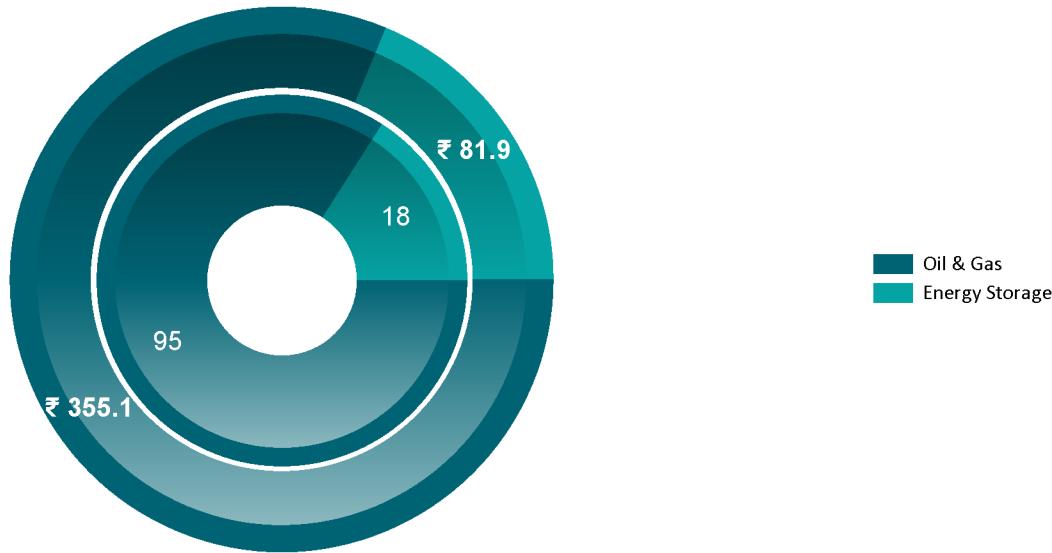


Physical & Financial progress (%) : Project count

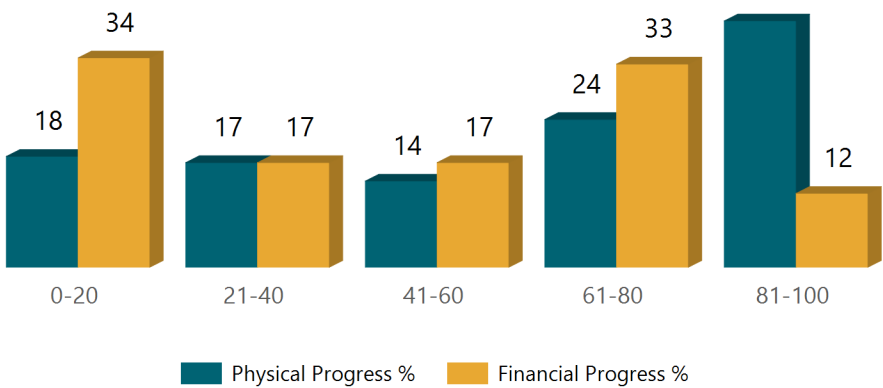

Cost Analytics : Major Sectors*

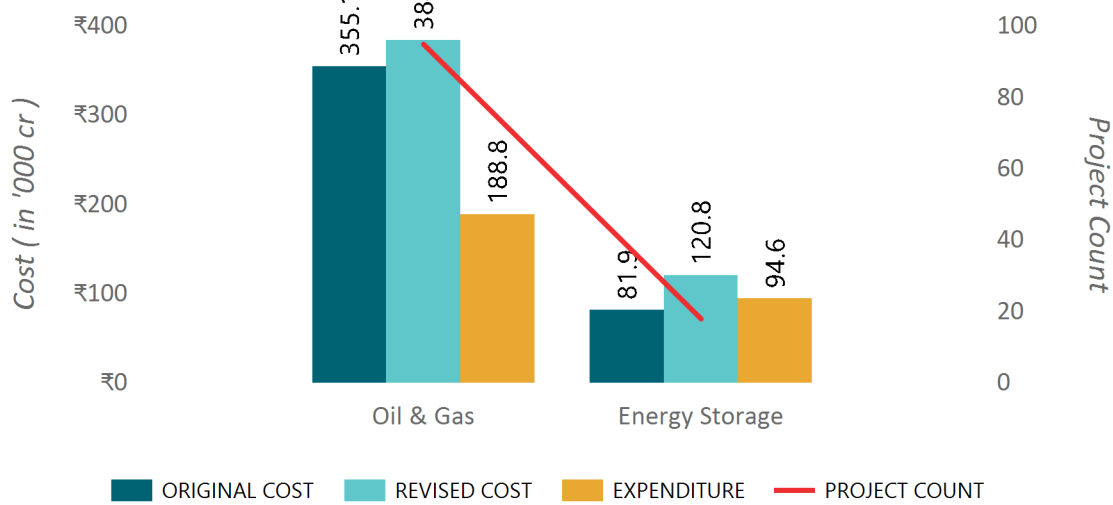

State Comparison : Major States*

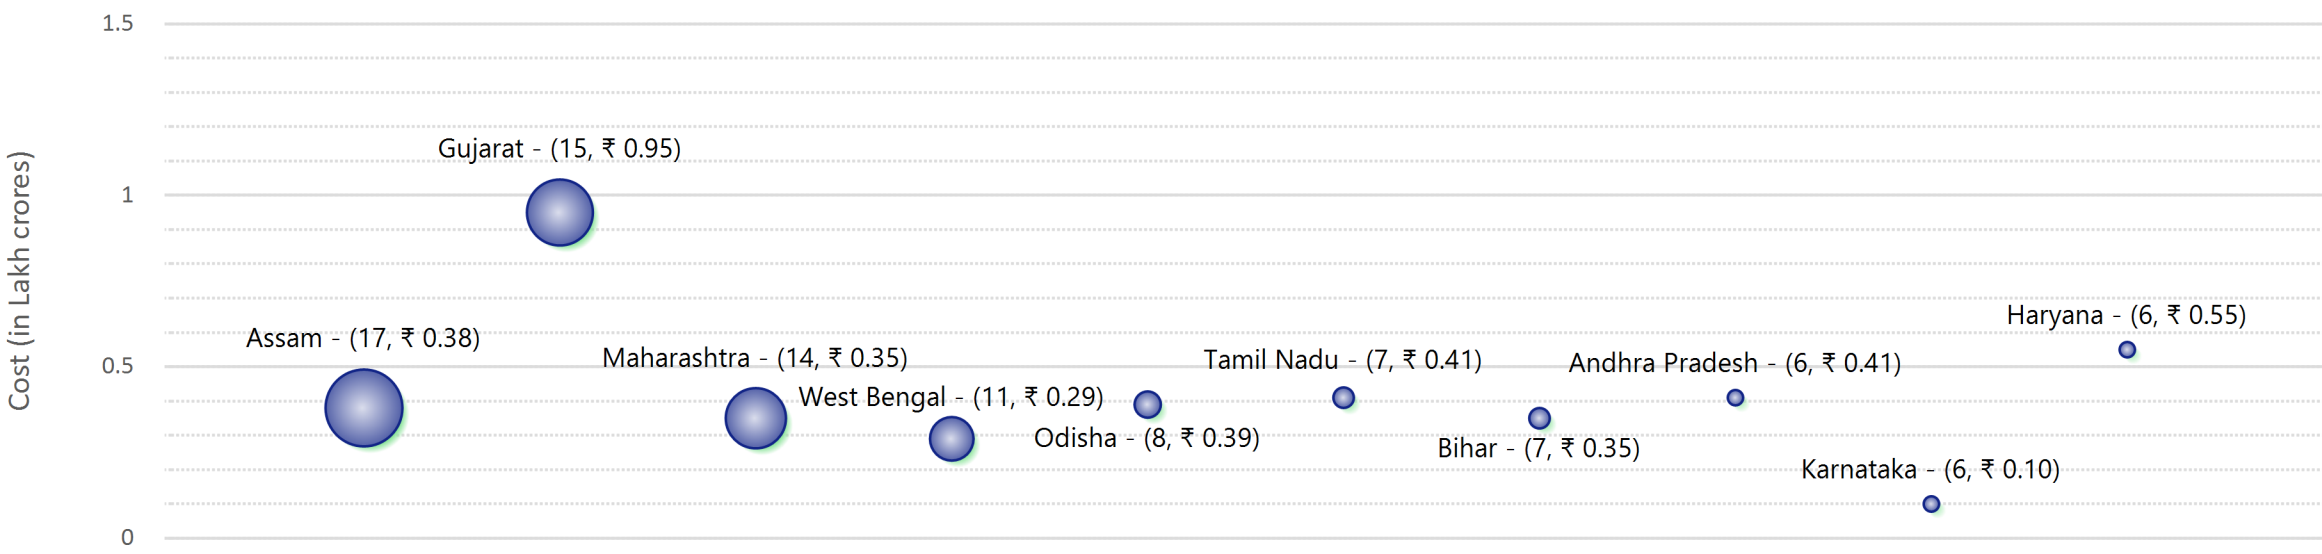

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	2,033	17
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	62,888	89
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	27,366	91
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	32,250	96
5	604795	CBR 9 MMTPA PROJECT	31,580	36,354	1,398	10



Ministry of Power

NOVEMBER 2025

96

Ongoing Projects

₹ 3,80,612

Original Cost
(crores)

₹ 4,43,317

Revised Cost
(crores)

₹ 1,97,423

(44.53% of Revised Cost)
Expenditure
(crores)

66 | ₹ 368,130

Mega Projects
Count | Original Cost (crores)

30 | ₹ 12,482

Major Projects
Count | Original Cost

7


Commissioned during month

3

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

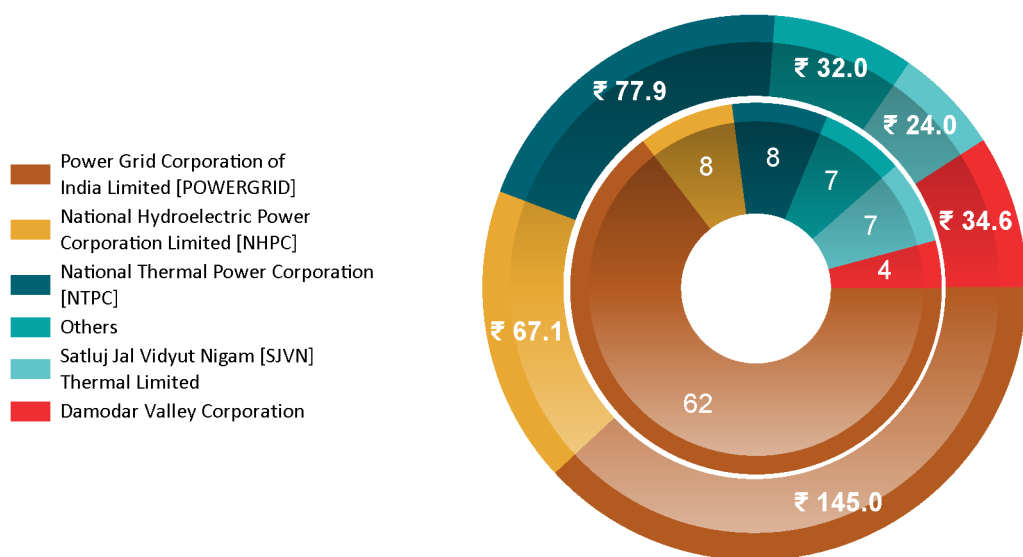


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

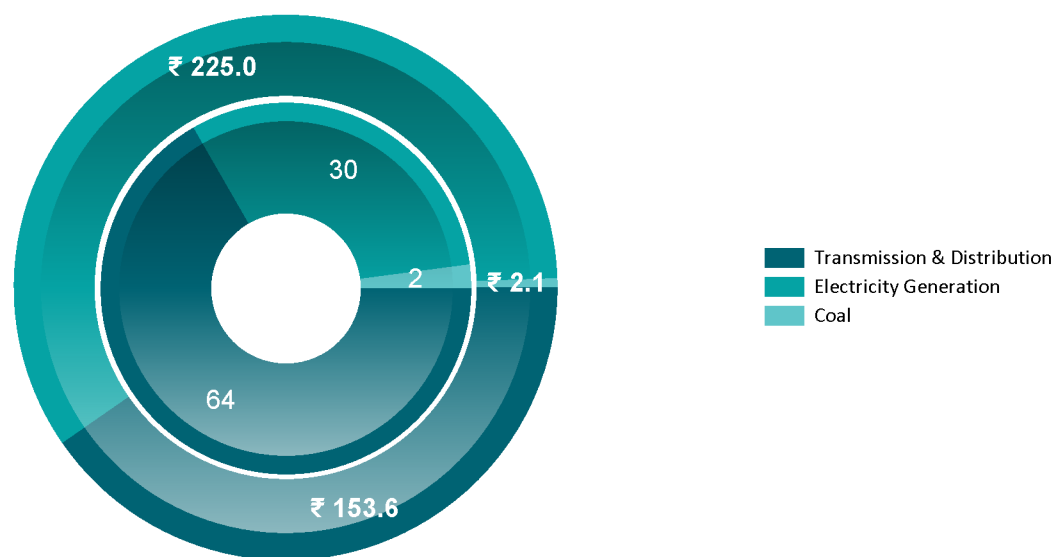


Physical & Financial progress (%) : Project count

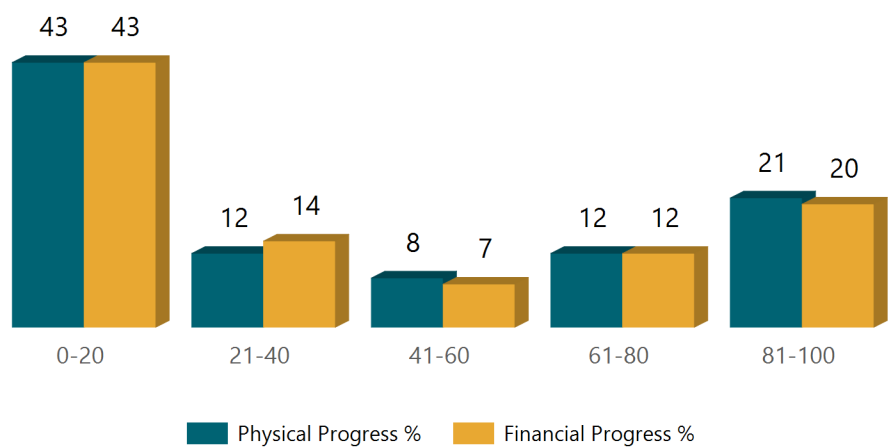

Cost Analytics : Major Sectors*

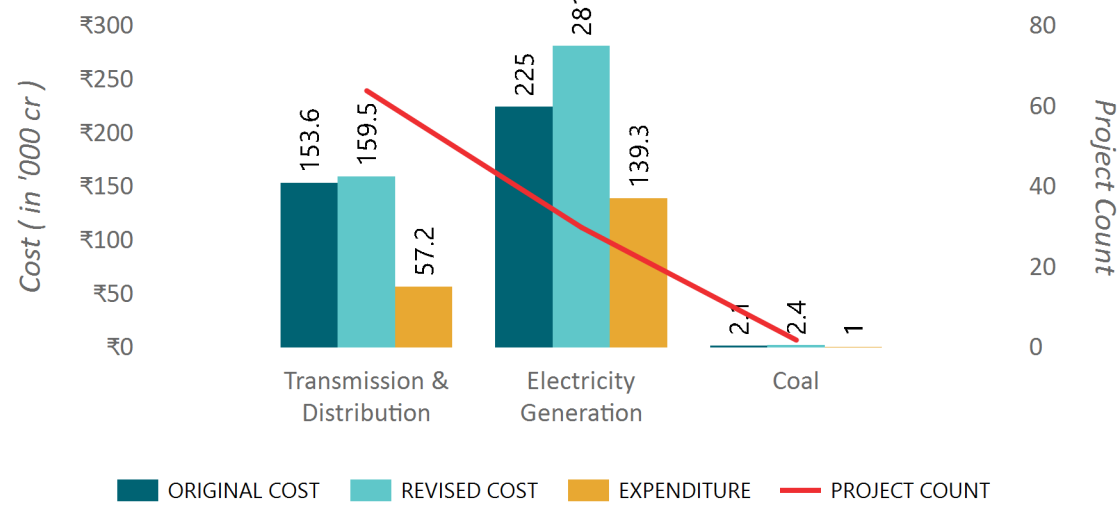

State Comparison : Major States*

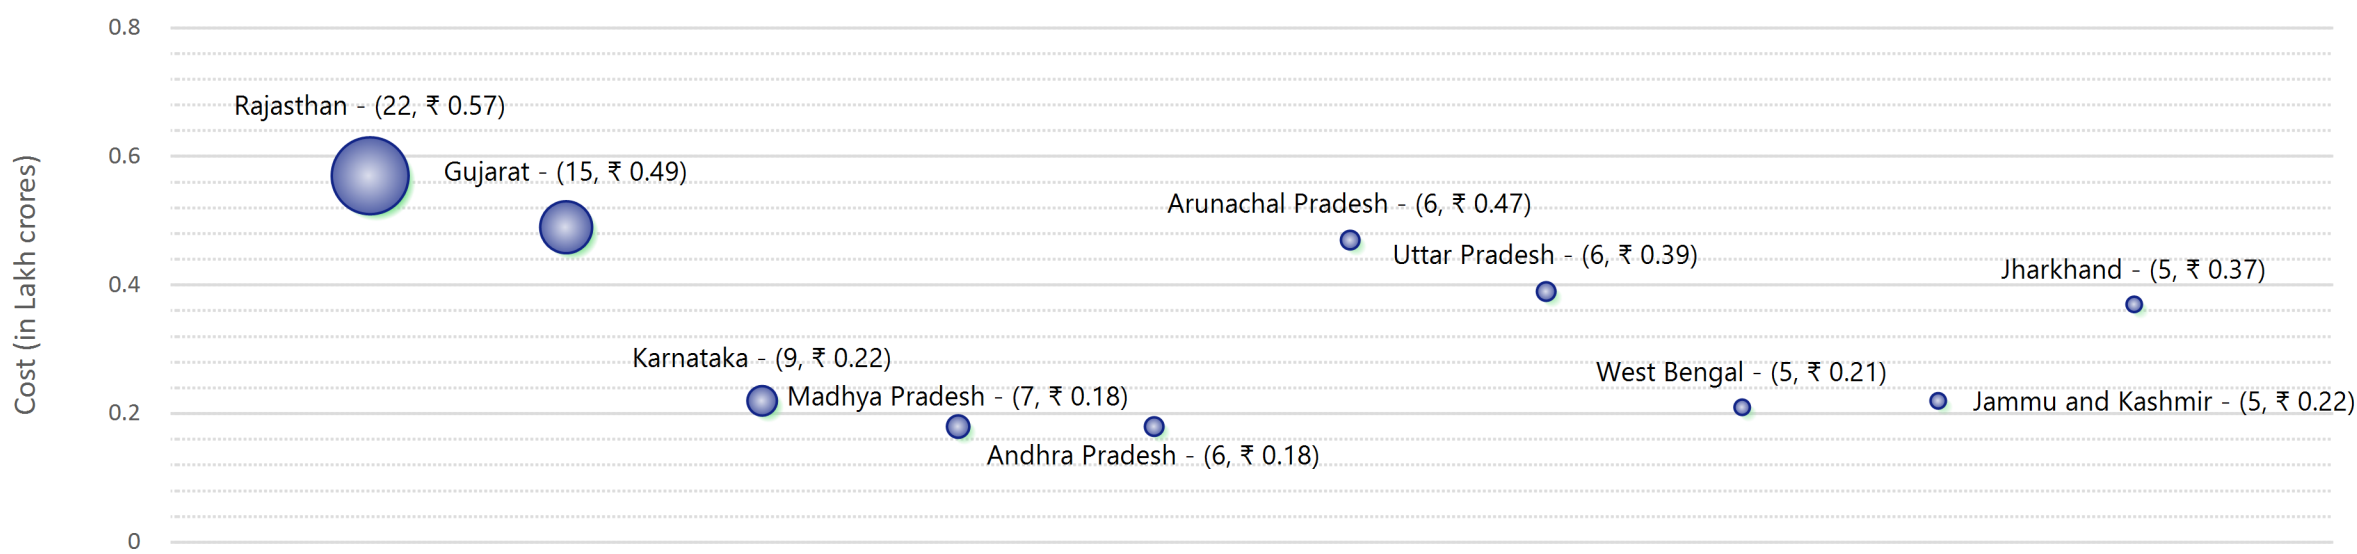

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRES (%)S
1	602182	DIBANG MULTIPURPOSE PROJECT	31,876	31,876	3,777	16
2	615347	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV NAME POWERGRID WEST CENTRAL TRANSMISSION LIMITED]	24,819	24,819	1,986	3
3	400261	PATRATU THERMAL POWER STATION EXPANSION PROJECT PHASE-I [3X800 MW]	18,668	20,302	17,929	86
4	400062	RAGHUNATHPUR THERMAL POWER STATION PHASE II [2X660 MW] AT RAGHUNATHPUR, PURULIA, WEST BENGAL	17,673	17,673	1,458	2
5	612142	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III [2X800 MW]	17,195	17,195	2,212	13



Ministry of Housing & Urban Affairs

NOVEMBER 2025

53

Ongoing Projects

₹ 3,42,382

Original Cost
(crores)

₹ 3,62,988

Revised Cost
(crores)

₹ 2,05,051

(56.49% of Revised Cost)

Expenditure
(crores)

22 | ₹ 333,166

Mega Projects
Count | Original Cost (crores)

31 | ₹ 9,216

Major Projects
Count | Original Cost

2


Commissioned during month

1

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

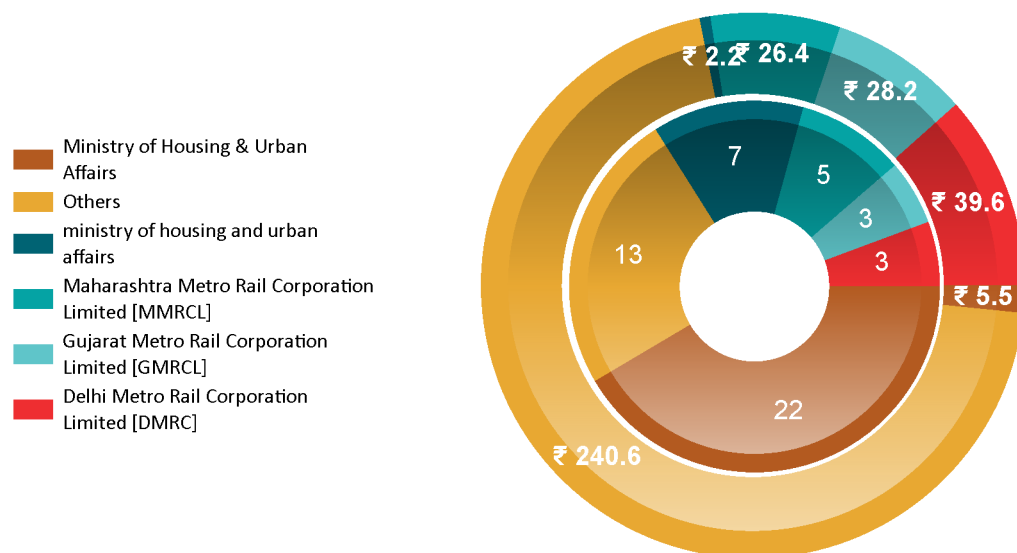


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

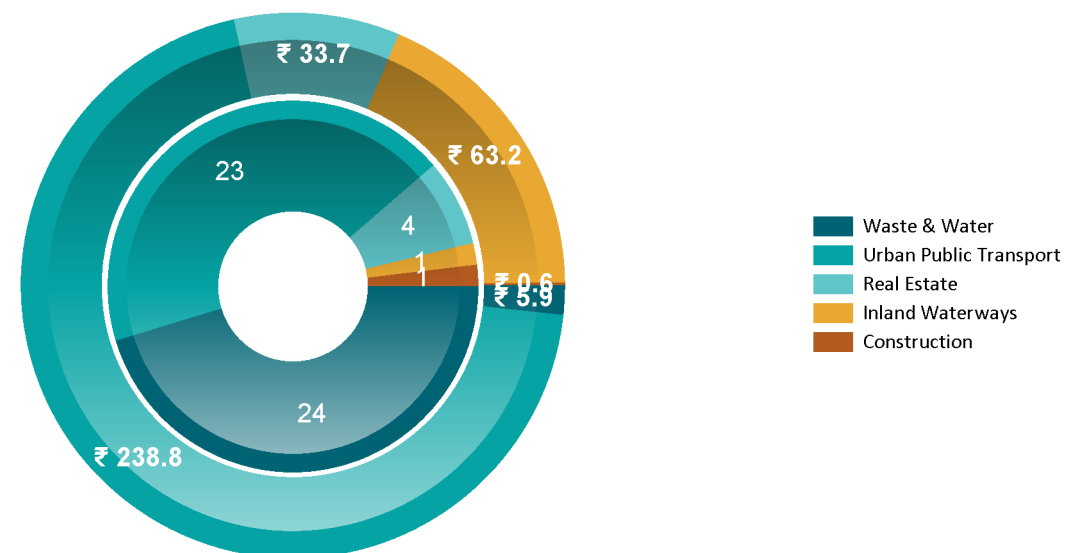


Physical & Financial progress (%) : Project count

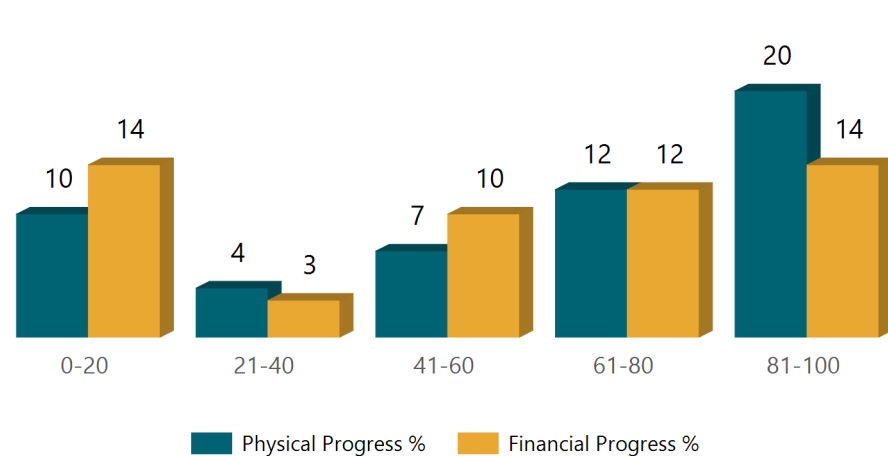

Cost Analytics : Major Sectors*

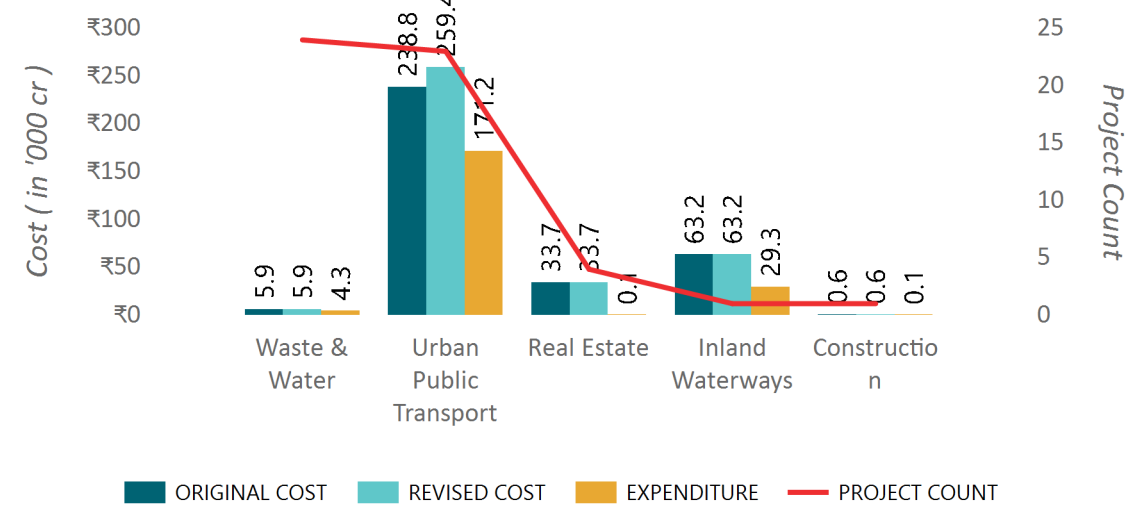

State Comparison : Major States*

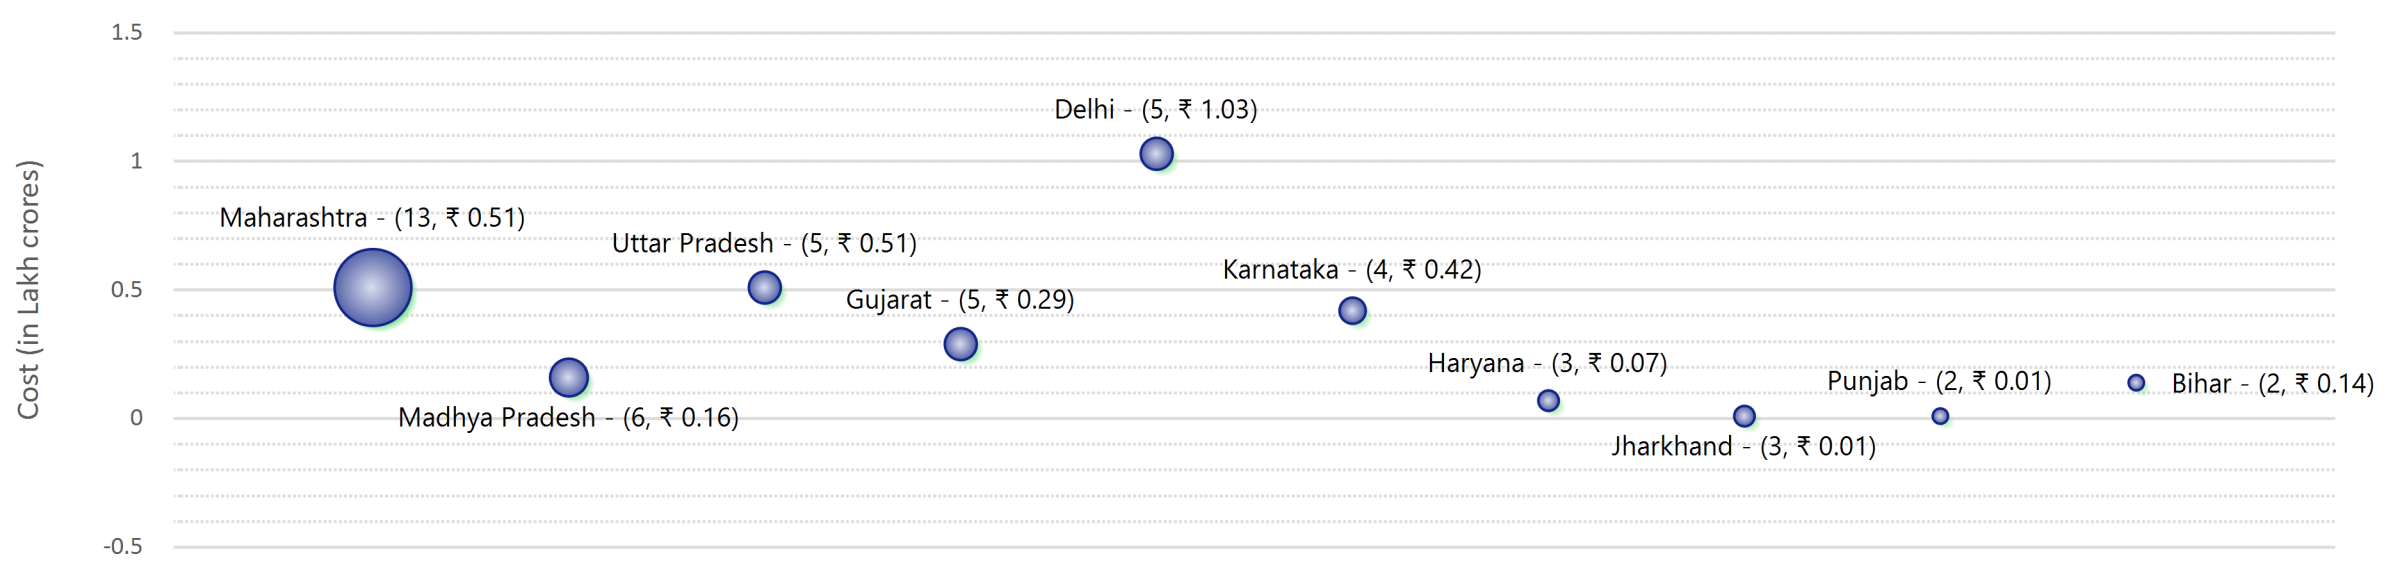

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246	63,246	29,336	47
2	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850	32,850	0	0
3	702633	DELHI-GHAZIABAD-MEERUT REGIONAL RAPID TRANSIT SYSTEM [RRTS] CORRIDOR	30,274	30,274	27,061	96
4	702635	CONSTRUCTION OF BANGALORE METRO RAIL PROJECT PHASE 2.	26,405	30,695	29,668	95
5	702632	DMRTS PHASE - IV [3 PRIORITY CORRIDORS]	24,949	24,949	18,022	73



List of Tables



Table 1: Ministry-wise Ongoing Projects





Ministry-wise Ongoing Projects

NOVEMBER 2025

Sl.No	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Department for Promotion of Industry & Internal Trade	Real Estate	2	3841.25 3841.25	656.65
		Total	2	3,841.25	656.65
2	Department of Higher Education	Education	30	15115.18 14922.5	7945.92
		Total	30	15,115.18	7,945.92
3	Department of Sports	Education	1	906.47 611.74	559.27
		Total	1	906.47	559.27
4	Department of Telecommunications	Telecommunication	15	152734.45 274827	77536
		Total	15	152,734.45	77,536.00
5	Department of Water Resources, River Development & GR	Waste & Water	8	4039.12 4039.12	1643.05
		Water Resources	39	93740.23 193594	139573
		Total	47	97,779.35	141,216.05
6	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	25	19949.84 20411	9093.09
		Total	25	19,949.84	9,093.09
7	Ministry of Coal	Coal	115	157276.32 154732	47909.7
		Electricity Generation	6	50201.48 54744.6	25878.3
		Railways	2	3485.86 4250.56	1929.72
		Total	123	210,963.66	75,717.72
8	Ministry of Health & Family Welfare	Healthcare	5	8954.19 9972.41	2547.1
		Total	5	8,954.19	2,547.10
9	Ministry of Housing & Urban Affairs	Construction	1	644 644	108.53
		Inland Waterways	1	63246 63246	29336
		Real Estate	4	33749.85 33749.8	58.58
		Urban Public Transport	23	238843.11 259425	171216
		Waste & Water	24	5898.8 5923.13	4331.96
		Total	53	342,381.76	205,051.07
10	Ministry of Labour and Employment	Healthcare	14	3365.08 3631.54	1727.44
		Total	14	3,365.08	1,727.44
11	Ministry of Mines	Construction	1	255.37 255.37	85.9
		Metals & Mining	6	8344.36 10724.5	6621.2
		Total	7	8,599.73	6,707.10
12	Ministry of Petroleum & Natural Gas	Energy Storage	18	81884.05 120807	94582
		Oil & Gas	95	355051.01 384190	188847
		Total	113	436,935.06	283,429.00
13	Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58
		Inland Waterways	2	5546.18 5258.15	3960.83
		Shipping	9	15124.41 15290.9	8975.5
		Tourism, Hospitality & Wellness	1	573 1238.05	515.97
		Total	13	21,936.59	13,510.30
14	Ministry of Power	Coal	2	2083 2365	986.91
		Electricity Generation	30	224974.07 281434	139252
		Transmission & Distribution	64	153554.68 159518	57184.5
		Total	96	380,611.75	197,423.41
15	Ministry of Railways	Railways	258	693157.3 846186	542700
		Total	258	693,157.30	542,700.00
16	Ministry of Steel	Metals & Mining	1	1700 1756.2	142.16
		Steel	20	19266.64 22504.9	8979.27
		Total	21	20,966.64	9,121.43
Total			823	2,418,198.30	1,574,941.55



Table 2: State-wise Ongoing Projects



Ongoing Projects State-Wise

NOVEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Offshore	Ministry of Petroleum & Natural Gas	Oil & Gas	6	19714.58 22972.8	11743.01
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	177 197	383.41
		Ministry of Railways	Railways	1	819 819	580.51
	PAN India	Department of Telecommunications	Telecommunication	6	141891.67 264213	74331.02
	Total			14	162602.25	87037.95
2	Andaman & Nicobar	Ministry of Housing & Urban Affairs	Real Estate	1	209.88 209.88	0.00
	Total			1	209.88	0.00
3	Andhra Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	1	2139.44 2139.44	503.39
		Department of Higher Education	Education	1	305 305	19.96
		Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1931.77
		Department of Water Resources, River Development & GR	Water Resources	3	10901.5 57269.5	26779.79
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1224.86 1224.86	709.41
		Ministry of Housing & Urban Affairs	Waste & Water	1	172.22 172.22	88.86
		Ministry of Labour and Employment	Healthcare	1	384.27 384.27	105.00
		Ministry of Petroleum & Natural Gas	Energy Storage	2	2898.34 3050	2355.24
			Oil & Gas	4	37804 37864	32540.57
		Ministry of Power	Transmission & Distribution	6	17931.23 17931.2	5200.43
		Ministry of Railways	Railways	27	52663.77 60620.7	34524.49
	Total			52	133571.8	104758.91
4	Arunachal Pradesh	Department of Higher Education	Education	1	592.61 592.61	550.61
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	284.04
		Ministry of Petroleum & Natural Gas	Energy Storage	1	43129 79459	62888.30
			Oil & Gas	1	9265 9265	6608.95
		Ministry of Power	Electricity Generation	4	41850.64 61640.8	29320.46
			Transmission & Distribution	2	4963.8 9338.7	7778.22
		Ministry of Railways	Railways	1	435 1250	771.10
	Total			11	101491.54	108201.68
5	Assam	Department of Higher Education	Education	1	153.71 153.71	125.03
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	284.04
		Department of Water Resources, River Development & GR	Water Resources	1	256.16 256.16	44.70
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1712 1712	2456.07
		Ministry of Coal	Coal	2	449.23 449.23	187.08
		Ministry of Labour and Employment	Healthcare	1	143.23 154.75	101.83
		Ministry of Petroleum & Natural Gas	Energy Storage	3	10768.4 11947.4	10284.90
			Oil & Gas	14	27584.43 37939.2	27381.12
		Ministry of Power	Electricity Generation	1	6285.33 26075.5	25415.23
			Transmission & Distribution	1	5111.33 6700	5410.25
		Ministry of Railways	Railways	7	14593.57 16308.6	10541.05
	Total			33	68312.88	82231.30
6	Bihar	Department of Higher Education	Education	1	499.21 499.21	444.87
		Department of Telecommunications	Telecommunication	4	4220.71 3992.24	1106.26
		Department of Water Resources, River Development & GR	Waste & Water	5	2351.43 2351.43	1303.45
			Water Resources	2	2193.34 3088.88	598.72
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3541.56 3541.56	1365.21
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	13365.77 13365.8	4670.21
			Waste & Water	1	158.78 158.78	60.50

Ongoing Projects State-Wise						NOVEMBER 2025
Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
6	Bihar	Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	10063.21
			Oil & Gas	6	24473.5 26338.2	13728.20
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3577.42
		Ministry of Power	Electricity Generation	1	10439.09 13756.6	12691.85
			Transmission & Distribution	3	3119.63 3119.63	1.13
		Ministry of Railways	Railways	24	52621.17 57089.5	22954.30
		Total		53	132581.37	72565.33
7	Chhattisgarh	Department of Higher Education	Education	1	1188.97 1188.97	0.00
		Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1931.77
		Department of Water Resources, River Development & GR	Water Resources	2	842.26 1109.33	855.96
		Ministry of Coal	Coal	13	30763.92 30763.9	12874.14
			Railways	1	1686.22 1686.22	439.98
		Ministry of Petroleum & Natural Gas	Oil & Gas	3	10613.29 11024	6741.00
		Ministry of Power	Electricity Generation	2	25321 25897	4095.14
		Ministry of Railways	Railways	19	34549.26 39024.3	20449.55
		Ministry of Steel	Metals & Mining	1	1700 1756.2	142.16
			Steel	6	7530.14 10050.1	5652.32
		Total		51	121342.23	53182.02
8	Dadra & Nagar Haveli and Daman & Diu	Ministry of Housing & Urban Affairs	Waste & Water	1	210 210	0.00
		Ministry of Power	Transmission & Distribution	1	4546.26 4546.26	4318.95
		Ministry of Railways	Railways	1	108000 108000	84199.89
		Total		3	112756.26	88518.84
9	Delhi	Department of Higher Education	Education	2	706.49 709.42	325.08
		Department of Telecommunications	Telecommunication	1	248.2 248.2	236.91
		Ministry of Health & Family Welfare	Healthcare	2	4799.19 4799.19	24.68
		Ministry of Housing & Urban Affairs	Real Estate	1	32850 32850	0.00
			Urban Public Transport	4	69853.45 69853.4	45211.07
		Ministry of Power	Transmission & Distribution	2	2331 2331	1667.42
		Ministry of Railways	Railways	15	28623.17 28623.2	6031.48
		Total		27	139411.5	53496.64
10	Goa	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	255.69 255.69	154.30
		Ministry of Railways	Railways	2	5804.49 6182.62	6215.96
		Total		3	6060.18	6370.26
11	Gujarat	Department of Higher Education	Education	1	490.63 490.63	314.51
		Department of Telecommunications	Telecommunication	1	336.89 301.13	235.96
		Department of Water Resources, River Development & GR	Water Resources	2	25739.93 40082.8	36817.94
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1305 1551	739.77
		Ministry of Coal	Electricity Generation	2	3719.69 3719.69	1058.05
		Ministry of Housing & Urban Affairs	Real Estate	1	539 539	39.63
			Urban Public Transport	3	28177.49 30329	24589.83
			Waste & Water	1	200 200	100.00
		Ministry of Labour and Employment	Healthcare	3	973.35 973.35	278.11
		Ministry of Petroleum & Natural Gas	Energy Storage	4	62601.86 98931.9	78394.04
			Oil & Gas	11	32704.12 32296.3	23765.14
		Ministry of Ports, Shipping and Waterways	Shipping	3	4514.64 4681.1	1141.96
			Tourism, Hospitality & Wellness	1	573 1238.05	515.97



Ongoing Projects State-Wise

NOVEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
11	Gujarat	Ministry of Power	Electricity Generation	1	339.35 339.35	317.59
			Transmission & Distribution	14	48255.1 48255.1	12289.29
		Ministry of Railways	Railways	26	185518.86 262039	221427.15
		Total		75	395988.91	402024.94
12	Haryana	Ministry of Health & Family Welfare	Healthcare	1	1299 1646.43	349.41
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	6230.99 6230.99	72.41
			Waste & Water	2	491.2 491.2	387.03
		Ministry of Petroleum & Natural Gas	Energy Storage	1	9028 9028	7357.45
			Oil & Gas	5	45925.07 49596.1	37098.98
		Ministry of Power	Transmission & Distribution	3	11696 11696	1386.80
		Ministry of Railways	Railways	4	53464 126368	125657.22
		Total		17	128134.26	172309.30
13	Himachal Pradesh	Department of Higher Education	Education	3	811.15 921.89	597.26
		Department of Telecommunications	Telecommunication	1	336.89 301.13	235.96
		Ministry of Power	Electricity Generation	4	7728.04 13398.6	4327.09
		Ministry of Railways	Railways	3	17005 17005.1	9807.55
		Total		11	25881.08	14967.86
14	Jammu and Kashmir	Department of Higher Education	Education	1	424.93 500.91	484.52
		Department of Telecommunications	Telecommunication	1	336.89 301.13	235.96
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	861.37 861.37	229.10
		Ministry of Health & Family Welfare	Healthcare	1	1828 2160.84	1354.55
		Ministry of Labour and Employment	Healthcare	1	131.05 164.93	162.05
		Ministry of Petroleum & Natural Gas	Energy Storage	1	676.89 715.89	559.45
			Oil & Gas	2	1059.9 1059.9	237.51
		Ministry of Power	Electricity Generation	4	22207.77 27945.1	13411.20
			Transmission & Distribution	1	218.6 218.6	2.61
		Total		13	27745.4	16676.95
15	Jharkhand	Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1931.77
		Department of Water Resources, River Development & GR	Water Resources	2	5430.04 12010.3	5941.33
		Ministry of Coal	Coal	28	51354.95 51119.3	10642.68
			Railways	1	1799.64 2564.34	1489.74
		Ministry of Housing & Urban Affairs	Waste & Water	3	654.14 654.14	403.16
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	10063.21
			Oil & Gas	3	2010.07 2010.07	635.82
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3577.42
		Ministry of Power	Coal	2	2083 2365	986.91
			Electricity Generation	2	33026 34660	19378.65
			Transmission & Distribution	1	1842.25 1842.25	1648.05
		Ministry of Railways	Railways	14	46589.07 47449.7	15195.29
		Ministry of Steel	Steel	6	2854.58 3572.87	1459.50
		Total		67	170388.09	73353.53
16	Karnataka	Department for Promotion of Industry & Internal Trade	Real Estate	1	1701.81 1701.81	153.26
		Department of Higher Education	Education	1	420.41 420.41	367.76
		Department of Water Resources, River Development & GR	Water Resources	1	770.16 1606.07	1515.32
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1143.4 1143.4	569.60
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	41193.24 45483.2	38716.19



Ongoing Projects State-Wise

NOVEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
16	Karnataka	Ministry of Housing & Urban Affairs	Waste & Water	2	337.69 337.69	178.89
		Ministry of Labour and Employment	Healthcare	2	428.92 428.92	27.80
		Ministry of Petroleum & Natural Gas	Energy Storage	1	678 1732	838.07
			Oil & Gas	5	9662 12693.6	9037.57
		Ministry of Ports, Shipping and Waterways	Shipping	1	153.23 153.23	24.00
		Ministry of Power	Transmission & Distribution	9	21604 21604	3901.83
		Ministry of Railways	Railways	17	25363.29 31781.9	17737.06
		Ministry of Steel	Steel	1	1043.63 1043.63	320.80
		Total		46	104499.78	73388.15
17	Kerala	Department of Higher Education	Education	2	2533.45 2744.4	652.05
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	484.57 484.57	96.26
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	1957.05 1957.05	477.04
		Ministry of Petroleum & Natural Gas	Oil & Gas	4	9126.87 12120.9	5268.91
		Ministry of Railways	Railways	3	2846 5183.64	2871.09
		Total		11	16947.94	9365.35
18	Ladakh	Department of Telecommunications	Telecommunication	1	336.89 301.13	235.96
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	480 640	483.12
		Total		2	816.89	719.08
19	Madhya Pradesh	Department of Higher Education	Education	1	496.28 496.28	38.62
		Department of Telecommunications	Telecommunication	3	3883.82 3691.11	870.30
		Department of Water Resources, River Development & GR	Water Resources	3	2628.27 2941.14	2923.41
		Ministry of Coal	Coal	14	8634.02 8634.02	3480.44
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	14442.2 14442.2	8009.06
			Waste & Water	4	1243.05 1267.38	1124.28
		Ministry of Mines	Metals & Mining	1	1856.36 1856.36	947.42
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10088 10088	8135.69
			Oil & Gas	3	53003.25 53414	9004.23
		Ministry of Power	Transmission & Distribution	7	17765 17765	4157.28
		Ministry of Railways	Railways	19	58468.02 72465.1	45519.56
		Total		58	172508.27	84210.29
20	Maharashtra	Department of Higher Education	Education	1	182.33 182.33	158.23
		Department of Telecommunications	Telecommunication	4	7608.59 7608.59	2097.79
		Department of Water Resources, River Development & GR	Water Resources	11	22660.36 32345.7	34204.14
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	339.10
		Ministry of Coal	Coal	25	12455.88 12455.9	2845.48
		Ministry of Housing & Urban Affairs	Urban Public Transport	8	50397.81 64537.8	34398.02
			Waste & Water	5	1088.72 1088.72	922.83
		Ministry of Labour and Employment	Healthcare	3	884.31 886.08	606.60
		Ministry of Petroleum & Natural Gas	Energy Storage	1	281.35 389.67	243.11
			Oil & Gas	13	34264.24 37660.4	21775.69
		Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58.00
			Shipping	2	6900 6900	6064.89
		Ministry of Power	Transmission & Distribution	4	30596.67 30596.7	6394.69
		Ministry of Railways	Railways	35	266858.79 358832	269785.92
		Total		114	435372.53	379894.49

Ongoing Projects State-Wise

NOVEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
21	Manipur	Department of Sports	Education	1	906.47 611.74	559.27
		Department of Water Resources, River Development & GR	Water Resources	1	1449.44 1822.24	1837.91
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	499 499	156.06
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6608.95
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5410.25
		Ministry of Railways	Railways	1	14323 21885.9	15782.48
		Total		6	31554.24	30354.92
22	Meghalaya	Department of Higher Education	Education	1	494.52 494.52	422.07
		Department of Telecommunications	Telecommunication	1	971.96 971.96	208.25
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6608.95
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5410.25
		Total		4	15842.81	12649.52
23	Mizoram	Department of Higher Education	Education	1	474.23 474.23	167.55
		Ministry of Petroleum & Natural Gas	Energy Storage	1	225.71 225.71	12.81
			Oil & Gas	1	9265 9265	6608.95
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5410.25
		Total		4	15076.27	12199.56
24	Nagaland	Department of Higher Education	Education	1	275.63 275.63	261.24
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	9492.62 9492.62	6620.36
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5410.25
		Ministry of Railways	Railways	2	8786.7 8786.7	5648.33
		Total		6	23666.28	17940.18
25	Odisha	Department of Higher Education	Education	1	1229.32 843.09	835.60
		Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1931.77
		Department of Water Resources, River Development & GR	Water Resources	2	1556.46 5291.33	5427.87
		Ministry of Coal	Coal	12	36526.28 34218	13278.19
			Electricity Generation	1	27212.96 27213	2550.76
		Ministry of Labour and Employment	Healthcare	1	164.6 164.6	16.40
		Ministry of Mines	Metals & Mining	4	6322 8702.17	5538.78
		Ministry of Petroleum & Natural Gas	Energy Storage	2	12886.34 14217	12346.19
			Oil & Gas	6	25800.35 24283.5	16310.03
		Ministry of Ports, Shipping and Waterways	Shipping	1	3004.63 3004.63	1277.52
		Ministry of Power	Electricity Generation	1	11843.75 12543	5042.25
			Transmission & Distribution	1	342.69 342.69	0.71
		Ministry of Railways	Railways	24	43946.78 49704	32836.86
			Railways	1	267.61 267.61	0.00
		Ministry of Steel	Steel	1	1105.23 1105.23	790.11
		Total		61	179356.17	98183.04
26	Puducherry	Department of Higher Education	Education	1	618.34 544.34	529.94
		Ministry of Railways	Railways	1	713 981	598.38
		Total		2	1331.34	1128.32
27	Punjab	Department of Higher Education	Education	2	559.3 559.3	311.28
		Department of Water Resources, River Development & GR	Water Resources	2	3727.07 5177.86	5182.41
		Ministry of Housing & Urban Affairs	Waste & Water	2	545.53 545.53	374.66
		Ministry of Petroleum & Natural Gas	Oil & Gas	5	12693.36 12693.4	8136.23
		Ministry of Power	Transmission & Distribution	1	5969 5969	698.04

Ongoing Projects State-Wise

NOVEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
27	Punjab	Ministry of Railways	Railways	3	15702.64 15703	9402.74
		Total		15	39196.9	24105.36
28	Rajasthan	Department of Telecommunications	Telecommunication	2	758.54 530.07	377.97
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1367 1367	739.85
		Ministry of Coal	Electricity Generation	1	1813 1813	1393.34
		Ministry of Petroleum & Natural Gas	Energy Storage	3	52618.05 88948.1	70398.82
			Oil & Gas	2	10599 10599	6686.34
		Ministry of Power	Electricity Generation	1	5491.89 5491.89	5376.34
			Transmission & Distribution	21	51980.51 51980.2	19417.16
		Ministry of Railways	Railways	23	88639.51 164210	140547.25
		Total		55	213267.5	244937.07
29	Sikkim	Department of Higher Education	Education	2	999.82 924.82	359.78
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	323.26 323.26	38.70
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6608.95
		Ministry of Power	Electricity Generation	2	6686.33 7576.15	5375.89
			Transmission & Distribution	1	4754.42 9129.32	7778.18
		Ministry of Railways	Railways	1	7877 11775	9647.55
		Total		8	29905.83	29809.05
30	Tamil Nadu	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1207 1207	193.59
		Ministry of Coal	Electricity Generation	1	218.03 218.03	164.70
		Ministry of Housing & Urban Affairs	Inland Waterways	1	63246 63246	29336.00
		Ministry of Labour and Employment	Healthcare	1	152.95 177.01	107.83
		Ministry of Mines	Metals & Mining	1	166 166	135.00
		Ministry of Petroleum & Natural Gas	Energy Storage	3	2334 3448.71	1825.73
			Oil & Gas	4	38385 46153	6246.49
		Ministry of Power	Transmission & Distribution	1	548 548	65.46
		Ministry of Railways	Railways	7	8370.7 11242.2	5856.10
		Total		20	114627.68	43930.90
31	Telangana	Department of Higher Education	Education	1	262 262	194.13
		Department of Telecommunications	Telecommunication	3	3923.59 3923.59	894.31
		Department of Water Resources, River Development & GR	Water Resources	4	11670.14 24129.6	11936.34
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	339.10
		Ministry of Coal	Coal	9	3890.03 3890.03	2514.49
		Ministry of Health & Family Welfare	Healthcare	1	1028 1365.95	818.46
		Ministry of Housing & Urban Affairs	Construction	1	644 644	108.53
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	215 215	0.00
		Ministry of Power	Transmission & Distribution	2	5694.56 5694.56	4910.28
		Ministry of Railways	Railways	11	19213.75 22977.8	11444.55
		Total		34	47041.55	33160.19
32	Tripura	Ministry of Petroleum & Natural Gas	Energy Storage	1	656 656	519.02
			Oil & Gas	2	9474.33 9396.51	6679.89
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5410.25
		Total		4	15241.66	12609.16
33	Uttar Pradesh	Department of Higher Education	Education	1	246 246	199.71
		Department of Telecommunications	Telecommunication	4	4220.71 3992.24	1106.26
		Department of Water Resources, River Development & GR	Waste & Water	2	1532.96 1532.96	243.43

Ongoing Projects State-Wise

NOVEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
33	Uttar Pradesh	Department of Water Resources, River Development & GR	Water Resources	3	2953.27 6309.81	4689.88
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	4	4168.31 4223.51	1050.76
		Ministry of Coal	Coal	2	1328.09 1328.09	1059.79
			Electricity Generation	1	17237.8 21780.9	20711.46
		Ministry of Housing & Urban Affairs	Urban Public Transport	3	49730.1 49730.1	42204.79
			Waste & Water	2	797.47 797.47	691.75
		Ministry of Petroleum & Natural Gas	Energy Storage	2	11068.45 11068.5	8370.29
			Oil & Gas	3	17824.68 18213.1	1691.72
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3577.42
		Ministry of Power	Electricity Generation	2	28284.42 30471.2	15163.68
			Transmission & Distribution	4	10482.81 10482.8	2172.56
		Ministry of Railways	Railways	26	92690.92 167547	147909.80
		Total		60	247935.17	250843.30
34	Uttarakhand	Department of Higher Education	Education	1	650.85 650.85	195.52
		Department of Water Resources, River Development & GR	Water Resources	1	2584.1 2584.1	968.52
		Ministry of Housing & Urban Affairs	Real Estate	1	150.97 150.97	18.95
		Ministry of Labour and Employment	Healthcare	1	102.4 297.63	321.82
		Ministry of Power	Electricity Generation	3	11663.95 26070	20788.82
		Ministry of Railways	Railways	1	38953 38953	24645.15
		Total		8	54105.27	46938.78
35	West Bengal	Department of Higher Education	Education	1	500 442	390.60
		Department of Telecommunications	Telecommunication	2	3462.17 3462.17	728.29
		Department of Water Resources, River Development & GR	Waste & Water	1	154.73 154.73	96.17
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1877.3 1877.3	450.39
		Ministry of Coal	Coal	13	15863.74 15863.7	2879.66
		Ministry of Mines	Construction	1	255.37 255.37	85.90
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	10063.21
			Oil & Gas	10	18910.65 19758.2	12019.34
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3577.42
			Shipping	2	551.91 551.91	467.13
		Ministry of Power	Electricity Generation	3	20091.84 21644.6	3962.96
			Transmission & Distribution	2	751.63 751.63	1.03
		Ministry of Railways	Railways	16	49558.46 60770.4	34805.18
		Ministry of Steel	Steel	6	6733.06 6733.06	756.54
		Total		61	134308.04	70283.82




Table 3: Completed Projects



Completed Projects During Month

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Actual Date of Completion (Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
	Ministry of Civil Aviation					
	Aviation & Aviation Infrastructure					
1	Lucknow Airport-Terminal 3- Phase 1 & Other Associated Works (Adani Airport Holdings Limited) 701091	Uttar Pradesh	06/2018 (09/2018)	03/2024 (03/2026) (-)	3100 (-)	3112.57
	Total (1)				3100	3112.57
	Ministry of Coal					
	Coal					
2	JAMPALI OC RCE [2.0 MTY] (South Eastern Coalfields Limited [SECL]) 613795	Chhattisgarh	05/2020 (05/2020)	08/2024 (03/2025) (06/2025)	278.64 (-)	210.07
	Total (1)				278.64	210.07
	Ministry of Housing & Urban Affairs					
	Construction					
3	C/o 184 MS Flats for Hon'ble MPs at BKS Marg, New Delhi (Central Public Works Department [CPWD]) 617282	Delhi	01/2022 (05/2022)	09/2025 (05/2025) (09/2025)	646.53 (646.52)	540.04
	Total (1)				646.53	540.04
	Waste & Water					
4	Dibrugarh Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) 702682	Assam	02/2016 (01/2020)	12/2025 (03/2023) (01/2026)	186.8 (-)	186.8
	Total (1)				186.8	186.8
	Ministry of Labour and Employment					
	Healthcare					
5	Construction of New OPD Block 200 Bed ward Basement + GF + 6 Floors at the location of old OPD block, at existing ESIC Hospital/ Medical college campus, Sanathnagar, Hyderabad (Employee's State Insurance Company [ESIC]) 612688	Telangana	11/2017 (10/2021)	06/2025 (06/2024) (06/2025)	211.13 (-)	198.95
	Total (1)				211.13	198.95
	Ministry of Ports, Shipping and Waterways					
	Shipping					
6	Construction of new dry dock at exisitng Cochin Shipyard Limited premises at Perumanoor, Kochi 682 015 (Cochin Shipyard) 701564	Kerala	04/2018 (05/2018)	03/2025 (12/2022) (03/2025)	1799 (-)	1558.39
	Total (1)				1799	1558.39
	Ministry of Power					
	Transmission & Distribution					
7	Western Region Expansion Scheme-XXV (Power Grid Corporation of India Limited [POWERGRID]) 611737	Chhattisgarh	05/2022 (05/2022)	NA (08/2023) (10/2025)	385.84 (-)	385.84
8	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan 8.1 GW under Phase II- Part- G1 (Power Grid Corporation of India Limited [POWERGRID]) 608301	Delhi	02/2022 (02/2022)	11/2025 (09/2023) (12/2025)	359.47 (-)	359.47
9	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part B (Power Grid Corporation of India Limited [POWERGRID]) 611656	Gujarat	03/2023 (03/2023)	12/2025 (03/2025) (12/2025)	1167.55 (1167)	1167
10	Establishment of Khavda Pooling Station-2 KPS2 in Khavda RE Park KPS2 TRANSMISSION SYSTEM LIMITED (Power Grid Corporation of India Limited [POWERGRID]) 611660	Gujarat	03/2023 (03/2023)	12/2025 (12/2024) (11/2025)	966.79 (-)	966.79
11	Transmission system for evacuation of Power from Pakaldul HEP in Chenab Valley HEPs - LTA System (Power Grid Corporation of India Limited [POWERGRID]) 608302	Jammu and Kashmir	02/2022 (02/2022)	11/2025 (04/2025) (11/2025)	318.12 (-)	318.12
12	Transmission System Strengthening Scheme for evacuation of power from SEZ in Rajasthan 8.1 GW under Phase II Part G (Power Grid Corporation of India Limited [POWERGRID]) 608922	Multi-States (Delhi, Haryana, Rajasthan)	05/2022 (05/2022)	NA (11/2023) (12/2025)	1666 (2218)	2218
13	Transmission System for Strengthening of Srinagar-Leh Tr. System (Power Grid Corporation of India Limited [POWERGRID]) 606781	Multi-States (Jammu and Kashmir, Ladakh)	03/2022 (03/2022)	11/2025 (12/2024) (11/2025)	288.71 (-)	288.71
	Total (7)				5152.48	5703.93

Note: Cumulative Expenditure is as per last reporting by Central Line Ministries/ Departments on the IPM portal, this may not be the actual completion cost.




Table 4: Newly Added Projects



Newly Added Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
	Department of Higher Education				
	Education				
1	Phase B of Construction of Permanent Campus of IIT Bhilai <i>(Indian Institute of Technology, Bhilai)</i> (617877)	Chhattisgarh	05/2025 (06/2025)	10/2028 (-)	1188.97 (-)
2	Phase B of Construction of Permanent Campus of IIT Palakkad <i>(INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD)</i> (617878)	Kerala	05/2025 (01/2026)	10/2028 (-)	1527 (-)
	Total (2)				2715.97
	Ministry of Health & Family Welfare				
	Healthcare				
3	Setting up IT Infrastructure including Network Security and Hosting at AIIMS, New Delhi <i>(PMSSY AND Institute of NATIONAL Importance)</i> (617882)	Delhi	09/2025 (09/2025)	09/2026 (-)	358.19 (-)
4	Redevelopment of Residential colonies at Ayur Vigyan Nagar and West Ansari Nagar campuses of AIIMS, New Delhi <i>(PMSSY AND Institute of NATIONAL Importance)</i> (617883)	Delhi	10/2016 (06/2022)	06/2027 (-)	4441 (-)
	Total (2)				4799.19
	Ministry of Housing & Urban Affairs				
	Urban Public Transport				
5	Pune Metro Rail Project Phase-2 Corridor 2A Vanaz to Chandani Chowk and Corridor 2B Ramwadi to Wagholi/Vitthalwadi <i>(Maharashtra Metro Rail Corporation Limited [MMRCL])</i> (618971)	Maharashtra	07/2025 (07/2025)	07/2029 (-)	3626.24 (-)
	Total (1)				3626.24
	Ministry of Petroleum & Natural Gas				
	Energy Storage				
6	Capacity Augmentation of Kandla LPG Import Terminal [KLIT] from 0.6 MMTPA to 2.5 MMTPA <i>(Ministry of Petroleum & Natural Gas)</i> (617839)	Gujarat	05/2023 (05/2023)	07/2026 (-)	356.86 (-)
7	LPG Bottling Plant at Mualkhang <i>(Ministry of Petroleum & Natural Gas)</i> (617829)	Mizoram	07/2024 (07/2024)	11/2027 (11/2027)	225.71 (225.71)
	Total (2)				582.57
	Oil & Gas				
8	Pipeline Rehabilitation Project, Phase-II <i>(Ministry of Petroleum & Natural Gas)</i> (617827)	Assam	12/2024 (12/2024)	12/2029 (12/2029)	680 (680)
9	Coke Drum Structure Package <i>(Ministry of Petroleum & Natural Gas)</i> (617836)	Assam	12/2022 (12/2022)	12/2025 (12/2025)	635.28 (635.28)
10	City Gas Distribution [CGD] Project in Kondagaon, Bastar, Sukma, Narayanpur, Bijapur & Dantewada GA <i>(Ministry of Petroleum & Natural Gas)</i> (617819)	Chhattisgarh	06/2022 (06/2022)	06/2030 (06/2030)	557.04 (557.04)
11	Augmentation of CCKPL and IDPL Pipelines capacity along with setting up of Palakkad TOP <i>(Ministry of Petroleum & Natural Gas)</i> (617838)	Kerala	09/2024 (09/2024)	08/2028 (08/2028)	1130 (1130)
12	C2/C3 Vijaipur Pata Pipeline <i>(Ministry of Petroleum & Natural Gas)</i> (617830)	Madhya Pradesh	05/2024 (05/2024)	01/2027 (-)	1792 (-)
13	City Gas Distribution [CGD] Project in Gajapati, Kandhamal, Boudh, & Sonepur GA <i>(Ministry of Petroleum & Natural Gas)</i> (617818)	Odisha	02/2022 (02/2022)	02/2030 (02/2030)	514.91 (514.91)
14	ATF Pipeline from BPCLs Malkapur POL Installation to Hyderabad International airport <i>(Ministry of Petroleum & Natural Gas)</i> (617822)	Telangana	(03/2025)	09/2027 (-)	215 (-)
15	Siliguri-Jhapa Pipeline Project <i>(Indian Oil Corporation Limited [IOCL])</i> (617828)	West Bengal	09/2024 (09/2024)	03/2029 (03/2029)	267 (267)
16	Siliguri Marketing Terminal [SMT] Capacity Augmentation Project <i>(Ministry of Petroleum & Natural Gas)</i> (617837)	West Bengal	11/2021 (11/2021)	12/2025 (12/2025)	484 (484)
	Total (9)				6275.23
	Ministry of Power				
	Transmission & Distribution				
17	Transmission System for Integration of Ananthapur 2 REZ Phase 1 for 4.5 GW. SPV Name Anantapuram 2 REZ Transmission Ltd <i>(Sterlite Power)</i> (617806)	Multi-States (Andhra Pradesh, Karnataka)	08/2024 (03/2025)	03/2027 (-)	4535.99 (-)
18	Inter-regional [NR-WR] Transmission System strengthening to relieve the loading of 765 kV Vindhyachal-Varanasi D/c line <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (617807)	Multi-States (Bihar, Uttar Pradesh)	10/2025 (10/2025)	10/2027 (-)	2368 (-)
19	Inter-Regional Strengthening between SR Grid and WR Grid <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (617808)	Multi-States (Karnataka, Maharashtra)	10/2025 (10/2025)	10/2027 (-)	1007 (-)
	Total (3)				7910.99

Newly Added Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
	Ministry of Railways				
	Railways				
20	Bakhtiyarpur-Rajgir-Tilaiya [Single line section]104km <i>(East Central Railway [ECR] - II)</i> (617824)	Bihar	10/2025 (10/2025)	10/2029 (-)	2017.38 (-)
21	Koderma-Arigada Doubling 133.38 Km of East Central Railway <i>(East Central Railway [ECR] - I)</i> (617832)	Jharkhand	06/2025 (06/2025)	12/2029 (-)	2887.11 (-)
	Total (2)				4904.49




Table 5: Ongoing Projects North Eastern Region



Ongoing Projects of North-East Region							NOVEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Civil Aviation							
Aviation & Aviation Infrastructure							
1	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (11/2025)	1712 (1712)	2456.07	94
2	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	156.06	42
3	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	02/2026 (-)	323.26 (323.26)	38.7	18
Total (3)					2534.26	2650.83	
Ministry of Coal							
Coal							
4	TIKAK EXTENSION OCP (MIS MoCoal Integration Logins) (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	81.47	4
5	TIRAP OCP (MIS MoCoal Integration Logins) (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.61	3
Total (2)					449.23	187.08	
Department of Higher Education							
Education							
6	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (-)	592.61 (592.61)	550.61	80
7	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (12/2025)	153.71 (153.71)	125.03	97
8	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2009 (09/2014)	03/2022 (07/2025)	494.52 (494.52)	422.07	90
9	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876)	Mizoram	09/2009 (06/2014)	12/2029 (12/2029)	474.23 (474.23)	167.55	4
10	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	261.24	97
11	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	121.56	14
12	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (03/2026)	314.06 (314.06)	238.22	85
Total (7)					2990.52	1886.28	
Department of Sports							
Education							
13	National Sports University [NSU], Imphal [Manipur] (Department of Sports & Youth Affairs) (400081)	Manipur	NA (01/2022)	08/2024 (11/2025)	906.47 (611.74)	559.27	95
Total (1)					906.47	559.27	
Ministry of Power							
Electricity Generation							
14	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	64.76	3
15	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	63.73	2
16	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited [NHPC]) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	3776.74	16
17	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited [NHPC]) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (05/2026)	6285.33 (26075.5)	25415.23	97
18	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181)	Sikkim	03/2019 (03/2020)	03/2024 (12/2027)	5748.04 (5748.04)	3887.11	70
19	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156)	Sikkim	03/2021 (08/2021)	05/2024 (12/2025)	938.29 (1828.11)	1488.78	93
Total (6)					48536.97	34696.35	
Transmission & Distribution							
20	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	0.04	0



Ongoing Projects of North-East Region

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
21	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	7778.18	82
22	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (03/2026)	5111.33 (6700)	5410.25	96
Total (3)					10075.13	13188.47	
Ministry of Petroleum & Natural Gas							
Energy Storage							
23	Rajasthan Refinery Project (Ministry of Petroleum & Natural Gas) (701263)	Arunachal Pradesh	10/2017 (10/2017)	10/2022 (03/2026)	43129 (79459)	62888.3	89
24	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Ministry of Petroleum & Natural Gas) (701349)	Assam	01/2019 (01/2019)	07/2024 (03/2026)	10228 (11407)	10063.21	88
25	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 (156.36)	70.91	53
26	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 (384.04)	150.78	62
27	LPG Bottling Plant at Mualkhang (Ministry of Petroleum & Natural Gas) (617829)	Mizoram	07/2024 (07/2024)	11/2027 (11/2027)	225.71 (225.71)	12.81	21
28	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) (400035)	Tripura	06/2022 (06/2022)	09/2025 (06/2026)	656 (656)	519.02	90
Total (6)					54779.11	73705.03	
Oil & Gas							
29	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (Ministry of Petroleum & Natural Gas) (701350)	Assam	06/2021 (06/2021)	12/2024 (12/2025)	860 (860)	636.92	99
30	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (Ministry of Petroleum & Natural Gas) (709776)	Assam	04/2022 (04/2022)	09/2026 (09/2026)	277 (323.09)	190.21	70
31	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (Ministry of Petroleum & Natural Gas) (709779)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768 (740)	125.07	46
32	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	07/2020 (07/2020)	07/2024 (12/2025)	12366 (22494)	17836.48	79
33	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	01/2018 (01/2018)	02/2020 (12/2025)	682.9 (726.93)	491.68	94
34	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery (Ministry of Petroleum & Natural Gas) (607701)	Assam	05/2021 (05/2021)	10/2023 (05/2026)	412.3 (577)	451.05	88
35	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	12/2020 (12/2020)	03/2024 (12/2025)	430.76 (430.76)	331.99	88
36	Pipeline Rehabilitation Project, Phase-II (Ministry of Petroleum & Natural Gas) (617827)	Assam	12/2024 (12/2024)	12/2029 (12/2029)	680 (680)	2.24	14
37	Coke Drum Structure Package (Ministry of Petroleum & Natural Gas) (617836)	Assam	12/2022 (12/2022)	12/2025 (12/2025)	635.28 (635.28)	58.68	45
38	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	01/2023 (01/2023)	04/2026 (04/2026)	344.99 (344.99)	220.37	48
39	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850)	Assam	09/2023 (09/2023)	05/2026 (05/2026)	198.7 (198.7)	58.92	40
40	DCU Revamp Project (NRL) (709864)	Assam	08/2021 (08/2021)	07/2024 (06/2026)	370 (370)	271.34	66
41	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865)	Assam	04/2023 (04/2023)	12/2024 (12/2025)	293.5 (293.5)	97.22	97
42	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura)	04/2020 (04/2020)	03/2024 (03/2026)	9265 (9265)	6608.95	86
43	Augmentation/ Revamping of Dimapur Depot, Dimapur (Ministry of Petroleum & Natural Gas) (709786)	Nagaland	08/2023 (08/2023)	11/2027 (11/2027)	227.62 (227.62)	11.41	26
44	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	03/2022 (03/2022)	05/2024 (05/2026)	209.33 (131.51)	70.94	66
Total (16)					28021.38	27463.47	

Ongoing Projects of North-East Region

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Labour and Employment						
	Healthcare						
45	Construction of 200 bedded ESIC Hospital with 62 Nos Staff quarters , Beltola (Employee's State Insurance Company [ESIC]) (612201)	Assam	12/2017 (10/2021)	04/2025 (02/2026)	143.23 (154.75)	101.83	94
	Total (1)				143.23	101.83	
	Ministry of Railways						
	Railways						
46	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3729.89	93
47	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
48	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project (GM/C/ NFR) (706940)	Assam	09/2018 (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
49	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942)	Assam	09/2018 (01/2022)	05/2024 (-)	237.52 (237.52)	0	0
50	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	15782.48	72
51	Murkongselek-Pasighat (Northeast Frontier Railway (NFR) - II) (705401)	Multi-States (Arunachal Pradesh, Assam)	02/2011 (03/2023)	03/2025 (05/2026)	435 (1250)	771.1	62
52	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2025)	6663 (6663)	5634.59	81
53	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	02/2024 (01/2025)	02/2028 (-)	2123.7 (2123.7)	13.74	0
54	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Sikkim	10/2009 (05/2010)	05/2015 (12/2027)	7877 (11775)	9647.55	89
	Total (9)				36793.57	35971.08	
	Department of Telecommunications						
	Telecommunication						
55	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (03/2026)	971.96 (971.96)	208.25	99
56	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (03/2026)	1255.49 (1255.49)	284.04	92
	Total (2)				2227.45	492.29	
	Department of Water Resources, River Development & GR						
	Water Resources						
57	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55
58	Thoubal Multipurpose Project (Water Resources Department-MN) (701400)	Manipur	04/1997 (04/1997)	12/2019 (03/2026)	1449.44 (1822.24)	1837.91	98
	Total (2)				1705.6	1882.61	




Table 6: All Ongoing Projects



All Ongoing Projects							NOVEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Construction of New Domestic Terminal Building Building and miscellaneous works including maintenance, operations and AICMC at Kadapa Airport (Airport Authority of India [AAI]) (612786)	Andhra Pradesh	03/2023 (01/2024)	01/2026 (03/2026)	265.91 (265.91)	76.65	42
2	Construction of New Integrated Terminal Building and associated works including apron to park 3 code E type of aircraft or 6 code C type of aircraft at Vijayawada Airport. (Airport Authority of India [AAI]) (701107)	Andhra Pradesh	06/2020 (09/2020)	09/2022 (03/2026)	611.8 (611.8)	523.14	86
3	Construction of New Domestic Terminal Building at Rajahmundry Airport. (Airport Authority of India [AAI]) (701121)	Andhra Pradesh	12/2022 (08/2023)	08/2025 (03/2026)	347.15 (347.15)	109.62	64
4	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (11/2025)	1712 (1712)	2456.07	94
5	Development of New Civil Enclave at Bihta (Airport Authority of India [AAI]) (612183)	Bihar	08/2024 (03/2025)	09/2027 (-)	1413 (1413)	0	1
6	Development of New Civil Enclave and associated works at Darbhanga Airport (Airport Authority of India [AAI]) (612194)	Bihar	07/2024 (07/2024)	07/2026 (-)	911.66 (911.66)	227.32	43
7	Construction of New Domestic Terminal Building [Phase-I and II] and other allied structures at JPNI Airport, Patna (Airport Authority of India [AAI]) (701101)	Bihar	10/2018 (10/2018)	07/2023 (11/2025)	1216.9 (1216.9)	1137.89	96
8	Goa Airport Terminal Building Extension Project (Airport Authority of India [AAI]) (701105)	Goa	11/2017 (12/2019)	12/2021 (01/2026)	255.69 (255.69)	154.3	97
9	Development of Dholera International Greenfield Airport , Gujarat (Airport Authority of India [AAI]) (701126)	Gujarat	06/2022 (07/2022)	06/2026 (06/2026)	1305 (1551)	739.77	68
10	Construction of NTB complex including apron, taxi track and other associated civil works and electrical & mechanical installations towards Tawi River side at CA Jammu. (Airport Authority of India [AAI]) (611047)	Jammu and Kashmir	07/2022 (07/2023)	06/2026 (06/2026)	861.37 (861.37)	229.1	39
11	Construction of New Domestic Terminal Building and Miscellaneous works at Hubli Airport (Airport Authority of India [AAI]) (612787)	Karnataka	06/2023 (01/2024)	01/2026 (03/2026)	320.47 (320.47)	89.99	51
12	Construction of New Domestic Terminal Building and Miscellaneous Works at Belagavi Airport. (Airport Authority of India [AAI]) (612788)	Karnataka	06/2023 (02/2024)	01/2026 (02/2026)	322.45 (322.45)	140.51	62
13	Development of additional RESA on either end on Runway 10-28 at Calicut Airport. Construction of embankment with slope protection, drainage system and associated works for additional RESA on either end on Runway 10-28 (Airport Authority of India [AAI]) (612789)	Kerala	06/2023 (02/2024)	09/2025 (03/2026)	484.57 (484.57)	96.26	25
14	Construction of Terminal Building & Associated works at Leh Airport, Ladakh (Airport Authority of India [AAI]) (400010)	Ladakh	07/2018 (09/2018)	09/2021 (07/2026)	480 (640)	483.12	78
15	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	156.06	42
16	SITC of ATM Automation System and ASMGCS [Including SMR & MLAT] for Mumbai, Navi Mumbai, Jewar [earlier MOPA, without ASMGCS], HIAL & BIAL (Airport Authority of India [AAI]) (611570)	Multi-States (Karnataka, Maharashtra, Telangana, Uttar Pradesh)	12/2020 (10/2022)	09/2025 (08/2026)	500.48 (500.48)	339.1	75
17	Construction of New Passenger Terminal Building for Domestic Operations at Jodhpur Airport. (Airport Authority of India [AAI]) (701127)	Rajasthan	05/2022 (04/2023)	11/2024 (01/2026)	480 (480)	323.18	98
18	Construction of New Integrated Passenger Terminal Building at Udaipur Airport (Airport Authority of India [AAI]) (701128)	Rajasthan	06/2023 (11/2023)	03/2026 (10/2026)	887 (887)	416.67	55
19	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	02/2026 (-)	323.26 (323.26)	38.7	18
20	Modernization of Chennai Airport, Phase II, Part 2 (Airport Authority of India [AAI]) (611602)	Tamil Nadu	05/2018 (06/2023)	07/2025 (06/2026)	1207 (1207)	193.59	26
21	Construction of New Terminal Building, Second Link Taxi Track, Apron Expansion, and associated works at Prayagraj Airport- On Design & Build Basis. (Airport Authority of India [AAI]) (612063)	Uttar Pradesh	NA (08/2023)	11/2024 (10/2025)	219.18 (274.38)	215.51	100
22	Development of Lal Bahadur Shastri International airport, Varanasi including C/o New Terminal Building, Apron Extension, Runway Extension, PTT and allied works. (Airport Authority of India [AAI]) (701113)	Uttar Pradesh	07/2024 (07/2024)	07/2027 (07/2027)	2869.65 (2869.65)	384.32	19
23	Development of New Integrated Civil Enclave at Agra Airport (Airport Authority of India [AAI]) (701122)	Uttar Pradesh	06/2024 (07/2024)	07/2026 (-)	579 (579)	111.83	24
24	Development of New Civil Enclave at Bagdogra Airport (Airport Authority of India [AAI]) (611495)	West Bengal	08/2024 (09/2024)	01/2027 (01/2027)	1549 (1549)	340.78	15
25	Re-Construction of Rigid portions of Secondary Runway, K and A Taxiway and Strengthening of C Taxiway at NSCB Airport Kolkata. (Airport Authority of India [AAI]) (612791)	West Bengal	04/2023 (12/2023)	02/2025 (08/2026)	328.3 (328.3)	109.61	49

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Total (25)				19949.84	9093.09	
	Ministry of Coal						
	Coal						
26	TIKAK EXTENSION OCP (MIS MoCoal Integration Logins) (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	81.47	4
27	TIRAP OCP (MIS MoCoal Integration Logins) (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.61	3
28	PORDA CHIMTAPANI OCP [10 MTY] (South Eastern Coalfields Limited [SECL]) (400144)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	2310.12 (2310.12)	88.94	10
29	CHHAL OC SEAM III [6 MTY] (South Eastern Coalfields Limited [SECL]) (400145)	Chhattisgarh	12/2013 (12/2013)	03/2022 (12/2025)	610.63 (610.63)	580.56	85
30	BAROUD OC EXPANSION [3.0-10.0M] (South Eastern Coalfields Limited [SECL]) (400149)	Chhattisgarh	08/2020 (08/2020)	03/2029 (-)	2309.8 (2309.8)	939.29	50
31	DIPKA EXPANSION OCP [40 MTY] (South Eastern Coalfields Limited [SECL]) (400354)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	5241.4 (5241.4)	2847.64	37
32	GEVRA OC [70 MTY] (South Eastern Coalfields Limited [SECL]) (400424)	Chhattisgarh	03/2016 (03/2016)	03/2023 (03/2027)	11816.4 (11816.4)	6710.57	78
33	AMERA OC RCE [1.0 MTY] (South Eastern Coalfields Limited [SECL]) (613798)	Chhattisgarh	02/2015 (02/2015)	03/2026 (-)	335.97 (335.97)	88.24	42
34	AMGAON OC RCE [1.0 MTY] (South Eastern Coalfields Limited [SECL]) (613799)	Chhattisgarh	07/2015 (07/2015)	03/2026 (-)	316.11 (316.11)	188.72	78
35	JAGANNATHPUR OC RCE PROJECT (South Eastern Coalfields Limited [SECL]) (613800)	Chhattisgarh	07/2016 (07/2016)	03/2025 (03/2026)	459.49 (459.49)	274.35	96
36	MAHAMAYA OCP [1.50 MTY] (South Eastern Coalfields Limited [SECL]) (613801)	Chhattisgarh	05/2018 (05/2018)	03/2026 (03/2028)	410.26 (410.26)	182.83	54
37	KATKONA RO UG MINE (South Eastern Coalfields Limited [SECL]) (615191)	Chhattisgarh	01/2023 (01/2023)	03/2029 (-)	329.21 (329.21)	61.34	2
38	PELMA OC MDO (South Eastern Coalfields Limited [SECL]) (616234)	Chhattisgarh	10/2022 (10/2022)	03/2033 (-)	1725.04 (1725.04)	15.66	40
39	KUSMUNDA OC EXPANSION PROJECT (SECL - CIL) (617287)	Chhattisgarh	11/2024 (11/2024)	03/2030 (-)	4516.88 (4516.88)	782.97	21
40	MANIKPUR OC EXPANSION PROJECT (South Eastern Coalfields Limited [SECL]) (617288)	Chhattisgarh	01/2025 (01/2025)	03/2029 (-)	382.61 (382.61)	113.03	21
41	HURA C OCP (ECL - CIL) (400018)	Jharkhand	08/2022 (08/2022)	03/2029 (-)	859.41 (859.41)	451.93	62
42	KONAR EXPANSION OCP (Ministry of Coal) (400073)	Jharkhand	01/2022 (01/2022)	03/2032 (-)	799.34 (799.34)	429.65	45
43	KARO EXPANSION OCP (Ministry of Coal) (400074)	Jharkhand	01/2022 (01/2022)	03/2029 (-)	908.47 (908.47)	269.26	22
44	SANGHMITRA OC (Ministry of Coal) (400136)	Jharkhand	03/2024 (03/2024)	03/2032 (-)	2660 (2660)	6.59	11
45	CHANDRAGUPT OCP (Ministry of Coal) (400138)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	973.5 (973.5)	440.75	24
46	KOTRE BASANTPUR PACHMO OCP (Ministry of Coal) (400139)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	861.06 (625.4)	455.95	42
47	Pachwara South Coal Block (NLC India Limited [NLCIL]) (400142)	Jharkhand	03/2016 (11/2019)	09/2028 (-)	2242.9 (2242.9)	1231.67	74
48	RPR MAGADH EXP OCP (Ministry of Coal) (400150)	Jharkhand	08/2020 (08/2020)	03/2028 (-)	7254.37 (7254.37)	1600.77	38
49	NORTH URIMARI EXPANSION OCP (Ministry of Coal) (400151)	Jharkhand	07/2021 (07/2021)	03/2029 (-)	778.8 (778.8)	696.05	67
50	EPR ROHINI - KARKETTA OCP (Ministry of Coal) (400153)	Jharkhand	01/2021 (01/2021)	03/2028 (-)	1020.42 (1020.42)	84.74	21
51	EPR PUNDI OCP (Ministry of Coal) (400154)	Jharkhand	11/2020 (11/2020)	03/2027 (-)	713.35 (713.35)	236.58	10
52	EPR ASHOK OC (Ministry of Coal) (400155)	Jharkhand	05/2021 (05/2021)	03/2031 (-)	2898.28 (2898.28)	185.06	24
53	EPR AMRAPALI OCP (Ministry of Coal) (400156)	Jharkhand	02/2020 (02/2020)	03/2028 (-)	5136.15 (5136.15)	1189.84	42
54	RAJRAPPA RCE OCP (Ministry of Coal) (400160)	Jharkhand	12/2009 (12/2009)	03/2016 (03/2027)	510.85 (510.85)	488.69	76



All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
55	CHITRA EAST OC (<i>Eastern Coal Fields Limited [ECL]</i>) (400172)	Jharkhand	08/2018 (08/2018)	03/2026 (03/2028)	513.99 (513.99)	230.12	51
56	JHARKHAND-LAIYO OCP (<i>Ministry of Coal</i>) (400352)	Jharkhand	08/2020 (08/2020)	03/2031 (-)	764.57 (764.57)	145.81	29
57	MOONIDIH XV SEAM UG (<i>Ministry of Coal</i>) (400425)	Jharkhand	08/2011 (08/2011)	03/2019 (05/2026)	1230.27 (1230.27)	633.27	82
58	2.5 MTPA PATHERDIH NLW WASHERY (<i>Ministry of Coal</i>) (611017)	Jharkhand	10/2015 (04/2016)	04/2018 (03/2026)	334.27 (334.27)	148.72	48
59	AMALAGAMATED NTST KUJAMA OCP 8.5MTY (<i>Ministry of Coal</i>) (611864)	Jharkhand	01/2023 (01/2023)	03/2030 (-)	4011.85 (4011.85)	414.41	28
60	MURAI DIH UG PROJECT (<i>Ministry of Coal</i>) (613808)	Jharkhand	02/2011 (02/2011)	04/2014 (12/2026)	339.87 (339.87)	191	70
61	TAPIN SOUTH EXPN (<i>Ministry of Coal</i>) (615349)	Jharkhand	11/2020 (11/2020)	03/2028 (-)	230.41 (230.41)	22.02	20
62	SIRKA OC (<i>Ministry of Coal</i>) (615822)	Jharkhand	05/2020 (05/2020)	03/2028 (-)	222.82 (222.82)	140.58	53
63	TETARIAKHAR OC (<i>Ministry of Coal</i>) (615843)	Jharkhand	11/2019 (11/2019)	03/2025 (03/2027)	243.52 (243.52)	49.54	29
64	CHUPERBHITA SIMLONG OCP MDO 6 (<i>Eastern Coal Fields Limited [ECL]</i>) (616225)	Jharkhand	12/2023 (12/2023)	03/2037 (-)	979.08 (979.08)	0	0
65	JARANGDIH EXPN. OCP 1.5 MTY (<i>CCL - CIL</i>) (616236)	Jharkhand	02/2020 (02/2020)	03/2029 (-)	414.37 (414.37)	85.6	32
66	BLOCK E OCP (<i>Ministry of Coal</i>) (616253)	Jharkhand	03/2024 (03/2024)	03/2029 (-)	5850.83 (5850.83)	20.32	3
67	Revised Jharia Master Plan for Dealing with Fire, Subsidence & Rehabilitation of affected families in Jharia Coalfield- Reg. (<i>Bharat Coking Coal Limited (BCCL)</i>) (617416)	Jharkhand	06/2025 (07/2025)	12/2028 (-)	5940.47 (5940.47)	1.31	12
68	AMADAND OCP[4.0MTY] (<i>Ministry of Coal</i>) (400148)	Madhya Pradesh	03/2016 (03/2016)	03/2021 (03/2027)	869.44 (869.44)	278.42	75
69	RAMPUR BATURA OCP [4.0MTY] (<i>South Eastern Coalfields Limited [SECL]</i>) (400152)	Madhya Pradesh	07/2019 (07/2019)	03/2026 (-)	1248.93 (1248.93)	498.36	44
70	BLOCK B EXPANSION [3.5 TO 8.0 (<i>Northern Coalfields Limited [NCL]</i>) (400162)	Madhya Pradesh	07/2019 (07/2019)	03/2023 (03/2027)	998.71 (998.71)	476.83	47
71	NIGAH I EXPANSION [15 TO 25 MTP (<i>Northern Coalfields Limited [NCL]</i>) (400321)	Madhya Pradesh	11/2020 (11/2020)	03/2025 (03/2028)	1729.68 (1729.68)	841.25	48
72	KANCHAN OC EXP (<i>South Eastern Coalfields Limited [SECL]</i>) (613802)	Madhya Pradesh	12/2014 (12/2014)	03/2026 (-)	371.04 (371.04)	144.61	58
73	JHIRIA WEST OCP [1.5 MTY] (<i>South Eastern Coalfields Limited [SECL]</i>) (613803)	Madhya Pradesh	01/2024 (01/2024)	03/2029 (-)	366.94 (366.94)	34.1	41
74	RPR TAWA-III UG 0.84 MTY (<i>Western Coalfields Limited [WCL]</i>) (613804)	Madhya Pradesh	12/2021 (12/2021)	03/2027 (-)	314.09 (314.09)	6.84	17
75	AMALGAMATED DHANKASA & JAMUNIA (<i>Western Coalfields Limited [WCL]</i>) (615185)	Madhya Pradesh	09/2022 (09/2022)	03/2027 (-)	399.2 (399.2)	93.52	66
76	RPR OF VISHNUPURI UG TO OC (<i>Western Coalfields Limited [WCL]</i>) (615187)	Madhya Pradesh	11/2022 (11/2022)	03/2029 (-)	220.62 (220.62)	0	11
77	URDHAN EXPANSION OC COST PLUS (<i>Western Coalfields Limited [WCL]</i>) (615194)	Madhya Pradesh	07/2022 (01/2023)	03/2031 (-)	206.88 (206.88)	27.19	0
78	SHARDA UG MINE (<i>Western Coalfields Limited [WCL]</i>) (615195)	Madhya Pradesh	07/2022 (09/2023)	03/2028 (-)	166.25 (166.25)	5.12	9
79	GANDHIGRAM UG MINE (<i>Western Coalfields Limited [WCL]</i>) (615206)	Madhya Pradesh	08/2019 (08/2019)	03/2026 (-)	414.15 (414.15)	14.41	56
80	BHATADI EXPANSION OC (<i>Western Coalfields Limited [WCL]</i>) (400033)	Maharashtra	02/2020 (05/2022)	03/2028 (-)	580.61 (580.61)	80.95	31
81	AMALGAMATED YEKONA I & YEKONA (<i>Western Coalfields Limited [WCL]</i>) (400177)	Maharashtra	08/2015 (08/2015)	03/2025 (03/2026)	727.28 (727.28)	539.9	80
82	DINESH[MAKARDHOKRA-III] OC (<i>Western Coalfields Limited [WCL]</i>) (400178)	Maharashtra	02/2020 (02/2020)	03/2027 (-)	822.88 (822.88)	622.29	34
83	DHUPTALA OC [SASTI UG TO OC] (<i>Western Coalfields Limited [WCL]</i>) (400353)	Maharashtra	02/2019 (10/2021)	03/2028 (-)	711.01 (711.01)	169.24	19
84	SAONER UG MINE -1 EXPANSION 1. (<i>Western Coalfields Limited [WCL]</i>) (615184)	Maharashtra	01/2022 (01/2022)	03/2028 (-)	228.64 (228.64)	143.48	68
85	SASTI EXPANSION OPENCAST (<i>Western Coalfields Limited [WCL]</i>) (615186)	Maharashtra	08/2020 (08/2020)	03/2026 (-)	319.04 (319.04)	91.6	20



All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
86	NEW MAJRI UG TO OC 3 MTY COST (<i>Western Coalfields Limited [WCL]</i>) (615188)	Maharashtra	05/2019 (09/2022)	03/2027 (-)	402.27 (402.27)	60.07	24
87	MAKARDHOKRA EXPN OC 4.9 MTY (<i>Western Coalfields Limited [WCL]</i>) (615189)	Maharashtra	06/2022 (06/2022)	03/2026 (-)	361.87 (361.87)	77.54	11
88	SINGHORI DEEP OC MIN 2.0 MTY (<i>Western Coalfields Limited [WCL]</i>) (615190)	Maharashtra	05/2022 (05/2022)	03/2029 (-)	335.75 (335.75)	26.98	6
89	GOKUL EXTENSION OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615192)	Maharashtra	04/2021 (04/2021)	03/2026 (-)	309.58 (309.58)	45.87	8
90	KOLGAON EXPANSION DEEP OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615199)	Maharashtra	01/2023 (09/2023)	03/2027 (-)	198.71 (198.71)	10.55	2
91	BALLARPUR NORTH WEST OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615330)	Maharashtra	12/2022 (12/2022)	03/2029 (-)	360.81 (360.81)	0.02	4
92	GADEGAON OC 3 MTY (<i>Western Coalfields Limited [WCL]</i>) (615331)	Maharashtra	10/2023 (10/2023)	03/2030 (-)	497.41 (497.41)	0.08	0
93	GHONSA EXPANSION DEEP OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615914)	Maharashtra	03/2021 (03/2021)	03/2029 (-)	184.71 (184.71)	14.48	5
94	AMLG GAURI PAUNI EXPANSION OC (<i>Western Coalfields Limited [WCL]</i>) (615916)	Maharashtra	04/2024 (04/2024)	03/2030 (-)	1225.21 (1225.21)	80.14	2
95	GAURIDEEP/GAURI CENTRAL OCP 7. (<i>Western Coalfields Limited [WCL]</i>) (615917)	Maharashtra	08/2023 (06/2024)	03/2030 (-)	973.07 (973.07)	0.67	0
96	RPR OF BHANEGAON OC (<i>Western Coalfields Limited [WCL]</i>) (615918)	Maharashtra	02/2017 (09/2022)	03/2028 (-)	405.2 (405.2)	12.39	7
97	N. EXTN. MUNGOLI NIRGUDA D OCP (<i>Western Coalfields Limited [WCL]</i>) (615919)	Maharashtra	06/2024 (06/2024)	03/2029 (-)	1024.91 (1024.91)	175.93	0
98	NILJAI EXPANSION DEEP OCP (<i>Western Coalfields Limited [WCL]</i>) (615982)	Maharashtra	08/2016 (08/2016)	03/2022 (03/2026)	319.75 (319.75)	185.91	79
99	UKNI DEEP OC MINE -COST PLUS (<i>Western Coalfields Limited [WCL]</i>) (616044)	Maharashtra	11/2018 (01/2019)	03/2021 (03/2026)	237.06 (237.06)	165.76	87
100	AMALGAMATED INDER-KAMPTEE DEEP (<i>Western Coalfields Limited [WCL]</i>) (616050)	Maharashtra	09/2018 (09/2018)	03/2024 (03/2026)	235.9 (235.9)	131.81	98
101	ADASA UG TO OC MINE (<i>Western Coalfields Limited [WCL]</i>) (616223)	Maharashtra	11/2018 (11/2018)	03/2024 (03/2026)	316 (316)	208.63	86
102	AMAL GONDEGAON GHATROHANA EXPN (<i>Western Coalfields Limited [WCL]</i>) (616229)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	668.54 (668.54)	1.19	0
103	WAGHODA UG MINE [1.02 MTY] (<i>Western Coalfields Limited [WCL]</i>) (617233)	Maharashtra	01/2024 (01/2025)	03/2030 (-)	379.3 (379.3)	0	0
104	KOLARPIMPRI EXPANSION OC [2.5 (<i>Western Coalfields Limited [WCL]</i>) (617278)	Maharashtra	06/2024 (02/2025)	03/2030 (-)	630.37 (630.37)	0	0
105	Master Plan for Jharia and Raniganj Coalfields (<i>Bharat Coking Coal Limited [BCCL]</i>) (400313)	Multi-States (Jharkhand, West Bengal)	08/2009 (08/2009)	08/2019 (12/2028)	2661.73 (2661.73)	792.45	43
106	BINA KAKRI AMALGAMATION EXPANS (<i>Northern Coalfields Limited [NCL]</i>) (400369)	Multi-States (Madhya Pradesh, Uttar Pradesh)	08/2020 (08/2020)	03/2024 (03/2027)	836.42 (836.42)	812.73	89
107	KHADIA EXPANSION [10 TO 16 MTP (<i>Northern Coalfields Limited [NCL]</i>) (615183)	Multi-States (Madhya Pradesh, Uttar Pradesh)	06/2021 (06/2021)	03/2025 (03/2027)	491.67 (491.67)	247.06	50
108	SUBHADRA OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400165)	Odisha	05/2021 (05/2021)	04/2032 (-)	1693.81 (1693.81)	1324.37	42
109	SIARMAL OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400166)	Odisha	02/2021 (02/2021)	03/2029 (-)	5194.95 (5194.95)	3460.35	57
110	BALARAM EXPANSION OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400183)	Odisha	06/2020 (08/2020)	03/2029 (-)	3504.21 (3504.21)	924.23	53
111	GOPALJI KANIHA OCP [10 TO 30 M (<i>MCL - CIL</i>) (400185)	Odisha	04/2022 (04/2022)	03/2030 (-)	8416.19 (6107.87)	1742.12	17
112	INTEGRATED LAKHANPUR-BELPAHAR- (<i>Mahanadi Coalfields Limited [MCL]</i>) (400187)	Odisha	05/2018 (05/2018)	03/2027 (-)	2434.75 (2434.75)	1840.93	71
113	BHARATPUR RE-ORGANIZATION OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400392)	Odisha	11/2018 (11/2018)	03/2029 (-)	2838.86 (2838.86)	1673.58	48
114	BASUNDHARA WEST EXTENSION OPEN (<i>MCL - CIL</i>) (615193)	Odisha	05/2014 (05/2014)	03/2019 (03/2029)	479.15 (479.15)	274.63	64
115	Naini Coal Mine (<i>Singareni Collieries Company Limited [SCCL]</i>) (615857)	Odisha	03/2020 (03/2020)	03/2026 (-)	494.3 (494.3)	491.33	80
116	INTEGRATED KULDA GARJANBAHAL O (<i>Mahanadi Coalfields Limited [MCL]</i>) (616226)	Odisha	04/2023 (04/2023)	03/2033 (-)	3563.5 (3563.5)	592.57	3

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
117	BHUBANESWARI EXPN OCP 50 MTY (MCL - CIL) (616231)	Odisha	03/2024 (03/2024)	03/2033 (-)	5366.27 (5366.27)	468.15	29
118	HINGULA II OC EXPN PH III 15 M (MCL - CIL) (616232)	Odisha	11/2022 (11/2022)	03/2029 (-)	1561.85 (1561.85)	272.99	24
119	BALABHADRA OCP (MCL - CIL) (616233)	Odisha	04/2023 (04/2023)	03/2030 (-)	978.44 (978.44)	212.94	12
120	Jawahar Khani Open Cast Mine (Singareni Collieries Company Limited [SCCL]) (615818)	Telangana	12/2021 (12/2021)	03/2025 (03/2027)	297.88 (297.88)	46.95	20
121	Kalyanikhani Opencast Project (Singareni Collieries Company Limited [SCCL]) (615858)	Telangana	03/2016 (05/2017)	03/2026 (-)	384.32 (384.32)	284.06	75
122	Kakathiya Khani Opencast - III Project Phase - I (Singareni Collieries Company Limited [SCCL]) (615859)	Telangana	03/2017 (05/2017)	03/2026 (-)	413.84 (413.84)	397.55	79
123	Godavarikhani Coal Mine - 5 (Singareni Collieries Company Limited [SCCL]) (615860)	Telangana	07/2019 (05/2019)	03/2025 (03/2026)	607.04 (607.04)	191.78	71
124	Indaram Opencast Project (Singareni Collieries Company Limited [SCCL]) (615861)	Telangana	08/2017 (12/2022)	03/2025 (03/2026)	424.81 (424.81)	405	80
125	Goleti Opencast Mine (Singareni Collieries Company Limited [SCCL]) (615862)	Telangana	07/2021 (08/2021)	03/2026 (-)	345.6 (345.6)	76.19	21
126	Venkatesh Khani Coal Mine (Singareni Collieries Company Limited [SCCL]) (615863)	Telangana	10/2020 (06/2020)	03/2026 (-)	484.5 (484.5)	477.14	97
127	Ramagundam OC-II Extension Project (Singareni Collieries Company Limited [SCCL]) (615864)	Telangana	11/2015 (06/2015)	03/2026 (-)	489.62 (489.62)	405.54	77
128	Kakatiyakhani OC - 2 Project (Singareni Collieries Company Limited [SCCL]) (615865)	Telangana	08/2017 (09/2017)	03/2025 (03/2026)	442.42 (442.42)	230.28	63
129	MOHANPUR EXPANSION OC -PHASE I (Eastern Coal Fields Limited [ECL]) (400173)	West Bengal	11/2020 (11/2020)	03/2026 (03/2030)	888.99 (888.99)	117.17	30
130	BONJEMEHARI EXPANSION OCP (Eastern Coal Fields Limited [ECL]) (400180)	West Bengal	08/2021 (08/2021)	03/2026 (03/2030)	570.11 (570.11)	82.77	16
131	NAKRAKONDA KUMARDIH- B OCP (Eastern Coal Fields Limited [ECL]) (400181)	West Bengal	08/2018 (08/2018)	03/2029 (-)	502.68 (502.67)	71.34	26
132	SIDULI [OC & UG] (ECL - CIL) (400182)	West Bengal	05/2018 (05/2018)	03/2027 (03/2030)	535.18 (535.17)	5.28	14
133	TILABONI UG (Eastern Coal Fields Limited [ECL]) (400186)	West Bengal	01/2023 (01/2023)	03/2029 (-)	749.08 (749.07)	52.86	10
134	JHANJRA EXPANSION UG (Eastern Coal Fields Limited [ECL]) (400312)	West Bengal	04/2020 (04/2020)	03/2029 (-)	1210.12 (1210.12)	542.09	44
135	SONEPUR BAZARI EXPANSION OCP [(Eastern Coal Fields Limited [ECL]) (400315)	West Bengal	07/2021 (07/2021)	03/2029 (-)	5365.88 (5365.88)	586.07	17
136	2.0 MTPA BHOJUDIH NLW WASHERY (Ministry of Coal) (611016)	West Bengal	12/2015 (03/2019)	09/2020 (12/2025)	384.57 (384.57)	357.14	97
137	ITAPARA OCP (Eastern Coal Fields Limited [ECL]) (612816)	West Bengal	12/2023 (12/2023)	03/2030 (-)	929.1 (929.1)	69.49	7
138	SHYAMSUNDARPUR UG INCLUDING SA (Eastern Coal Fields Limited [ECL]) (613793)	West Bengal	04/2020 (04/2020)	03/2026 (03/2028)	483.65 (483.65)	60.99	12
139	PARASEA-BELBAID UG PROJECT (Eastern Coal Fields Limited [ECL]) (613794)	West Bengal	01/2023 (01/2023)	03/2028 (-)	389.1 (389.1)	132.48	21
140	PARASCOLE JAMBAD OCP (Eastern Coal Fields Limited [ECL]) (616230)	West Bengal	11/2024 (11/2024)	03/2037 (-)	1193.55 (1193.55)	9.53	0
Total (115)					157276.32	47909.71	
Electricity Generation							
141	50 MW Wind Power Project (NLC India Limited [NLCIL]) (617299)	Gujarat	07/2022 (01/2024)	06/2025 (01/2026)	383.84 (383.84)	319.71	47
142	600 MW Khavda Solar Power Project (NLC India Limited [NLCIL]) (617730)	Gujarat	08/2023 (06/2024)	06/2026 (-)	3335.85 (3335.85)	738.34	22
143	NLC Talabira Thermal Power Project (NLC India Limited [NLCIL]) (400231)	Odisha	01/2017 (01/2024)	03/2030 (-)	27212.96 (27213)	2550.76	1
144	300 MW SPP part of 510 MW CPSU scheme (NLC India Limited [NLCIL]) (612819)	Rajasthan	07/2022 (03/2023)	09/2024 (12/2025)	1813 (1813)	1393.34	86
145	50 MW Solar PP Minedout Area (NLC India Limited [NLCIL]) (615327)	Tamil Nadu	08/2023 (02/2024)	03/2025 (12/2025)	218.03 (218.03)	164.7	75
146	Ghatampur Thermal Power Plant 3 X 660 MW (NLC India Limited [NLCIL]) (400259)	Uttar Pradesh	07/2016 (08/2016)	11/2020 (03/2026)	17237.8 (21780.9)	20711.46	93

All Ongoing Projects							NOVEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Total (6)				50201.48	25878.31	
	Railways						
147	Dharamjaigarh-Korba (Railway) (400203)	Chhattisgarh	05/2018 (03/2017)	12/2026 (08/2026)	1686.22 (1686.22)	439.98	42
148	Shivpur-Kathautia New Rail [BG] Line [49 km] [Package II of Tori-Shivpur-Kathautia line] (Ministry of Coal) (400416)	Jharkhand	02/2018 (05/2022)	06/2025 (06/2026)	1799.64 (2564.34)	1489.74	64
	Total (2)				3485.86	1929.72	
	Ministry of Power						
	Coal						
149	Tubed Coal Mine (Damodar Valley Corporation) (400192)	Jharkhand	07/2016 (10/2016)	05/2026 (05/2026)	1581 (1581)	598.62	36
150	Badam Coal Mining project of NTPC (National Thermal Power Corporation [NTPC]) (603293)	Jharkhand	02/2019 (09/2019)	12/2056 (04/2027)	502 (784)	388.29	59
	Total (2)				2083	986.91	
	Electricity Generation						
151	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited [NHPC]) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	3776.74	16
152	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	64.76	3
153	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	63.73	2
154	Buxar Thermal Power Project [1320 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602579)	Bihar	03/2019 (06/2019)	01/2024 (12/2025)	10439.09 (13756.6)	12691.85	93
155	Lara Super Thermal Power Project Stage-II [2 x 800 MW] (National Thermal Power Corporation [NTPC]) (611930)	Chhattisgarh	08/2023 (08/2023)	06/2028 (-)	15530 (16106)	3131.26	19
156	Sipat Super Thermal Power Project, Stage-III [1x800 MW] (National Thermal Power Corporation [NTPC]) (617188)	Chhattisgarh	09/2024 (09/2024)	09/2029 (-)	9791 (9791)	963.88	8
157	Bagodara Solar Power Project (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (709747)	Gujarat	03/2021 (05/2021)	12/2025 (12/2025)	339.35 (339.35)	317.59	51
158	Dhauilasidh Hydro Electric Project [66 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602582)	Himachal Pradesh	10/2020 (05/2021)	11/2025 (03/2027)	687.97 (1561.21)	997.55	71
159	Luhri Stage-I Hydro Electric Project [210 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602593)	Himachal Pradesh	11/2020 (11/2020)	01/2026 (02/2030)	1810.56 (4681.64)	1818.61	51
160	382 MW Sunni Dam HEP (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602633)	Himachal Pradesh	NA (04/2018)	03/2027 (-)	2615 (2615)	495.57	0.5
161	Sunni Dam Hydro Electric Project [382 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (611586)	Himachal Pradesh	01/2023 (01/2023)	04/2028 (12/2029)	2614.51 (4540.71)	1015.36	30
162	Pakal Dul [Drangdhuran] Hydroelectric Project, 1000 MW (National Hydroelectric Power Corporation Limited [NHPC]) (602525)	Jammu and Kashmir	10/2014 (02/2018)	04/2020 (12/2026)	8112.12 (12728)	7785.72	76
163	Kiru HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (602532)	Jammu and Kashmir	03/2019 (02/2020)	09/2023 (12/2026)	4287.59 (5409)	3186.98	73
164	Rattle HE Project - 850 MW, Rattle Hydroelectric Power Corporation Limited. (National Hydroelectric Power Corporation Limited [NHPC]) (602535)	Jammu and Kashmir	02/2021 (01/2022)	02/2026 (11/2028)	5281.94 (5281.94)	1298.42	26
165	Kwar HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (605155)	Jammu and Kashmir	05/2022 (11/2022)	11/2026 (03/2028)	4526.12 (4526.12)	1140.08	25
166	Patratu Thermal Power Station Expansion Project Phase-I [3x800 MW] (National Thermal Power Corporation [NTPC]) (400261)	Jharkhand	11/2017 (11/2017)	03/2023 (11/2026)	18668 (20302)	17928.61	86
167	Koderma Thermal Power Station Phase II [2X800 MW] At Koderma, Jharkhand (Damodar Valley Corporation) (611509)	Jharkhand	04/2023 (11/2024)	03/2029 (-)	14358 (14358)	1450.04	4
168	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited [NHPC]) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (05/2026)	6285.33 (26075.5)	25415.23	97
169	Talcher Thermal Power Station Stage III [2 x 660 MW] Expansion (National Thermal Power Corporation [NTPC]) (602961)	Odisha	08/2022 (09/2022)	05/2027 (03/2028)	11843.75 (12543)	5042.25	43
170	BIKANER SOLAR POWER PROJECT (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (709748)	Rajasthan	10/2021 (05/2022)	04/2024 (12/2025)	5491.89 (5491.89)	5376.34	92
171	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181)	Sikkim	03/2019 (03/2020)	03/2024 (12/2027)	5748.04 (5748.04)	3887.11	70
172	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156)	Sikkim	03/2021 (08/2021)	05/2024 (12/2025)	938.29 (1828.11)	1488.78	93
173	Khurja super Thermal Power Plant [2X660 MW] (THDC India Limited) (602194)	Uttar Pradesh	03/2019 (08/2019)	02/2024 (09/2025)	11089.42 (13276.2)	12951.99	100



All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
174	Singrauli Super Thermal Power Project, Stage-III [2x800 MW] (National Thermal Power Corporation [NTPC]) (612142)	Uttar Pradesh	03/2024 (03/2024)	02/2030 (-)	17195 (17195)	2211.69	13
175	Tapovan-Vishnugad HEP [4x130 MW] (National Thermal Power Corporation [NTPC]) (602185)	Uttarakhand	11/2006 (11/2006)	03/2013 (04/2029)	2978 (10907.3)	7291	77
176	Tehri Pumped Storage Plant Project [4x250 MW] (THDC India Limited) (602193)	Uttarakhand	07/2006 (06/2011)	06/2022 (01/2026)	4825.6 (8339)	8169.51	98
177	Vishnugad Pipalkoti Hydro Electric Project [444 MW] (THDC India Limited) (602195)	Uttarakhand	08/2008 (01/2014)	12/2022 (03/2027)	3860.35 (6823.72)	5328.31	73
178	Raghunathpur Thermal Power Station Phase II [2X660 MW] at Raghunathpur, Purulia, West Bengal (Damodar Valley Corporation) (400062)	West Bengal	01/2023 (02/2025)	06/2029 (-)	17673 (17673)	1458.01	2
179	Rammam-III HEPP [3x40 MW] (National Thermal Power Corporation [NTPC]) (602184)	West Bengal	09/2014 (09/2014)	09/2019 (03/2029)	1381.84 (2865.56)	1393.94	51
180	Installation of FGD for 4x210 & 2x250 MW MTPS U 1-6 (Damodar Valley Corporation) (602538)	West Bengal	06/2019 (02/2021)	01/2024 (12/2025)	1037 (1106)	1111.01	93
Total (30)					224974.07	139251.92	
Transmission & Distribution							
181	Transmission Scheme for Solar Energy Zone in Ananthpuram 2500MW and Kurnool 1000MW (Power Grid Corporation of India Limited [POWERGRID]) (611967)	Andhra Pradesh	09/2023 (09/2023)	09/2025 (03/2026)	1248.69 (1248.69)	1023.92	90
182	Augmentation of 1x1500 MVA 3rd 765/400 kV transformation capacity at Kurnool New Substation (Power Grid Corporation of India Limited [POWERGRID]) (612856)	Andhra Pradesh	05/2023 (12/2023)	09/2025 (01/2026)	163.61 (163.61)	88.34	82
183	Transmission system strengthening at Kurnool- III PS for integration of additional RE generation projects [POWERGRID Kurnool III PS RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617183)	Andhra Pradesh	03/2025 (03/2025)	12/2027 (-)	2886 (2886)	141.7	7
184	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	0.04	0
185	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part C (Power Grid Corporation of India Limited [POWERGRID]) (611657)	Gujarat	03/2023 (03/2023)	03/2025 (12/2025)	2820.99 (2820.99)	2783.19	95
186	Transmission system for Evacuation of Additional 7 GW RE power from Khavda RE park under Phase-III Part B [Vataman Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (612139)	Gujarat	12/2023 (12/2023)	12/2025 (12/2026)	3751.82 (3751.82)	2025.98	32
187	Transmission System for Evacuation of Power from potential Renewable Energy zone in Khavda Area of Gujarat under Phase IV [7 GW] Part E3 (Power Grid Corporation of India Limited [POWERGRID]) (612151)	Gujarat	07/2023 (07/2023)	07/2025 (03/2026)	334 (334)	207.08	78
188	Transmission System for Evacuation of Power from Potential Energy Renewable Zone in Khavda Area of Gujarat under Ph-IV [7GW] Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (612855)	Gujarat	05/2024 (05/2024)	05/2026 (06/2026)	679 (679)	142.59	30
189	Augmentation of Transformation Capacity at jam Khambhaliya PS [GIS] [SPV Name POWERGRID Jam Khambhaliya Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615342)	Gujarat	10/2024 (10/2024)	07/2026 (-)	329 (329)	13.17	3
190	Provision of Dynamic Reactive Compensation at Khavda pooling Station 1 [KPS1] and Khavda Pooling station 3 [KPS3] (Power Grid Corporation of India Limited [POWERGRID]) (615343)	Gujarat	11/2024 (11/2024)	11/2026 (-)	501 (501)	8.11	2
191	Transmission System for Evacuation of Power from Potential Renewable Energy Zone in Khavda area of Gujarat under Phase-IV [7GW] Part B [SPV Name POWERGRID South Olpad Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615345)	Gujarat	10/2024 (10/2024)	10/2026 (03/2027)	4766 (4766)	762.56	10
192	Augmentation of Transformation Capacity at KPS1 [GIS] and KPS2 [GIS] [Phase-V Part B1 and Part B2 Scheme] [SPV Name- POWERGRID KPS1 and 2 Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617069)	Gujarat	02/2025 (02/2025)	02/2027 (-)	466 (466)	23.99	1
193	Augmentation of Banaskantha [Raghnesda] PS [GIS] [POWERGRID Banaskantha Transco Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617182)	Gujarat	03/2025 (03/2025)	03/2027 (-)	172 (172)	17.27	18
194	Augmentation of Transformation Capacity at Bhuj-II PS [GIS] (Power Grid Corporation of India Limited [POWERGRID]) (617391)	Gujarat	02/2025 (02/2025)	11/2026 (03/2027)	488.29 (488.29)	0.22	0
195	Jamnagar Transmission Limited (Adani Transmission Limited) (617405)	Gujarat	NA (10/2024)	10/2026 (-)	4000 (4000)	0	0
196	Provision of ICT Augmentation & Bus Reactor at Bhuj-II PS (Power Grid Corporation of India Limited [POWERGRID]) (617801)	Gujarat	03/2025 (03/2025)	12/2026 (03/2027)	581.74 (581.74)	0.2	0
197	Implementation of LILO of both circuits of 400KV vindhyachal PS-Sasan D/C Line at Hindalco Switchyard (Power Grid Corporation of India Limited [POWERGRID]) (617272)	Haryana	06/2024 (06/2024)	12/2026 (-)	370 (370)	22.2	6
198	Transmission Scheme for evacuation of Power from Ratle HEP [850 MW] & kiru [624 MW] Part B (Power Grid Corporation of India Limited [POWERGRID]) (617179)	Jammu and Kashmir	07/2024 (07/2024)	07/2026 (03/2027)	218.6 (218.6)	2.61	0

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
199	Implementation of Transmission Systems in the State of Jharkhand consisting of 400/220/132/33 kV transmission lines and substations under Jharkhand Consultancy Project (Power Grid Corporation of India Limited [POWERGRID]) (617326)	Jharkhand	02/2012 (02/2012)	03/2026 (-)	1842.25 (1842.25)	1648.05	95
200	Transmission Scheme for Integration of Renewable Energy Zone [Phase II] in Koppal II [Phase A&B] and gadag II[Phase A] in Karnataka [POWERGRID KOPPAL GADAG TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (612140)	Karnataka	12/2023 (12/2023)	12/2025 (06/2026)	2889.39 (2889.39)	1733.63	61
201	System Strengthening at Koppal-II and GadagII for integration of RE generation projects [SPV Name POWERGRID Koppal Gadag Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616672)	Karnataka	01/2025 (01/2025)	06/2027 (-)	1354 (1354)	44	1
202	Augmentation of Transformation Capacity by 3x500 MVA, 400/220 KV ICTS [6th-8th] and 1x1500 MVA, 765/400 KV ICT [4th] at Bidar PS [SPV Name- POWERGRID Bidar Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617068)	Karnataka	02/2025 (02/2025)	06/2027 (-)	288 (288)	7.41	1
203	Transmission Scheme for integration of Davanagere/ Chitradurga and Bellary REZ in Karnataka [POWERGRID Chitradurga Bellary REZ Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617184)	Karnataka	03/2025 (03/2025)	09/2027 (-)	3453 (3453)	62.15	1
204	Transmission System Strengthening at Davanagere for Integration of RE Generation [SPV Name - POWERGRID Davanagere Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617803)	Karnataka	09/2025 (09/2025)	09/2027 (-)	379 (379)	6.97	0
205	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5GW] [Jaisalmer/Barmer Complex] Part H1 [POWERGRID KURAWAR TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615344)	Madhya Pradesh	10/2024 (10/2024)	10/2026 (03/2027)	3674 (3674)	808.28	18
206	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part C [SPV Name POWERGRID Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615346)	Madhya Pradesh	08/2024 (08/2024)	08/2026 (12/2026)	2708 (2708)	1056.12	44
207	Transmission System for evacuation of power from Mahan Energen Limited Generating Station in Madhya Pradesh [SPV Name - POWERGRID MEL Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617279)	Madhya Pradesh	06/2025 (06/2025)	12/2027 (-)	558 (558)	33.48	1
208	Augmentation of Transformation Capacity and Implementation of Line Bays at Mandsaur S/S for RE Interconnection [SPV Name- POWERGRID Mandsaur I RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617802)	Madhya Pradesh	10/2025 (10/2025)	03/2028 (-)	319 (319)	0.1	0
209	Transmission System for Evacuation of power from Potential RE Zone in Khavda Area of Gujarat under phase IV 7GW-Part E4 (Power Grid Corporation of India Limited [POWERGRID]) (611966)	Maharashtra	11/2023 (11/2023)	07/2025 (03/2026)	224.41 (224.41)	89.66	44
210	Transmission System for Integration of Kurnool-IV REZ Phase-I [for 4.5 GW] [POWERGRID Kurnool-IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617185)	Multi-States (Andhra Pradesh, Karnataka)	03/2025 (03/2025)	03/2027 (-)	5550 (5550)	333	1
211	Transmission System for Integration of Ananthapur 2 REZ Phase 1 for 4.5 GW. SPV Name Anantapuram 2 REZ Transmission Ltd (Sterlite Power) (617806)	Multi-States (Andhra Pradesh, Karnataka)	08/2024 (03/2025)	03/2027 (-)	4535.99 (4535.99)	208.88	26
212	Transmission System for Kurnool Wind Energy Zone/ Solar Energy Zone Part-A and Part-B (Power Grid Corporation of India Limited [POWERGRID]) (900808)	Multi-States (Andhra Pradesh, Telangana)	11/2022 (03/2023)	11/2024 (01/2026)	3546.94 (3546.94)	3404.59	98
213	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	7778.18	82
214	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (03/2026)	5111.33 (6700)	5410.25	96
215	Eastern Region Expansion Scheme-43 [ERES-43] (Power Grid Corporation of India Limited [POWERGRID]) (617271)	Multi-States (Bihar, Odisha, West Bengal)	09/2024 (09/2024)	03/2026 (06/2026)	342.69 (342.69)	0.71	0
216	Inter-regional [NR-WR] Transmission System strengthening to relieve the loading of 765 kV Vindhyachal-Varanasi D/c line (Power Grid Corporation of India Limited [POWERGRID]) (617807)	Multi-States (Bihar, Uttar Pradesh)	10/2025 (10/2025)	10/2027 (-)	2368 (2368)	0.1	0
217	Eastern Region Expansion Scheme-44 [ERES-44] (Power Grid Corporation of India Limited [POWERGRID]) (617270)	Multi-States (Bihar, West Bengal)	11/2024 (11/2024)	05/2026 (06/2026)	408.94 (408.94)	0.32	0
218	Transmission Network Expansion in Gujarat to increase its ATC from ISTS Part B (Power Grid Corporation of India Limited [POWERGRID]) (400005)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	01/2022 (07/2022)	06/2023 (12/2025)	4546.26 (4546.26)	4318.95	94
219	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part J (Power Grid Corporation of India Limited [POWERGRID]) (611735)	Multi-States (Delhi, Rajasthan)	12/2022 (12/2022)	03/2025 (07/2026)	331 (331)	139.02	37
220	Transmission Scheme for Evacuation of power from REZ in Rajasthan [20 GW] under Phase-III Part D [Sikar Khetri Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612132)	Multi-States (Delhi, Rajasthan)	02/2024 (02/2024)	08/2025 (06/2026)	2000 (2000)	1528.4	72

All Ongoing Projects							NOVEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
221	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV Name POWERGRID West Central Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615347)	Multi-States (Gujarat, Maharashtra)	11/2024 (11/2024)	05/2029 (-)	24819 (24819)	1985.98	3
222	Transmission system for evacuation of power from Rajasthan REZ Ph-IV [Part-3/6GW] [Bikaner complex] Part A [SPV Name POWERGRID Bikaner IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615339)	Multi-States (Haryana, Punjab, Rajasthan)	11/2024 (11/2024)	11/2026 (03/2027)	5969 (5969)	698.04	11
223	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3/ 6 GW] [BIKANER COMPLEX] PART B [SPV Name POWERGRID Siwani Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615340)	Multi-States (Haryana, Rajasthan)	11/2024 (11/2024)	11/2026 (03/2027)	5357 (5357)	666.56	17
224	Inter-Regional Strengthening between SR Grid and WR Grid (Power Grid Corporation of India Limited [POWERGRID]) (617808)	Multi-States (Karnataka, Maharashtra)	10/2025 (10/2025)	10/2027 (-)	1007 (1007)	0.1	0
225	Transmission Scheme for Solar Energy Zone in Bidar [2500 MW], Karnataka [Bidar Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612138)	Multi-States (Karnataka, Telangana)	02/2024 (02/2024)	02/2026 (06/2026)	2147.62 (2147.62)	1505.69	71
226	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part D [SPV Name POWERGRID Beawar Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615333)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (-)	2227 (2227)	801.72	25
227	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part E [SPV Name POWERGRID Mewar Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615334)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (03/2027)	3251 (3251)	1137.85	28
228	Rajasthan REZ Ph-V [Part-1- 4 GW] [Sirohi/Nagaur] Complex [Rajasthan V Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617186)	Multi-States (Madhya Pradesh, Rajasthan)	03/2025 (03/2025)	03/2027 (-)	5028 (5028)	319.73	5
229	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part D [Neemrana Bareilly Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612133)	Multi-States (Rajasthan, Uttar Pradesh)	12/2023 (12/2023)	12/2025 (06/2026)	2056 (2056)	1603.68	64
230	Transmission System for evacuation of Power from Rajasthan REZ Ph-IV [Part-4 3.5 GW] Part A [SPV name POWERGRID Ghiror Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616670)	Multi-States (Rajasthan, Uttar Pradesh)	12/2024 (12/2024)	12/2026 (03/2027)	5846 (5846)	566.68	11
231	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan[8.1 GW] under phase-II- Part E (Power Grid Corporation of India Limited [POWERGRID]) (611659)	Rajasthan	03/2023 (03/2023)	09/2024 (12/2025)	1433.28 (1433)	1418.67	98
232	Transmission System for Evacuation of Power from REZ in Rajasthan 20GW under Phase III- Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (611947)	Rajasthan	11/2023 (11/2023)	06/2025 (03/2026)	428.3 (428.3)	308.38	80
233	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part H (Power Grid Corporation of India Limited [POWERGRID]) (611948)	Rajasthan	10/2023 (10/2023)	04/2025 (01/2026)	2211.29 (2211.29)	1975.34	92
234	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part C1 (Power Grid Corporation of India Limited [POWERGRID]) (611949)	Rajasthan	10/2023 (10/2023)	04/2025 (03/2026)	1796.02 (1796.02)	1580.49	92
235	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part B1 (Power Grid Corporation of India Limited [POWERGRID]) (611950)	Rajasthan	09/2023 (09/2023)	04/2025 (12/2025)	2190.54 (2190.54)	2000.84	96
236	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part E1 (Power Grid Corporation of India Limited [POWERGRID]) (611951)	Rajasthan	12/2021 (08/2023)	02/2025 (12/2025)	688.74 (688.74)	668	98
237	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part A [Bikaner Neemrana Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612134)	Rajasthan	12/2023 (12/2023)	12/2025 (06/2026)	2998.34 (2998.34)	2098.83	60
238	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW][Jaisalmer/Barmer Complex] Part B [SPV Name POWERGRID Sirohi Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615332)	Rajasthan	08/2024 (08/2024)	08/2026 (12/2026)	3279 (3279)	1040.75	29
239	Transmission System Strengthening for Interconnections of Bhadla-III & Bikaner III Complex [SPV Name POWERGRID BHADLA BIKANER TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615335)	Rajasthan	08/2024 (08/2024)	08/2026 (12/2026)	1382 (1382)	201.08	12
240	Additional Transmission System for evacuation of Power from Bhadla-III PS as part of Rajasthan REZ Phase III Scheme [20 GW] [SPV Name POWERGRID Bhadla-III Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615337)	Rajasthan	08/2024 (08/2024)	02/2026 (03/2026)	369 (369)	113.89	30
241	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BARMER COMPLEX] PART F [SPV Name POWERGRID BARMER I TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615338)	Rajasthan	11/2024 (11/2024)	11/2026 (06/2027)	2735 (2735)	533.05	17
242	Augmentation at Fatehgarh-II PS, Fatehgarh-IV PS [Section-II] and Barmer-I PS [POWERGRID Fatehgarh Barmer Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617181)	Rajasthan	03/2025 (03/2025)	12/2026 (03/2027)	404 (404)	16.16	1

All Ongoing Projects							NOVEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
243	Transmission System under ISTS for evacuation of Power from Kudankulam Unit-3&4 [2x1000 MW] [SPV Name POWERGRID Kudankulam Tarnsmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616671)	Tamil Nadu	01/2025 (01/2025)	12/2026 (12/2026)	548 (548)	65.46	11
244	Transmission System for Strengthening to facilitate evacuation of power from Bhadla/Bikaner Complex (Power Grid Corporation of India Limited [POWERGRID]) (617269)	Uttar Pradesh	12/2024 (12/2024)	06/2026 (08/2026)	212.81 (212.81)	2.1	0
Total (64)					153554.68	57184.49	
Ministry of Housing & Urban Affairs							
Construction							
245	Construction of One Tower of Office Complex and another Tower of Residential quarters consisting of 10Nos. Type-V, 10Nos. Type-VI & 1No.Type-VII Quarters i/c internal water supply, sanitary installation and all development and bulk services, Horticulture works on EPC Mode-I basis i/c comprehensive operation and maintenance of Civil, E&M services for 7 years after completion of original construction work for Ranga Reddy, Secunderabad, Medchal, Audittl, Audit-II Commissionerates of Central Tax at Khajaguda, Serilingampally, Hyderabad. (Central Public Works Department - CPWD) (617412)	Telangana	03/2024 (11/2024)	09/2027 (-)	644 (644)	108.53	9
Total (1)					644	108.53	
Inland Waterways							
246	Chennai Metro Rail Phase-II Development Project (Chennai Metro Rail Limited [CMRL]) (702668)	Tamil Nadu	10/2024 (11/2020)	08/2029 (-)	63246 (63246)	29336	47
Total (1)					63246	29336	
Real Estate							
247	Integrated Command control Center [ICCC] - Construction and Development of Integrated Command Control Center with Security, Surveillance, ITMS, Connecting Port, Ship Service, Smart Solid Waste Management, Smart Public Transport System (ministry of housing and urban affairs) (707229)	Andaman & Nicobar	07/2021 (11/2021)	05/2023 (-)	209.88 (209.88)	0	70
248	Redevelopment of Seven General Pool Residential Accommodation [GPRA] Colonies in Delhi (National Buildings Construction Corporation [NBCC]) (400188)	Delhi	07/2016 (05/2018)	12/2025 (12/2025)	32850 (32850)	0	0
249	Rehabilitation in Junavadaj Area Smart City Project (ministry of housing and urban affairs) (701719)	Gujarat	02/2016 (06/2016)	07/2022 (-)	539 (539)	39.63	50
250	Green Building Development Project (ministry of housing and urban affairs) (701766)	Uttarakhand	11/2019 (08/2019)	11/2023 (-)	150.97 (150.97)	18.95	31
Total (4)					33749.85	58.58	
Urban Public Transport							
251	Patna Metro Rail Project (Patna Metro Rail Corporation Ltd. [PMRCL]) (702627)	Bihar	02/2019 (02/2019)	02/2024 (06/2027)	13365.77 (13365.8)	4670.21	48
252	Delhi Metro Rail Phase-IV [2 Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (617207)	Delhi	03/2024 (03/2024)	03/2029 (-)	8399.81 (8399.81)	55.92	0
253	DMRTS Phase - IV [3 Priority Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (702632)	Delhi	07/2019 (07/2019)	03/2025 (03/2026)	24948.65 (24948.7)	18022.09	73
254	Surat Metro Rail Project (Gujarat Metro Rail Corporation Limited [GMRCL]) (702630)	Gujarat	03/2019 (04/2019)	03/2024 (06/2026)	12020.32 (12020.3)	8040.59	73
255	Ahmedabad Metro Rail Project, Phase-II (Gujarat Metro Rail Corporation Limited [GMRCL]) (702631)	Gujarat	03/2019 (03/2019)	03/2024 (12/2025)	5384.17 (5384.17)	4332.87	93
256	Ahmedabad Metro Rail Project [Phase-I] (Gujarat Metro Rail Corporation Limited [GMRCL]) (702639)	Gujarat	11/2014 (02/2015)	03/2018 (01/2026)	10773 (12924.5)	12216.37	99
257	Construction of Bangalore Metro Rail Project Phase 2. (Bengaluru Metro Rail) (702635)	Karnataka	02/2014 (02/2016)	03/2021 (09/2026)	26405.14 (30695.1)	29667.97	95
258	Construction Bangalore Metro Rail Project Phase-2A & 2B (Bengaluru Metro Rail) (702665)	Karnataka	06/2021 (01/2019)	06/2026 (06/2026)	14788.1 (14788.1)	9048.22	59
259	Kochi Metro Rail Phase 2 Development Project (CSPCC Projects) (702664)	Kerala	11/2022 (11/2022)	11/2026 (11/2026)	1957.05 (1957.05)	477.04	21
260	Bhopal Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702625)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (06/2028)	6941.4 (6941.4)	3715.92	49
261	Indore Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702626)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (12/2028)	7500.8 (7500.8)	4293.14	58
262	PCMC To Nigdi- Extension Of North South Corridor Of Phase-1 (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617225)	Maharashtra	10/2023 (10/2023)	01/2027 (-)	910.18 (910.18)	167.3	28
263	Pune Metro Phase-1 Extension line towards south from Swargate to Katraj (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617226)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	2954.53 (2954.53)	23.12	4
264	Thane Integral Ring Metro Rail Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617327)	Maharashtra	09/2024 (09/2024)	09/2029 (-)	12200.1 (12200.1)	8.7	4
265	Pune Metro Rail Project Phase-2 Corridor 2A Vanaz to Chandani Chowk and Corridor 2B Ramwadi to Wagholi/Vitthalwadi (Maharashtra Metro Rail Corporation Limited [MMRCL]) (618971)	Maharashtra	07/2025 (07/2025)	07/2029 (-)	3626.24 (3626.24)	0.41	0

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
266	New Suburba Station Development Project (<i>Ministry of Housing and Urban Affairs</i>) (701745)	Maharashtra	04/2018 (03/2019)	07/2022 (-)	262.76 (262.76)	17.62	6
267	Kalyan Station Precinct Imporvement Project (<i>Ministry of Housing and Urban Affairs</i>) (701991)	Maharashtra	04/2018 (07/2020)	07/2023 (-)	600 (600)	272.42	70
268	Mumbai Metro Line 3 (<i>Mumbai Metro Rail Corporation Limited [MMRC]</i>) (702637)	Maharashtra	07/2013 (06/2016)	03/2023 (08/2025)	23136 (37276)	32562.27	96
269	Nagpur Metro Rail Phase II Development Project (<i>Maharashtra Metro Rail Corporation Limited [MMRCL]</i>) (702658)	Maharashtra	12/2022 (12/2022)	12/2027 (-)	6708 (6708)	1346.18	30
270	Delhi Metro Rail Phase-IV [Rithala - Kundli Corridor] (<i>Delhi Metro Rail Corporation Limited [DMRC]</i>) (617206)	Multi-States (Delhi, Haryana)	01/2025 (01/2025)	01/2029 (-)	6230.99 (6230.99)	72.41	0
271	Delhi-Ghaziabad-Meerut Regional Rapid Transit System [RRTS] corridor (<i>National Capital Region Transport Corporation [NCRTC]</i>) (702633)	Multi-States (Delhi, Uttar Pradesh)	03/2019 (03/2019)	06/2025 (12/2025)	30274 (30274)	27060.65	96
272	Kanpur Metro Rail Project (<i>Uttar Pradesh metro rail corporation [UPMRC]</i>) (702628)	Uttar Pradesh	05/2019 (11/2019)	05/2024 (03/2027)	11076.48 (11076.5)	9084.56	76
273	Agra Metro Rail Project (<i>Uttar Pradesh metro rail corporation [UPMRC]</i>) (702629)	Uttar Pradesh	05/2019 (12/2020)	05/2024 (06/2027)	8379.62 (8379.62)	6059.58	64
Total (23)					238843.11	171215.56	
Waste & Water							
274	ESR - 8 nos., distribution system - 216 Km, new house service connections - 38760 nos. upgrading of feeder mains, pumping station etc. - Phase II (<i>Ministry of Housing & Urban Affairs</i>) (702674)	Andhra Pradesh	02/2017 (07/2018)	03/2023 (01/2026)	172.22 (172.22)	88.86	82
275	Muzaffarpur Storm Water Drainage Phase-I Project (<i>Ministry of Housing & Urban Affairs</i>) (702699)	Bihar	11/2016 (02/2019)	10/2023 (01/2026)	158.78 (158.78)	60.5	83
276	Storm water drainag Development Project (<i>Ministry of Housing and Urban Affairs</i>) (702355)	Dadra & Nagar Haveli and Daman & Diu	08/2020 (12/2021)	03/2024 (-)	210 (210)	0	20
277	Upgradation of Sewerage system in Gandhinagar City (<i>Ministry of Housing and Urban Affairs</i>) (707267)	Gujarat	07/2020 (03/2021)	06/2023 (-)	200 (200)	100	10
278	Sewerage Management Scheme Part-3 Implementation (<i>Ministry of Housing & Urban Affairs</i>) (702734)	Haryana	03/2017 (11/2017)	09/2023 (03/2026)	278.01 (278.01)	218.89	88
279	Sewerage Management Scheme Part-3 Implementation (<i>Ministry of Housing & Urban Affairs</i>) (702735)	Haryana	03/2017 (10/2018)	03/2023 (01/2026)	213.19 (213.19)	168.14	91
280	Dhanbad Water Supply Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702741)	Jharkhand	02/2017 (12/2018)	03/2023 (03/2026)	216.55 (216.55)	129.16	74
281	SAAP-3 Water Supply Infrastructure SAAP-3 Project (<i>Ministry of Housing & Urban Affairs</i>) (702742)	Jharkhand	02/2017 (12/2018)	10/2023 (03/2026)	159.31 (159.31)	87.5	66
282	Augmentation and Strenghthning of Urban Water Supply Phase 1 - SAAP 3 (<i>Ministry of Housing & Urban Affairs</i>) (702746)	Jharkhand	02/2017 (12/2018)	03/2023 (03/2026)	278.28 (278.28)	186.5	79
283	Belgavi Improvement in Sewerage System Project (<i>Ministry of Housing & Urban Affairs</i>) (702760)	Karnataka	12/2015 (10/2016)	07/2023 (12/2025)	162.73 (162.73)	85.71	80
284	24/7 water supply under AMRUT for Davanagere (<i>Ministry of Housing & Urban Affairs</i>) (702764)	Karnataka	11/2016 (01/2018)	03/2023 (12/2025)	174.96 (174.96)	93.18	65
285	Indore Water Supply Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702793)	Madhya Pradesh	12/2016 (11/2017)	03/2023 (12/2025)	287.17 (287.17)	252.5	99
286	Jabalpur Sewerage Management and Treatment Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702798)	Madhya Pradesh	10/2018 (12/2017)	03/2023 (12/2025)	362.31 (362.31)	322.31	93
287	Satna Sewerage Management and Treatment Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702808)	Madhya Pradesh	11/2015 (12/2016)	03/2024 (12/2025)	191.56 (215.89)	191.79	86
288	Singrauli Sewerage Management and Treatment Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702810)	Madhya Pradesh	05/2016 (11/2017)	03/2023 (12/2025)	402.01 (402.01)	357.68	90
289	Kalyan-Dombivali Water Supply Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702833)	Maharashtra	07/2016 (09/2019)	10/2023 (12/2025)	194.2 (194.2)	130.6	70
290	Mira-Bhayandar Water Supply Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702840)	Maharashtra	11/2016 (08/2018)	03/2023 (12/2025)	204.55 (204.55)	186.13	99
291	Nagpur Water Supply Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702842)	Maharashtra	12/2015 (08/2018)	03/2023 (12/2025)	273.78 (273.78)	266.11	99
292	Pune Water Supply Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702851)	Maharashtra	03/2017 (07/2017)	03/2023 (10/2025)	235.95 (235.95)	184.98	92
293	Solapur Sewerage Management Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702854)	Maharashtra	03/2017 (04/2018)	03/2023 (12/2025)	180.24 (180.24)	155.01	91
294	Jalandhar Water Supply Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (703021)	Punjab	11/2016 (08/2020)	08/2023 (03/2026)	258.53 (258.53)	161.02	58
295	Patiala Water Supply Infrastructure Part-2 Project (<i>Ministry of Housing & Urban Affairs</i>) (703057)	Punjab	11/2016 (08/2020)	10/2023 (12/2025)	287 (287)	213.64	99

All Ongoing Projects							NOVEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
296	Jaunpur Sewerage Management Infrastructure Project (Ministry of Housing & Urban Affairs) (702948)	Uttar Pradesh	03/2017 (08/2019)	06/2023 (12/2025)	235.73 (235.73)	205.84	87
297	Jhansi Water Supply Infrastructure Phase-II Project (Ministry of Housing & Urban Affairs) (702949)	Uttar Pradesh	03/2017 (06/2019)	07/2023 (12/2025)	561.74 (561.74)	485.91	93
Total (24)					5898.8	4331.96	
Ministry of Mines							
Construction							
298	Construction of Basement + Ground Floor+ 10 Storeyed building for State of the Art Director General, GSI Building at plot No.GN-40, Sector-V, Salt Lake, Kolkata (Central Public Works Department (CPWD)) (617280)	West Bengal	04/2019 (02/2020)	08/2026 (-)	255.37 (255.37)	85.9	46
Total (1)					255.37	85.9	
Metals & Mining							
299	Expansion of Malanjkhand Copper Project (Hindustan Copper Limited [HCL]) (400426)	Madhya Pradesh	09/2011 (04/2015)	04/2020 (04/2026)	1856.36 (1856.36)	947.42	82
300	Expansion of Alumina Refinery Plant with addition of 5th Stream having capacity enhancement of 1.0 Million Tonne Per Annum (National Aluminium Company Limited [NALCO]) (400141)	Odisha	04/2017 (04/2017)	12/2022 (09/2025)	4103 (5677.4)	4310.44	79
301	Pottangi Bauxite Mines Project (National Aluminium Company Limited [NALCO]) (400299)	Odisha	05/2018 (05/2018)	03/2025 (05/2026)	1381 (1960.77)	650.04	51
302	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (Ministry of Mines) (709830)	Odisha	NA (04/2017)	11/2026 (-)	355 (581)	163.55	12
303	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PANCHPATMAILI MINES (National Aluminium Company Limited [NALCO]) (709831)	Odisha	11/2017 (11/2019)	05/2025 (06/2026)	483 (483)	414.75	91
304	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (National Aluminium Company Limited [NALCO]) (709832)	Tamil Nadu	09/2017 (12/2017)	03/2025 (03/2026)	166 (166)	135	65
Total (6)					8344.36	6621.2	
Department of Higher Education							
Education							
305	Construction of Permanent Campus of Central Tribal University of Andhra Pradesh Phase-1 (Central Tribal University of Andhra Pradesh) (613008)	Andhra Pradesh	09/2019 (12/2023)	06/2027 (-)	305 (305)	19.96	32
306	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (-)	592.61 (592.61)	550.61	80
307	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (12/2025)	153.71 (153.71)	125.03	97
308	Additional Campus of NITPatna (NIT Patna) (606013)	Bihar	07/2022 (08/2022)	07/2024 (01/2026)	499.21 (499.21)	444.87	97
309	Phase B of Construction of Permanent Campus of IIT Bhilai (Indian Institute of Technology, Bhilai) (617877)	Chhattisgarh	05/2025 (06/2025)	10/2028 (-)	1188.97 (1188.97)	0	0
310	Phase 1B - Construction of Academic Block, Hostel, Residential Tower, Directors Residence and External Development works at National Institute of Technology, Delhi Campus on Engineering, Procurement and Construction basis (National Institute of Technology Delhi) (612851)	Delhi	09/2009 (11/2022)	09/2025 (01/2026)	333.49 (336.42)	296.45	97
311	Delhi University Eastern Campus at Surajmal Vihar (Delhi University) (616886)	Delhi	09/2024 (03/2025)	10/2026 (-)	373 (373)	28.63	20
312	Construction of permanent campus of Central University of Gujarat at Village kundhela, Dist. Vadodara, Gujarat. (Central University of Gujarat) (612916)	Gujarat	12/2020 (02/2021)	03/2025 (03/2026)	490.63 (490.63)	314.51	81
313	Establishment of Permanent campus Phase 1 of IIM Sirmaur (Indian Institute of Management, Sirmaur) (602099)	Himachal Pradesh	09/2018 (08/2020)	10/2023 (02/2026)	392.51 (454.78)	327.78	94
314	Hostel blocks & dining hall block (Indian Institute of Technology, Mandi) (612128)	Himachal Pradesh	03/2023 (03/2024)	03/2026 (03/2026)	166.66 (166.66)	85.92	75
315	Construction of Permanent Campus of Central University of Himachal Pradesh at Dehra, District - Kangra, [H.P.] on Engineering. Procurement and Construction [EPC Mode 1] Basis. (Central University, Himachal Pradesh) (612894)	Himachal Pradesh	03/2021 (08/2022)	11/2024 (11/2025)	251.98 (300.45)	183.56	81
316	Construction of Permanent Campus for IIM Jammu Phase-1 at Jagti, Nagrota, Jammu, J&K (Indian Institute of Management, Jammu) (602098)	Jammu and Kashmir	03/2019 (10/2020)	06/2023 (11/2025)	424.93 (500.91)	484.52	96
317	Additional Infrastructure at IISc Bangalore-RCC Monolithic for Men Hostel S14, Women Hostel S11, Postdoctoral Hostel S12 2 Block, International Hostel S 12, D&E Block S 12 2 Block FR. (IISC Bangalore) (610940)	Karnataka	08/2021 (08/2021)	03/2024 (12/2025)	420.41 (420.41)	367.76	99
318	CONSTRUCTION OF PERMANENT CAMPUS FOR IIT PALAKKAD UNDER PHASE 1A (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (606431)	Kerala	07/2017 (03/2020)	06/2022 (06/2026)	1006.45 (1217.4)	652.05	76

All Ongoing Projects							NOVEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
319	Phase B of Construction of Permanent Campus of IIT Palakkad (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (617878)	Kerala	05/2025 (01/2026)	10/2028 (-)	1527 (1527)	0	0
320	Phase III A works at IIT Indore [03 Hostels, 01 Studio Apartment, 01 Housing, Heavy & Sophisticated lab complex, Academic POD and Infrastructure for center of excellence] (Indian Institute of Technology, Indore) (611957)	Madhya Pradesh	12/2023 (04/2024)	02/2027 (-)	496.28 (496.28)	38.62	37
321	Hostel 4 -Earlier Known as Hostel 20 (Indian Institute of Technology, Bombay) (612135)	Maharashtra	09/2022 (12/2023)	09/2025 (12/2025)	182.33 (182.33)	158.23	99
322	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2009 (09/2014)	03/2022 (07/2025)	494.52 (494.52)	422.07	90
323	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876)	Mizoram	09/2009 (06/2014)	12/2029 (12/2029)	474.23 (474.23)	167.55	4
324	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	261.24	97
325	IISER BERHAMPUR (Indian Institutes of Science Education and Research, Behrampur) (610315)	Odisha	10/2018 (09/2019)	03/2021 (06/2026)	1229.32 (843.09)	835.6	97
326	Establishment of NIT Puducherry Permanent Campus [Phase-I and Phase-II] (National Institute of Technology, Puducherry) (612877)	Puducherry	09/2009 (07/2013)	12/2024 (08/2025)	618.34 (544.34)	529.94	96
327	Construction of Permanent Campus of Indian Institute of Management [IIM] Amritsar, Punjab, Phase-I (Indian intitue of Management, Amritsar) (605292)	Punjab	10/2019 (07/2020)	06/2023 (12/2025)	348.31 (348.31)	290.39	91
328	Construction of Girls Hostel 400 seater, Boys Hostel 600 seater, Academic Block, International Hostel 100 seater, VC Residence and Purchase of Equipment (Central University of Punjab) (617221)	Punjab	08/2024 (04/2025)	10/2027 (-)	210.99 (210.99)	20.89	13
329	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (03/2026)	314.06 (314.06)	238.22	85
330	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	121.56	14
331	Construction of Precast housing and hostels at IIT Hyderabad (Indian Institute of Technology, Hyderabad) (609996)	Telangana	09/2022 (11/2022)	10/2024 (01/2026)	262 (262)	194.13	80
332	Banaras Hindu University [Kayakalp of Institute of Medical Sciences] (Banaras Hindu University) (606479)	Uttar Pradesh	06/2020 (06/2020)	09/2022 (03/2026)	246 (246)	199.71	97
333	Construction & Development of Infrastructural Facilities in the main campus of NIT Uttarakhand at Sumari, Pauri Garhwal (National Institute of Technology Uttarakhand) (611963)	Uttarakhand	06/2020 (04/2024)	09/2027 (-)	650.85 (650.85)	195.52	37
334	HEFA projects on development of student hostels, playgrounds, departmental buildings, class room complex and other campus facilities in IIT Kharagpur (Indian Institute of Technology, Kharagpur) (609019)	West Bengal	06/2018 (04/2019)	03/2023 (03/2026)	500 (442)	390.6	89
Total (30)					15115.18	7945.92	
Department of Sports							
Education							
335	National Sports University [NSU], Imphal [Manipur] (Department of Sports & Youth Affairs) (400081)	Manipur	NA (01/2022)	08/2024 (11/2025)	906.47 (611.74)	559.27	95
Total (1)					906.47	559.27	
Ministry of Petroleum & Natural Gas							
Energy Storage							
336	Construction of Aviation Fuel farm Facilities at Bhogapuram Airport (Ministry of Petroleum & Natural Gas) (616235)	Andhra Pradesh	08/2024 (08/2024)	03/2026 (03/2026)	240 (240)	72.26	83
337	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 (156.36)	70.91	53
338	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 (384.04)	150.78	62
339	Capacity Augmentation of Kandla LPG Import Terminal [KLIT] from 0.6 MMTPA to 2.5 MMTPA (Ministry of Petroleum & Natural Gas) (617839)	Gujarat	05/2023 (05/2023)	07/2026 (-)	356.86 (356.86)	12.6	51
340	Setting up a common user Petroleum Terminal at Jammu, J&K for resitement of existing PSU OMC's Depots from Jammu City (Bharat Petroleum Corporation Limited [BPCL]) (400235)	Jammu and Kashmir	04/2023 (04/2023)	03/2025 (01/2026)	676.89 (715.89)	559.45	87
341	Andheri Residential Towers, Mumbai (Ministry of Petroleum & Natural Gas) (604833)	Maharashtra	06/2017 (06/2017)	05/2025 (06/2026)	281.35 (389.67)	243.11	54
342	LPG Bottling Plant at Mualkhang (Ministry of Petroleum & Natural Gas) (617829)	Mizoram	07/2024 (07/2024)	11/2027 (11/2027)	225.71 (225.71)	12.81	21
343	Srikakulam Angul Gas Pipeline Project (Ministry of Petroleum & Natural Gas) (701343)	Multi-States (Andhra Pradesh, Odisha)	09/2019 (09/2019)	07/2022 (12/2025)	2658.34 (2810)	2282.98	96

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
344	Rajasthan Refinery Project (<i>Ministry of Petroleum & Natural Gas</i>) (701263)	Multi-States (Arunachal Pradesh, Gujarat, Rajasthan)	10/2017 (10/2017)	10/2022 (03/2026)	43129 (79459)	62888.3	89
345	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (<i>Ministry of Petroleum & Natural Gas</i>) (701349)	Multi-States (Assam, Bihar, Jharkhand, Odisha, West Bengal)	01/2019 (01/2019)	07/2024 (03/2026)	10228 (11407)	10063.21	88
346	New Mundra Panipat Crude Oil Pipeline (<i>Ministry of Petroleum & Natural Gas</i>) (400078)	Multi-States (Gujarat, Haryana, Rajasthan)	12/2021 (12/2021)	12/2024 (06/2026)	9028 (9028)	7357.45	86
347	Kandla Gorakhpur LPG Pipeline (<i>Ministry of Petroleum & Natural Gas</i>) (400012)	Multi-States (Gujarat, Madhya Pradesh, Uttar Pradesh)	12/2018 (12/2018)	12/2021 (12/2025)	10088 (10088)	8135.69	93
348	Multi Product Pipeline from Irugur to Devangonhi (<i>Department of Water Resources, River Development & GR</i>) (400301)	Multi-States (Karnataka, Tamil Nadu)	11/2012 (11/2012)	02/2017 (09/2026)	678 (1732)	838.07	74
349	Petrochemical evacuation marketing terminal at Barmer, Rajasthan (<i>Hindustan Petroleum Corporation Limited [HPCL]</i>) (709759)	Rajasthan	12/2023 (12/2023)	12/2026 (12/2026)	461.05 (461.05)	153.07	67
350	Laying of POL Pipelines in Common Corridor for proposed grass root terminal at Vallur [Chennai] (<i>Ministry of Petroleum & Natural Gas</i>) (400043)	Tamil Nadu	01/2022 (01/2022)	05/2026 (05/2026)	829 (829)	338.15	67
351	Grass root POL Terminal at Vallur, Chennai (<i>Indian Oil Corporation Limited [IOCL]</i>) (400077)	Tamil Nadu	01/2022 (01/2022)	12/2024 (03/2026)	827 (887.71)	649.51	90
352	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (<i>Indian Oil Corporation Limited [IOCL]</i>) (400035)	Tripura	06/2022 (06/2022)	09/2025 (06/2026)	656 (656)	519.02	90
353	Grass-root Terminal at Mirzapur, Uttar Pradesh (<i>Ministry of Petroleum & Natural Gas</i>) (604852)	Uttar Pradesh	09/2022 (09/2022)	11/2026 (11/2026)	980.45 (980.45)	234.6	58
Total (18)					81884.05	94581.97	
Oil & Gas							
354	KG-DWN-98/2 Cluster - II Development Project - NELP Block (<i>Oil and Natural Gas Corporation Limited [ONGC]</i>) (400120)	Andhra Pradesh	03/2016 (03/2016)	06/2020 (06/2026)	34012 (34012)	32250	96
355	HP-COAT [Crude to Olefins and Aromatics Technology] demo unit at Visakh Refinery (<i>Hindustan Petroleum Corporation Limited</i>) (709752)	Andhra Pradesh	09/2021 (09/2021)	06/2024 (03/2026)	160 (220)	99.49	79
356	City Gas Distribution Project at Kurnool, Guntur & Prakasam Districts (<i>Ministry of Petroleum & Natural Gas</i>) (709766)	Andhra Pradesh	03/2022 (03/2022)	03/2030 (03/2030)	1420 (1420)	168.51	6
357	Numaligarh Refinery Expansion Project (<i>Ministry of Petroleum & Natural Gas</i>) (604791)	Assam	07/2020 (07/2020)	07/2024 (12/2025)	12366 (22494)	17836.48	79
358	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (<i>Ministry of Petroleum & Natural Gas</i>) (604863)	Assam	01/2018 (01/2018)	02/2020 (12/2025)	682.9 (726.93)	491.68	94
359	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery (<i>Ministry of Petroleum & Natural Gas</i>) (607701)	Assam	05/2021 (05/2021)	10/2023 (05/2026)	412.3 (577)	451.05	88
360	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (<i>Ministry of Petroleum & Natural Gas</i>) (616858)	Assam	12/2020 (12/2020)	03/2024 (12/2025)	430.76 (430.76)	331.99	88
361	Pipeline Rehabilitation Project, Phase-II (<i>Ministry of Petroleum & Natural Gas</i>) (617827)	Assam	12/2024 (12/2024)	12/2029 (12/2029)	680 (680)	2.24	14
362	Coke Drum Structure Package (<i>Ministry of Petroleum & Natural Gas</i>) (617836)	Assam	12/2022 (12/2022)	12/2025 (12/2025)	635.28 (635.28)	58.68	45
363	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (<i>Ministry of Petroleum & Natural Gas</i>) (709776)	Assam	04/2022 (04/2022)	09/2026 (09/2026)	277 (323.09)	190.21	70
364	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (<i>Ministry of Petroleum & Natural Gas</i>) (709779)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768 (740)	125.07	46
365	Pipeline Network Project Rudrasagar (<i>Ministry of Petroleum & Natural Gas</i>) (709847)	Assam	01/2023 (01/2023)	04/2026 (04/2026)	344.99 (344.99)	220.37	48
366	Borholla GGS Life Extension Project [BLEP] (<i>Ministry of Petroleum & Natural Gas</i>) (709850)	Assam	09/2023 (09/2023)	05/2026 (05/2026)	198.7 (198.7)	58.92	40
367	DCU Revamp Project (<i>NRL</i>) (709864)	Assam	08/2021 (08/2021)	07/2024 (06/2026)	370 (370)	271.34	66
368	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (<i>NRL</i>) (709865)	Assam	04/2023 (04/2023)	12/2024 (12/2025)	293.5 (293.5)	97.22	97
369	Setting up of LPG Plant with Rail Unloading Facility at Hathua, Dist. Gopalganj, Bihar (<i>Ministry of Petroleum & Natural Gas</i>) (617304)	Bihar	10/2023 (10/2023)	03/2027 (03/2027)	340.15 (340.15)	116.08	34
370	Barauni Refinery Capacity Expansion from 6.0 to 9.0 MMTPA (<i>Ministry of Petroleum & Natural Gas</i>) (701324)	Bihar	01/2020 (01/2020)	04/2023 (08/2026)	14810 (16724)	12327.39	88



All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
371	Installation of Bitumen Manufacturing Unit along with allied facilities at Barauni Refinery (Ministry of Petroleum & Natural Gas) (709777)	Bihar	01/2022 (01/2022)	04/2025 (10/2026)	389.35 (340)	77.72	50
372	City Gas Distribution Projects at Darbhanga, Madhubani, Supaul, Sitamarhi and Sheohar districts (Bharat Petroleum Corporation Limited [BPCL]) (709792)	Bihar	12/2022 (12/2022)	03/2030 (03/2030)	3638 (3638)	428.18	29
373	City Gas Distribution Projects at Gopalganj, Siwan, West Champaran, East Champaran and Deoria districts (Bharat Petroleum Corporation Limited [BPCL]) (709793)	Bihar	12/2022 (12/2022)	06/2030 (06/2030)	3919 (3919)	431.68	21
374	City Gas Distribution [CGD] Project in Kondagaon, Bastar, Sukma, Narayanpur, Bijapur & Dantewada GA (Ministry of Petroleum & Natural Gas) (617819)	Chhattisgarh	06/2022 (06/2022)	06/2030 (06/2030)	557.04 (557.04)	8.33	2
375	Redevelopment of Sobhasan Complex (Oil and Natural Gas Corporation Limited [ONGC]) (400087)	Gujarat	08/2021 (08/2021)	02/2026 (02/2026)	885.63 (1286.67)	876.84	80
376	Redevelopment of Santhal Field [Onshore-Mehsana Asset] (Oil and Natural Gas Corporation Limited [ONGC]) (400167)	Gujarat	02/2017 (02/2017)	03/2026 (03/2026)	1162.56 (1162.56)	1140.98	95
377	Redevelopment of Linch Field (Oil and Natural Gas Corporation Limited [ONGC]) (400169)	Gujarat	04/2021 (04/2021)	03/2025 (03/2026)	631.03 (860.04)	572.91	87
378	Petrochemical and Lube Integration Project at Gujarat Refinery (Ministry of Petroleum & Natural Gas) (701329)	Gujarat	09/2020 (09/2020)	08/2024 (06/2026)	18936 (17825)	12940.13	85
379	Installation of new Biturox Unit along with allied facilities at Gujarat Refinery (Ministry of Petroleum & Natural Gas) (709778)	Gujarat	01/2022 (01/2022)	08/2025 (09/2026)	328.29 (287)	172.32	67
380	Commercial Polymer Flooding Project in Bechraji field (Oil and Natural Gas Corporation Limited [ONGC]) (709838)	Gujarat	01/2022 (01/2022)	11/2024 (05/2027)	621.4 (739.02)	137.74	24
381	Restoration of Gas Terminal, Phase-I [Part-A], Hazira (Oil and Natural Gas Corporation Limited [ONGC]) (709840)	Gujarat	05/2022 (05/2022)	02/2025 (12/2025)	249.43 (249.43)	210.42	95
382	Old Pipe Line Replacement [OPRP] Group-A (Oil and Natural Gas Corporation Limited [ONGC]) (709841)	Gujarat	07/2021 (07/2021)	07/2025 (03/2026)	173.03 (169.84)	154.84	89
383	Kalol Redevelopment Project, Ahmedabad Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709842)	Gujarat	08/2022 (08/2022)	03/2027 (03/2027)	1487.41 (1487.41)	937.75	62
384	Revamping of SV Stations, Gas Terminal & Kribhco Terminal (Oil and Natural Gas Corporation Limited [ONGC]) (709845)	Gujarat	11/2022 (11/2022)	08/2026 (08/2026)	837.34 (837.34)	301.21	57
385	Indian Oil Technology Development and Deployment Centre at R&D Campus-II, Faridabad (Ministry of Petroleum & Natural Gas) (604853)	Haryana	06/2019 (06/2019)	12/2022 (10/2026)	2281.94 (3200)	1850.35	64
386	Poly Butadiene Rubber plant at Panipat (Indian Oil Corporation Limited [IOCL]) (611917)	Haryana	03/2022 (03/2022)	03/2025 (06/2026)	1459 (2531.44)	1418.65	77
387	Capacity Expansion of Panipat Refinery from 15 to 25 MMTPA (Ministry of Petroleum & Natural Gas) (701289)	Haryana	02/2021 (02/2021)	09/2024 (06/2026)	34627 (36225)	27366.2	91
388	Installation of Multiple Effect Evaporator [MEE] for ETP-1, 2 & 4 of Panipat Refinery and Petrochemical Complex. (Ministry of Petroleum & Natural Gas) (709783)	Haryana	12/2020 (12/2020)	06/2023 (06/2026)	165.13 (247.69)	143.78	77
389	City Gas Distribution Project at Jammu, Udhampur, Reasi, Samba and Kathua Districts (Ministry of Petroleum & Natural Gas) (709773)	Jammu and Kashmir	03/2022 (03/2022)	03/2032 (03/2032)	538 (538)	4.11	0
390	Development of Jharia CBM Block [Phase-1] (Oil and Natural Gas Corporation Limited [ONGC]) (610984)	Jharkhand	11/2019 (11/2019)	01/2024 (03/2026)	431 (431)	227	61
391	Laying of Natural Gas Pipeline from Hazaribagh to Ranchi [HRPL] (Ministry of Petroleum & Natural Gas) (709785)	Jharkhand	02/2023 (02/2023)	02/2026 (02/2026)	202.07 (202.07)	61.67	50
392	Power System Upgradation Project (Mangalore Refinery and Petrochemicals Limited) (612790)	Karnataka	10/2023 (10/2023)	11/2025 (05/2026)	385 (385)	164.35	72
393	Demo Bio-ATF Project (Ministry of Petroleum & Natural Gas) (616879)	Karnataka	03/2024 (03/2024)	01/2027 (01/2027)	364 (364)	39.1	22
394	Revamping/ Augmentation of facilities at existing port terminal at Mangalore (Ministry of Petroleum & Natural Gas) (709774)	Karnataka	01/2022 (01/2022)	12/2025 (06/2027)	463 (500.62)	290.86	75
395	Augmentation of CCKPL and IDPL Pipelines capacity along with setting up of Palakkad TOP (Ministry of Petroleum & Natural Gas) (617838)	Kerala	09/2024 (09/2024)	08/2028 (08/2028)	1130 (1130)	173.9	20
396	Replacement and Extension of Jetty Pipelines [REJP] at KR (Bharat Petroleum Corporation Limited [BPCL]) (709790)	Kerala	03/2023 (03/2023)	03/2026 (03/2026)	621.87 (621.87)	211.67	91
397	Setting up Polypropylene Unit at Kochi Refinery (Ministry of Petroleum & Natural Gas) (709799)	Kerala	12/2023 (12/2023)	10/2027 (10/2027)	4460 (4460)	351.85	18
398	C2/C3 Vijaipur Pata Pipeline (Ministry of Petroleum & Natural Gas) (617830)	Madhya Pradesh	05/2024 (05/2024)	01/2027 (-)	1792 (1792)	261.13	38



All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
399	Ethylene Cracker Project at Bina Refinery including downstream Petrochemical Plants and expansion of Refinery (Ministry of Petroleum & Natural Gas) (709798)	Madhya Pradesh	05/2023 (05/2023)	05/2028 (05/2028)	43367 (43367)	2033	17
400	Debottlenecking and Augmentation of Cryogenic facilities at Uran LPG Import Terminal (Department of Water Resources, River Development & GR) (400158)	Maharashtra	04/2021 (04/2021)	02/2024 (12/2025)	1164.69 (1629.86)	1012.27	90
401	500 KTA PDHPP Project, Usar (Ministry of Petroleum & Natural Gas) (400168)	Maharashtra	04/2021 (04/2021)	04/2025 (06/2026)	8797 (11256)	7212.88	87
402	Construction of lube oil blending plant at Rasayani (Ministry of Petroleum & Natural Gas) (610985)	Maharashtra	05/2022 (05/2022)	12/2023 (12/2025)	423.39 (526.26)	326.5	88
403	Lube Modernization & Bottom Upgradation Project at Mumbai Refinery (Ministry of Petroleum & Natural Gas) (616933)	Maharashtra	12/2024 (12/2024)	03/2028 (03/2028)	4679 (4679)	213.91	6
404	HP TDAE Unit in Mumbai Refinery (Hindustan Petroleum Corporation Limited) (709760)	Maharashtra	06/2024 (06/2024)	04/2026 (04/2026)	240 (240)	70.12	62
405	City Gas Distribution Project at Beed, Jalgaon and Jalna Districts (Ministry of Petroleum & Natural Gas) (709771)	Maharashtra	03/2022 (03/2022)	09/2031 (09/2031)	865 (865)	73.18	3
406	Construction of Additional Tankages and Allied Facilities at JNPT Terminal (Ministry of Petroleum & Natural Gas) (709780)	Maharashtra	04/2022 (04/2022)	08/2026 (08/2026)	341.43 (436.14)	289.92	55
407	ATF Pipeline from Jawaharlal Nehru Port Trust to Navi Mumbai International Airport (Indian Oil Corporation Limited [IOCL]) (709782)	Maharashtra	08/2022 (08/2022)	08/2025 (03/2026)	165 (165)	94.28	79
408	Installation of Independent De-Aromatized Solvents [DAS] production facilities at MR (Bharat Petroleum Corporation Limited [BPCL]) (709789)	Maharashtra	03/2023 (03/2023)	07/2025 (02/2026)	405 (343)	227.3	95
409	POL & LOBS Installations with Receipt Pipelines at Rasayani (Bharat Petroleum Corporation Limited [BPCL]) (709797)	Maharashtra	05/2023 (05/2023)	05/2026 (05/2026)	2585 (2585)	788.46	67
410	Part Replacement Pipeline Project [PRPP] (Oil and Natural Gas Corporation Limited [ONGC]) (709846)	Maharashtra	11/2022 (11/2022)	05/2024 (01/2026)	1219.48 (1145.1)	745	90
411	Visakh Raipur Pipeline Project (Ministry of Petroleum & Natural Gas) (616254)	Multi-States (Andhra Pradesh, Chhattisgarh, Odisha)	09/2024 (09/2024)	09/2027 (09/2027)	2212 (2212)	22.57	14
412	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura, West Bengal)	04/2020 (04/2020)	03/2024 (03/2026)	9265 (9265)	6608.95	86
413	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (Ministry of Petroleum & Natural Gas) (701350)	Multi-States (Assam, West Bengal)	06/2021 (06/2021)	12/2024 (12/2025)	860 (860)	636.92	99
414	CGD Project in Banka, Dumka, Godda, Jamtara, Pakur, Sahibganj GA ID 11A.02 (Hindustan Petroleum Corporation Limited) (709757)	Multi-States (Bihar, Jharkhand)	06/2022 (06/2022)	06/2030 (06/2030)	1377 (1377)	347.15	31
415	Mumbai Nagpur Jharsuguda Pipeline Project (Ministry of Petroleum & Natural Gas) (701354)	Multi-States (Chhattisgarh, Madhya Pradesh, Maharashtra, Odisha)	06/2020 (06/2020)	05/2023 (12/2025)	7844.25 (8255)	6710.1	97
416	Mehsana-Bhatinda & Bhatinda-Jammu Natural Gas Pipeline (Ministry of Petroleum & Natural Gas) (701330)	Multi-States (Gujarat, Haryana, Punjab, Rajasthan)	07/2011 (07/2011)	06/2024 (12/2025)	7392 (7392)	6320	90
417	Gurdaspur Jammu Pipeline (Gas Authority of India Limited [GAIL]) (612853)	Multi-States (Jammu and Kashmir, Punjab)	07/2023 (07/2023)	07/2026 (07/2026)	521.9 (521.9)	233.4	42
418	Kochi - Kootanad - Bangalore - Mangalore Pipeline Phase-II (Ministry of Petroleum & Natural Gas) (701228)	Multi-States (Karnataka, Kerala, Tamil Nadu)	06/2009 (06/2009)	12/2012 (12/2025)	2915 (5909)	4531.49	95
419	City Gas Distribution Maharashtra Natural Gas Limited (Ministry of Petroleum & Natural Gas) (701338)	Multi-States (Karnataka, Maharashtra)	01/2006 (01/2006)	06/2031 (06/2031)	5535 (5535)	4011.77	0
420	Dhamra Haldia Pipeline Project (Ministry of Petroleum & Natural Gas) (701344)	Multi-States (Odisha, West Bengal)	03/2020 (03/2020)	11/2022 (12/2025)	1030.65 (1125)	879.9	90
421	City Gas Distribution Projects at Fazilka [except area already authorized], Ganganagar and Hanumangarh districts (Bharat Petroleum Corporation Limited [BPCL]) (709794)	Multi-States (Punjab, Rajasthan)	12/2022 (12/2022)	06/2030 (06/2030)	3207 (3207)	366.34	26
422	Augmentation/ Revamping of Dimapur Depot, Dimapur (Ministry of Petroleum & Natural Gas) (709786)	Nagaland	08/2023 (08/2023)	11/2027 (11/2027)	227.62 (227.62)	11.41	26
423	Integrated Para Xylene [PX] and Purified Terephthalic Acid [PTA] Project at Paradip Refinery (Ministry of Petroleum & Natural Gas) (604859)	Odisha	07/2020 (07/2020)	01/2024 (08/2026)	13805 (11783)	8552.2	91
424	City Gas Distribution [CGD] Project in Gajapati, Kandhamal, Boudh, & Sonapur GA (Ministry of Petroleum & Natural Gas) (617818)	Odisha	02/2022 (02/2022)	02/2030 (02/2030)	514.91 (514.91)	22.2	4

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
425	CUF POL Depot at Sadashibpur [Meramundali], Odisha <i>(Ministry of Petroleum Natural Gas)</i> (709800)	Odisha	04/2021 (04/2021)	03/2026 (03/2026)	393.54 (393.54)	123.06	52
426	Life Extension of 48 well platforms of Mumbai High & Heera Fields <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (400119)	Offshore	12/2015 (12/2015)	04/2018 (03/2026)	3190.69 (3375.9)	3122.39	90
427	PRP-VIII [Group-A] <i>(Ministry of Petroleum & Natural Gas)</i> (616950)	Offshore	09/2024 (09/2024)	02/2026 (05/2026)	1486.4 (1486.4)	272.3	24
428	Daman Upside Development Project <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709839)	Offshore	06/2022 (06/2022)	10/2025 (02/2026)	4144.41 (6406.9)	4694.85	90
429	MHN TCPP PGC BGC Project [MTPBP] <i>(Ministry of Petroleum & Natural Gas)</i> (709848)	Offshore	06/2022 (06/2022)	05/2026 (05/2026)	2329.45 (2354.23)	1148.9	61
430	PRP-VIII Group B [NH & BS Asset] <i>(Ministry of Petroleum & Natural Gas)</i> (709849)	Offshore	06/2024 (06/2024)	02/2026 (05/2026)	2379.84 (3165.53)	1806.9	70
431	Integrated Development of 4 Contract Areas under DSF-II <i>(Ministry of Petroleum & Natural Gas)</i> (709851)	Offshore	05/2023 (05/2023)	04/2027 (04/2027)	6183.79 (6183.79)	697.67	24
432	2G Ethanol Biorefinery at Bathinda <i>(Hindustan Petroleum Corporation Limited [HPCL])</i> (400171)	Punjab	05/2020 (05/2020)	02/2023 (03/2026)	1421.46 (1421.46)	1207.72	95
433	City Gas Distribution Project at Pathankot District <i>(Ministry of Petroleum Natural Gas)</i> (709770)	Punjab	03/2022 (03/2022)	09/2033 (09/2033)	151 (151)	8.77	2
434	CBR 9 MMTPA Project <i>(Chennai Petroleum Corporation Limited [CPCL])</i> (604795)	Tamil Nadu	09/2021 (09/2021)	06/2025 (10/2028)	31580 (36354)	1397.8	10
435	Laying of new 28 inch Desal Water Pipeline and 10 inch Reject Water Pipeline between CPCL Manali Refinery and CPCL Desalination plant at Ennore <i>(Chennai Petroleum Corporation Limited [CPCL])</i> (709750)	Tamil Nadu	01/2024 (01/2024)	09/2025 (12/2025)	205 (205)	66.22	52
436	City Gas Distribution Projects at the Nilgiris and Erode districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709796)	Tamil Nadu	12/2022 (12/2022)	03/2030 (03/2030)	3685 (3685)	250.98	21
437	ATF Pipeline from BPCLs Malkapur POL Installation to Hyderabad International airport <i>(Ministry of Petroleum Natural Gas)</i> (617822)	Telangana	NA (03/2025)	09/2027 (-)	215 (215)	0	10
438	Creation of Gas Dehydration Facilities, Tripura Asset <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709837)	Tripura	03/2022 (03/2022)	05/2024 (05/2026)	209.33 (131.51)	70.94	66
439	PP Project, Pata <i>(Gas Authority of India Limited [GAIL])</i> (400161)	Uttar Pradesh	03/2019 (03/2019)	01/2024 (12/2025)	910.56 (1299.02)	1051	99
440	Revamping / Augmentation of Facilities at Mathura Bitumen Plant <i>(Ministry of Petroleum Natural Gas)</i> (709781)	Uttar Pradesh	04/2022 (04/2022)	06/2027 (12/2026)	260.12 (260.12)	10.38	33
441	City Gas Distribution Projects at Lakhimpur Kheri , Sitapur, Bahraich, Shravasti, Balrampur, Siddharth Nagar & Maharajganj districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709795)	Uttar Pradesh	12/2022 (12/2022)	06/2030 (06/2030)	16654 (16654)	630.34	12
442	Durgapur - Haldia Pipeline [Section-3B of JHBDPL Project] <i>(Ministry of Petroleum & Natural Gas)</i> (617302)	West Bengal	03/2017 (03/2017)	12/2020 (12/2025)	1740 (2493.15)	2304.3	91
443	Siliguri-Jhapa Pipeline Project <i>(Indian Oil Corporation Limited [IOCL])</i> (617828)	West Bengal	09/2024 (09/2024)	03/2029 (03/2029)	267 (267)	1.37	7
444	Siliguri Marketing Terminal [SMT] Capacity Augmentation Project <i>(Ministry of Petroleum & Natural Gas)</i> (617837)	West Bengal	11/2021 (11/2021)	12/2025 (12/2025)	484 (484)	282.21	79
445	Haldia Panagarh Pipeline Project <i>(Hindustan Petroleum Corporation Limited)</i> (709753)	West Bengal	11/2022 (11/2022)	11/2025 (05/2026)	1010 (1010)	699.07	87
446	CGD Project in Malda, Birbhum, Murshidabad, Dakshin Dinajpur GA ID 11A.03 <i>(Hindustan Petroleum Corporation Limited)</i> (709758)	West Bengal	06/2022 (06/2022)	06/2030 (06/2030)	2628 (2628)	348.91	30
447	City Gas Distribution Project at East Mednipore, West Mednipore & Jhargram Districts <i>(Ministry of Petroleum Natural Gas)</i> (709772)	West Bengal	03/2022 (03/2022)	06/2031 (06/2031)	609 (609)	58.09	2
448	City Gas Distribution Projects at Alipurduar and Cooch Behar <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709791)	West Bengal	12/2022 (12/2022)	03/2030 (03/2030)	1017 (1017)	199.62	40
Total (95)					355051.01	188847.4	
Ministry of Health & Family Welfare							
Healthcare							
449	Setting up IT Infrastructure including Network Security and Hosting at AIIMS, New Delhi <i>(PMSSY AND Institute of NATIONAL Importance)</i> (617882)	Delhi	09/2025 (09/2025)	09/2026 (-)	358.19 (358.19)	0	0
450	Redevelopment of Residential colonies at Ayur Vigyan Nagar and West Ansari Nagar campuses of AIIMS, New Delhi <i>(PMSSY AND Institute of NATIONAL Importance)</i> (617883)	Delhi	10/2016 (06/2022)	06/2027 (-)	4441 (4441)	24.68	61
451	AIIMS Majra Rewari Haryana <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701173)	Haryana	02/2019 (02/2019)	12/2026 (12/2026)	1299 (1646.43)	349.41	45
452	AIIMS Kashmir at Awantipora Jammu & Kashmir <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701167)	Jammu and Kashmir	01/2019 (03/2019)	12/2025 (06/2026)	1828 (2160.84)	1354.55	2

All Ongoing Projects							NOVEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
453	AIIMS Bibinagar (PMSSY AND Institute of NATIONAL Importance) (701171)	Telangana	12/2018 (07/2022)	06/2026 (06/2026)	1028 (1365.95)	818.46	85
	Total (5)				8954.19	2547.1	
	Ministry of Labour and Employment						
	Healthcare						
454	Construction of 350 beds + 50 Super Specialty beds ESIC Hospital Sheelanagar, Visakhapatnam, Andhra Pradesh (Employee's State Insurance Company [ESIC]) (612167)	Andhra Pradesh	02/2021 (04/2023)	10/2025 (01/2026)	384.27 (384.27)	105	40
455	Construction of 200 bedded ESIC Hospital with 62 Nos Staff quarters , Beltola (Employee's State Insurance Company [ESIC]) (612201)	Assam	12/2017 (10/2021)	04/2025 (02/2026)	143.23 (154.75)	101.83	94
456	C/o Construction of 200 bedded [Up-gradable to 300 bedded] ESI Hospital at Surat Gujarat. (Employee's State Insurance Company [ESIC]) (612185)	Gujarat	06/2019 (03/2021)	06/2025 (01/2026)	209.36 (209.36)	185.96	98
457	350 Bedded [Upgradable to 500 beds] ESI Hospital at Sanand (Employee's State Insurance Company [ESIC]) (612186)	Gujarat	06/2022 (04/2023)	03/2026 (05/2027)	558.12 (558.12)	60.66	8
458	Demolition, Construction and upgradation of ESI Hospital, Kalol, Gujarat from 50 beds to 150 beds. (Employee's State Insurance Company [ESIC]) (612211)	Gujarat	08/2022 (10/2023)	10/2025 (06/2026)	205.87 (205.87)	31.49	18
459	Construction of 100 bedded ESIC Hospital & 32 nos. of Staff qtrs at OMPURA J&K. (Employee's State Insurance Company [ESIC]) (612239)	Jammu and Kashmir	09/2019 (12/2021)	09/2024 (12/2025)	131.05 (164.93)	162.05	99
460	Construction of 200 bed ESI Hospital at Bommasandra, Karnataka (Employee's State Insurance Company [ESIC]) (612745)	Karnataka	02/2015 (10/2024)	01/2027 (-)	278 (278)	27.8	0
461	Construction of 100 bed ESI Hospital and Staff Quarters [32 Nos.] at Harohalli, Karnataka (Employee's State Insurance Company [ESIC]) (612748)	Karnataka	07/2019 (03/2025)	02/2027 (-)	150.92 (150.92)	0	0
462	Construction of 200 Bedded [Upgradable to 500 Bedded including 50 beds of SST] ESIC Hospital at Bibewadi, Pune (Employee's State Insurance Company [ESIC]) (612188)	Maharashtra	05/2018 (03/2023)	09/2025 (02/2026)	429.25 (429.25)	282.09	70
463	Construction of 200 Bedded ESIC Hospital at Butibori, Nagpur, Maharashtra. (Employee's State Insurance Company [ESIC]) (612213)	Maharashtra	10/2013 (08/2022)	08/2025 (09/2026)	194.93 (196.7)	114.39	62
464	Upgradation & Extension of ESIC Hospital and Construction of PG Hostel / Staff Housing for ESIC Hospital at Andheri, Mumbai (Employee's State Insurance Company [ESIC]) (616691)	Maharashtra	12/2008 (06/2009)	08/2025 (12/2025)	260.13 (260.13)	210.12	89
465	Construction of 100 Bedded ESI Hospital at Duburi, Odisha. (Employee's State Insurance Company [ESIC]) (612513)	Odisha	12/2010 (02/2025)	06/2027 (-)	164.6 (164.6)	16.4	7
466	Construction of 100 Bedded ESIC Hospital building and 32 Nos Residential Quarters at Vallam Vadangal, SIPCOT, Sriperumbudur (Employee's State Insurance Company [ESIC]) (612178)	Tamil Nadu	02/2015 (03/2023)	06/2025 (01/2026)	152.95 (177.01)	107.83	99
467	CONSTRUCTION OF 300 BEDDED HOSPITAL AT HARIDWAR (Employee's State Insurance Company [ESIC]) (612259)	Uttarakhand	02/2021 (12/2021)	10/2024 (03/2026)	102.4 (297.63)	321.82	80
	Total (14)				3365.08	1727.44	
	Ministry of Ports, Shipping and Waterways						
	Healthcare						
468	Establishment of 600 bed super specialty hospital with optional development of Medical college and further expansion on PPP basis. (Mumbai Port Trust [MPT]) (708662)	Maharashtra	08/2019 (01/2022)	06/2026 (12/2027)	693 (693)	58	11
	Total (1)				693	58	
	Inland Waterways						
469	Jal Marg Vikas Project (Inland Waterways Authority of India [IWAI]) (701565)	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	01/2018 (02/2018)	12/2023 (12/2025)	5369.18 (5061.15)	3577.42	73
470	Fairway Development in West Bengal Farakka - Kahelgaon (Inland Waterways Authority of India [IWAI]) (611142)	Offshore	01/2018 (08/2018)	07/2023 (04/2024)	177 (197)	383.41	100
	Total (2)				5546.18	3960.83	
	Shipping						
471	Development of Container Terminal at Tuna-Tekra, Deendayal Port on BOT Basis Under PPP Mode (Deendayal Port Trust) (609424)	Gujarat	10/2022 (03/2024)	03/2027 (-)	4243.64 (4243.64)	817.98	34
472	Construction of oil jetty No.8 at old kandla through internal resources (Deendayal Port Trust [DPT]) (701568)	Gujarat	02/2018 (02/2021)	02/2023 (07/2024)	100 (225.85)	186.47	90
473	Replacement and revamping of pipeline projects in oil jetty area, Kandla (Deendayal Port Trust [DPT]) (701570)	Gujarat	09/2021 (09/2021)	09/2023 (03/2025)	171 (211.61)	137.51	71
474	Mechanization of Berth No.14 for handling Containers and other cargo on DBFOT basis - Phase II (New Mangalore Port Authority) (617804)	Karnataka	12/2023 (06/2024)	03/2027 (-)	153.23 (153.23)	24	33

All Ongoing Projects

NOVEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
475	Rewas Port Project (Reliance Industries Ltd) (400382)	Maharashtra	12/2019 (01/2020)	03/2023 (-)	6000 (6000)	5999.89	88
476	Setting up of a Floating Storage and Regasification Unit [FSRU] - Mumbai (Mumbai Port Trust [MPT]) (701586)	Maharashtra	11/2020 (04/2021)	11/2026 (11/2026)	900 (900)	65	0
477	Deepening and Optimization of Inner Harbour facilities including development of Western Dock on BOT basis to handle Cape size vessels (Paradip Port Trust [PPT]) (701574)	Odisha	05/2022 (01/2023)	12/2027 (10/2028)	3004.63 (3004.63)	1277.52	50
478	Berth No. 2 [previously Berth 3] of HDC Mechanization Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701576)	West Bengal	11/2022 (03/2023)	09/2025 (01/2026)	298.26 (298.26)	457.85	99
479	Shalukkhali Liquid Cargo Handling Facility Development Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701577)	West Bengal	01/2022 (08/2022)	08/2025 (-)	253.65 (253.65)	9.28	0
Total (9)					15124.41	8975.5	
Tourism, Hospitality & Wellness							
480	National Maritime Heritage Complex [NMHC] Phase-I (Indian Port Rail & Ropeway Corporation Ltd. [IPRCL]) (707215)	Gujarat	02/2019 (01/2022)	03/2024 (09/2025)	573 (1238.05)	515.97	70
Total (1)					573	515.97	
Ministry of Steel							
Metals & Mining							
481	Capacity expansion of Deposit-14 and 14 NMZ at Kirandul (National Mineral Development Corporation Limited [NMDC]) (615202)	Chhattisgarh	08/2021 (07/2022)	12/2028 (03/2028)	1700 (1756.2)	142.16	7
Total (1)					1700	142.16	
Steel							
482	Replacement of Hot Leveller No.1 of Plate Mill at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617243)	Chhattisgarh	07/2024 (08/2024)	07/2026 (-)	198.62 (198.62)	20.98	20
483	Replacement of Converter Vessels, Trunnion Rings, Support System & Installation of Secondary Emission at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617255)	Chhattisgarh	10/2023 (12/2023)	06/2026 (-)	471.83 (471.83)	161.45	51
484	Rebuilding of Coke Oven Battery No.7 & 8 at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617256)	Chhattisgarh	11/2023 (01/2024)	10/2025 (03/2026)	884.1 (884.1)	530.05	82
485	NMDC Slurry Pipeline Project Phase-1 (National Mineral Development Corporation Limited [NMDC]) (706811)	Chhattisgarh	11/2015 (09/2020)	06/2023 (12/2025)	2907 (5427)	3243.55	90
486	SCREENING PLANT-III AT KIRANDUL (National Mineral Development Corporation Limited [NMDC]) (709826)	Chhattisgarh	NA (10/2021)	01/2026 (-)	2718.84 (2718.84)	1396.9	78
487	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (National Mineral Development Corporation Limited [NMDC]) (709827)	Chhattisgarh	NA (10/2022)	12/2025 (-)	349.75 (349.75)	299.39	94
488	New Sinter Plant at BSL, SAIL (Steel Authority of India Limited [SAIL]) (400174)	Jharkhand	03/2015 (10/2015)	10/2017 (06/2027)	1034.01 (1752.3)	885.61	53
489	Replacement of existing Grinders in CRM-I & II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617249)	Jharkhand	01/2025 (02/2025)	01/2027 (-)	211.94 (211.94)	20.54	16
490	Secondary Emission Control in Converters of SMS-II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617250)	Jharkhand	01/2025 (02/2025)	10/2026 (-)	207.13 (207.13)	15.76	11
491	Revamping of old sub-systems of Blast Furnace 3 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617253)	Jharkhand	08/2023 (03/2023)	07/2025 (11/2025)	513.82 (513.82)	310.02	76
492	Replacement of remaining 04 sets of Battery Cyclones with 04 Nos. of ESPs in Sinter Plant-1 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617254)	Jharkhand	03/2024 (04/2024)	06/2026 (-)	260.37 (260.37)	58.19	25
493	Rebuilding of Coke Oven Battery No.6 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617257)	Jharkhand	11/2023 (12/2023)	11/2026 (-)	627.31 (627.31)	169.38	49
494	Construction of Screening Plant-II for Donimalai and Kumaraswamy Iron Ore Mining Complex of NMDC Limited at Ballari Dt, Karnataka. (National Mineral Development Corporation Limited [NMDC]) (400121)	Karnataka	11/2014 (06/2024)	08/2026 (-)	1043.63 (1043.63)	320.8	40
495	Installation of 4th Slab Caster along with its Auxiliaries and a New Ladle Furnace in SMS-II at Rourkela Steel Plant (Steel Authority of India Limited [SAIL]) (400065)	Odisha	01/2022 (02/2022)	05/2025 (09/2025)	1105.23 (1105.23)	790.11	100
496	Rebuilding of COB 4 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (612781)	West Bengal	09/2023 (09/2023)	12/2026 (-)	916.78 (916.78)	154.56	21
497	Installation of New Bar Mill at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617242)	West Bengal	07/2024 (08/2024)	06/2027 (-)	2115.44 (2115.44)	257.17	37
498	Up-gradation of Blast Furnace No. 3 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617246)	West Bengal	09/2024 (08/2024)	06/2026 (-)	758.09 (758.09)	95.38	8
499	Third Ladle Furnace in Secondary Refinery Unit at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617248)	West Bengal	11/2024 (12/2024)	07/2026 (-)	227.96 (227.96)	27.2	34
500	Revamping of Air Pollution Control Systems of SP-1 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617251)	West Bengal	07/2024 (12/2024)	05/2026 (-)	196.4 (196.4)	11.72	6

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
501	Stamp Charge Battery No.12 Battery Proper at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617338)	West Bengal	01/2025 (02/2025)	07/2028 (-)	2518.39 (2518.39)	210.51	8
Total (20)					19266.64	8979.27	
Ministry of Railways							
Railways							
502	Nadikudi - Srikalahasti New Line (South Central Railway [SCR] - II) (400298)	Andhra Pradesh	03/2012 (12/2016)	05/2027 (03/2028)	2312 (5932)	2421.35	54
503	Malugur- Palasamudram New Line Project [17.975 Km] (South Western Railway [SWR] - II) (611615)	Andhra Pradesh	09/2022 (07/2026)	11/2027 (12/2027)	342 (342)	0	0
504	GOOTY-PENDEKALLU DOUBLING 29.225 Km (South Central Railway [SCR] - II) (611752)	Andhra Pradesh	03/2023 (06/2023)	03/2027 (03/2027)	351.83 (351.83)	18	25
505	GUNTAKAL WEST-MALLAPPA GATE RAIL OVER RAIL - ROR TRACK (South Central Railway [SCR] - II) (611754)	Andhra Pradesh	07/2023 (07/2023)	07/2026 (-)	293.3 (293.3)	0	0
506	Kurnool - Setting up facilities for coach midlife rehabilitation workshop (WPO/Patna) (611927)	Andhra Pradesh	01/2014 (10/2017)	12/2023 (-)	560.72 (560.72)	276.66	65
507	Flyover between Pendurthi and Simhachalam North to avoid surface crossing at Simhachalam 7.135 km PB 73 of 2023 24 NR (East Coast Railway [ECOR] - II) (612827)	Andhra Pradesh	04/2023 (05/2024)	04/2027 (-)	183.65 (183.65)	5.15	11
508	3rd & 4th line between Vadlapudi -Gate Jn. cabin and Tie line between Gate Junction to Gangavaram port (East Coast Railway [ECOR] - II) (616697)	Andhra Pradesh	04/2023 (03/2024)	06/2026 (-)	154.28 (154.28)	20.58	32
509	Tiupati Katpadi 104.39 kms (South Central Railway [SCR] - II) (617210)	Andhra Pradesh	04/2025 (04/2025)	03/2029 (-)	1215.56 (1215.56)	0.1	0
510	3rd Line between Gudur Renigunta 83.17 Km (South Central Railway [SCR] - II) (617216)	Andhra Pradesh	10/2024 (10/2024)	03/2027 (-)	877.34 (877.34)	29.04	0
511	Kurnool Coach Midlife Rehabilitation Project (WPO/Patna) (705253)	Andhra Pradesh	05/2016 (07/2014)	12/2020 (-)	563 (563)	120	0
512	Kotapalli - Narasapur New Line (South Central Railway [SCR] - II) (705436)	Andhra Pradesh	03/2009 (09/2013)	03/2028 (03/2028)	2501 (2501)	1320.81	29
513	Guntur-Guntakal Doubling Project (South Central Railway [SCR] - II) (705633)	Andhra Pradesh	03/2017 (11/2017)	12/2025 (12/2026)	3733 (4295)	4475.93	93
514	Vijaywada-Gudur 3rd Line (RVNL - II) (705648)	Andhra Pradesh	08/2016 (04/2018)	11/2024 (12/2025)	6654 (6654)	5922	90
515	Penukonda - Dharmavaram Doubling Project [41.5 Km] (South Western Railway [SWR] - II) (705789)	Andhra Pradesh	06/2018 (12/2018)	03/2026 (03/2026)	307.66 (307.66)	276.34	85
516	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3729.89	93
517	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
518	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project (GM/C/ NFR) (706940)	Assam	09/2018 (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
519	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942)	Assam	09/2018 (01/2022)	05/2024 (-)	237.52 (237.52)	0	0
520	Sakri -Hasanpur [via Harnagar - Kusheshwar Asthan] New Railway line (East Central Railway [ECR] - I) (400254)	Bihar	12/2023 (08/1997)	12/2024 (03/2027)	735.2 (735.2)	588.66	84
521	Construction of Bulb line at Nabinagar Ankorah of East Central Railway (East Central Railway [ECR] - I) (617231)	Bihar	06/2024 (06/2024)	06/2028 (-)	611.74 (611.74)	0	0
522	Jhajha-Batai New Line Project (East Central Railway [ECR] - I) (617373)	Bihar	03/2023 (03/2023)	03/2027 (-)	588.18 (588.18)	3.05	0
523	Bakhtiyarpur-Rajgir-Tilaiya [Single line section]104km (East Central Railway (ECR) - II) (617824)	Bihar	10/2025 (10/2025)	10/2029 (-)	2017.38 (2017.38)	0	0
524	Khagaria-Kusheshwar Asthan [42Km] new line project (East Central Railway [ECR] - I) (705364)	Bihar	04/2019 (12/1998)	12/2024 (03/2027)	614 (1384.16)	487.99	55
525	Hajipur-Sagauli New line (East Central Railway [ECR] - I) (705366)	Bihar	10/2007 (10/2004)	03/2020 (12/2026)	2067 (2087)	2015.02	74
526	Araria Supaul New BG Line (East Central Railway [ECR] - I) (705368)	Bihar	06/2018 (03/2009)	03/2024 (01/2027)	1605 (2514)	1604.02	40
527	Fatuha-Islampur incl. MM for extn.of NL from Neora to Daniawan , Daniawan to Biharsharif, Biharsharif to Barbigha , Barbigha to Shekhpura (East Central Railway [ECR] - I) (705373)	Bihar	08/2002 (03/2002)	03/2023 (08/2025)	1473 (2882)	2538.21	95
528	Jogbani-Biratnagar New Rail Line project (Indian Railway Construction International Limited [IRCON]) (705450)	Bihar	06/2010 (01/2011)	03/2022 (12/2026)	402 (486)	367.54	86

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
529	Samastipur-Darbhanga Doubling Railway Project (East Central Railway [ECR] - I) (705526)	Bihar	11/2015 (12/2015)	03/2025 (10/2025)	519 (519)	380.73	85
530	Sagauli-Valmiknagar (East Central Railway [ECR] - I) (705527)	Bihar	03/2018 (03/2017)	12/2025 (12/2025)	1216 (2222)	2074.54	92
531	Muzaffarpur-Sugauli (East Central Railway [ECR] - I) (705528)	Bihar	03/2018 (03/2017)	06/2024 (02/2026)	1586 (1586)	1471.11	99
532	Rampur Dumra-Tal-Rajendrapul Additional Bridge and Railway Line Doubling (Indian Railway Construction International Limited [IRCON]) (706759)	Bihar	03/2016 (05/2017)	12/2024 (12/2025)	2373.64 (1700.24)	1427.78	97
533	Barauni-Bachwara [16 km] - 3rd & 4th line incl. Barauni yard remodelling [32 km] (East Central Railway [ECR] - I) (706860)	Bihar	10/2022 (08/2025)	08/2025 (10/2026)	645 (645)	27.98	55
534	JHAJHA - BATIA (East Central Railway [ECR] - I) (900874)	Bihar	03/2023 (03/2023)	03/2028 (01/2030)	588.18 (588.18)	0.82	0
535	Kharsia-Dharamjaygarh with Spur line [East Corridor-Phase 1] (Indian Railway Construction International Limited [IRCON]) (400220)	Chhattisgarh	03/2016 (01/2014)	09/2018 (03/2026)	3055 (3438)	2624.33	94
536	Doubling of Kirandul-Jagdalpur Line [150 km] (East Coast Railway [ECOR] - II) (400291)	Chhattisgarh	02/2013 (03/2013)	03/2020 (12/2025)	1589 (1798)	1576.81	94
537	Gauge Conversion of Kendri-Dhamtari including Abhanpur - Rajim Branch line 67.20 Kms - 2nd Material Modification to Raipur Titlagarh doubling. (SECR) (602792)	Chhattisgarh	07/2011 (05/2021)	02/2025 (03/2026)	1171 (1171)	377.41	100
538	4th line between Nipania Bhatapara 14.4 Km (South East Central Railway [SECR] - II) (612815)	Chhattisgarh	12/2022 (05/2024)	03/2027 (-)	170.49 (170.49)	1.34	5
539	Dharamjaigarh-Korba 63 km (CERL) (613003)	Chhattisgarh	08/2023 (07/2022)	08/2026 (-)	1686.26 (1686.26)	288.83	18.5
540	KHARSIA- NAYA RAIPUR-PARMALKASA 5th and 6th Line [278KM] (CAO/C/SECR) (617200)	Chhattisgarh	04/2025 (04/2025)	03/2031 (-)	7853.84 (7853.84)	0	0
541	Dallirajhara - Rowghat New Rail Line Project, Phase-I (Rail Vikas Nigam Limited) (617374)	Chhattisgarh	NA (11/2009)	03/2025 (02/2026)	1516.45 (1881.26)	2053.12	94
542	Dallirajhra- Rowghat New Railway Line - Phase I [95 km] (Rail Vikas Nigam Limited) (705433)	Chhattisgarh	07/2009 (12/2009)	09/2025 (12/2025)	1628 (1628)	1440.85	82
543	Gevra Road-Pendra Road New Railway Line [135 km] (Indian Railway Construction International Limited [IRCON]) (705444)	Chhattisgarh	04/2014 (04/2014)	03/2022 (12/2025)	4970 (7448.52)	4696.68	75
544	Boridand - Ambikapur Doubling Line Project (South East Central Railway [SECR] - II) (706854)	Chhattisgarh	06/2022 (04/2022)	06/2030 (06/2030)	1376 (1576.72)	139.49	21
545	4TH LINE - BHATAPARA-HATHBAND [8.8 KM] [PB-72/NR/2022-23] (SECR) (709815)	Chhattisgarh	09/2022 (05/2024)	01/2027 (12/2027)	177.03 (177.03)	0	3
546	4TH LINE - BHILAI-BHILAI NAGAR [8.8 KM] [PB-72/NR/2022-23] (SECR) (709816)	Chhattisgarh	09/2022 (05/2024)	02/2027 (02/2027)	177.34 (177.34)	1.64	6
547	4TH LINE - DADHAPARA-BELHA [9.2 KM] [PB-72/NR/2022-23] (SECR) (709817)	Chhattisgarh	09/2022 (05/2024)	11/2026 (11/2026)	169.06 (169.06)	18.37	60
548	4TH LINE RAJNANDGAON-DONGARHGARH [31.2 KM] [PB-72/NR/2022-23] (SECR) (709818)	Chhattisgarh	09/2022 (05/2024)	01/2027 (01/2027)	328.34 (328.34)	57.3	27
549	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (709819)	Chhattisgarh	09/2022 (05/2025)	12/2026 (12/2026)	167.64 (167.64)	0.11	4
550	Redevelopment of New Delhi Railway Station and construction of associated infrastructure (Rail Land Development Authority) (613785)	Delhi	01/2023 (06/2024)	12/2028 (-)	4744 (4744)	129.61	1
551	Development of New Bijwasan Railway Terminal (Northern Railways) (617379)	Delhi	02/2008 (03/2013)	03/2020 (12/2025)	446.21 (446.21)	521.74	80
552	North Region Video Surveillance Project (RCIL) (705298)	Delhi	06/2020 (04/2023)	03/2024 (-)	274.39 (274.39)	0	0
553	Anand Vihar-Tilak Bridge 3rd & 4th line (CAO/C/NR) (705583)	Delhi	03/2013 (03/2013)	03/2023 (12/2027)	667 (667)	289.26	63
554	Provision of Work-site Tampers [WST] Railway Project (EDTK[MC]/RB) (705694)	Delhi	01/2016 (01/2016)	12/2023 (01/2026)	187.72 (187.72)	141.91	100
555	WST Machine Procurement Project (EDTK[MC]/RB) (705708)	Delhi	06/2018 (06/2018)	03/2024 (12/2027)	176 (176)	0	0
556	PCT Machine Procurement Project (EDTK[MC]/RB) (705710)	Delhi	04/2019 (04/2019)	04/2024 (06/2027)	336 (336)	74.32	85
557	RBMV Machine Procurement Project (EDTK[MC]/RB) (705712)	Delhi	10/2019 (10/2019)	06/2024 (12/2027)	480 (480)	20.65	27
558	SRGM Machine Procurement Project (EDTK[MC]/RB) (705717)	Delhi	10/2019 (10/2019)	12/2023 (03/2026)	440 (440)	390.03	90

All Ongoing Projects

NOVEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
559	WST Machine Procurement Project (EDTK[MC]/RB) (705720)	Delhi	12/2019 (12/2019)	04/2024 (12/2026)	384 (384)	0	0
560	DTS Machine Procurement Project (EDTK[MC]/RB) (705721)	Delhi	12/2019 (12/2019)	12/2024 (12/2030)	447.6 (447.6)	0	0
561	BRM Machine Procurement Project (EDTK[MC]/RB) (705722)	Delhi	09/2019 (09/2019)	06/2024 (12/2027)	210 (210)	0.02	0
562	Track Machine Procurement Project (EDTK[MC]/RB) (705726)	Delhi	04/2020 (04/2020)	03/2025 (01/2028)	6339 (6339)	4201.26	62
563	Kosamba Umarpada 70 Km (PCE/WR) (611918)	Gujarat	07/2023 (07/2022)	03/2027 (-)	468 (468)	20.28	8
564	Adraj Moti Vijapur 40 Kms (Western Railway (WR) - II) (611937)	Gujarat	05/2022 (05/2022)	05/2026 (12/2025)	417.53 (417.53)	502.23	90
565	New Broad Gauge line between Naliya to Jakhau Port (Western Railway (WR) - II) (611943)	Gujarat	02/2023 (02/2023)	01/2028 (01/2028)	410.26 (410.26)	7	5
566	Quadrupling between Gandhidham Adipur with Y connection at Adipur for providing direct entry towards Mundra Port and Bhuj and high level platform at Gopalpur 11Kms (Western Railway (WR) - II) (611944)	Gujarat	02/2023 (02/2023)	03/2026 (01/2026)	152.44 (152.44)	102.65	85
567	Petlad Bhadran 23 Kms (Western Railway) (611945)	Gujarat	05/2022 (05/2022)	05/2030 (05/2030)	307.11 (307.11)	13.59	17
568	Samlaya Timba Road 54 km (PCE/WR) (611970)	Gujarat	02/2023 (02/2023)	03/2030 (03/2030)	670.17 (670.17)	45.02	12
569	Samni Jambusar 24 km (PCE/WR) (611971)	Gujarat	05/2022 (05/2022)	03/2030 (03/2030)	350 (349.93)	67.73	31
570	Western Railway Samakhiali Gandhidham Quadrupiling 53 Kms (Western Railway (WR) - II) (611974)	Gujarat	08/2023 (08/2023)	12/2026 (06/2027)	1430 (1430)	230.24	21
571	Dahod Creation of Infrastructure facilities for 9000 HP Electric locomotives Manufacturing at (PCE/WR) (611977)	Gujarat	05/2022 (02/2023)	02/2025 (-)	487 (487)	108.69	0
572	Dahod Rolling Stock Workshop Provision of Infrastructure for CBS at (PCE/WR) (611978)	Gujarat	11/2022 (03/2023)	03/2025 (-)	158 (158)	47.31	0
573	Sabarmati Setting up of Maintenance Facilities for Train Sets Phase ii (Western Railway (WR) - II) (611979)	Gujarat	01/2023 (04/2023)	06/2025 (03/2026)	250 (250)	103.21	60
574	4th LINE BETWEEN BAREJADI NANDEJ-SANAND-AHMEDABAD BYPASS (Western Railway (WR) - II) (612072)	Gujarat	02/2023 (02/2023)	03/2027 (07/2028)	961.67 (961.67)	359.61	18
575	Redevelopment of Ahmedabad railway station and associated infrastructure on engineering, procurement and construction mode (Rail Land Development Authority) (613786)	Gujarat	01/2023 (11/2023)	03/2028 (-)	2379 (2379)	753.62	22
576	Miyagam-Karjan-Dabhoi-Samlaya [GC] (Western Railway [WR] - II) (705458)	Gujarat	01/2017 (01/2017)	03/2021 (12/2026)	483.88 (1039.13)	621.61	41
577	Modasa-Shamlaji Road Railway Line Project (Western Railway (WR) - II) (706757)	Gujarat	09/2012 (04/2008)	03/2025 (03/2027)	262 (262)	337.67	63
578	Rajkot - Kanalus Doubling Project [111.2 Kms] (Western Railway (WR) - II) (706763)	Gujarat	10/2021 (12/2021)	10/2026 (10/2026)	1080.58 (1080.58)	829.85	80
579	NADIAD-PETLAD [37.26 KM] (Railway) (709812)	Gujarat	05/2022 (10/2023)	06/2030 (06/2030)	461.91 (461.91)	93.31	8
580	NEW BG LINE INTERSECTION [5 NOS] BETWEEN GERATPUR-SANAND & BOTAD-AHMEDABAD [16.51 KM] (Western Railway (WR) - II) (709813)	Gujarat	10/2022 (07/2025)	06/2028 (10/2027)	437.21 (437.21)	19.37	18
581	Bhiwani - Dobh Bahali Doubling Project [42.30 Km] (North Western Railway [NWR]) (611884)	Haryana	02/2023 (02/2023)	02/2028 (02/2028)	471 (471)	219.67	66
582	Doubling between Pradhankunta-Patherih-Bhjudih of East Central Railway (East Central Railway [ECR] - I) (617372)	Jharkhand	11/2022 (11/2022)	12/2025 (-)	349.22 (349.22)	108.89	70
583	Koderma-Arigada Doubling 133.38 Km of East Central Railway (East Central Railway [ECR] - I) (617832)	Jharkhand	06/2025 (06/2025)	12/2029 (-)	2887.11 (2887.11)	0	0
584	Gomoh - Flyover for DN trains (East Central Railway [ECR] - I) (705765)	Jharkhand	01/2018 (01/2018)	03/2026 (03/2026)	686 (686)	578.93	59
585	Lodhma - Piska - Link Line bypassing Hatia/Ranchi with Y connection (South Eastern Railway [SER] - I) (705785)	Jharkhand	08/2021 (03/2019)	06/2026 (05/2027)	473 (473)	288.72	5
586	Pradhan Kuntha Jn Line Doubling Project (East Central Railway [ECR] - I) (706837)	Jharkhand	11/2022 (11/2022)	11/2027 (11/2027)	349.22 (349.22)	108.89	62
587	Construction of New BG line between Hassan to Belur [27 Km] (South Western Railway [SWR] - II) (400023)	Karnataka	03/2019 (12/2025)	04/2028 (04/2027)	749 (749)	0	0
588	Yeshvanthpur - Channasandra Doubling Project [21.70 Km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703585)	Karnataka	04/2019 (10/2019)	03/2024 (03/2026)	314.1 (683.57)	152.31	53

All Ongoing Projects

NOVEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
589	New Railway Line between Ginigera and Raichur [165.57 km] (South Western Railway [SWR] - II) (705434)	Karnataka	03/2008 (05/2009)	03/2019 (03/2027)	2565 (3034.98)	2108.54	66
590	Gadag-Wadi New Railway Line [257 km] (South Western Railway [SWR] - II) (705490)	Karnataka	04/2013 (08/2017)	03/2027 (12/2027)	2842 (6700)	1419.19	30
591	Kadur - Chickamagalur - Sakleshpur [93km] (South Western Railway [SWR] - II) (705492)	Karnataka	01/2014 (11/2016)	06/2025 (12/2025)	825 (825)	705.64	83
592	Bagalkot-Kudachi New Railway Line [142 km] (South Western Railway [SWR] - II) (705495)	Karnataka	10/2013 (11/2012)	03/2027 (01/2027)	1378 (1649)	729.34	35
593	Tumkur-Chitradurga-Davangere New Rail Line Project [191 km] (South Western Railway [SWR] - II) (705496)	Karnataka	10/2013 (01/2017)	03/2019 (12/2027)	1876 (1876)	461.98	14
594	Bangalore-Whitefield-Bangalore City-Krishnarajapuram [23.08 km] - Quadrupling (South Western Railway [SWR] - II) (705663)	Karnataka	02/2018 (06/2022)	02/2026 (02/2026)	493 (493)	252.45	82
595	SHIMOGA - SHIKARIPURA - RANEBENNUR [96 Km] (South Western Railway [SWR] - II) (705761)	Karnataka	09/2019 (02/2023)	12/2027 (06/2028)	1454 (1454)	72.26	11
596	Belgaum-Dharwad via Kittur [73.10Km] (South Western Railway [SWR] - II) (706835)	Karnataka	09/2020 (03/2025)	12/2027 (03/2029)	1591 (1591)	0.38	0
597	Kumbalam-Turavur doubling project [15.59 Km] (Ministry of Railways) (705638)	Kerala	04/2023 (04/2023)	03/2027 (03/2027)	813 (802.8)	72.62	19
598	Ernakulam-Kumbalam doubling project [7.71 Km] (SR-ERS) (705639)	Kerala	04/2023 (04/2023)	03/2028 (02/2027)	601 (595.39)	292.67	20
599	Lalitpur-Satna, Rewa-Singrauli & Mahoba-Khajuraho (North Central Railway) (705480)	Madhya Pradesh	01/2007 (03/1998)	03/2027 (12/2027)	8914 (8914)	6447.32	73
600	Katni - Bina Third Railway Line [279 km] (West Central Railway WCR I) (705651)	Madhya Pradesh	06/2016 (01/2017)	03/2022 (12/2025)	2478.23 (4127.23)	3332.06	95
601	Satna-Rewa Railway Line Doubling Project (West Central Railway [WCR] - II) (705659)	Madhya Pradesh	11/2015 (08/2017)	03/2026 (03/2026)	500 (584)	565.66	82
602	Doubling of Katni - Singrauli Railway Line [261 km] (Indian Railway Construction International Limited [IRCON]) (705660)	Madhya Pradesh	03/2016 (03/2017)	12/2025 (12/2025)	2445 (4377)	3242.32	100
603	Katni Grade Separator/Bye Pass (Indian Railway Construction International Limited [IRCON]) (705661)	Madhya Pradesh	03/2016 (09/2017)	09/2024 (03/2026)	1248 (1248)	1662.02	95
604	Indore - Budni New Railway Line [198 kms] (RVNL - II) (705763)	Madhya Pradesh	08/2019 (10/2020)	09/2030 (09/2030)	7474 (7474)	1841.69	25
605	Nimach-Ratlam Doubling [133 Km] (Western Railway [WR] - II) (705933)	Madhya Pradesh	10/2021 (10/2021)	10/2027 (10/2027)	1095.88 (1095.88)	1067.49	89
606	DHULE [BORVIHIR] - NARDANA NEW LINE [50.60 KMS] (Central Railway) (400019)	Maharashtra	01/2019 (04/2023)	12/2026 (09/2027)	492.76 (1170.83)	288.08	17
607	Wardha-Nanded Via Yavatmal New BG Line (Central Railway [CR] - II) (400271)	Maharashtra	12/2017 (04/2008)	03/2025 (12/2026)	3445 (3445)	3002.93	50
608	AURANGABAD-ANKAI - DOUBLING PROJECT 98.25 Km (South Central Railway [SCR] - II) (611751)	Maharashtra	05/2023 (05/2023)	03/2027 (-)	960.64 (960.64)	555.02	1
609	Redevelopment of Chhatrapati Shivaji Maharaj Terminus [CSMT] and construction of associated infrastructure (Rail Land Development Authority) (613015)	Maharashtra	04/2023 (07/2023)	03/2027 (-)	1813 (1813)	614.86	17
610	Gondia-Balharshah [Chanda Fort] Doubling [240 Km] (South East Central Railway) (617201)	Maharashtra	04/2025 (04/2025)	03/2031 (-)	4373.04 (4373.04)	0.29	0
611	Doubling between Parbhani Parli Vajjanath stations 64.71 Km (South Central Railway [SCR] - II) (617215)	Maharashtra	12/2023 (12/2023)	03/2028 (-)	769.93 (769.93)	25.4	0
612	Babupeth - Sasti New Rail Line [13.114 KMS] (CentralRailway) (617361)	Maharashtra	10/2024 (10/2024)	03/2028 (-)	362.81 (362.81)	0.47	0
613	Double Chord line Between Nilaje-Kopar (CentralRailway) (617364)	Maharashtra	01/2025 (01/2025)	07/2028 (-)	338.33 (205)	6.39	0
614	Western Region Video Surveillance Project (RCIL) (705300)	Maharashtra	06/2020 (04/2023)	12/2023 (-)	227.59 (227.59)	0	0
615	Ahmednagar - Beed - Parli - Vajjnath New Broad Gauge Line Railway Project [261.3 km] (Central Railway [CR] - II) (705356)	Maharashtra	01/1999 (10/2002)	03/2026 (03/2026)	2538.67 (4957.27)	5140.63	98
616	Baramati Lonand New Line Project (Central Railway) (705357)	Maharashtra	03/2016 (03/1999)	03/2027 (03/2027)	138.48 (1843.9)	850.75	51
617	Wadsa-Gadchiroli (South East Central Railway) (705479)	Maharashtra	05/2017 (03/2012)	03/2027 (03/2027)	1886 (1886)	728.36	53
618	3rd Line Kalyan - Kasara [67.35 Kilometres] (Central Railway) (705498)	Maharashtra	09/2015 (09/2015)	12/2026 (12/2026)	792.89 (1395.79)	981.36	52

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
619	3rd Line Wardha - Sewagram - Nagpur (Central Railway [CR] - II) (705500)	Maharashtra	09/2015 (05/2016)	12/2025 (12/2025)	540.02 (944.24)	783.01	83
620	3rd Line Wardha - Ballarshah [132 Kilometres] (Central Railway [CR] - II) (705502)	Maharashtra	03/2016 (12/2016)	12/2025 (02/2026)	1384.72 (2033.59)	1713.23	80
621	Pune - Miraj-Londa [467 Kilometres] (Central Railway) (705503)	Maharashtra	06/2016 (06/2016)	02/2025 (08/2025)	4027.53 (4872.52)	4969.74	100
622	Doubling of Daund Manmad Line [247.6 km] (Central Railway) (705504)	Maharashtra	10/2017 (03/2017)	12/2025 (03/2026)	2081.27 (3267.06)	2874.47	92
623	4th Line Wardha - Nagpur [78.7 Kilometres] (Central Railway [CR] - II) (705505)	Maharashtra	04/2017 (05/2018)	12/2025 (02/2026)	637.95 (1341.28)	1012.82	83
624	3rd Line Manmad - Jalgaon [160 Kilometres] (Central Railway [CR] - II) (705506)	Maharashtra	05/2017 (04/2018)	12/2024 (08/2025)	1035.16 (1558.75)	1726.94	95
625	Solapur-tuljapur-Osmanabad (Central Railway) (705735)	Maharashtra	08/2018 (12/2023)	03/2027 (03/2028)	904.92 (3295.74)	1154.89	12
626	Nagpur- Nagbhir Railway Line Gauge Conversion Project (MRIDC) (705799)	Maharashtra	10/2019 (04/2020)	12/2025 (12/2025)	1400 (1400)	1472	80
627	Mumbai Urban Transport Project [MUTP] - PHASE II (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706779)	Maharashtra	05/2008 (04/2008)	03/2014 (12/2027)	8087 (8087)	7364	87
628	Mumbai Urban Transport Project [MUTP] Phase-III A (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706780)	Maharashtra	04/2019 (04/2019)	12/2027 (12/2027)	33690 (33690)	2805	16
629	Mumbai Urban Transport Project Phase-III (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706781)	Maharashtra	11/2016 (12/2016)	03/2022 (12/2026)	10947 (10947)	5588.85	65
630	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (709808)	Maharashtra	08/2022 (01/2022)	08/2027 (03/2028)	955.39 (2093.82)	130.42	11
631	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	15782.48	72
632	Marikuppam - Kuppam New Line Project [23.70 Km] (South Western Railway [SWR] - II) (705491)	Multi-States (Andhra Pradesh, Karnataka)	04/2012 (10/2018)	06/2026 (06/2026)	297 (297)	135.5	20
633	Rayadurg-Tumkur via Kalyandurg New Line [207 km] (South Western Railway [SWR] - II) (705494)	Multi-States (Andhra Pradesh, Karnataka)	03/2008 (07/2010)	09/2015 (02/2028)	2496 (2496)	1787.43	70
634	Renigunta, Wadi & Gooty Bypass Railway Project (South Central Railway [SCR] - I) (705610)	Multi-States (Andhra Pradesh, Karnataka)	04/2016 (04/2016)	12/2025 (12/2025)	302 (543)	381	50
635	Doubling between Mudkhed Medchal & Mahbubnagar Dhone section 417.88 Km (South Central Railway [SCR] - II) (617212)	Multi-States (Andhra Pradesh, Maharashtra, Telangana)	08/2023 (08/2023)	03/2029 (-)	4686.09 (4686.09)	778.34	1
636	Vizianagaram - Titlagarh 3rd line [272 Km including By - pass line of 7.68 KM] (RVNL - II) (400253)	Multi-States (Andhra Pradesh, Odisha)	06/2016 (11/2016)	12/2025 (12/2025)	4803 (6669.91)	5722.01	89
637	Doubling of Kottavalasa-Koraput Rail Line [189 KM] (East Coast Railway [ECOR] - II) (705512)	Multi-States (Andhra Pradesh, Odisha)	12/2015 (01/2016)	03/2022 (03/2028)	2500 (2500)	2037.7	71
638	Vizianagaram-Sambhalpur 3rd Line Project (RVNL) (705520)	Multi-States (Andhra Pradesh, Odisha)	06/2016 (12/2016)	03/2025 (-)	4803.16 (4803.16)	2979.23	0
639	Tindivanam-Nagari New Line Project [184.5 km] (Ministry of Railways) (400275)	Multi-States (Andhra Pradesh, Tamil Nadu)	07/2008 (10/2008)	09/2025 (03/2028)	3631 (3631)	1113.53	18
640	Doubling between Motumari Vishnupuram - 88.81 Km and Rail over Rail - RoR at Motumari - 10.877 Km (South Central Railway [SCR] - II) (616857)	Multi-States (Andhra Pradesh, Telangana)	02/2024 (03/2025)	03/2029 (-)	1595.55 (1595.55)	14.45	1
641	Doubling of Guntur Bibinagar 239 Km (South Central Railway [SCR] - II) (617211)	Multi-States (Andhra Pradesh, Telangana)	08/2023 (08/2023)	03/2029 (-)	2853.23 (2853.23)	75.78	1
642	Rail Connectivity to Errupalem Amravati Namburu 57 Km (South Central Railway [SCR] - II) (617214)	Multi-States (Andhra Pradesh, Telangana)	11/2024 (11/2024)	03/2027 (-)	2047.4 (2047.4)	14.49	0
643	Kazipet-Vijayawada 3rd line with electrification [220 km] (South Central Railway [SCR] - II) (705612)	Multi-States (Andhra Pradesh, Telangana)	03/2013 (08/2014)	02/2025 (12/2025)	1953 (3363)	3625.29	94
644	Vijayawada - Kazipet Bypass line (South Central Railway [SCR] - II) (705632)	Multi-States (Andhra Pradesh, Telangana)	04/2016 (04/2016)	01/2025 (12/2025)	647 (904)	973.78	93
645	Murkongselek-Pasighat (Northeast Frontier Railway [NFR] - II) (705401)	Multi-States (Arunachal Pradesh, Assam)	02/2011 (03/2023)	03/2025 (05/2026)	435 (1250)	771.1	62
646	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	02/2024 (01/2025)	02/2028 (-)	2123.7 (2123.7)	13.74	0
647	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2025)	6663 (6663)	5634.59	81
648	New Delhi- Howrah Speed Booster[160Kmph] Project (PCE/NCR) (705794)	Multi-States (Bihar, Delhi, Jharkhand, Uttar Pradesh, West Bengal)	09/2019 (09/2019)	03/2024 (-)	6684.81 (6684.81)	127.03	0

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
649	Third Railway Line between Patratu-Sonnagar [281 kms] (RVNL - II) (400234)	Multi-States (Bihar, Jharkhand)	11/2016 (08/2018)	03/2026 (07/2026)	8975 (8975)	4950	88
650	Multi tracking of Son Nagar-Andal 374.53 rkm & 814.38 tkm (East Central Railway [ECR] - I) (616699)	Multi-States (Bihar, Jharkhand)	08/2023 (08/2023)	03/2028 (-)	12333.57 (12333.6)	420.86	13
651	Koderma-Tilaiya New Line (East Central Railway [ECR] - I) (705375)	Multi-States (Bihar, Jharkhand)	11/2004 (03/2002)	02/2025 (02/2026)	1626 (2486.62)	2122.42	94
652	Pirpainti - Jasidih [100.52 Km] New BG line (Eastern Railway [ER] - I) (705385)	Multi-States (Bihar, Jharkhand)	03/2014 (03/2022)	03/2028 (03/2028)	2555 (2555)	784.18	49
653	NER Provision of Automatic Block Signalling on Gorakhpur Cantt[Excl] Chhapra Gramin & Burhwal Jn [Excl] Sitapur Jn section of high density routes (North Eastern Railway [NER]) (611669)	Multi-States (Bihar, Uttar Pradesh)	NA (06/2023)	03/2027 (-)	380.47 (380.47)	24.53	0
654	Gorakhpur-Valmikinagar Doubling project (NER) (617224)	Multi-States (Bihar, Uttar Pradesh)	08/2023 (03/2024)	12/2027 (-)	1120 (1120)	269.67	26
655	Chhapra-Ballia Patch Doubling (North Eastern Railway [NER]) (705562)	Multi-States (Bihar, Uttar Pradesh)	03/2013 (12/2015)	02/2025 (03/2026)	963 (1046)	912.16	95
656	Katihar - Kumedpur Doubling Line Project (GM/C/ NFR) (706844)	Multi-States (Bihar, West Bengal)	08/2022 (-)	08/2027 (08/2027)	942 (942)	356	45
657	Rajnandgaon - Nagpur [Kalumna] Third Railway Line [228.30 km] (South East Central Railway [SECR] - II) (705617)	Multi-States (Chhattisgarh, Maharashtra)	09/2016 (12/2016)	12/2024 (06/2026)	3545 (3545)	3518.69	96
658	Sardega - Bhalumuda New Double line [37.24 Km] (SECR) (617390)	Multi-States (Chhattisgarh, Odisha)	09/2024 (09/2024)	03/2028 (-)	1281.81 (1281.81)	128	2
659	Jagdulpur-Koraput (East Coast Railway [ECoR] - II) (705511)	Multi-States (Chhattisgarh, Odisha)	12/2015 (03/2016)	03/2024 (12/2026)	1547 (1547)	1336.83	91
660	Jharsuguda-Bilaspur Fourth Railway Line [206 km] (SECR) (705616)	Multi-States (Chhattisgarh, Odisha)	09/2016 (09/2016)	10/2024 (03/2026)	2140 (2979)	2189.75	93
661	Mumbai-Ahmedabad High Speed Rail Project- 508 km (National High Speed Rail Corporation [NHSRC]) (705728)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	03/2015 (09/2017)	08/2027 (12/2029)	108000 (108000)	84199.89	55
662	New Delhi- Mumbai Speed Booster[160Kmph] Project (PCE/WR) (705793)	Multi-States (Delhi, Gujarat, Madhya Pradesh, Maharashtra, Rajasthan)	09/2019 (09/2019)	03/2024 (-)	6806.44 (6806.44)	135.65	0
663	Hospet - Tinaighat - Vasco Rail Doubling Project (RVNL - II) (705650)	Multi-States (Goa, Karnataka)	03/2010 (07/2012)	03/2027 (12/2027)	5060 (5060)	5246.91	86
664	Hospet-Hubli-Vasco da Gama Line Electrification Project (RVNL) (706950)	Multi-States (Goa, Karnataka)	07/2015 (05/2018)	03/2023 (03/2024)	744.49 (1122.62)	969.05	95
665	Western Dedicated Freight Corridor (DFCCIL) (705237)	Multi-States (Gujarat, Haryana, Maharashtra, Rajasthan, Uttar Pradesh)	02/2008 (01/2012)	03/2022 (12/2025)	51101 (124005)	124623	96
666	New line Dahod-Indore via Sardarpur, Jabuwa and Dhar (Western Railway [WR] - II) (705453)	Multi-States (Gujarat, Madhya Pradesh)	06/2012 (06/2012)	02/2027 (02/2027)	456.07 (3516.77)	3725.91	50
667	Chhota Udaipur - Dhar New Line Project [157 km] (Western Railway [WR] - II) (705454)	Multi-States (Gujarat, Madhya Pradesh)	11/2008 (01/2014)	12/2025 (12/2025)	1794 (1794)	1815.94	80
668	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (Western Railway) (611452)	Multi-States (Gujarat, Maharashtra)	09/2019 (03/2023)	12/2025 (12/2026)	311 (311)	263.42	93
669	Taranga Hill-Abu Road via Ambaji (North Western Railway [NWR]) (400022)	Multi-States (Gujarat, Rajasthan)	07/2022 (07/2022)	07/2030 (07/2030)	2798 (2798)	2037.04	17
670	LUNI- SAMDARI- BHILDI DOUBLING (North Western Railway [NWR]) (616842)	Multi-States (Gujarat, Rajasthan)	02/2024 (02/2024)	07/2027 (-)	3085.59 (3085.59)	363.31	13
671	Chandigarh-Baddi New Rail Line- 36 km (Northern Railway [NR]) (705424)	Multi-States (Haryana, Himachal Pradesh)	02/2018 (02/2018)	12/2026 (12/2026)	1540 (1540.13)	539.29	35
672	Rewari - Kathuwas Doubling Project [27.72 Km] (North Western Railway [NWR]) (611861)	Multi-States (Haryana, Rajasthan)	02/2023 (12/2022)	06/2027 (06/2027)	352 (352)	275.26	66
673	Nangal Dam-Talwara New Broad Gauge Line [84 KM] and Taking Over Siding Mukerian-Talwara [29 KM] (Northern Railway [NR]) (705410)	Multi-States (Himachal Pradesh, Punjab)	03/1983 (05/1985)	12/2025 (12/2027)	2018 (2018)	2259.62	82
674	Bhanupalli-Bilaspur-Beri New Railway Line Project (RVNL - II) (705428)	Multi-States (Himachal Pradesh, Punjab)	03/2009 (04/2015)	12/2026 (12/2027)	13447 (13447)	7008.64	61
675	Doubling of Hatia [Ranchi]-Bondamunda Rail Line - 159 km (South Eastern Railway - JH) (705628)	Multi-States (Jharkhand, Odisha)	03/2016 (02/2017)	06/2025 (06/2026)	3029 (3029.04)	2525.28	87
676	Buramara-Chakulia new line [59.96 km] (South Eastern Railway [SER] - I) (616588)	Multi-States (Jharkhand, Odisha, West Bengal)	08/2024 (12/2024)	12/2029 (-)	1459.13 (1459.13)	3.33	0

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
677	Chandil - Anara - Damodar - 3rd line [121.26 km] (CAO/C/SER) (616227)	Multi-States (Jharkhand, West Bengal)	09/2024 (07/2025)	09/2029 (-)	1932.01 (1932.01)	0.3	0
678	KHARAGPUR-ADITYAPUR THIRD RAIL LINE- 132 KM (RVNL - I) (705668)	Multi-States (Jharkhand, West Bengal)	09/2016 (01/2018)	03/2025 (12/2025)	3250 (3250)	3176.46	97
679	Hotgi-Kudgi-Gadag Doubling Project (South Western Railway [SWR] - II) (705662)	Multi-States (Karnataka, Maharashtra)	04/2014 (01/2016)	12/2024 (03/2026)	1878 (2459)	2684.67	92
680	Baiyyappanahalli - Hosur Doubling Project [48 km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703586)	Multi-States (Karnataka, Tamil Nadu)	04/2019 (02/2019)	03/2024 (01/2026)	498.7 (748.7)	630.41	86
681	Trivandrum- Kanyakumari (Southern Railway (SR) - I) (705635)	Multi-States (Kerala, Tamil Nadu)	08/2017 (03/2016)	03/2025 (12/2026)	1432 (3785.45)	2505.8	50
682	Ratlam-Mhow-Khandwa-Akola Gauge Conversion (Western Railway [WR] - II) (705457)	Multi-States (Madhya Pradesh, Maharashtra)	04/2008 (03/2010)	03/2027 (09/2028)	1656.25 (6499.86)	4445.82	81
683	Itarsi - Nagpur Third Railway Line [280 km] (Central Railway (CR) - II) (705507)	Multi-States (Madhya Pradesh, Maharashtra)	09/2016 (09/2016)	03/2027 (12/2027)	2449.91 (2506.68)	1937.22	55
684	RATLAM- DUNGARPUR VIA BANSWARA NEW LINE PROJECT (North Western Railway [NWR]) (617406)	Multi-States (Madhya Pradesh, Rajasthan)	10/2015 (05/2023)	03/2028 (-)	2417.24 (2417.24)	6.79	8
685	Gwalior - Seopurkala with extension to Kota [Gauge Conversion] (North Central Railway) (705419)	Multi-States (Madhya Pradesh, Rajasthan)	03/2011 (07/2018)	03/2025 (02/2026)	2913 (2913)	2120.66	85
686	Ramganjmandi-Bhopal New Line Project [262 km] (West Central Railway [WCR] - II) (705481)	Multi-States (Madhya Pradesh, Rajasthan)	03/2001 (10/2004)	12/2025 (12/2027)	3032 (5073)	3764.11	70
687	Nimach-Badi Sadri New Rail Line Project (Western Railway [WR] - II) (705764)	Multi-States (Madhya Pradesh, Rajasthan)	04/2017 (09/2021)	03/2026 (06/2026)	495 (825)	130.09	57
688	Mathura-Jhansi Third Railway Line [274 Km] (RVNL - II) (705667)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	12/2015 (03/2018)	12/2024 (12/2026)	5961 (5961)	4990.85	94
689	Jhansi - Bina Third Railway Line [153 Km] (CAO/C/NCR) (705598)	Multi-States (Madhya Pradesh, Uttar Pradesh)	09/2016 (03/2018)	03/2022 (03/2026)	2002 (2002)	1831.86	93
690	Jhansi-Khairar-Manikpur & Khirar-Bhimsen (North Central Railway) (705608)	Multi-States (Madhya Pradesh, Uttar Pradesh)	03/2018 (04/2019)	03/2026 (03/2026)	4330 (4330)	2456.1	62
691	Third Line [new] between Kazipet - Balharshah with electrification [201.04 Km] (South Central Railway [SCR] - II) (705613)	Multi-States (Maharashtra, Telangana)	09/2016 (10/2016)	01/2025 (11/2025)	2595 (3071)	3409.31	94
692	Narayangarh-Bhadrak 3rd line (South Eastern Railway [SER] - I) (705629)	Multi-States (Odisha, West Bengal)	03/2019 (03/2017)	12/2025 (06/2026)	2400 (3425.32)	2344.37	66
693	Nagapattinam-Tiruturaipundi and Karaikal-Peralam New Line (Ministry of Railways) (400223)	Multi-States (Puducherry, Tamil Nadu)	07/2008 (01/2019)	03/2027 (03/2028)	713 (981)	598.38	80
694	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Multi-States (Sikkim, West Bengal)	10/2009 (05/2010)	05/2015 (12/2027)	7877 (11775)	9647.55	89
695	Sainthia, Sitarampur, Mughalsarai, Allahabad & Etawah - Bypass Line Project (Eastern Railway [ER] - I) (602797)	Multi-States (Uttar Pradesh, West Bengal)	08/2017 (12/2017)	03/2027 (03/2027)	461.64 (461.64)	193.39	8
696	Proposed 6 nos Road Over Bridge [ROB] at different locations under MCL Talcher Under Deposit Scheme. (East Coast Railway [ECoR] - II) (400045)	Odisha	08/2022 (07/2022)	03/2025 (01/2025)	168.32 (168.32)	69.85	82
697	Brundamal-Jharsuguda- flyover connection for joining downline (East Coast Railway [ECoR] - II) (400232)	Odisha	01/2014 (01/2014)	12/2026 (12/2026)	297 (297)	209.57	45
698	3rd & 4th line between Sarla - Sason [8 km] [PB 73/2023-24/NR] (East Coast Railway [ECoR] - II) (612834)	Odisha	04/2023 (04/2023)	12/2025 (-)	252 (252)	91.45	65
699	Bangriposi-Gorumahisani new line [85.60 km] (CAO/C/SER) (616586)	Odisha	08/2024 (09/2025)	12/2029 (-)	2269.49 (2269.49)	4.08	0
700	Badampahar-Kendujhargarh new line [82.06 km] (CAO/C/SER) (616587)	Odisha	08/2024 (09/2025)	12/2029 (-)	1875.72 (1875.72)	1.04	0
701	Paradeep - Badabandha 3rd & 4th Line / 18.51kms (East Coast Railway [ECoR] - II) (616695)	Odisha	08/2023 (04/2025)	11/2028 (-)	300.15 (300.15)	0	0
702	Khurda-Bolangir New Broad Gauge Rail Link [301km] (East Coast Railway [ECoR] - II) (705358)	Odisha	03/1994 (03/2001)	12/2026 (12/2026)	3792 (5089)	5194.05	89
703	Talcher-Bimlagarh New Railway Line (East Coast Railway [ECoR] - II) (705359)	Odisha	03/2004 (12/2004)	03/2025 (03/2027)	1928 (1928)	1972.31	49
704	Bhadrak-Nergundi Third Line (East Coast Railway [ECoR] - II) (705510)	Odisha	10/2015 (04/2015)	11/2024 (01/2026)	1284 (1284)	1298	80
705	Koraput - Singapur Railway Doubling (East Coast Railway [ECoR] - II) (705513)	Odisha	12/2015 (12/2015)	12/2027 (03/2028)	2362 (2362)	1834.53	70
706	Jarapada- Budhapank with flyover at Talcher road 3rd and 4th Line (East Coast Railway [ECoR] - II) (705514)	Odisha	11/2015 (12/2015)	11/2018 (03/2026)	1000 (810.02)	421.59	58

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
707	3rd & 4th Railway Line Project from Salegaon to Budhapank via Rajathgarh. (East Coast Railway [ECOR] - II) (705515)	Odisha	07/2013 (12/2015)	03/2026 (03/2026)	1173 (2092)	1971	80
708	Jeypore-Navarangpur New Rail Line Project (East Coast Railway [ECOR] - II) (705741)	Odisha	07/2017 (04/2023)	07/2028 (12/2029)	748 (748)	12.76	1
709	Jeypore-Malkanagiri New Railway Line Project (East Coast Railway [ECOR] - II) (705742)	Odisha	02/2018 (12/2023)	07/2033 (07/2033)	2344 (2344)	490.13	20
710	Khurda Road - Balangir Electrification of Railway Track Project (Ministry of Railways) (706898)	Odisha	09/2018 (09/2019)	03/2021 (-)	267.61 (267.61)	0	0
711	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION/12.76kms (East Coast Railway [ECOR] - II) (709811)	Odisha	09/2022 (05/2025)	09/2027 (09/2027)	190 (189.93)	0	0
712	Jaynagar-Bijalpura, incl. extn. Bet, Bijalpura-Bardibas [Nepal] (East Central Railway [ECR] - I) (705362)	Offshore	08/2015 (03/2011)	03/2022 (03/2026)	819 (819)	580.51	75
713	Ludhiana- Killa Raipur Railway Doubling Project (Railway) (705783)	Punjab	03/2019 (12/2022)	03/2025 (03/2026)	237.64 (238)	134.48	50
714	Dedicated Test Track for RDSO Phase II (North Western Railway [NWR]) (611614)	Rajasthan	11/2021 (11/2021)	11/2026 (11/2026)	819.48 (967.06)	471	86
715	Devgarh Madariya - Nathdwara Gauge Conversion [82.54 Km] part of Marwar - Mavli Gauge Conversion [152 Km] (North Western Railway [NWR]) (611849)	Rajasthan	01/2023 (01/2023)	06/2028 (06/2028)	968.92 (968.92)	151.53	52
716	Maintenance cum workshop depot for Vande Bharat Sleeper Trains as per conditions under WTA 527 (WPO/Patna) (611929)	Rajasthan	09/2022 (06/2023)	12/2024 (-)	166.86 (166.86)	0	0
717	PUSHKAR- MERTA CITY NEW LINE (North Western Railway [NWR]) (616841)	Rajasthan	02/2024 (02/2024)	12/2026 (-)	799.64 (799.64)	14.64	4
718	AJMER- CHANDERIYA DOUBLING (North Western Railway [NWR]) (616843)	Rajasthan	02/2024 (02/2024)	06/2027 (-)	1634.79 (1634.79)	140.65	7
719	SADULPUR - CHURU DOUBLING PROJECT (North Western Railway [NWR]) (617403)	Rajasthan	01/2024 (01/2024)	06/2026 (-)	468.64 (468.64)	128.6	52
720	POKHRAN - RAMDEVRA New Line (North Western Railway [NWR]) (617404)	Rajasthan	04/2025 (04/2025)	03/2028 (-)	189.21 (189.21)	0	0
721	NATHDWARA- NATHDWARA TOWN NL (North Western Railway [NWR]) (617408)	Rajasthan	03/2019 (04/2024)	03/2027 (-)	166.33 (166.33)	83.34	2
722	Dholpur - Sirmuttra Gauge Conversion (North Central Railway) (705482)	Rajasthan	03/2022 (04/2020)	02/2019 (02/2027)	747 (747)	431.82	44
723	Gudha-Thatha Mithri Construction of Railway Track Project (North Western Railway [NWR]) (705752)	Rajasthan	04/2019 (04/2019)	11/2026 (11/2026)	819.48 (967.06)	393.06	99
724	Sawai Madhopur-Jaipur Railway Line Project (North Western Railway [NWR]) (705912)	Rajasthan	02/2024 (04/2023)	03/2027 (-)	1203.89 (1203.89)	109.85	13
725	Agra Fort-Bandikui Doubling Line Project (CAO/C/NCR) (705919)	Rajasthan	06/2022 (02/2021)	06/2027 (06/2027)	1390 (1390)	123	25
726	Sawaimadhopur Bye Pass Line Project (North Western Railway [NWR]) (706866)	Rajasthan	12/2022 (01/2023)	03/2026 (05/2027)	304 (304)	53	46
727	Ph II extension of MRTS from Velachery to St Thomas Mount (Ministry of Railways) (400280)	Tamil Nadu	11/2007 (11/2008)	07/2025 (09/2025)	734 (734.01)	475.73	99
728	Redevelopment of Chennai Egmore Station (Ministry of Railways) (613002)	Tamil Nadu	05/2022 (10/2022)	03/2026 (-)	842 (842)	340	0
729	Coach Production Factory Upgradation Project (CPM/ICF) (705244)	Tamil Nadu	12/2017 (07/2018)	12/2021 (-)	520 (520)	192.25	0
730	Doubling between Bhadrachalam Road and Dornakal (South Central Railway [SCR] - II) (616856)	Telangana	08/2023 (04/2025)	04/2029 (-)	770.12 (770.12)	16.34	0
731	Railway Manufacturing Unit (South Central Railway [SCR] - II) (617409)	Telangana	07/2016 (02/2023)	12/2026 (-)	521.36 (521.36)	420	58
732	Kazipet Wagon Overhauling Project (RVNL) (705252)	Telangana	09/2017 (07/2017)	12/2023 (-)	385 (385)	0	0
733	Manoharabad-Kothapalli New Rail Line [151 km] (South Central Railway [SCR] - II) (705437)	Telangana	07/2016 (01/2017)	03/2027 (12/2027)	1160 (2781)	2116.77	71
734	Bahraich-Shravasti-Balrampur-Siddharthnagar -Santkabar nagar (North Eastern Railway [NER]) (400204)	Uttar Pradesh	10/2018 (03/2017)	10/2030 (10/2030)	4939.78 (4939.78)	1253.71	8
735	Sahjanwa-Dohrighat (North Eastern Railway [NER]) (400205)	Uttar Pradesh	08/2019 (03/2017)	03/2029 (03/2029)	1319.75 (1319.75)	485.96	3
736	Anandnagar - Ghugli via Maharajganj New line 52.7 km (Construction NER) (617252)	Uttar Pradesh	10/2023 (11/2023)	03/2028 (-)	958.27 (958.27)	454.36	23

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
737	Chunar-Chopan doubling project (North Central Railway) (617284)	Uttar Pradesh	08/2023 (01/2025)	03/2028 (-)	1423.96 (1423.96)	58.77	5
738	Surface triangle line bet. Bhadura stn and new crossing stn Karma (East Central Railway [ECR] - I) (617333)	Uttar Pradesh	10/2022 (05/2024)	02/2027 (-)	199.96 (199.96)	0	0
739	Doubling between Jaunpur Jn - Zaffarabad 6.28 km (M/S SRC company Infra Private Limited) (617370)	Uttar Pradesh	03/2023 (02/2025)	01/2027 (-)	180.66 (180.66)	4	12
740	Burhwal Gonda 3rd line (North Eastern Railway [NER]) (705567)	Uttar Pradesh	11/2017 (07/2019)	03/2025 (01/2026)	1016 (1118)	1435.86	88
741	Janghai-Pratapgarh- Amethi (CAO/C/II/IR) (705588)	Uttar Pradesh	11/2017 (03/2017)	03/2025 (03/2026)	722 (1194)	1567	70
742	Lalitpur-Birari with flyover at Lalitpur- 16 Km (North Central Railway) (705766)	Uttar Pradesh	03/2017 (11/2017)	12/2024 (01/2026)	304.44 (356)	234.88	80
743	Allahabad-Bamhrauli Flyover Construction & 4th Railway Line Project (North Central Railway) (705771)	Uttar Pradesh	04/2019 (10/2020)	03/2026 (03/2026)	494 (494)	333	70
744	Mughalsarai-Allahabad, 3rd line (North Central Railway) (705772)	Uttar Pradesh	12/2015 (03/2016)	12/2026 (03/2027)	2649 (2649.44)	1688.13	65
745	Aligarh -Daud Khan Flyover Construction & 3rd Railway Line Project (CAO/C/NCR) (705774)	Uttar Pradesh	04/2019 (09/2020)	01/2025 (03/2027)	758 (779.49)	412.67	73
746	Bhandai - Flyover for Etawah bound down train- 10 Km (North Central Railway (NCR) - II) (705777)	Uttar Pradesh	07/2020 (04/2021)	02/2026 (02/2027)	250.18 (250.18)	115.68	8
747	Phephna-Indara, Mau-Shahganj doubling excluding Indara-Mau (RVNL - I) (705779)	Uttar Pradesh	05/2017 (10/2019)	12/2024 (03/2026)	1178 (1777)	1489.5	85
748	Bhatni-Aurnihar with electrification excluding Indara-Mau (RVNL - I) (705780)	Uttar Pradesh	03/2018 (03/2017)	12/2024 (12/2025)	2529 (2529.46)	2051.69	94
749	Barabanki-Malhaur 3rd & 4th Railway Line Project (CAO/C/IR) (705782)	Uttar Pradesh	01/2019 (04/2017)	03/2025 (03/2026)	407 (407)	317	75
750	Janghai-Phaphamau Doubling Rail Line Project (RVNL) (705784)	Uttar Pradesh	11/2018 (03/2020)	03/2025 (03/2025)	357 (978.77)	579	95
751	Rishikesh-Karnaprayag New Rail Line- 125 km (RVNL - I) (705429)	Uttarakhand	11/2016 (08/2018)	12/2025 (03/2027)	38953 (38953)	24645.15	65
752	Kalinarayanpur-Krishnanagar Doubling Alongwith Krishnanagar - Chapra New Line And Naihati-Ranaghat 3rd Line. (Eastern Railway [ER] - I) (400247)	West Bengal	07/2015 (11/2005)	02/2027 (02/2027)	1000 (1000)	1053.99	69
753	Tarakeshwar-Bishnupur New Line [82.47 km] (Eastern Railway [ER] - I) (400273)	West Bengal	03/2001 (02/2008)	03/2019 (02/2026)	1189 (1542)	1330.49	91
754	Dum Dum Airport-New Garia via Rajarhat-Construction of Metro Railway (RVNL - II) (400277)	West Bengal	03/2010 (10/2011)	12/2025 (03/2026)	8964 (8964)	8316.32	81
755	Construction of Balurghat-Hilli new BG Line (Northeast Frontier Railway [NFR]) (612096)	West Bengal	12/2010 (12/2010)	03/2027 (03/2027)	1209 (1181.57)	405.31	9
756	SER Upgradation of maintenance infrastructure at Shalimar into Vande Bharat Chair Car maintenance cum workshop depot. (South Eastern Railway - JH) (617345)	West Bengal	03/2024 (12/2024)	10/2026 (-)	226.87 (226.87)	21.22	20
757	Joka-BBD Bag new metro project (RVNL - II) (705730)	West Bengal	03/2010 (04/2010)	12/2026 (12/2029)	4835 (10362)	4672.28	51
758	Noapara-Barasat via Bimanbandar - Construction of Metro railway [18 km] (Metro Railway, Kolkata) (706776)	West Bengal	11/2010 (03/2010)	08/2026 (03/2029)	4830 (4830)	2764.13	32
759	Baranagar-Barrackpore and Dakshineshwar- Construction of Metro Railway (RVNL - II) (706777)	West Bengal	03/2010 (03/2010)	12/2026 (12/2025)	2298 (2734)	393.01	17
Total (258)					693157.3	542700.33	
Department for Promotion of Industry & Internal Trade							
Real Estate							
760	Krishnapatnam Node - Phase 1 - Roads and Services Development (National Industrial Corridor Development Corporation) (701658)	Andhra Pradesh	12/2020 (02/2024)	02/2028 (-)	2139.44 (2139.44)	503.39	24
761	Tumakuru Node - Phase 1 - Roads and Services Development (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (701657)	Karnataka	12/2020 (02/2023)	09/2026 (-)	1701.81 (1701.81)	153.26	14
Total (2)					3841.25	656.65	
Department of Telecommunications							
Telecommunication							
762	SETTING UP OF PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE [NICF] AT GHITORNI (National Communication Academy - Finance (Erstwhile NICF)) (709859)	Delhi	10/2014 (04/2018)	02/2020 (10/2025)	248.2 (248.2)	236.91	98
763	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (03/2026)	971.96 (971.96)	208.25	99

All Ongoing Projects							NOVEMBER 2025
SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
764	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase 1 Upgradation (Department of Telecommunications [DoT]) (617413)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	04/2022 (05/2024)	05/2025 (03/2026)	1884.6 (1884.6)	100	87
765	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase2 (Department of Telecommunications [DoT]) (701599)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	NA (09/2021)	03/2023 (03/2026)	1577.57 (1577.57)	628.29	87
766	Provision of 4G based mobile services in 7,287 uncovered villages of 44 Aspirational District across 5 states of Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra & Odisha (Department of Telecommunications [DoT]) (701602)	Multi-States (Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra, Odisha)	11/2021 (05/2022)	11/2023 (05/2026)	3685 (3685)	1203.48	82
767	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (03/2026)	1255.49 (1255.49)	284.04	92
768	354 Uncovered Villages Scheme (Department of Telecommunications [DoT]) (701600)	Multi-States (Bihar, Gujarat, Himachal Pradesh, Jammu and Kashmir, Ladakh, Rajasthan, Uttar Pradesh)	12/2019 (04/2020)	10/2021 (08/2025)	336.89 (301.13)	235.96	100
769	502 Aspirational District Scheme in Four states - Bihar, Madhya Pradesh, Rajastha and Uttar Pradesh (Department of Telecommunications [DoT]) (704495)	Multi-States (Bihar, Madhya Pradesh, Rajasthan, Uttar Pradesh)	NA (03/2021)	03/2022 (12/2025)	421.65 (228.94)	142.01	97
770	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (709749)	Multi-States (Maharashtra, Telangana)	03/2020 (03/2020)	06/2021 (12/2025)	461.42 (461.42)	166.02	81
771	Saturation 4G mobile coverage of Uncovered Villages through USOF (Department of Telecommunications [DoT]) (400013)	PAN India	07/2022 (07/2022)	06/2024 (03/2026)	26316 (30620)	9791.8	78
772	4G Services by BSNL (Department of Telecommunications [DoT]) (701593)	PAN India	11/2020 (11/2020)	03/2024 (03/2026)	28466 (19592)	8471.19	97
773	BharatNet (Department of Telecommunications [DoT]) (706775)	PAN India	07/2017 (10/2011)	08/2023 (03/2027)	61109 (188000)	46431.54	81
774	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (709856)	PAN India	05/2023 (05/2023)	08/2024 (11/2025)	645.13 (645.13)	377.59	92
775	Planning, Engineering, Supply, Installation, Testing, Commissioning, Integration & Annual Maintenance of 4G mobile network at 1 Lakh sites on PAN India basis including Mumbai & Delhi LSA on turnkey basis under Phase IX.2 Project. (BSNL) (709857)	PAN India	05/2023 (06/2023)	06/2025 (03/2026)	24544.55 (24544.5)	8472.04	97
776	OPTICAL TRANSPORT NETWORK [OTN] PH-4 IN BSNL (BSNL) (709858)	PAN India	02/2024 (02/2024)	08/2025 (11/2025)	810.99 (810.99)	786.86	100
Total (15)					152734.45	77535.98	
Department of Water Resources, River Development & GR							
Waste & Water							
777	Interception and Diversion and STP works in Bhagalpur under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616600)	Bihar	10/2017 (03/2022)	02/2025 (12/2025)	413.29 (413.29)	126.67	97
778	Sewage Treatment Plant 100MLD and Sewerage Network 288 km in Digha-Patna under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616611)	Bihar	08/2017 (07/2019)	12/2025 (-)	824 (824)	396.71	56
779	Sewage Treatment Plant 50MLD and Sewerage Network 150 km in Kankarbagh-Patna under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616612)	Bihar	08/2017 (07/2019)	12/2025 (-)	578.89 (578.89)	171.79	54
780	Sewer Network, SPS and STP at Begusarai (National Mission for Clean Ganga) (616615)	Bihar	03/2010 (03/2018)	04/2025 (12/2025)	230.06 (230.06)	261.82	97
781	Sewer Networks, SPS and STP at Hajipur (National Mission for Clean Ganga) (616616)	Bihar	03/2010 (03/2018)	06/2025 (12/2025)	305.19 (305.19)	346.46	95
782	Interception & Diversion with Rehabilitation of sewerage scheme at Agra under Hybrid annuity based PPP model-Namami Gange Programme (National Mission for Clean Ganga) (616594)	Uttar Pradesh	05/2020 (04/2023)	04/2025 (12/2025)	842.25 (842.25)	208.64	77

All Ongoing Projects							NOVEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
783	Pollution Abatement Works for River Kali Meerut under Meerut Municipality Interception & Diversion with STP (National Mission for Clean Ganga) (616605)	Uttar Pradesh	05/2020 (11/2024)	12/2024 (05/2027)	690.71 (690.71)	34.79	38
784	Pollution Abatement works for River Ganga at Hooghly Chinsurah- Municipal Town Interception & Diversion with STP (National Mission for Clean Ganga) (616604)	West Bengal	05/2018 (12/2021)	03/2025 (12/2025)	154.73 (154.73)	96.17	92
	Total (8)				4039.12	1643.05	
	Water Resources						
785	Sardar Gouthu Latchanna Thotapalli Barrage Project (Water Resources-AP) (400100)	Andhra Pradesh	04/2005 (01/2006)	12/2019 (06/2026)	353.05 (1023.24)	869.11	95
786	Gundlakamma project (Water Resources-AP) (400101)	Andhra Pradesh	04/2005 (04/2005)	12/2019 (03/2027)	397.41 (697.39)	619.09	98
787	Polavaram Irrigation Project (Water Resources-AP) (701415)	Andhra Pradesh	01/2009 (11/2009)	04/2022 (03/2026)	10151.04 (55548.9)	25291.59	84
788	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55
789	Punpun Barrage Project (Water Resources-BR) (400104)	Bihar	04/2007 (04/2007)	12/2019 (03/2026)	571.07 (658.12)	447.68	44
790	Kelo Irrigation Project (Water Resources-CT) (400111)	Chhattisgarh	04/2008 (04/2008)	12/2019 (06/2026)	459.97 (727.04)	616.93	72
791	Kudali Irrigation Project (Department of Water Resources, River Development & GR) (701399)	Chhattisgarh	04/2009 (12/2009)	12/2025 (-)	382.29 (382.29)	239.03	86
792	Sardar Sarovar CADWM Project (Narmada and Water Resources, Water Supply and Kalpsar Department-GJ) (400097)	Gujarat	04/2017 (04/2017)	12/2019 (03/2026)	5021.76 (6670.31)	4957.08	90
793	Sardar Sarovar Project (Narmada and Water Resources, Water Supply and Kalpsar Department-GJ) (701372)	Gujarat	04/1996 (04/1996)	12/2019 (03/2026)	20718.17 (33412.5)	31860.86	93
794	Subernarekha Multipurpose Project, Jharkhand (Department of Water Resources-JH) (701376)	Jharkhand	04/2011 (01/2012)	12/2019 (03/2026)	3807.77 (9579.58)	5790.29	70
795	Upper Tunga Irrigation Project (Water Resources-KA) (701377)	Karnataka	04/2014 (04/2014)	12/2019 (03/2026)	770.16 (1606.07)	1515.32	99
796	Omkareshwar CADWM Project (Water resource-mp) (400096)	Madhya Pradesh	04/2017 (04/2017)	12/2019 (03/2026)	648.09 (648.09)	203.06	49
797	Bargi Diversion Project Phase - IV [km. 154 to km 197] (Water Resources-MP) (400115)	Madhya Pradesh	04/2008 (01/2009)	12/2019 (03/2026)	751.03 (893.35)	783.1	75
798	Bargi Diversion Project Phase - III [km. 104 to km 154] (Water Resources-MP) (400116)	Madhya Pradesh	04/2007 (04/2007)	12/2019 (03/2026)	1229.15 (1399.7)	1937.25	80
799	Gosikhurd CADWM Project (Department of water resources-MH - II) (400095)	Maharashtra	04/2017 (04/2017)	12/2019 (06/2026)	743.73 (743.73)	365.86	52
800	Urmodi Irrigation Project (Department of water resources-MH - II) (400105)	Maharashtra	04/2017 (04/2018)	06/2022 (12/2026)	580.79 (895.81)	713.46	76
801	Sulwade-Jamphal-Kanoli Lift Irrigation Scheme (Department of water resources-MH - II) (400107)	Maharashtra	04/2017 (02/2019)	06/2023 (06/2027)	2407.67 (2407.67)	2579.27	80
802	Purna Barrage-2 [Ner Dhamana] Medium Irrigation Project (Department of water resources-MH - II) (400109)	Maharashtra	04/2017 (04/2018)	06/2020 (06/2026)	848.07 (888.43)	690.49	69
803	Jigaon Irrigation Project (Department of water resources-MH - II) (400112)	Maharashtra	04/2017 (04/2018)	06/2028 (-)	7222.95 (7222.95)	9035.2	90
804	Bodwad Parisar Sinchan Yojna (Department of Water Resources-MH) (617422)	Maharashtra	05/2002 (01/2017)	07/2027 (-)	1923.81 (1923.81)	1770.13	49
805	Waghur Project (Department of water resources-MH - II) (701383)	Maharashtra	04/1996 (04/1996)	12/2019 (03/2026)	1058.99 (1758.51)	1557.64	89
806	Gosikhurd Project (Department of water resources-MH - II) (701386)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2028)	7196.47 (12770.1)	13837.78	72
807	Aruna Medium Irrigation Project (Department of water resources-MH - II) (701391)	Maharashtra	04/2009 (01/2010)	12/2019 (12/2025)	210.45 (1472.14)	1705.83	97
808	Lower Pedhi Project (Department of water resources-MH - II) (701396)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2026)	255.97 (1480.7)	1324.98	65
809	Nardave Medium Irrigation Project (Department of water resources-MH - II) (701398)	Maharashtra	04/2009 (04/2009)	12/2019 (06/2026)	211.46 (781.85)	623.5	72
810	Thoubal Multipurpose Project (Water Resources Department-MN) (701400)	Manipur	04/1997 (04/1997)	12/2019 (03/2026)	1449.44 (1822.24)	1837.91	98
811	North Koel Reservoir Project (Department of Water Resources, River Development & GR) (701412)	Multi-States (Bihar, Jharkhand)	08/2017 (01/2021)	03/2021 (03/2026)	1622.27 (2430.76)	151.04	32

All Ongoing Projects

NOVEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
812	Integrated Anandpur Barrage Project (<i>Water Resources-OR</i>) (603945)	Odisha	04/1997 (01/1998)	12/2019 (06/2026)	567.03 (2990.05)	2715.12	62
813	Kanupur Irrigation Project (<i>Irrigation and CAD-TG</i>) (701404)	Odisha	04/2003 (01/2004)	12/2019 (06/2026)	989.43 (2301.28)	2712.75	79
814	Relining of Rajasthan feeder and Sirhind Feeder canal (<i>Department of Water Resources-PB</i>) (701410)	Punjab	02/2016 (04/2018)	06/2021 (06/2026)	1441.26 (2462.16)	3012.69	80
815	Shahpur Kandi Dam Project (<i>Department of Water Resources-PB</i>) (701411)	Punjab	02/2010 (04/2018)	06/2022 (10/2025)	2285.81 (2715.7)	2169.72	88
816	Sri Ram Sagar Project Stage - II (<i>Irrigation and CAD-TG</i>) (400102)	Telangana	04/2005 (04/2005)	12/2019 (03/2026)	736.13 (949.87)	940.7	96
817	Indiramma Flood Flow Canal Project (<i>Irrigation and CAD-TG</i>) (400103)	Telangana	04/2005 (01/2006)	12/2019 (12/2026)	1331.3 (5940.09)	4491.08	92
818	J. Chokka Rao Devadula Lift Irrigation Scheme (<i>Irrigation and CAD-TG</i>) (701405)	Telangana	04/2006 (04/2006)	12/2019 (12/2025)	8200.71 (14730)	4664.8	87
819	Rajiv Bhima Lift Irrigation Scheme (<i>Irrigation and CAD-TG</i>) (701406)	Telangana	04/2007 (01/2008)	12/2019 (03/2026)	1402 (2509.66)	1839.76	100
820	Saryu Nahar CADWM Project (<i>Irrigation & Water Resources-UP</i>) (400093)	Uttar Pradesh	04/2017 (04/2017)	12/2019 (03/2026)	1672.7 (1672.7)	22.24	1
821	Morna [Gureghar] Irrigation Project (<i>Department of Water Resources, River Development & GR</i>) (701395)	Uttar Pradesh	04/2007 (12/2007)	12/2025 (-)	219.9 (219.9)	115.2	31
822	Madhya Ganga canal Phase-II (<i>Irrigation & Water Resources-UP</i>) (701408)	Uttar Pradesh	04/2008 (04/2008)	12/2019 (12/2025)	1060.67 (4417.21)	4552.44	82
823	Jamrani Dam Multipurpose Project (<i>Irrigation-UK</i>) (613787)	Uttarakhand	10/2023 (11/2023)	06/2029 (-)	2584.1 (2584.1)	968.52	16
Total (39)					93740.23	139573.2	

Note: For projects 626227 & 709811 (at S.no. 677 & 711 above), stage has changed from 'Under Development' to 'Under Implementation' during month November 2025.



सत्यमेव जयते

Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.ipm.mospi.gov.in>
